


ID	Task Name	Duration	Start	Finish	Predecessors	17	24	31	7	14	21	28	4	11	18	25	3	10	17	24	31	7	14	21	28	5	12	19	26	2	9	16
1	The Highwaymen Museum	145 days	Tue 6/11/24	Mon 12/30/24	17																											
2	CoFP Department Permitting	41 days	Tue 12/19/23	Tue 2/13/24																												
3	COA Application Approval	12 days	Tue 12/19/23	Wed 1/3/24																												
4	DPCR Application Approval	1 day	Thu 1/4/24	Thu 1/4/24	3																											
5	Planning Department Prescreen Review	3 days	Thu 1/4/24	Mon 1/8/24	4SS																											
6	DPCR Application Resubmission request from City	0 days	Thu 1/4/24	Thu 1/4/24	4																											
7	AOR resubmit drawings per 2023 FBC & ASCE codes	9 days	Thu 1/18/24	Tue 1/30/24	5																											
8	Planning Department Approval	4 days	Thu 2/8/24	Tue 2/13/24	6,7																											
9	Fire Department Permitting	46 days	Thu 3/21/24	Thu 5/23/24																												
10	FD Permit Check Payment	21 days	Fri 3/22/24	Fri 4/19/24	8																											
11	Building Drawing Submission	33 days	Thu 3/21/24	Mon 5/6/24	8																											
12	Fire Sprinkler Drawing Submission	33 days	Thu 3/21/24	Mon 5/6/24	3																											
13	Fire Alarm Drawing Submission	14 days	Wed 4/17/24	Mon 5/6/24	3																											
14	Low Voltage Drawing Submission	23 days	Thu 4/4/24	Mon 5/6/24	3																											
15	Department Approval	14 days	Mon 5/6/24	Thu 5/23/24	3																											
16	Building Department Permitting	12 days	Fri 5/24/24	Mon 6/10/24																												
17	Building Permit Approval	12 days	Fri 5/24/24	Mon 6/10/24	15																											
18	Exterior Finishes	14 days	Tue 6/11/24	Fri 6/28/24																												
19	Demo exterior concrete stairs / railing - 2nd FL	3 days	Tue 6/11/24	Thu 6/13/24	17																											
20	Remove concrete slab - East	1 day	Tue 6/11/24	Tue 6/11/24	19SS																											
21	Relocate domestic water line - East	5 days	Wed 6/12/24	Tue 6/18/24	20																											
22	Build temp. exterior stairs & railing - East	2 days	Wed 6/19/24	Thu 6/20/24	20,21																											
23	Install concrete pad for Generator	2 days	Wed 6/12/24	Thu 6/13/24	17FS+1 day																											
24	Inspection	3 days	Fri 6/21/24	Tue 6/25/24	22,20,23																											
25	Stucco	2 days	Wed 6/26/24	Thu 6/27/24	24																											
26	Paint	3 days	Wed 6/26/24	Fri 6/28/24	24																											
27	Exterior Openings	12 days	Wed 6/12/24	Thu 6/27/24																												
28	Remove exterior door & frames	4 days	Wed 6/12/24	Mon 6/17/24	20SS+1 day																											



Project: Highwaymen Museum
Date: Mon 5/6/24

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			

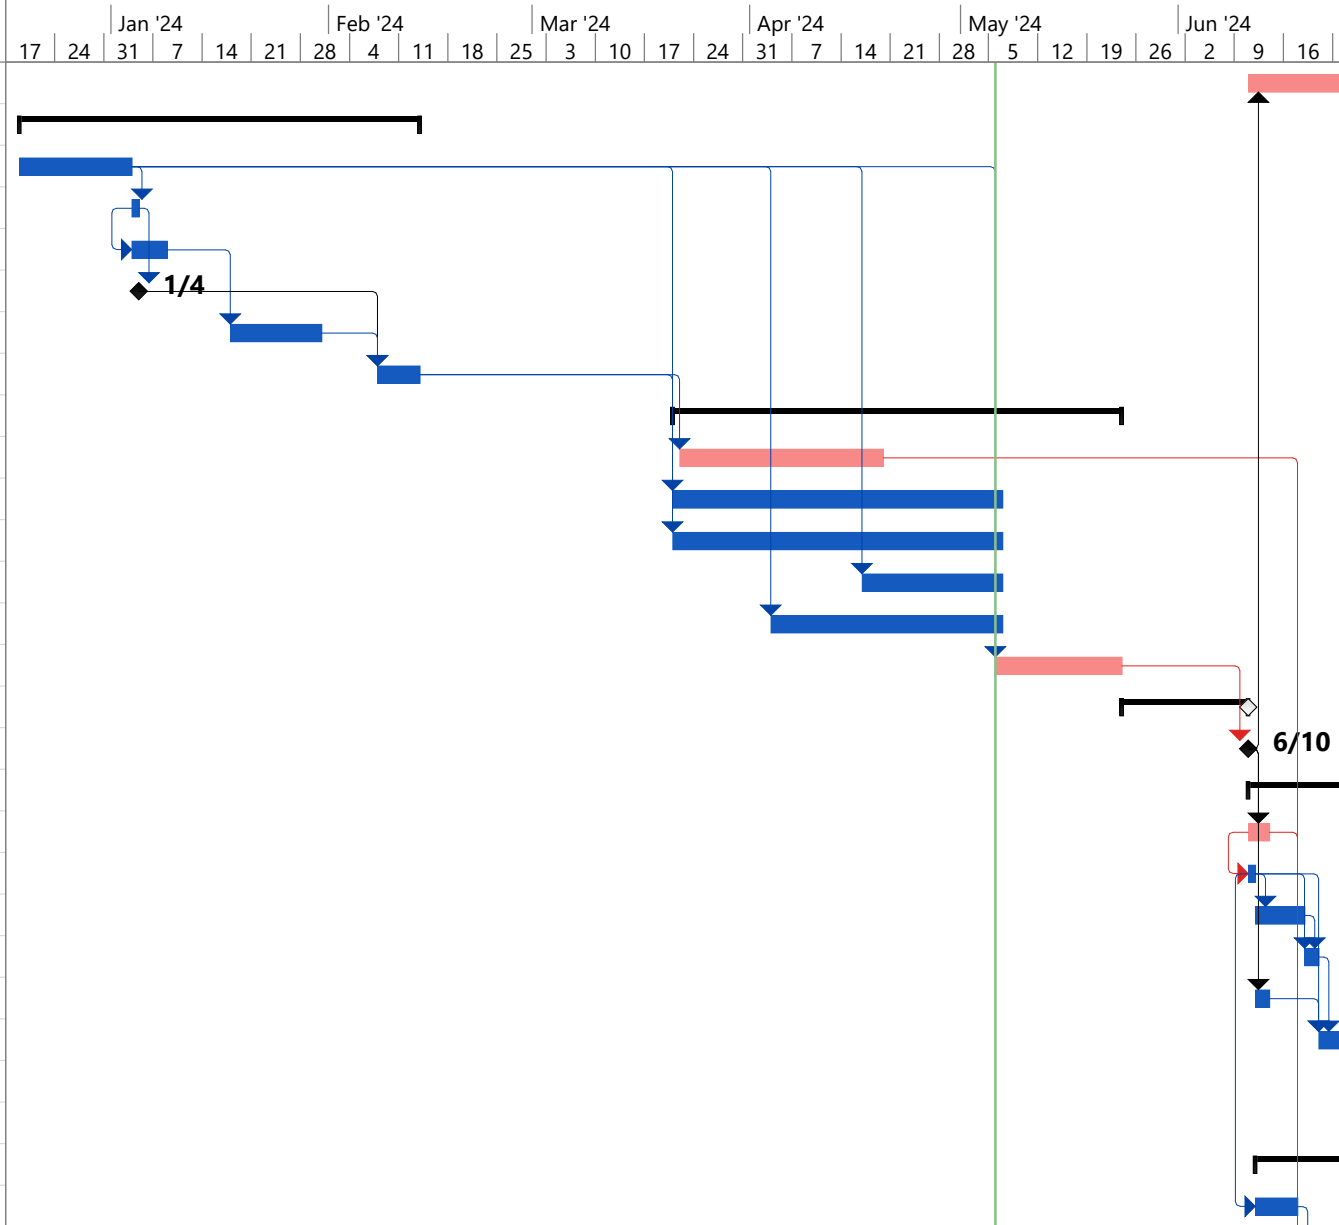
