

12/09/08

### APPLICATION FOR PAYMENT NO. 1

To: Hidalgo County (OWNER)  
 From: Valley Paving, Inc. (CONTRACTOR)  
 Contract: CAP-08-008-03-26 LRM  
 Project: Road and Drainage Construction of Villa Capri Subdivision  
 OWNER's Contract No. CAP-08-008-03-26 04-22 ENGINEER's Project No. 06-167  
 For Work accomplished through the date of: 11/17/2008

1. Original Contract Price:		\$	<del>98,217.37</del>
2. Net change by Change Orders and Written Agreements (+ or -):		\$	<del>2,437.50</del>
3. Current Contract Price (1 plus 2):		\$	<del>100,654.87</del>
4. Total completed and stored to date:		\$	44,531.00
5. Retainage (per Agreement):			
<u>10%</u> of completed Work:	\$	<u>4,453.10</u>	
<u>0%</u> of stored material:	\$	-	
Total Retainage:		\$	<del>4,453.10</del>
6. Total completed and stored to date less retainage (4 minus 5):		\$	<del>40,077.90</del>
7. Less previous Application for Payments:		\$	-
8. AMOUNT DUE THIS APPLICATION (6 MINUS 7):		\$	<del>40,077.90</del>

P.O. 605.351

Accompanying Documentation: 8-1311-431-00-123-784-1-733 - \$3,431.00 - (343.10) = \$3,087.90  
8-1311-431-00-123-784-1-734 - \$41,100.01 - (4,110.00) = \$36,990.01  
8-1203-431-00-123-005-0-734 \$40,077.91


CONTRACTOR'S Certification: The undersigned CONTRACTOR certifies that (1) all previous progress payments received from OWNER on account of Work done under the Contract referred to above have been applied on account to discharge CONTRACTOR's legitimate obligations incurred in connection with Work covered by prior Applications for Payment numbered 1 through 2 inclusive; (2) title of all Work, materials and equipment incorporated in said Work or otherwise listed in or covered by this Application for Payment will pass to OWNER at time of payment free and clear of all Liens, security interests and encumbrances (except such as are covered by a Bond acceptable to OWNER indemnifying OWNER against any such Lien, security interest or encumbrance); and (3) all Work covered by this Application for Payment is in accordance with the Contract Documents and not defective.

Dated 11/19/08 Valley Paving Inc.  
 CONTRACTOR

By: [Signature]

State of Texas  
 County of Hidalgo  
 Subscribed and sworn to before me this 19th  
 day of November, 2008

Rosalinda Trevino  
 Notary Public  
 My Commission expires: 02-23-11



Payment of the above AMOUNT DUE THIS APPLICATION is recommended.

Dated 11-20-08 HINDJOSA ENGINEERING INC  
 ENGINEER  
 By: [Signature]



Estimate Quantity Update Worksheet  
 Villa Capri Subdivision  
 Colonia Access Program Project - Precinct No.3  
 CAP-08-008-83-2622  
 Contractor: Valley Paving

Item No.	Description	Quantity	Unit	Unit Price	Project Amount	RFP 1		
						Monthly Quantity	Quantity to Date	Item Cost (Monthly)
<b>Roadway</b>								
100	Preparing ROW	10.63	STA	\$855.00	\$9,088.65	10.63	10.63	\$9,088.65
110	Excavation	1445	CY	\$4.20	\$6,069.00	1445	1445	\$6,069.00
247	Flex Base	735	CY	\$21.45	\$15,765.75	367.5	367.5	\$7,882.88
251	Reworking Base Material (DC)(TY D CL2)	735	CY	\$5.80	\$4,263.00	315	315	\$1,827.00
262	Lime Treated Base (6")	2835	SY	\$1.50	\$4,252.50	1417.5	1417.5	\$2,126.25
262	Lime for Base (TY A or B)	15.73	TON	\$127.86	\$2,011.24	7.86	7.86	\$1,004.98
310	Prime Coat (MC-30)	570	GAL	\$3.95	\$2,251.50	0	0	\$0.00
340	Asphalt Concrete Pavement Type "D"	242.36	TON	\$66.05	\$16,007.88	0	0	\$0.00
502	Barricades, Signs & Traffic Handling	1.5	MO	\$1,500.00	\$2,250.00	1.5	1.5	\$2,250.00
506	Construction Exits (TY 2) (Install)	145	SY	\$40.00	\$5,800.00	72	72	\$2,880.00
506	Construction Exits (TY 2) (Remove)	145	SY	\$20.00	\$2,900.00	72	72	\$1,440.00
529	Concrete Curb and Gutter	0	LF	\$5.25	\$0.00	1145	1145	\$6,011.25
5249	Temp Sediment Control Fence	260	LF	\$4.00	\$1,040.00	130	130	\$520.00
5249	Temp Sediment Control Fence (Remove)	260	LF	\$1.50	\$390.00	0	0	\$0.00
530	Tumouts (Asph-Conc-Pav)	145	EA	\$11.20	\$1,624.00	0	0	\$0.00
644	Small Road Sign Assm (TY A)	2	EA	\$500.00	\$1,000.00	0	0	\$0.00
<b>Drainage</b>								
464	RCP (CL III) (15")	345	LF	\$15.50	\$5,347.50	0	0	\$0.00
464	RCP (CL III) (18")	108	LF	\$17.50	\$1,890.00	0	0	\$0.00
467	Safety End Treatment	4	EA	\$600.00	\$2,400.00	0	0	\$0.00
530	Driveways (TY PRB-1) (ACP) (1")	73	SY	\$11.20	\$817.60	0	0	\$0.00
530	Driveways (TY PRB-1) (Concrete)	357.5	SY	\$36.50	\$13,048.75	94	94	\$3,431.00
<b>TOTAL</b>						<b>\$98,217.37</b>	<b>Totals:</b>	<b>\$44,531.00</b>

Totals to Date:  
 Roadway: \$41,100.00  
 Drainage: \$3,431.00  
 Total: \$44,531.00

Roadway: \$41,100.00  
 Drainage: \$3,431.00

Prepared and Checked by:   
 Signature:   
 Printed Name: Ricardo Hinojosa, P.E.

Date: 11-20-08

Tabulation of Change Order No.1  
 Villa Capri Subdivision  
 Colonia Access Program Project - Precinct No.3  
 CAP-08-008-05-26 22  
 Contractor: Valley Paving

Item No.	Description	Original Bid			Change Order No.1			(+)/Increase/ (-)/decrease
		Quantity	Unit	Unit Price	Quantity	Unit Price	Total	
<b>Roadway</b>								
100	Preparing ROW	10.63	STA	\$855.00	10.63	\$855.00	\$9,088.85	\$0.00
110	Excavation	1445	CY	\$4.20	1445	\$4.20	\$6,089.00	\$0.00
247	Flex Base	735	CY	\$21.45	735	\$21.45	\$15,765.75	\$0.00
251	Reworking Base Material (DC)(TY D CL2)	735	CY	\$5.80	735	\$5.80	\$4,283.00	\$0.00
252	Lime Treated Base (6")	2835	SY	\$1.50	2835	\$1.50	\$4,252.50	\$0.00
252	Lime for Base (TY A or B)	15.73	TON	\$127.86	15.73	\$127.86	\$2,011.24	\$0.00
310	Prime Coat (MC-30)	570	GAL	\$3.95	570	\$3.95	\$2,251.50	\$0.00
340	Asphalt Concrete Pavement Type "D"	242.36	TON	\$66.05	242.36	\$66.05	\$16,007.88	\$0.00
502	Barricades, Signs & Traffic Handling	1.5	MO	\$1,500.00	1.5	\$1,500.00	\$2,250.00	\$0.00
506	Construction Exits (TY 2) (Install)	145	SY	\$40.00	145	\$40.00	\$5,800.00	\$0.00
506	Construction Exits (TY 2) (Remove)	145	SY	\$20.00	145	\$20.00	\$2,900.00	\$0.00
5249	Temp Sediment Control Fence	260	LF	\$4.00	260	\$4.00	\$1,040.00	\$0.00
5249	Temp Sediment Control Fence (Remove)	260	LF	\$1.50	260	\$1.50	\$390.00	\$0.00
530	Concrete Curb and Gutter	0	LF	\$5.25	2300	\$5.25	\$12,075.00	\$12,075.00
530	Turnouts (Asph-Conc-Pav)	145	SY	\$11.20	145	\$11.20	\$1,624.00	\$0.00
644	Small Road Sign Assm (TY A)	2	EA	\$500.00	2	\$500.00	\$1,000.00	\$0.00
<b>Drainage</b>								
464	RCP (CL III) (16")	345	LF	\$15.50	0	\$15.50	\$5,347.50	-\$5,347.50
464	RCP (CL III) (18")	108	LF	\$17.50	0	\$17.50	\$1,890.00	-\$1,890.00
467	Safety End Treatment	4	EA	\$600.00	0	\$600.00	\$2,400.00	-\$2,400.00
530	Driveways (TY PRB-1) (ACP) (1")	73	SY	\$11.20	73	\$11.20	\$817.60	\$0.00
530	Driveways (TY PRB-1) (Concrete)	357.5	SY	\$36.50	357.5	\$36.50	\$13,048.75	\$0.00

Roadway: \$74,713.52  
 Drainage: \$23,503.85  
 TOTAL: \$98,217.37

Roadway: \$86,788.52  
 Drainage: \$13,866.35  
 TOTAL: \$100,654.87

\$2,437.60

Progress Estimate

Project: Hidalgo County Pct. No. 3  
Villa Capri Subdivision

Project No.: <sup>04 22</sup> CAP-08-008-03-26-LRM Estimate No.1  
For Period from 10/08/08 to 11/17/08

Notice to Proceed Date: 05/12/08  
Contract Completion Date: \_\_\_\_\_  
Approved Time Extensions: \_\_\_\_\_  
Revised Contract Completion Date: 12/30/08

Contract Date: 04/22/08  
Original Contract Amount: \$ 98,217.37  
Revised Contract Amount: \$ 100,654.87

TOTAL AMOUNT WORK DONE TO DATE: \$ 44,530.99  
Less Amount Due Retained: (4,453.10)  
Less Previous Payments: ( -0- )  
AMOUNT DUE TO CONTRACTOR: \$ 40,077.89

Owner: Hidalgo County Pct. No. 3

Contractor: Valley Paving, Inc.

CERTIFICATE OF THE CONTRACTOR OR HIS DULY AUTHORIZED REPRESENTATIVE

To the best of my knowledge, I certify that all times, quantities and prices of work and materials shown on the face of this estimate are correct; that all work has been performed and materials supplied in full accordance to the terms and conditions of the corresponding construction contractual documents between the Owner and the Contractor, including all changes authorized thereto; that the foregoing is a true and correct statement of the contract amount up to and including the last day of the period covered by this estimate and that no part of the "AMOUNT DUE CONTRACTOR" has been received.

I further certify that all just and lawful bills against the below named Contractor, for labor, material and Expandable equipment employed in the performance of said contract have been paid in full accordance with the Contract requirements.

DATE: 11/17/08 BY:  TITLE: President

CERTIFICATE OF ENGINEER'S REPRESENTATIVE

I certify that a qualified project representative was present on the project on a continual basis to observe Construction and that all materials and work included in this statement have been performed in general accordance with the construction plans and specifications and authorized changes thereto. I further certify that I have verified this estimate and that, to the best of my knowledge and belief, it is a true and correct statement of work performed and materials supplied by the Contractor, that the amount due him is correct and just.

PROJECT MANAGER:  DATE: 11-20-08

OWNER'S ACCEPTANCE: \_\_\_\_\_ DATE: \_\_\_\_\_

VALLEY PAVING INC.  
 321 E. 2 MILE LINE  
 MISSION, TX. 78574

PHONE (956) 585-5908  
 PHONE (956) 581-1370  
 FAX (956) 584-0057

TO: HIDALGO CO. PCT.3  
 C/O HINOJOSA ENGINEERING  
 108 W. 18TH. ST.  
 MISSION, TX. 78572

PAYMENT  
 REQUEST #1

DATE: 11/17/2008

PROJECT: HIDALGO COUNTY PCT.3-VILLA CAPRI (ROADWAY CONSTRUCTION)

PAGE 1

ITEM NUMBER	DESCRIPTION	ESTIMATED QUANTITIES	UNIT	UNIT PRICE	CONTRACT TOTAL	COMP. TO DATE	TOTAL AMOUNT
100	PREPARING ROW	10.63	STA.	\$ 855.00	\$ 9,088.65	10.63	\$ 9,088.65
110	EXCAVATION	1445	CY	\$ 4.20	\$ 6,069.00	1445	\$ 6,069.00
247	FLEXIBLE BASE	735	CY	\$ 21.45	\$ 15,765.75	367.5	\$ 7,882.87
251	REWORKING BASE MATERIAL (DC) (TY D CL2	735	CY	\$ 5.80	\$ 4,263.00	315	\$ 1,827.00
262	LIME TREATMENT FOR BASE (6")	2835	SY	\$ 1.50	\$ 4,252.50	1417.5	\$ 2,126.25
262	LIME FOR BASE (TY A OR B)	15.73	TON	\$ 127.86	\$ 2,011.24	7.86	\$ 1,004.97
310	PRIME COAT (MC-30)	570	GAL	\$ 3.95	\$ 2,251.50	0	\$ -
340	ASPHALT CONCRETE PAVEMENT TYPE "D"	242.36	TON	\$ 66.05	\$ 16,007.88	0	\$ -
502	BARRICADES SIGNS & TRAFFIC HANDLING	1.5	MO	\$ 1,500.00	\$ 2,250.00	1.5	\$ 2,250.00
506	CONSTRUCTION EXITS (TY2) (INSTALL)	145	SY	\$ 40.00	\$ 5,800.00	72	\$ 2,880.00
506	CONSTRUCTION EXITS (TY2) (REMOVE)	145	SY	\$ 20.00	\$ 2,900.00	72	\$ 1,440.00
5249	TEMP SEDIMENT CONTROL FENCE (INSTALL)	260	LF	\$ 4.00	\$ 1,040.00	130	\$ 520.00
5249	TEMP SEDIMENT CONTROL FENCE (REMOVE)	260	LF	\$ 1.50	\$ 390.00	0	\$ -
529	CONCRETE CURB & GUTTER	0	LF.	\$ 5.25	\$ -	1145	\$ 6,011.25
530	TURN-OUTS (ASPH CONC-PAV)	145	SY	\$ 11.20	\$ 1,624.00	0	\$ -
644	SMALL ROAD SIGN (TY A)	2	EA	\$ 500.00	\$ 1,000.00	0	\$ -
464	RCP (CL III) (15")	345	LF	\$ 15.50	\$ 5,347.50	0	\$ -
464	RCP (CL III) (18")	108	LF	\$ 17.50	\$ 1,890.00	0	\$ -
467	SAFETY END TREATMENT	4	EA	\$ 600.00	\$ 2,400.00	0	\$ -
530	DRIVEWAYS (TY PRB-1) (ACP) (1")	73	SY	\$ 11.20	\$ 817.60	0	\$ -
530	DRIVEWAYS (TY PRB-1) (CONCRETE)	357.5	SY	\$ 36.50	\$ 13,048.75	94	\$ 3,431.00
<b>TOTAL CONTRACT AMOUNT</b>					<b>\$ 98,217.37</b>		
<b>TOTAL AMOUNT DUE &amp; COMPLETED TO DATE</b>							<b>\$ 44,530.99</b>

# CHANGE ORDER

NO. 1

PROJECT: Villa Capri Subdivision

DATE OF ISSUANCE: 7/30/2008

OWNER: Hidalgo County Precinct No.3  
 ADDRESS: 301 East State Street  
 Pharr, Tx 78577

OWNER'S PROJECT NO.: CAP-08-008-03-26-LRM  
04-22

CONTRACTOR: Valley Paving, Inc.  
 ADDRESS: 321 E. 2 Mile Line  
 Mission, TX 78572

ENGINEER: Hinojosa Engineering, Inc

CONTRACT FOR: \$98,217.37

ENGINEER'S PROJECT NO.: 06-167


You are hereby directed to make the following changes in the Contract Documents.


Description: Curb and Gutter added to Roads


Purpose: Final Quantitative Adjustments.

Attachments: 1. Tabulation of items to be reconciled.

CHANGE IN CONTRACT PRICE:	CHANGE IN CONTRACT TIME:
Original Contract Price: <u>                  \$98,217.37                  </u>	Original Contract Time: <u>                  90 working days                  </u> days
Previous Change Order No.s: <u>          0          </u> <u>                  \$0.00                  </u>	Change from Previous Change Orders <u>                  0 working days                  </u> days
Contract Price prior to this Change Order <u>                  \$98,217.37                  </u>	Contract Time prior to this Change Order <u>                  0 working days                  </u> days
Net Increase of this Change Order <u>                  \$2,437.50                  </u>	Net Increase of this Change Order <u>                  0 working days                  </u> days
Contract Price with all approved Change Orders <u>                  \$100,654.87                  </u>	Contract Time with all approved Change Orders <u>                  90 working days                  </u> days

APPROVED:  8/26/08  
 Owner Date  
 Hidalgo County Judge

APPROVED:  7/30/08  
 Contractor Date  
 Valley Paving, Inc.

RECOMMENDED:  7-31-08  
 Engineer Date  
 Hinojosa Engineering, Inc.

INVOICE RECEIVED BY: Upliu ON 7/31/08  
 GOODS/SERVICES RECEIVED BY: Ugarrto ON 7/30/08  
Vargas

**CONTRACT CHANGE ORDER No.1**


Contract No. <sup>04-22</sup> CAP-08-008-03-26-LRM Date: July 30, 2008  
 Change Order No. 1 Project: Villa Capri Subdivision  
 To: Valley Paving, Inc. Location: Hidalgo County, TX

You are hereby requested to comply with the following changes from the contract plans and/or specifications:

Item No.	Description of Changes	Decrease in Contract	Increase in Contract
464	RCP CL III (15")	\$5,347.50	
464	RCP CL III (18")	\$1,890.00	
467	Safety End Treatment	\$2,400.00	
529	Concrete Curb and Gutter		\$12,075.00
	Total Decrease	\$9,637.50	
	Total Increase		\$ 00,000.00
	Net Increase in Contract Price		\$ 2,437.50

The sum of **\$ 2,437.50** is hereby added to the total contract price of **\$ 98,217.37**, and the total adjusted contract price to date is **\$ 100,654.87**. The time for completion of the contract is 90 calendar days. This document shall become an amendment to the contract and all provisions of the contract will apply hereto.

Accepted by:  Date: 7/30/08  
 Valley Paving, Inc.

Recommended by:  Date: 7-31-08  
 Hinojosa Engineering, Inc.

Approved by:  Date: \_\_\_\_\_  
 Hidalgo County Judge

**Note:** Please refer to page 3 for description of changes in quantities and unit prices.



### Contract Time Statement

ESTIMATE NO. 1 <sup>04-22</sup> CONTRACTOR Valley Paving, Inc.  
 PROJECT NO. CAP-08-008-03-26-1RM COUNTY Hidalgo DATE WORK BEGAN 10/13/08  
 TIME COMPUTED FROM 7:00 AM DATE WORK COMPLETED \_\_\_\_\_

MONTH	DATE OR DAYS	WORKING DAYS CHARGED	DAYS CREDITED AND REASONS THEREFORE	
October	13	1	8 hrs.	Royal Dr. & King Dr. - Put up Traffic Control & Relocate mailboxes
	14	1	8	Royal Dr. & King Dr. - Start to sawcut existing concrete Drives
	15	1	8	Royal Dr. & King Dr. - Continued to sawcut & Demolish Drives
	16	1	8	Rained out- Too wet
	17	1	8	Royal Dr. & King Dr. - Clear Right-of-Ways to demolish Drives
	20	1	8	Royal Dr. - Demolish Street to cut subgrade
	21	1	8	Continued to demolish street to cut subgrade
	22	1	8	King Dr. - Continued to Demolish Street to cut subgrade
	23	1	8	- Air out subgrade
	24	1/2	5 hrs	- Cut subgrade to air out
	27	1	8	- Cut subgrade to air out
	28	1	8	- Dumping Lime Material
	29	1	8	- Mix Lime Subgrade
	30	1	8	- Cut subgrade
November	31			No Work
	3	1	8	Royal Dr. - Air out subgrade
	4	1	8	Royal Dr. - Air out subgrade Too wet & Spangy
	5	1	8	King Dr. - Finish subgrade
	6	1	8	Royal Dr. - Cut subgrade
	7	1	4 1/2	Royal Dr. - Cut subgrade
		1/2	4 1/2	King Dr. - Rtx caliche Drives for Asphalt Paving
	10	1	8	Dumping caliche
11	1	8	Set caliche & Densities before curb, tested caliche & Passed.	
12	1	8	Cut, grade & Line & subcontractor Poured curb	
13	1	8	Backfill curb & caliche	
14	1/2	4 1/2	Poured concrete Drives	
17	1	8	King Dr. - Dumping caliche & backfill concrete Drive	

TOTALS 0 0

NO. OF CONTRACT WORKING DAYS \_\_\_\_\_ NO. WORKING DAYS CHARGED TO DATE 0  
 ASSESSED LIQUIDATED DAMAGES: NO. \_\_\_\_\_ PER DAY \$ \_\_\_\_\_ TOTAL \$ 0.00  
 CERTIFIED AS CORRECT (ONE COPY HAS BEEN GIVEN TO THE Resident Engineer)  
 RESIDENT ENGINEER

INSTRUCTIONS: PROJECT IDENTIFICATION SHOULD COVER CONTRACT. TIME CREDITED AND REASONS THEREFORE MUST CONFORM TO PROVISIONS OF CONTRACT. NO HOLIDAY CREDIT ALLOWED FOR DAYS PRECEDING OR FOLLOWING LEGAL HOLIDAYS. TIME SUSPENDED AND RESUMED MUST BE SUPPORTED BY COPY EACH OF LETTERS TO CONTRACTOR DATED ON OR BEFORE EFFECTIVE DATES. TIME EXTENSION MUST BE INDICATED AND REFERENCED TO RELATED PROVISION OF CONTRACT. SEE BOOKLET OF INSTRUCTIONS, CONSTRUCTION ESTIMATES DATED SEPTEMBER 1, 1956

PARTIAL/FINAL WAIVER OF LIEN

THE STATE OF TEXAS

COUNTY OF HIDALGO

The undersigned contracted with Hidalgo County Precinct No. 3  
to furnish Construction Material and Labor  
in connection with certain improvements to real property in located in Mission, Texas, Hidalgo  
County, Texas and owned by Hidalgo County Precinct No. 3  
Which improvements are described as follows:

Roadway Paving and Drainage Construction for Villa Capri Subdivision

In consideration of Pay Estimate No. 1 in the amount of Forty Thousand, Five Hundred Thirty Dollars and 99/100 (\$ 40,530.99 ) and other good and valuable consideration, the receipt and sufficiency of which is hereby acknowledged and confessed, the undersigned does hereby waive and release any mechanic's lien or materialmen's lien or claims of lien that the undersigned has or hereafter has on the above mentioned real property on account of any labor performed or materials furnished or to be furnished or labor performed and materials furnished by the undersigned pursuant to the above-mentioned contract or any constitutional lien that the undersigned may have.


Undersigned hereby guarantees that all bids for labor performed and/or materials furnished in the erection and construction of such improvements on the Property have been fully paid and satisfied and Undresigned does further guarantee that if for any reason a lien or liens are filed for material or labor against said Property arising out of any bill for material or labor in connection with the erection or construction of said Improvements thereon, Undersigned will obtain a settlement of such lien or liens and a proper release thereof shall be obtained.

Valley Paving, Inc.

CONTRACTOR

By: [Signature] Oscar Cordova, President  
TITLE

SWORN TO AND SUBSCRIBED BEFORE ME, on this the 17<sup>th</sup> day of November, 2008, to certify which witness my hand and seal of office.



[Signature]  
NOTARY PUBLIC in and for the State of Texas

My Commission Expires: 02/23/11

**Prevailing Wage Rates  
Certification Statement**

**Date:** November 26, 2008

**Project Name:** Villa Capri Subdivision

**CSJ#** M108078421

**Contractor:** Valley Paving Inc.

**Application#** 1

I, Agapito Vargas do hereby state:  
(Name of Project Director)


1. That a payroll (form WH-347 or similar form) was submitted for contract work performed for the period covered by the attached application.
2. That a statement of compliance (form WH-347 or similar form) was submitted with the payroll.
3. The certified payroll complies with the classifications and minimum wage rates stipulated in the contract.
4. That a minimum of one interview was conducted with laborers using Form HUD-11 or similar.

\_\_\_\_\_  
Signature

Villa Capri Subdivision  
 Colonia Testing Requirements

MATERIAL	TEST	DESCRIPTION	REQUIRED	REMARKS	Villa Capri Subdivision	
					Kings Drive CSJ#2C10878421	Royal Drive CSJ#2C10878421
FILEX BASE	Ter:101-E Ter:103-E	Prep. Soil and Flex. Base Moisture Content	YES Optional			
	Ter:104-E	Determining Liquid Limit of Soils	YES			
	Ter:105-E	Determining Plastic Limit of Soils	NO			
	Ter:106-E	Calculating Plasticity Index	YES			
	Ter:110-E	Particle Size Analysis	YES			
	Ter:113-E	Moisture Density Relation of Base Materials (excluding lime)	YES			
	Ter:116-E	Wet Ball Mill Method	YES			
	Ter:117-E	Tensile Compression for Base Material (Excludes lime)	YES			
	Ter:115-E	In-Place Density	YES			
		Thickness	YES			
LIME	Ter:600-J	Lime Testing Procedure	YES	Required for all flexible bases (Callings)		
HOT MIX	Ter:207-F	Determining Density of Compacted Bituminous Mixtures	YES			
	Ter:208-F	Test for Stabilometer Value of Bituminous Mixtures	Optional			
	Ter:210-F	Deter. Asph. Content of Bituminous Mixtures by Extraction	YES			
	Ter:229-F	Combined HMA/C Cold Ball Sampling and Testing Procedures	YES			
	Ter:236-F	Deter. Asph. Content from Asph. Paving Struct. by Ignition Method	Optional			
	Ter:212-E	Determining Moisture Content of Bituminous Mixtures	NO			
	Ter:213-E	Determining Hydrocarbon - Bolelle Content of Bituminous Mixtures	NO			
EMBANKMENTS	Ter:114-E	Laboratory Compaction Charact. & Moist. - Density Relat. Of Subgrade & Embankments Soils	NO			
	Ter:115-E	In-Place Density	NO			
	Texas SDPHT Bulkin C-14		NO			
	ASTM-D-2950.76		NO			
	AASHTO-T-166		NO			

Prepared and Checked By:

Signature:   
 Printed Name: Ricardo Hinojosa, P.E.

Date: 11-20-08

1) Testing for this procedure has been performed and passed.

**L&G Engineering Laboratory**  
 Construction Material Testing  
 Geotechnical Engineering

2100 W. Expressway 83 Mercedes, TX 78570 (956) 585-0760  
 900 S. Stewart Rd. Ste. 6 Mission, TX 78572 (956) 583-7117

**PROCTOR  
 TEST REPORT**

Project Description: Villa De Capri Subdv.  
 Client: Hidalgo County Pct. 3  
 Engineer: Hinojosa Engineering  
 Contractor: Valley Paving

L&G Project Number: L37811  
 L&G Report Number: R001  
 Sample Date: 10/28/2008  
 Date Reported: 10/30/2008

Field Number: LS # 1

Page 1 of 2


Compaction Method: TEX-114  
 Material Description: Limed Subgrade

Specific Gravity: 2.65

Liquid Limit: 37  
 Plastic Limit: 29  
 Plasticity Index: 8  
 % Passing No. 200: 0.0

Specimen No.:	1	2	3	4
Molsture, %:	7.5	11.1	14.3	17.8
Dry Density (pcf):	94.6	100.0	101.5	97.8

Maximum Dry Density in P.C.F.: 101.5  
 Optimum Molsture (%): 14.2

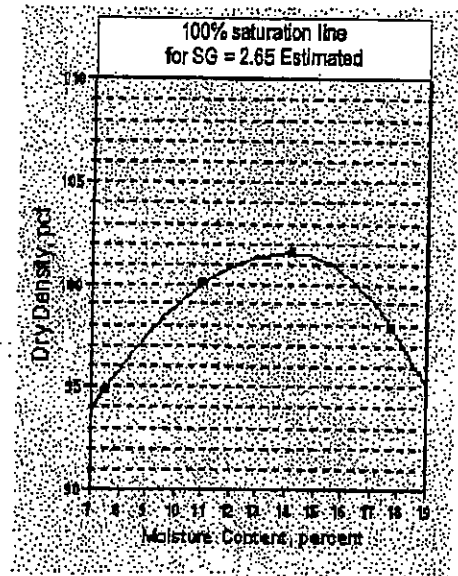

Remarks: \* -200 Not Performed  
 Test Method: TEX 114 Method-A, Tex 104-E, 105-E, 106-E

Orig: Hidalgo County Pct. 3 (Mission, TX)  
 (1-cc copy)  
 1-cc Hinojosa Engineering  
 1-cc Valley Paving  
 1-cc Laboratory

Respectfully Submitted,  
 L&G Engineering Laboratory

Ricardo A. Gil, Lab Manager


**PROCTOR  
 TEST REPORT**

Project Description: Villa De Capri Subdv.  
 Client: Hidalgo County Pct. 3  
 Engineer: Hinojosa Engineering  
 Contractor: Valley Paving

L&G Project Number: L37811  
 L&G Report Number: R001  
 Sample Date: 10/28/2008  
 Date Reported: 10/30/2008

Field Number: LS # 1

Page 2 of 2

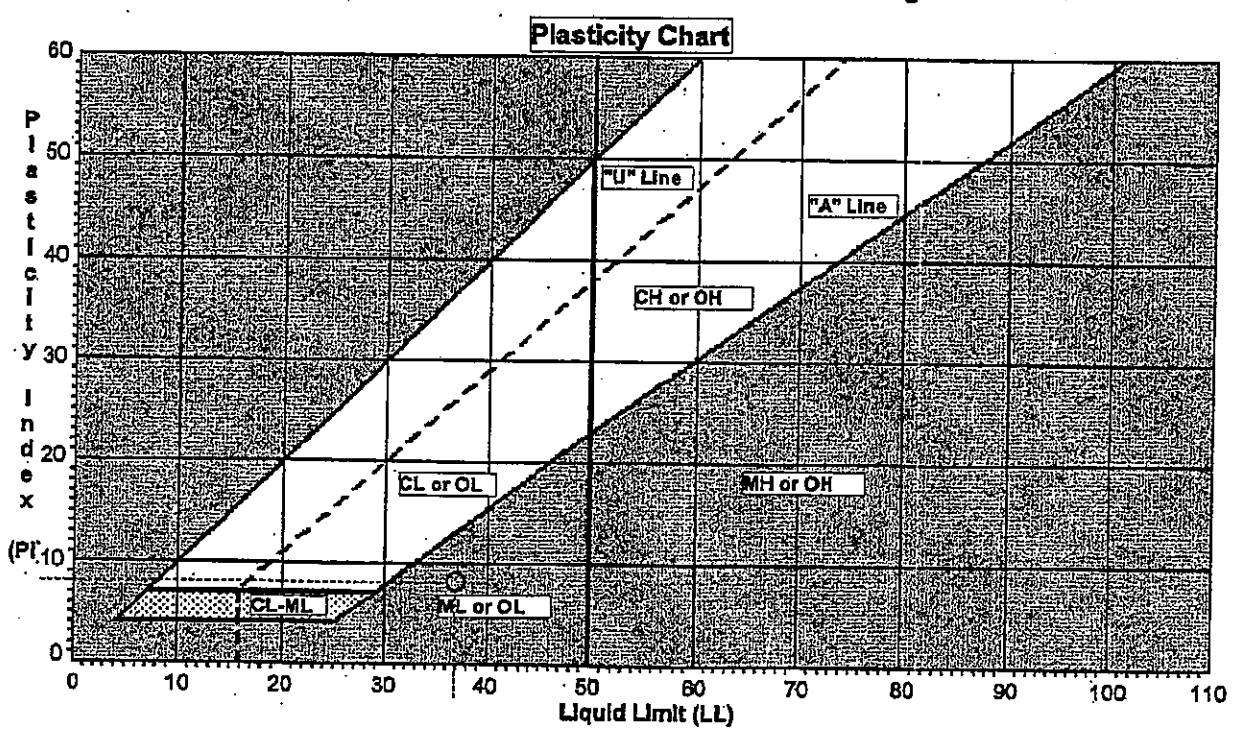

Orig: Hidalgo County Pct. 3 (Mission, TX)  
 (1-cc copy)  
 1-cc Hinojosa Engineering  
 1-cc Valley Paving  
 1-cc Laboratory

Respectfully Submitted,  
 L&G Engineering Laboratory

*Ricardo A. Gil*

Ricardo A. Gil, Lab Manager

**L&G Engineering Laboratory**  
 Construction Material Testing  
 Geotechnical Engineering

2100 W. Expressway 83 Mercedes, TX 78570 (956) 585-0760  
 900 S. Stewart Rd. Ste. 6 Mission, TX 78572 (956) 583-7117

**SIEVE ANALYSIS  
 TEST REPORT**

Project Description: Villa De Capri Subdv.  
 Client: Hidalgo County Pct. 3  
 Engineer: Hinojosa Engineering  
 Contractor: Valley Paving

L&G Project Number: L37811  
 L&G Report Number: R003  
 Sample Date: 10/28/2008  
 Date Reported: 11/19/2008

Field Number: C - #1

Page 1 of 1


Description: Base Material

<u>Sieve</u>	<u>% Retained</u>	<u>Low</u>	<u>High</u>
2 in	0	0	0
1/2 in	42	20	60
No. 4	61	40	75
No. 40	83	70	90

Remarks: Texas Wet Ball Mill Value - 50 %  
 Test Method (As Applicable): Tex Method 401-A, Tex 116-E

Orig: Hidalgo County Pct. 3 (R&B) (Hidalgo County Pct. 3)  
 (Mission, TX) (1-cc copy)  
 1-cc Hinojosa Engineering  
 1-cc Valley Paving  
 1-cc Laboratory

Respectfully Submitted,  
 L&G Engineering Laboratory



Ricardo A. Gil, Lab Manager



**L&G Engineering Laboratory**  
Construction Material Testing  
Geotechnical Engineering

2100 W. Expressway 83 Mercedes, TX 78570 (956) 565-0760  
900 S. Stewart Rd. Ste. 6 Mission, TX 78572 (956) 583-7117

**FIELD DENSITIES  
TEST REPORT**

Project Description: Villa De Capri Subdv.  
Client: Hidalgo County Pct. 3  
Engineer: Hinojosa Engineering  
Contractor: Valley Paving

L&G Project Number: L37811  
L&G Report Number: R004  
Sample Date: 10/30/2008  
Date Reported: 10/30/2008

Page 1 of 1

Material Description	Limed Subgrade		
Required % Proctor	95	Moisture Tolerance	-2 + 3
	Proctor No	Optimum % Moisture	Opt. Density, LB/CF
	LS # 1	14.2	101.5


Test No.	Test Location	Proctor No	Moisture Content	Dry Density	Percent Compaction	Inches
1	King James P.O.C. Centerline	LS # 1	14.8%	109.6 pcf	108.0% (Pass)	6"
2	King James Sta. 3 + 50 4' S. of Centerline	LS # 1	14.6%	106.6 pcf	105.0% (Pass)	6"
3	King James Center of Cul-de-Sac Centerline	LS # 1	16.9%	105.8 pcf	104.2% (Pass)	6"

Remarks: Test results are in general compliance with the project specifications except as noted.  
Test Methods: ASTM D2922, D3017

Orig: Hidalgo County Pct. 3 (R&B) (Hidalgo County Pct. 3)  
(Mission, TX) (1-cc copy)  
1-cc Hinojosa Engineering  
1-cc Valley Paving  
1-cc Laboratory

Respectfully Submitted,  
L&G Engineering Laboratory

Ricardo A. Gil, Lab Manager



2100 W. Expressway 83 Mercedes, TX 78570 (956) 565-0760  
 900 S. Stewart Rd. Ste. 6 Mission, TX 78572 (956) 583-7117

**FIELD DENSITIES  
 TEST REPORT**

Project Description: Villa De Capri Subdv.  
 Client: Hidalgo County Pct. 3  
 Engineer: Hinojosa Engineering  
 Contractor: Valley Paving

L&G Project Number: L37811  
 L&G Report Number: R005  
 Sample Date: 11/11/2008  
 Date Reported: 11/11/2008

Page 1 of 1

Material Description	Kings Street Undercurb Caliche		
Required % Proctor	121.6	Moisture Tolerance	-2+3
	Proctor No	Optimum % Moisture	Opt. Density, LB/CF
	C - #1	9.5	121.6

Test No.	Test Location	Proctor No	Moisture Content	Dry Density	Percent Compaction	Inches
1	King St. Station 0+80 Undercurb Eastside	C - #1	11.2%	138.4 pcf	113.8% (Pass)	4"
2	King St. Station 2+75 Undercurb Southside	C - #1	12.3%	136.8 pcf	112.5% (Pass)	4"
3	King St. Station 3+70 Undercurb Northside of Culdesac	C - #1	8.7%	133.1 pcf	109.5% (Pass)	4"

Remarks: Test results are in general compliance with the project specifications except as noted.  
 Test Methods: ASTM D2922, D3017

Orig: Hidalgo County Pct. 3 (R&B) (Hidalgo County Pct. 3)  
 (Mission, TX) (1-cc copy)  
 1-cc Hinojosa Engineering  
 1-cc Valley Paving  
 1-cc Laboratory

Respectfully Submitted,  
 L&G Engineering Laboratory

Ricardo A. Gil, Lab Manager

**REPORT OF SITE VISIT  
 TEST REPORT**

Project Description: Villa De Capri Subdv.  
 Client: Hidalgo County Pct. 3  
 Engineer: Hinojosa Engineering  
 Contractor: Valley Paving

L&G Project Number: L37811  
 L&G Report Number: R006  
 Sample Date: 11/12/2008  
 Date Reported: 11/12/2008

Page 1 of 1

On November 12th, 2008 a representative of L&G Engineering Laboratory was dispatched to Villa de Capri to perform inspection of the placement of ready-mix concrete on the curb & gutter.

Specimen Number 10 was obtained and tested at 1:15 PM, and the following were determined:

Concrete Temperature: 81°f                      Entrapped / Entrained Air Content: 2.2%  
 Ambient Temperature: 86°f                      Slump: 1 1/4 inches


From Specimen Number 10, a total of three (3) 6x12 cylindrical test specimens were cast for Compressive Strength Testing at intervals of 7 and 28 days.

On November 13th 2008, a representative of L&G Engineering Laboratory was dispatched to the referenced project to collect the cylindrical specimens cast on the placement of curb & gutter. The specimens were delivered to the laboratory where they were stripped, labeled, and placed in a curing tank for testing at intervals of 7 & 28 days.

Test Methods (If Applicable): ASTM C-231, ASTM C-143, STM C-1064, ASTM C-31, ASTM C-172

Orig: Hidalgo County Pct. 3 (R&B) (Hidalgo County Pct. 3)  
 (Mission, TX) (1-cc copy)  
 1-cc Hinojosa Engineering  
 1-cc Valley Paving  
 1-cc Laboratory

Respectfully Submitted,  
 L&G Engineering Laboratory



Ricardo A. Gil, Lab Manager

Border Colonia Access Program  
Checklist for Documentation Required for Road Construction

**Contractor:** Valley paving Inc.  
**Contact Amount:** \$98,217.37  
**Project/Precinct:** Villa Capri Sub. 1 Pct. 3  
**Owner's Contract No.:** C-CAP-08-008-04-22

Item	Required Documents	Submitted & Reviewed	Approved	Comments:
	<b>INITIATION OF PROJECT</b>			
1	Approval to Bid (Purchasing)			
2	Contract - Signed and Executed			
3	Gen. Liability Insurance - (Expiration Date)			
4	Automobile Liab. Insurance - (Expiration Date)			
5	Worker's Comp. & Empl. Liab. (Expiration Date)			
6	Notice to Proceed			
7	Material Sample & Testing Table Sent to Auditor's Office			
8	Application and Certification of Payment (A)	✓	✓	
9	Schedule of Values a/k/a 1257/1258	✓	✓	
10	Estimate Quantity Update Worksheet	✓	✓	
11	List of Suppliers and Sub-contractors	✓	✓	
12	Partial Waiver of Liens (Sub-contractors/suppliers)	✓	✓	
13	TxDot Form 252 Contract Time Statement	✓	✓	
14	Payroll Report w/signed Wage Form	✓	✓	
15	Change Order (Requires TxDot Concurrence)	✓	✓	
16	Punch List			
17	Certificate of Construction Completion			
18	Approval by Commissioner's Court			
19	Contractor's Affidavit of Release (Waiver) of Liens (with power of attorney)(B)			
20	Affidavit of Payment of Debts & Claims-lien bond & indemnity bonds(w/power of attorney)(B)			
21	Consent of Surety to Final Payment(with power of attorney)(B)			
22	Final Blue Prints			
