

AI-13296 11/20/09

APPLICATION FOR PAYMENT NO. 1

To: Hidalgo County (OWNER)
From: Sascon, Inc. (CONTRACTOR)
Contract: CAP-08-012-07-11
Project: Road and Drainage Construction of Ezequiel Acevedo #2
OWNER's Contract No. CAP-08-012-07-11 ENGINEER's Project No. 06-206
For Work accomplished through the date of: 11/19/2008

Table with 2 columns: Description and Amount. Rows include: 1. Original Contract Price (\$ 117,335.80), 2. Net change by Change Orders and Written Agreements (+ or -): (\$ -), 3. Current Contract Price (1 plus 2): (\$ 117,335.80), 4. Total completed and stored to date: (\$ 68,541.80), 5. Retainage (per Agreement): 10% of completed Work (\$ 6,854.18), 0% of stored material (\$ -), Total Retainage (\$ 6,854.18), 6. Total completed and stored to date less retainage (4 minus 5): (\$ 61,687.62), 7. Less previous Application for Payments: (\$ -), 8. AMOUNT DUE THIS APPLICATION (6 MINUS 7): (\$ 61,687.62)

Accompanying Documentation: 8-1311-431-00-123-267-1-734 \$52,625.80<-5,262.58> = \$47,363.22
8-1311-431-00-123-267-1-733 \$15,916.00<-1,591.60> = \$14,324.40

CONTRACTOR'S Certification: The undersigned CONTRACTOR certifies that (1) all previous progress payments received from OWNER on account of Work done under the Contract referred to above have been applied on account to discharge CONTRACTOR's legitimate obligations incurred in connection with Work covered by prior Applications for Payment numbered 1 through 2 inclusive; (2) title of all Work, materials and equipment incorporated in said Work or otherwise listed in or covered by this Application for Payment will pass to OWNER at time of payment free and clear of all Liens, security interests and encumbrances (except such as are covered by a Bond acceptable to OWNER indemnifying OWNER against any such Lien, security interest or encumbrance); and (3) all Work covered by this Application for Payment is in accordance with the Contract Documents and not defective.

Dated 12-9-08 SASCON INC CONTRACTOR
By: [Signature]

State of Texas
County of Hidalgo
Subscribed and sworn to before me this 9 day of December, 2008

[Signature]
Notary Public
My Commission expires: 11/21/2009

INVOICE RECEIVED BY: [Signature] ON 12/10/08
GOODS/SERVICES RECEIVED BY: [Signature] ON 12/10/08

Payment of the above AMOUNT DUE THIS APPLICATION is recommended.

Dated 12-09-08 HINOJOSA ENGINEERING INC. ENGINEER
By: [Signature]



Engineer: Hinojosa Engineering, Inc.
 Contractor: Sascon, Inc.
 Retainage Percent: 10%
 Starting Date:


Summary												
Contract No.	Description	Original Schedule Value	Revised Schedule Value	Application No. 1	Application No. 2	Application No. 3	Total to Date	Balance to Finish	Retainage	Net	Payments to Date	Payment Due
CAP 08-012-07-11	Ezequiel Acevedo #2	\$117,335.80	\$117,335.80	\$68,541.80			\$68,541.80	\$48,794.00	\$6,854.18	\$61,687.62	\$0.00	\$61,687.62
	TOTALS:						\$68,541.80	\$48,794.00	\$6,854.18	\$61,687.62	\$0.00	\$61,687.62

Estimate Quantity Update Worksheet
 Ezequiel Acevedo Jr. #2
 Colonia Access Program Project - Precinct No.3
 CAP-08-012-07-11
 Contractor: Sascon, Inc.

Item No.	Description	Quantity	Unit	Unit Price	Project Amount	Monthly Quantity	Quantity to Date	Item Cost (Monthly)
RFP 1								
100	Preparing ROW	13.12	STA	\$ 400.00	\$5,248.00	13.12	13.12	\$5,248.00
134	Backfill	13.12	STA	\$ 400.00	\$5,248.00	13.12	13.12	\$5,248.00
247	Flex Base	907	CY	\$ 21.00	\$19,047.00	907	907	\$19,047.00
251	Reworking Base Material (DC)(TY D CL2)	907	CY	\$ 9.00	\$8,163.00	907	907	\$8,163.00
262	Lime Treated Base Course	4,085	SY	\$ 2.00	\$8,170.00	4085	4085	\$8,170.00
262	Lime (TY A or B)	19.42	TON	\$ 190.00	\$3,689.80	19.42	19.42	\$3,689.80
310	Asphalt Material (MC-30)	700	GAL	\$ 5.00	\$3,500.00	0	0	\$0.00
340	Asphalt Concrete (Type "D")	3,500.00	SY	\$ 8.70	\$30,450.00	0	0	\$0.00
502	Barricades, Signs & Traffic Handling	1.5	MO	\$ 1,800.00	\$2,700.00	1.5	1.5	\$2,700.00
506	Construction Exits (TY 2) (Install)	72.0	SY	\$ 5.00	\$360.00	72	72	\$360.00
506	Construction Exits (TY 2) (Remove)	72.0	SY	\$ 3.00	\$216.00	0	0	\$0.00
530	Turnouts (Asph-Conc-Pav)	72.0	LF	\$ 21.00	\$1,512.00	0	0	\$0.00
5249	Temp Sediment Control Fence	500	LF	\$ 5.00	\$2,500.00	0	0	\$0.00
5249	Temp Sediment Control Fence (Remove)	500	LF	\$ 2.00	\$1,000.00	0	0	\$0.00
Drainage								
464	RCP (CL III) (18")	40	LF	\$ 30.00	\$1,200.00	40	40	\$1,200.00
464	RCP (CL III) (15")	508	LF	\$ 27.00	\$13,716.00	508	508	\$13,716.00
467	Safety End Treatment	2	EA	\$ 500.00	\$1,000.00	2	2	\$1,000.00
530	Driveways (Ty PRB-1) (ACP) (1")	406	SY	\$ 15.00	\$6,090.00	0	0	\$0.00
530	Driveways (Ty PRB-1) (Concrete)	86	SY	\$ 41.00	\$3,526.00	0	0	\$0.00
TOTAL					\$117,335.80		Totals:	\$68,541.80

Totals to Date: Roadway: \$52,625.80
 Drainage: \$15,916.00
 Total: \$68,541.80

Prepared and Checked by:  Signature: Ricardo Hinojosa, P.E.
 Date: 12-09-08



SASCON INC.

5200 N. 26TH Lane
McAllen, Texas 78504

Phone: (956) 682-3454

Fax: (956) 682-2542

- ✔ Paving
- ✔ Excavation
- ✔ Trucking
- ✔ Equipment

December 3, 2008

**Hidalgo County Pct. 3
Barney Groves Subdivision &
Ezequiel Acevedo Subdivision**

VENDORS LIST:

**Please be advised that the suppliers for this project are Varmicon Industries,
Central Ready Mix, and Valley Caliche Products and no other.**

Thank You,

A handwritten signature in cursive script, appearing to read 'H. A. Skloss'.

**H. A. Skloss
President
Sascon, Inc.**

COPY

PARTIAL LIEN WAIVER

DATE: Dec. 4, 2008

PROJECT: Plot 3 Barney Grove - Final Acct #2 Sub.


COUNTY: Hidalgo

The undersigned, having the position of CFO
With Dan Dill, first being duly sworn, states that he is duly
authorized and appointed as its agent to execute this Partial Lien Waiver. That he does
hereby certify that Varmicon Industries has furnished materials
under its contract with Sascon Incorporated on the above described
project.

That the sum of _____
(\$ 0), is the sum now due and owing for all materials furnished
by the undersigned, on the above described project and that on the receipt of such sum
from Sascon Incorporated, the
undersigned does waive and release to the extent of such payment received, claims and
lien rights for an in connection with the above described project for said materials
furnished.

Executed this 4th day of December, 2008.

BY D Dill CFO
NAME TITLE



Subscribed and sworn to before me this 4th day of December, 2008

July 8, 2009
My Commission Expires

Veronica Ramos
Notary Public

COPY

PARTIAL LIEN WAIVER

DATE: 12/4/2008

PROJECT: PCT 3 BARNEY GROVE + EZEQUIAL ACERED #2 Subdv.

COUNTY: Hidalgo

The undersigned, having the position of VICE PRES.
With CENTRAL READY MIX first being duly sworn, states that he is duly authorized and appointed as its agent to execute this Partial Lien Waiver. That he does hereby certify that RICHARD M. LINN has furnished materials under its contract with SASCON INC. on the above described project.

That the sum of ONE HUNDRED FIFTY ONE DOLLARS & 55/100
(\$ 151.55), is the sum now due and owing for all materials furnished by the undersigned, on the above described project and that on the receipt of such sum from RICHARD M. LINN, VICE PRES. the undersigned does waive and release to the extent of such payment received, claims and lien rights for an in connection with the above described project for said materials furnished.

Executed this 4 day of DEC, 2008


[Signature]

BY RICHARD M. LINN VICE PRES.
NAME TITLE

Subscribed and sworn to before me this 4 day of DEC, ~~2004~~ 2008

AUG 5, 2009
My Commission Expires

[Signature]
Notary Public



SASCON Inc

COPY

PARTIAL LIEN WAIVER

DATE: DECEMBER 3, 2008

PROJECT: PLOT 3 BARLEY GROVES + EQUIPMENT ACQUIRED #2 Subd.

COUNTY: Hidalgo

The undersigned, having the position of V. PRES./GEN. MGR.
With VALLEY CALICHE PRODUCTS first being duly sworn, states that he is duly
authorized and appointed as its agent to execute this Partial Lien Waiver. That he does
hereby certify that VALLEY CALICHE PRODUCTS, INC. has furnished materials
under its contract with SASCON, INC. on the above described
project.

That the sum of N/A
(\$ N/A), is the sum now due and owing for all materials furnished
by the undersigned, on the above described project and that on the receipt of such sum
from SASCON, the
undersigned does waive and release to the extent of such payment received, claims and
lien rights for an in connection with the above described project for said materials
furnished.

Executed this 3RD day of DECEMBER, 2008


VALLEY CALICHE PRODUCTS, INC.

BY Mark Mothard, V. PRES./GEN. MGR.
NAME TITLE

Subscribed and sworn to before me this 3RD day of DECEMBER, 2008

AUG. 7, 2011
My Commission Expires

Irma P. Price
Notary Public



SASCON INC

Ezequiel Acevedo Jr. #2
 Colonia Testing Requirements

MATERIAL	TEST	DESCRIPTION	REQUIRED	REMARKS	Acevedo Lane CS#2C1080267	Ezequiel Acevedo Jr. #2
FLEX. BASE	Tex-101-E	Prep. Soils and Flex. Base	YES			
	Tex-103-E	Moisture Content	Optional			
	Tex-104-E	Determining Liquid Limit of Soils	YES			
	Tex-105-E	Determining Plastic Limit of Soils	NO			
	Tex-106-E	Calculating Plasticity Index	YES			
	Tex-110-E	Particle Size Analysis	YES			
	Tex-113-E	Moisture Density Relation of Base Materials (including fine)	YES			
	Tex-116-E	Wet Ball Mill Method	YES			
	Tex-117-E	Thermal Compression for Base Material (includes fine)	YES			
	Tex-115-E	In-Place Density	YES			
		Thickness	YES			
LIME	Tex-600-J	Lime Testing Procedure	YES	Required for all flexible bases (Caliche)		
HOT MIX	Tex-207-F	Determining Density of Compacted Bituminous Mixtures	YES			
	Tex-208-F	Test for Stabilometer Value of Bituminous Mixtures	Optional			
	Tex-210-F	Deter. Asph. Content of Bituminous Mixtures by Extraction	YES			
	Tex-228-F	Combined HMA/C Cold Bed Sampling and Testing Procedures	YES			
	Tex-235-F	Deter. Asph. Content from Asph. Paving Struct. By Ignition Method	Optional			
	Tex-212-E	Determining Moisture Content of Bituminous Mixtures	NO			
	Tex-213-E	Determining Hydrocarbon - Bottle Content of Bituminous Mixtures	NO			
EMBANKMENTS	Tex-114-E	Laboratory Compaction Charact. & Modul. - Density Relat. Of Subgrade & Embankments Soils	NO			
	Tex-115-E	In-Piece Density	NO			
	Texas SDHPPT Bulletin C-14		NO			
	ASTM-D-2950.76		NO			
	AASHTO-T-166		NO			

1) Testing for this procedure has been performed and passed.

Date: 12-09-08

Signature: 
 Printed Name: Ricardo Hinojosa, PE

Prepared and Checked By:



L&G Engineering Laboratory

Construction Material Testing
Geotechnical Engineering

2100 W. Expressway 83 Mercedes, TX 78570 (956) 565-0760
900 S. Stewart Rd. Ste. 6 Mission, TX 78572 (956) 583-7117

**PROCTOR
TEST REPORT**

DRAFT

Project Description: Ezequiel Acevedo Jr. Subdv. #2 (Acevedo Lane)
Client: Hidalgo County Pct. #3 (CAP)
Engineer: Javier Hinojosa Engineering
Contractor: Sascon Construction

L&G Project Number: L37813
L&G Report Number: R001
Sample Date: 11/18/2008
Date Reported: 11/20/2008

Page 1 of 1


Compaction Method: ASTM D-698
Material Description: caliche

Specific Gravity: 2.56

Liquid Limit: 31
Plastic Limit: 21
Plasticity Index: 10
% Passing No. 200: 0.0
Group Symbol: cl

Specimen No.:	1	2	3	4
Moisture, %:	5.7	8.7	11.6	15.4
Dry Density (pcf):	113.5	120.5	122.1	114.8

Maximum Dry Density in P.C.F.: 122.2
Optimum Moisture (%): 11.1

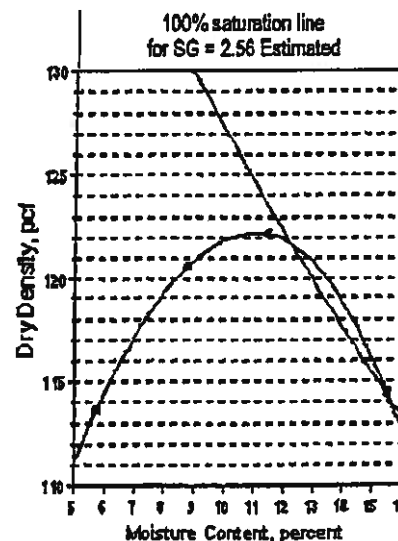

Test Method: ASTM D-698

Orig: Hidalgo County Pct. #3 (CAP) (Mission, TX)
(1-cc copy)
1-cc Javier Hinojosa Engineering
1-cc Sascon Construction
1-cc Laboratory

Respectfully Submitted,
L&G Engineering Laboratory

Orlando A. De Leon, Laboratory Manager
