

Hidalgo County – New Courthouse Project

Monthly Update

April 17, 2018



JACOBS[®]

www.jacobs.com | worldwide

Progress to Date

- Complete Project Team is under contract (HDR and Morganti)
- Schematic Design Plans have been presented and approved by Commissioner's Court; HDR given NTP to move into Design Development phase
- Jacobs' and HDR's Independent Estimates have been completed; Morganti SD estimate in progress
- Geotechnical and Topographical Surveys are underway; Soils boring completed
- Closner Road transition to Hidalgo County ownership is in progress

Looking Ahead

- Design Development Key User Group Meetings – April 2018
- Design Development Steering Committee Meetings – April 2018
- HCCH Project Team Meeting with City of Edinburg – April 2018
- CMAR VE effort is ongoing with workshop scheduled for May 2018
- Court Mock Up Construction – June 2018
- Design Development Phase Completion – July 2018
- Expected Ground Breaking in late 3rd Quarter 2018

PROJECT PHASE

DESIGN DEVELOPMENT




SUMMARY UPDATE

3/29/2018


Project Notes

- 01 Schematic Design Approved by CC on 3/20/2018
- 02 CMAR Contract Finalized; NTP issued on 3/28/2018
- 03 Design Development Phase Underway
- 04 Site Survey, Geotechnical Underway

TOTAL PROJECT BUDGET

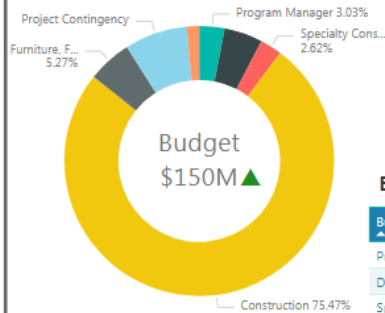

% SPENT



BUDGET STATUS

Under Budget

SCHEDULE % COMPLETE

12.74%

BUDGET DETAILS

Budget Category	Original Budget	Budget Changes	Current Budget	Commitments	ETC*	Projected Total	(Over)/Under	Spent to Date
Program Manager	\$4,500,000	\$45,000	\$4,545,000	\$4,545,000	\$0	\$4,545,000	\$0	\$735,288
Design / AE Fees	\$7,920,000	(\$1,024,700)	\$6,895,300	\$6,895,300	\$0	\$6,895,300	\$0	\$223,080
Specialty Consultants	\$2,900,000	\$1,024,700	\$3,924,700	\$2,107,175	\$1,817,525	\$3,924,700	\$0	\$226,920
Construction	\$113,200,000	\$0	\$113,200,000	\$515,065	\$112,684,935	\$113,200,000	\$0	\$0
Furniture, Fixtures, & Equipment	\$7,900,000	\$0	\$7,900,000	\$0	\$7,900,000	\$7,900,000	\$0	\$0
Project Contingency	\$11,350,000	(\$45,000)	\$11,305,000	\$0	\$11,305,000	\$11,305,000	\$0	\$0
Miscellaneous Fees & Permits	\$2,230,000	\$0	\$2,230,000	\$0	\$2,230,000	\$2,230,000	\$0	\$0
Total	\$150,000,000	\$0	\$150,000,000	\$14,062,540	\$135,937,460	\$150,000,000	\$0	\$1,185,288

*ETC = Estimate to Complete

Project Facts:

- 1) - 333,000 SF; 7 Stories High
- 2) 31 Courtrooms (6 shelled)
- 3) Various County Government Functions
- 4) Sullyport, Secure Parking, and Central Plant

Key Firms:

- Program Manager - Jacobs Project Management Co.
- Architect - HDR Architecture, Inc.
- Construction Manager - Morganti Texas, Inc.

Disclaimer

Important

The material in this presentation has been prepared by Jacobs®.

Copyright and other intellectual property rights in this presentation vest exclusively with Jacobs. Apart from any use permitted under applicable copyright legislation, no part of this work may in any form or by any means (electronic, graphic, mechanical, photocopying, recording or otherwise) be reproduced, copied, stored in a retrieval system or transmitted without prior written permission.

Jacobs is a trademark of Jacobs Engineering Group Inc.

© Copyright

April 17, 2018

Jacobs Engineering Group Inc. All rights reserved.
