



INVOICE
 Invoice Date: 12/31/2023
 Invoice No: 23-12-0032

JAN 18 2024

Page 1 of 1

Pharr, Texas 78577
 Harlingen, Texas 78550
 Laredo, Texas 78041

Client Address: Hidalgo County Precinct 4
 1051 N. Doolittle
 Edinburg, TX. 78542 USA

Account No.: HCP4-2019
 Project No: 01-23-19176
 Project Desc.: San Carlos Parking Lot

P.O. 847671

===== Invoice Detail by Report =====

Report No.	Sampled	Qty	Billing Code	Unit Type	Unit Rate	Extension
34528-1	12/08/2023	1.00	M500-5 - Soil Vehicle Trip (each)	Each	\$70.00	\$70.00
34528-1	12/08/2023	0.50	M510 - Project Management (hourly)	Hour	\$105.00	\$52.50
34528-1	12/08/2023	1.00	M511 - Report Prep. & Administration	Report	\$85.50	\$85.50
34528-1	12/08/2023	0.50	P101 - Project Engineer (hourly)	Hour	\$135.00	\$67.50
34528-1	12/08/2023	1.00	S100 - Atterberg Limits (each)	Each	\$85.00	\$85.00
34528-1	12/08/2023	1.00	S104 - Percent Passing No. 200 Sieve (each)	Each	\$85.00	\$85.00
34528-1	12/08/2023	1.00	S105 - Standard Proctor (each)	Each	\$220.00	\$220.00
34528-1	12/08/2023	5.00	T702 - Soil Field Testing & Observation (hourly)	Hour	\$55.00	\$275.00

Client PO Nbr: 847671

Report Number 34528-1 for a Subtotal of: \$940.50
Total for this Invoice: \$940.50

INVOICE RECEIVED BY:
 Mike Pinyon on 1/18/2024
 COORDINATOR RECEIVED BY:
 Mike Pinyon on 12/8/2023

4-1100-419-00-124-228-0-740

REMIT TO: Millennium Engineers Group, Inc.
 PO BOX 4569
 Edinburg, Texas 78540

Net 30 Days



5804 N. Gumwood Ave. Pharr, Texas 78577 956-702-8500
1221 E. Tyler Ave. Harlingen, Texas 78550 956-454-8832
5918 McPherson Rd., Ste. 5 Laredo, Texas 78041 956-568-1664

Report On: Proctor - Soils

Lab No: 34528-1

Report No: 34528-1

Project No: 01-23-19176 Acct. No.: HCP4-2019

Page 1 of 1

Client: Hidalgo County Precinct 4
1051 N. Doolittle
Edinburg, TX 78542

Project: San Carlos Parking Lot

Report Date: 12/13/2023

Sample Date: 12/08/2023

Sampled By: Flores, Zenon


By Order Of: Joshua

Client PO: 847671

Field ID: 1208-03

Location: Footings

Material: Subgrade

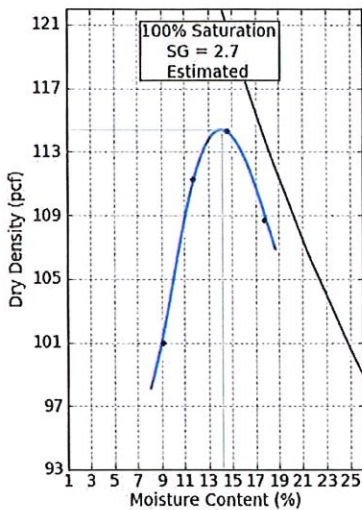

<u>% Moisture</u>		<u>Dry Density Lbs./Cu.Ft.</u>	
9.1		101.0	
11.7		111.3	
14.5		114.3	
17.7		108.7	
14.1	Optimum	114.4	Maximum

<u>Sieve</u>	<u>% Passing</u>	Color: Brown
3/4 in	100	Description: Clayey Sand
No. 4	98	
No. 10	98	
No. 40	97	
No. 200	49	
		Texture: Sandy Loam
		Liquid Limit: 30
		Plastic Limit: 14
		Plasticity Index: 16
		Group Symbol: SC

Desc of Rammer:Manual
Preparation Method:Moist

Test Method (As Applicable): ASTM D 1140, ASTM D 2487, ASTM D 4318, ASTM D-698 Method-B

Respectfully Submitted,
Millennium Engineers Group, Inc.

Juan Borjon
Juan Borjon, P.E.



12/14/2023



RO ENGINEERING, PLLC
Engineering & Construction Management
www.ro-engineering.com

2705 E. Davis Rd.
Edinburg, TX 78542
o. (956) 513-1849
r.olivarez@ro-engineering.com

January 11, 2024

Hidalgo County Precinct 4
2812 S. Business Highway 281
1501 N. Doolittle Rd.
Edinburg, Texas 78542

Re: MEG Invoice 23-12-0032 for Hidalgo Co. Pct4 San Carlos Parking HeadStart Lot Improvement Project

Dear Mr. Nick:

I have reviewed the attached invoice 23-12-0032 submitted by Millennium Engineers Group for the San Carlos HeadStart Parking Lot Improvement Project located on 86th & Hwy 107. I find the invoice to be in general compliance with the work completed. Therefore, we recommend payment be issued.

Should you have any questions don't hesitate to contact me on (956) 513-1849.

Respectfully,

A handwritten signature in black ink, appearing to read 'René R. Olivarez'.

René R. Olivarez, P.E., CSSGB
Principal
