

**RAIN DAY REQUEST FORM**



**NM Contracting, LLC**  
2022 ORCHID AVENUE  
MCALLEN, TEXAS 78504

Office: 956-631-5667 Fax: 956-627-3959

**Project:** Hidalgo County El Paraiso  
Health Clinic & Community  
Resource Center

**Location:** 1901 N Los Ebanos Rd.  
ALTON, TEXAS 78573

**Date:** Wednesday April, 18th

NM Contracting, LLC is requesting the following 3 days due to inclement weather and ground saturation (Mud days) prohibiting construction progress.

**Rain days for the month of March**

<p>March, 2024 18th Rain 19th Rain/Mud 20th Mud</p>		
---	--	--




March 18th



March 19th



March 20

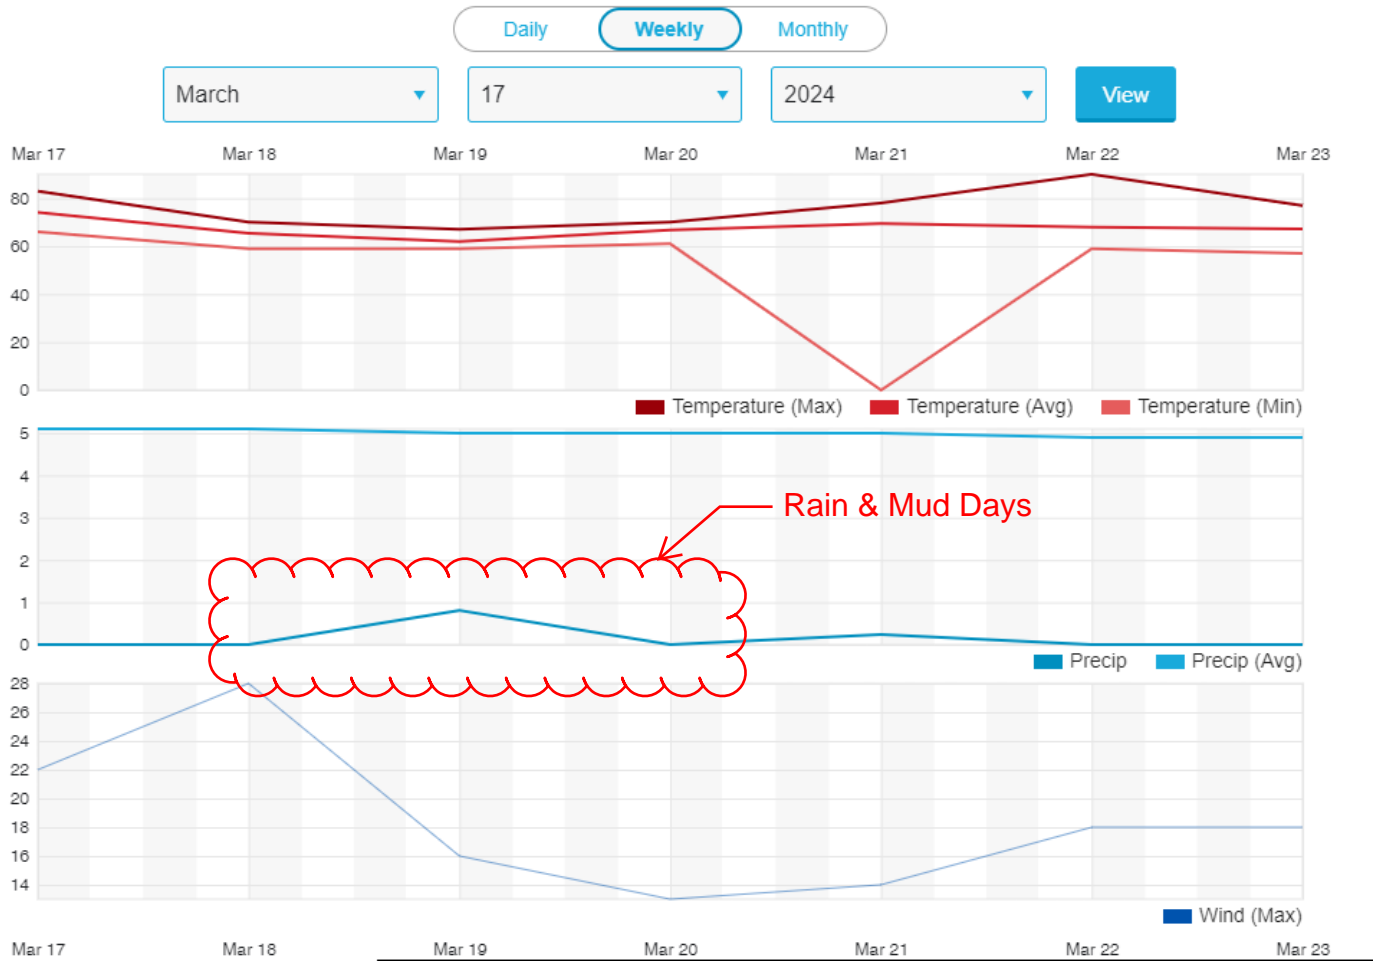

**APPLICATION AND CERTIFICATE FOR PAYMENT**

**TO OWNER:**

Hidalgo County  
100 E. Cano, 2nd Floor  
Edingburg, Texas 78539

**PROJECT:**

Hidalgo County El Paraiso Project  
1901 N. Los Ebanos Rd.  
Alton, TX 78573

**APPLICATION #:**

**2 MAR**

**Distribution to:**

**DATE:** 03/26/24

**PERIOD TO:** 3/31/2024

**PROJECT NO:** 2134

- Owner  
 Const. Mgr  
 Architect  
 Contractor

**FROM CONTRACTOR:**

NM Contracting, LLC  
2022 Orchid Ave  
McAllen, Texas 78504

**VIA Engineer:**

ERO Architect & Engineering  
P.O. Box 720428  
McAllen, Texas 78504

**CONTRACT DATE:** 11/28/23

**PROJECT NO:**

**ARPA-21-340-019 / Health Clinic**

**ARPA-22-123-075 / Community Resource Center**

**CONTRACT FOR:** Hidalgo County El Paraiso Project

**CONTRACTOR'S APPLICATION FOR PAYMENT**

Application is made for payment, as shown below, in connection with the Contract.  
Continuation Sheet is attached.

<b>1. ORIGINAL CONTRACT SUM</b> -----	\$	6,877,000.00
<b>2. Net change by Change Orders</b> -----	\$	
<b>3. CONTRACT SUM TO DATE (Line 1 +/- 2)</b>	\$	6,877,000.00
<b>4. TOTAL COMPLETED &amp; STORED TO DATE</b> -\$		669,254.99
<small>(Column G on Continuation Sheet)</small>		
<b>5. RETAINAGE:</b>		
a. <b>5.0%</b> of Completed Work <small>(Columns D+E on Continuation Sheet)</small>	\$	33,462.75
b. <b>5.0%</b> of Stored Material <small>(Column F on Continuation Sheet)</small>	\$	
Total Retainage (Line 5a + 5b or Total in Column 1 of Continuation Sheet-----	\$	33,462.75
<b>6. TOTAL EARNED LESS RETAINAGE</b> -----	\$	635,792.24
<small>(Line 4 less Line 5 Total)</small>		
<b>7. LESS PREVIOUS CERTIFICATES FOR PAYMENT</b> <small>(Line 6 from prior Certificate)-----</small>	\$	350,996.15
<b>8. CURRENT PAYMENT DUE</b> -----	\$	284,796.09
<b>9. BALANCE TO FINISH, INCLUDING RETAINAGE</b> <small>(Line 3 less Line 6)</small>	\$	6,241,207.76

CHANGE ORDER SUMMARY	ADDITIONS	DEDUCTIONS
Total changes approved in previous months by Owner		
Total approved this Month		
TOTALS		
NET CHANGES by Change Order		

The undersigned Contractor certifies that to the best of the Contractor's knowledge, information and belief the Work covered by this Application for Payment has been completed in accordance with the Contract Documents, that all amounts have been paid by the Contractor for Work for which previous Certificates for Payment were issued and payments received from the Owner, and that current payment shown therein is now due.


CONTRACTOR:

By: [Signature] Date: 4/22/24

State of: Texas  
County of: Hidalgo

Subscribed and sworn to before me this 22nd day of April, 2024

Notary Public: M. Solano  
My Commission expires: 06/26/25



**CERTIFICATE FOR PAYMENT**

In accordance with Contract Documents, based on on-site observations and the data comprising application, the Architect certifies to the Owner that to the best of the Architect's knowledge, information and belief the Work has progressed as indicated, the quality of the Work is in accordance with the Contract Documents, and the Contractor is entitled to payment of the AMOUNT CERTIFIED.

**AMOUNT CERTIFIED** ----- \$ 284,796.09

*(Attach explanation if amount certified differs from the amount applied for. Initial all figures on this application and on the Continuation Sheet that are changed to conform to the amount certified.)*

ARCHITECT: ERO Architects

By: [Signature] Date: 04/23/2024

This Certificate is not negotiable. The AMOUNT CERTIFIED is payable only to the Contractor named herein. Issuance, payment and acceptance of payment are without prejudice to any rights of the Owner of Contractor under this Contract.

**Approved**  
**David Chacon, PE**  
04/22/2024

**CONTINUATION SHEET**

ATTACHMENT TO PAY APPLICATION

APPLICATION NUMBER: **2**

**PROJECT:**

APPLICATION DATE: **03/26/24**

Hidalgo County El Paraiso Project  
1901 N. Los Ebanos Rd.  
Alton, TX 78573

PERIOD TO: **03/31/24**

A Item No.	B Description of Work	C Scheduled Value	D Work Completed		F Materials Presently Stored (Not In D or E)	G Total Completed And Stored To Date (D + E + F)	H % (G/C)	I Balance To Finish (C - G)	J Retainage
			From Previous Application (D + E)	This Period					
<b>HEALTH CLINIC</b>									
1	<b>DIVISION 1- GENERAL REQUIREMENTS</b>								
2	General Conditions	\$27,033.00	1,081.32	1,621.98		2,703.30	10%	24,329.70	135.16
3	Overhead & Profit	\$70,975.00	2,839.00	4,258.50		7,097.50	10%	63,877.50	354.87
4	P&P Bonds / Insurance	\$83,992.37	83,992.37			83,992.37	100%	0.00	4,199.62
5	Building Permit	\$732.00	732.00			732.00	100%	0.00	36.60
6	Superintendent	\$13,355.38	934.88	400.66		1,335.54	10%	12,019.84	66.78
7	GC Mobilization	\$5,960.00	5,960.00			5,960.00	100%	0.00	298.00
8	<b>DIVISION 3 - CONCRETE</b>								
9	Mobilization	\$10,000.00	7,500.00			7,500.00	75%	2,500.00	375.00
10	Submittals / Shop drawings	\$12,500.00	12,500.00			12,500.00	100%	0.00	625.00
11	Foundation Excavation Perimeter Beams	\$12,500.00				0.00	0%	12,500.00	0.00
12	Reinforcement/accessories Material	\$16,500.00				0.00	0%	16,500.00	0.00
13	Reinforcement/accessories Labor	\$15,000.00				0.00	0%	15,000.00	0.00
14	Concrete placement Material	\$45,630.00				0.00	0%	45,630.00	0.00
15	Concrete placement Labor	\$31,600.00				0.00	0%	31,600.00	0.00
16	Termite Treatment Material	\$3,500.00				0.00	0%	3,500.00	0.00
17	Termite Treatment Labor	\$1,500.00				0.00	0%	1,500.00	0.00
18	Lifting accessories/Bracing rental	\$35,001.00				0.00	0%	35,001.00	0.00
19	Reinforcement/accessories concrete TWP Material	\$19,800.00				0.00	0%	19,800.00	0.00
20	Reinforcement/accessories concrete TWP Labor	\$12,500.00				0.00	0%	12,500.00	0.00
21	Concrete TWP accessories/bracing/lifting Material	\$1,200.00				0.00	0%	1,200.00	0.00
22	Concrete placement concrete TWP Material	\$12,500.00				0.00	0%	12,500.00	0.00
23	Concrete placement concrete TWP Labor	\$36,800.00				0.00	0%	36,800.00	0.00
24	<b>DIVISION 4 - MASONRY</b>								
25	Submittals/Mobilization	\$10,315.00	5,157.50			5,157.50	50%	5,157.50	257.88
26	Cast Stone Material	\$6,950.00				0.00	0%	6,950.00	0.00
27	Cast Stone Labor	\$7,150.00				0.00	0%	7,150.00	0.00
28	Thin Brick Material	\$4,110.00				0.00	0%	4,110.00	0.00
29	Thin Brick Labor	\$3,217.00				0.00	0%	3,217.00	0.00
30	Brick Veneer Material	\$24,472.00				0.00	0%	24,472.00	0.00
31	Brick veneer Labor	\$39,120.00				0.00	0%	39,120.00	0.00
32	Reinforcement	\$2,370.00				0.00	0%	2,370.00	0.00
33	CMU Material	\$6,210.00				0.00	0%	6,210.00	0.00
34	CMU Labor	\$6,195.00				0.00	0%	6,195.00	0.00
35	Plaster Material	\$12,211.00				0.00	0%	12,211.00	0.00
36	Plaster Labor	\$14,320.00				0.00	0%	14,320.00	0.00
37	<b>DIVISION 5 - METALS</b>								
38	Mobilization	\$15,000.00				0.00	0%	15,000.00	0.00
39	Shop Drawing	\$2,500.00				0.00	0%	2,500.00	0.00

40	Structural Steel Materials	\$23,539.00				0.00	0%	23,539.00	0.00	
41	Steel Bar joist & deck material	\$55,000.00				0.00	0%	55,000.00	0.00	
42	Steel Fabrication	\$18,000.00				0.00	0%	18,000.00	0.00	
43	Freight	\$1,000.00				0.00	0%	1,000.00	0.00	
44	Steel Erection	\$31,000.00				0.00	0%	31,000.00	0.00	
45	Equipment	\$4,416.00				0.00	0%	4,416.00	0.00	
46	TWP Erection labor	\$30,961.00				0.00	0%	30,961.00	0.00	
47	Aluminum Wall canopies Material	\$15,205.80				0.00	0%	15,205.80	0.00	
48	Aluminum Wall canopies labor	\$10,137.20				0.00	0%	10,137.20	0.00	
49	<b>DIVISION 6 - WOODS &amp; PLASTICS</b>									
50	Shop Drawings	\$1,500.00				0.00	0%	1,500.00	0.00	
51	Millwork Material	\$22,500.00				0.00	0%	22,500.00	0.00	
52	Millwork Labor	\$14,250.00				0.00	0%	14,250.00	0.00	
53	<b>DIVISION 7 - THERMAL &amp; MOISTURE PROTECTION</b>									
54	Mobilizaiton	\$5,000.00				0.00	0%	5,000.00	0.00	
55	Roof Material	\$84,968.00				0.00	0%	84,968.00	0.00	
56	TPO Labor	\$24,000.00				0.00	0%	24,000.00	0.00	
57	Metal Material	\$9,000.00				0.00	0%	9,000.00	0.00	
58	Metal Labor	\$8,000.00				0.00	0%	8,000.00	0.00	
59	Rentals	\$3,000.00				0.00	0%	3,000.00	0.00	
60	<b>DAMPROOFING</b>									
61	Mobilization / Submittals	\$5,500.00				0.00	0%	5,500.00	0.00	
62	Embedded flashing Material	\$1,009.80				0.00	0%	1,009.80	0.00	
63	Embedded flashing Labor	\$673.20				0.00	0%	673.20	0.00	
64	Thermal Insulation Material	\$12,565.80				0.00	0%	12,565.80	0.00	
65	Thermal flashing Labor	\$8,377.20				0.00	0%	8,377.20	0.00	
66	Membrane Air Barrier Material	\$12,113.40				0.00	0%	12,113.40	0.00	
67	Membrane Air barrier Labor	\$8,075.60				0.00	0%	8,075.60	0.00	
68	Flex flashing Material	\$330.00				0.00	0%	330.00	0.00	
69	Flex flashing Labor	\$220.00				0.00	0%	220.00	0.00	
70	Joint Sealant panel Material	\$2,482.80				0.00	0%	2,482.80	0.00	
71	Joint sealant panel Labor	\$1,655.20				0.00	0%	1,655.20	0.00	
72	Joint sealant SOG Material	\$892.80				0.00	0%	892.80	0.00	
73	Joint sealant SOG Labor	\$565.20				0.00	0%	565.20	0.00	
74	Joint sealant sidewalk Material	\$1,005.60				0.00	0%	1,005.60	0.00	
75	Joint sealant sidewalk Labor	\$670.40				0.00	0%	670.40	0.00	
76	<b>DIVISION 8 - DOORS &amp; WINDOWS</b>									
77	H M Frames / Doors Material	\$14,450.00				0.00	0%	14,450.00	0.00	
78	Wood Doors Material	\$23,670.00				0.00	0%	23,670.00	0.00	
79	Doors Hardware Material	\$36,611.25				0.00	0%	36,611.25	0.00	
80	Storefront Glazing Mobilization	\$10,000.00				0.00	0%	10,000.00	0.00	
81	Glass Material	\$12,738.00				0.00	0%	12,738.00	0.00	
82	Glass Labor	\$4,752.00				0.00	0%	4,752.00	0.00	
83	Aluminum Material	\$14,756.00				0.00	0%	14,756.00	0.00	
84	Aluminum Labor	\$4,752.00				0.00	0%	4,752.00	0.00	
85	<b>METAL STUD / DRYWALL / SAC / CARPENTRY</b>									
86	Mobilization/Submittals	\$12,605.00				0.00	0%	12,605.00	0.00	
87	Metal studs Material	\$23,000.00				0.00	0%	23,000.00	0.00	
88	Metal studs Labor	\$14,000.00				0.00	0%	14,000.00	0.00	
89	Rough Carpentry Material	\$2,000.00				0.00	0%	2,000.00	0.00	
90	Rough Carpentry Labor	\$1,000.00				0.00	0%	1,000.00	0.00	

91	Sheating Material	\$10,000.00				0.00	0%	10,000.00	0.00
92	Sheating Labor	\$5,100.00				0.00	0%	5,100.00	0.00
93	Insulation Material	\$11,820.00				0.00	0%	11,820.00	0.00
94	Insulation Labor	\$5,880.00				0.00	0%	5,880.00	0.00
95	Drywall Material	\$48,300.00				0.00	0%	48,300.00	0.00
96	Drywall Labor	\$20,700.00				0.00	0%	20,700.00	0.00
97	Ceilings Material	\$17,125.00				0.00	0%	17,125.00	0.00
98	Ceilings Labor	\$8,375.00				0.00	0%	8,375.00	0.00
99	HMF, Doors, Hardware Labor	\$9,900.00				0.00	0%	9,900.00	0.00
100	Bathroom Accessories Labor	\$4,300.00				0.00	0%	4,300.00	0.00
101	<b>DIVISION 9 - FINISHES</b>								
102	Flooring Submittals	\$1,750.00	1,750.00			1,750.00	100%	0.00	87.50
103	Ceramic Tile Material	\$18,151.00				0.00	0%	18,151.00	0.00
104	Ceramic Tile Labor	\$8,735.00				0.00	0%	8,735.00	0.00
105	LVT Material	\$9,360.00				0.00	0%	9,360.00	0.00
106	LVT Labor	\$500.00				0.00	0%	500.00	0.00
107	Resilient base Material	\$2,240.00				0.00	0%	2,240.00	0.00
108	Resilient base Labor	\$1,200.00				0.00	0%	1,200.00	0.00
109	VCT Material	\$14,189.00				0.00	0%	14,189.00	0.00
110	VCT Labor	\$4,125.00				0.00	0%	4,125.00	0.00
111	Painting Mobilization / Submittals	\$3,500.00	1,750.00			1,750.00	50%	1,750.00	87.50
112	Interior scope Material	\$10,809.00				0.00	0%	10,809.00	0.00
113	Interior scope Labor	\$18,748.00				0.00	0%	18,748.00	0.00
114	Interior rental equipment	\$3,200.00				0.00	0%	3,200.00	0.00
115	Exterior scope Material	\$6,049.00				0.00	0%	6,049.00	0.00
116	Exterior scope Labor	\$9,213.00				0.00	0%	9,213.00	0.00
117	Exterior scope rental	\$3,070.00				0.00	0%	3,070.00	0.00
118	<b>DIVISION 10 - SPECIALTIES</b>								
119	Bathroom Accessories Material	\$4,020.00				0.00	0%	4,020.00	0.00
120	Bathroom Partitions Material	\$9,860.00				0.00	0%	9,860.00	0.00
121	Exterior Dimensional Lettering Material	\$12,300.00				0.00	0%	12,300.00	0.00
122	Lettering Labor	\$2,000.00				0.00	0%	2,000.00	0.00
123	Building Plaque	\$22,900.00				0.00	0%	22,900.00	0.00
124	Visual Display Signage	\$7,350.00				0.00	0%	7,350.00	0.00
125	FEC Material	\$2,050.00				0.00	0%	2,050.00	0.00
126	FEC Labor	\$1,000.00				0.00	0%	1,000.00	0.00
127	Marker Board Material	\$44,000.00				0.00	0%	44,000.00	0.00
128	Cubicle Curtains Material	\$2,500.00				0.00	0%	2,500.00	0.00
129	Corner Guards Material	\$1,375.00				0.00	0%	1,375.00	0.00
130	Defibrillator Material	\$600.00				0.00	0%	600.00	0.00
131	KnoxBox	\$1,000.00				0.00	0%	1,000.00	0.00
132	<b>DIVISION 11 - EQUIPMENT</b>								
133	Video Display Mounts	\$4,100.00				0.00	0%	4,100.00	0.00
134	<b>DIVISION 12 - FURNISHINGS</b>								
135	Louver Blinds Material and Labor	\$1,600.00				0.00	0%	1,600.00	0.00
136	Furnishing and Accessories Material	\$72,758.00				0.00	0%	72,758.00	0.00
137	<b>DIVISION 22 - PLUMBING</b>								
138	Submittals	\$6,500.00				0.00	0%	6,500.00	0.00
139	Mobilization	\$10,000.00				0.00	0%	10,000.00	0.00
140	Sanitary Waste, Drain BFF Material	\$25,020.00				0.00	0%	25,020.00	0.00
141	Sanitary Waste, Vent AFF Material	\$7,007.00				0.00	0%	7,007.00	0.00

142	Domestic water Material	\$7,007.00				0.00	0%	7,007.00	0.00
143	Insulation Material	\$7,007.00				0.00	0%	7,007.00	0.00
144	Fixtures Material	\$19,520.00				0.00	0%	19,520.00	0.00
145	Sanitary Waste, Drain, BFF Labor	\$16,086.00				0.00	0%	16,086.00	0.00
146	Sanitary Waste, Vent AFF Labor	\$4,505.00				0.00	0%	4,505.00	0.00
147	Domestic water Labor	\$4,505.00				0.00	0%	4,505.00	0.00
148	Insulation Labor	\$4,505.00				0.00	0%	4,505.00	0.00
149	Fixtures Labor	\$15,015.00				0.00	0%	15,015.00	0.00
150	<b>DIVISION 23 - HVAC</b>								
151	Mobilize, Permit, Shop Drawing	\$4,500.00				0.00	0%	4,500.00	0.00
152	A/C equipment Material	\$94,900.00				0.00	0%	94,900.00	0.00
153	A/C equipment Labor	\$12,224.00				0.00	0%	12,224.00	0.00
154	Metal Duct Material	\$26,200.00				0.00	0%	26,200.00	0.00
155	Metal duct Labor	\$56,500.00				0.00	0%	56,500.00	0.00
156	Mechanical Material	\$3,200.00				0.00	0%	3,200.00	0.00
157	Mechanical Labor	\$4,200.00				0.00	0%	4,200.00	0.00
158	Air devices, exhaust fans Material	\$10,700.00				0.00	0%	10,700.00	0.00
159	Air devices Exhaust fans Labor	\$2,600.00				0.00	0%	2,600.00	0.00
160	Test and Balance	\$4,676.00				0.00	0%	4,676.00	0.00
161	<b>DIVISION 26 - ELECTRICAL</b>								
162	Mobilization/Submittals	\$13,500.00	6,750.00	6,750.00		13,500.00	100%	0.00	675.00
163	Temporary Power	\$2,250.00				0.00	0%	2,250.00	0.00
164	Rough-In Labor	\$52,300.00				0.00	0%	52,300.00	0.00
165	Rough-In Material	\$48,465.00				0.00	0%	48,465.00	0.00
166	Wire Labor	\$25,800.00				0.00	0%	25,800.00	0.00
167	Wire Material	\$18,500.00				0.00	0%	18,500.00	0.00
168	Lighting Labor	\$17,500.00				0.00	0%	17,500.00	0.00
169	Lighting Material	\$54,008.00				0.00	0%	54,008.00	0.00
170	Device Labor	\$6,500.00				0.00	0%	6,500.00	0.00
171	Device Material	\$4,500.00				0.00	0%	4,500.00	0.00
172	Switchboard Labor	\$16,200.00				0.00	0%	16,200.00	0.00
173	Switchboard Material	\$28,450.00				0.00	0%	28,450.00	0.00
174	<b>SPECIAL SYSTEMS</b>								
175	Data Material	\$50,335.00				0.00	0%	50,335.00	0.00
176	Data Labor	\$17,745.00				0.00	0%	17,745.00	0.00
177	A/V Material	\$40,150.00				0.00	0%	40,150.00	0.00
178	A/V Labor	\$8,299.00				0.00	0%	8,299.00	0.00
179	Access control Material	\$11,950.00				0.00	0%	11,950.00	0.00
180	Access control Labor	\$3,400.00				0.00	0%	3,400.00	0.00
181	Intrusion Material	\$5,182.00				0.00	0%	5,182.00	0.00
182	Intrusion Labor	\$3,540.00				0.00	0%	3,540.00	0.00
183	Fire Alarm Material	\$13,095.00				0.00	0%	13,095.00	0.00
184	Fire alarm Labor	\$6,105.00				0.00	0%	6,105.00	0.00
185	<b>ALLOWANCES</b>								
186	Health Clinic Allowance	\$170,430.00				0.00	0%	170,430.00	0.00
187	<b>HEALTH CLINIC GRAND TOTAL</b>	<b>\$2,625,000.00</b>	<b>\$130,947.07</b>	<b>\$13,031.14</b>	<b>\$0.00</b>	<b>\$143,978.21</b>	<b>5%</b>	<b>\$2,481,021.79</b>	<b>\$7,198.91</b>

188	<b>COMMUNITY RESOURCE CENTER</b>								
189	<b>DIVISION 1- GENERAL REQUIREMENTS</b>								
190	General Conditions	\$167,702.00	6,708.08	10,062.12		16,770.20	10%	150,931.80	838.51
191	Overhead & Profit	\$196,995.00	7,879.80	11,819.70		19,699.50	10%	177,295.50	984.97
192	P&P Bonds / Insurance	\$117,475.63	117,475.63			117,475.63	100%	0.00	5,873.78
193	Building Permit	\$1,098.00	1,098.00			1,098.00	100%	0.00	54.90
194	Superintendent	\$70,384.62	5,046.55	1,991.91		7,038.46	10%	63,346.16	351.92
195	GC Mobilization	\$8,940.00	8,940.00			8,940.00	100%	0.00	447.00
196	<b>DIVISION 3 - CONCRETE</b>								
197	Mobilization	\$10,000.00		5,000.00		5,000.00	50%	5,000.00	250.00
198	Foundation Excavation perimeter beams	\$10,600.00				0.00	0%	10,600.00	0.00
199	Reinforcement/accessories Material	\$11,200.00				0.00	0%	11,200.00	0.00
200	Reinforcement/accessories Labor	\$7,500.00				0.00	0%	7,500.00	0.00
201	Concrete placement Material	\$27,000.00				0.00	0%	27,000.00	0.00
202	Concrete placement Labor	\$27,487.00				0.00	0%	27,487.00	0.00
203	Termite Treatment Material	\$1,500.00				0.00	0%	1,500.00	0.00
204	Termite Treatment Labor	\$1,000.00				0.00	0%	1,000.00	0.00
205	Lifting accessories/Bracing rental	\$27,500.00				0.00	0%	27,500.00	0.00
206	Reinforcement/accessories concrete TWP Material	\$17,358.00				0.00	0%	17,358.00	0.00
207	Reinforcement/accessories concrete TWP Labor	\$13,500.00				0.00	0%	13,500.00	0.00
208	Concrete TWP accessories/bracing/lifting Material	\$1,800.00				0.00	0%	1,800.00	0.00
209	Concrete placement concrete TWP Material	\$11,500.00				0.00	0%	11,500.00	0.00
210	Concrete placement concrete TWP Labor	\$24,842.00				0.00	0%	24,842.00	0.00
211	Dumpster pad Material	\$1,500.00				0.00	0%	1,500.00	0.00
212	Dumpster pad Labor	\$3,200.00				0.00	0%	3,200.00	0.00
213	Concrete Mock up	\$20,000.00				0.00	0%	20,000.00	0.00
214	Concrete mock up accessories	\$7,000.00				0.00	0%	7,000.00	0.00
215	Transformer pad Material	\$1,000.00				0.00	0%	1,000.00	0.00
216	Transformer pad Labor	\$1,900.00				0.00	0%	1,900.00	0.00
217	Monument sign pad Material	\$900.00				0.00	0%	900.00	0.00
218	Monument sign pad Labor	\$2,000.00				0.00	0%	2,000.00	0.00
219	Flag Pole base	\$500.00				0.00	0%	500.00	0.00
220	Fence gate footing	\$6,000.00				0.00	0%	6,000.00	0.00
221	Light pole base Material	\$2,000.00				0.00	0%	2,000.00	0.00
222	Light pole base Labor	\$3,000.00				0.00	0%	3,000.00	0.00
223	<b>DIVISION 4 - MASONRY</b>								
224	Submittals/Mobilization	\$10,315.00	5,157.50			5,157.50	50%	5,157.50	257.88
225	Cast Stone Material	\$6,320.00				0.00	0%	6,320.00	0.00
226	Cast Stone Labor	\$8,913.00				0.00	0%	8,913.00	0.00
227	Brick veneer Material	\$39,612.00				0.00	0%	39,612.00	0.00
228	Brick veneer Labor	\$57,420.00				0.00	0%	57,420.00	0.00
229	<b>DIVISION 5 - METALS</b>								
230	Mobilization	\$10,000.00				0.00	0%	10,000.00	0.00
231	Shop Drawings	\$2,000.00				0.00	0%	2,000.00	0.00
232	Structural Steel Materials	\$23,500.00				0.00	0%	23,500.00	0.00
233	Steel Bar joist & deck Material	\$40,000.00				0.00	0%	40,000.00	0.00
234	Steel Fabrication	\$14,375.00				0.00	0%	14,375.00	0.00
235	Freight	\$750.00				0.00	0%	750.00	0.00
236	Fabrication	\$25,000.00				0.00	0%	25,000.00	0.00
237	Equipment	\$3,404.00				0.00	0%	3,404.00	0.00
238	TWP Erection Labor	\$20,625.00				0.00	0%	20,625.00	0.00

239	Aluminum Wall canopies Material	\$32,095.20				0.00	0%	32,095.20	0.00
240	Aluminum Wall canopies Labor	\$21,396.80				0.00	0%	21,396.80	0.00
241	Dumpster Gates and Bollards Material	\$6,562.50				0.00	0%	6,562.50	0.00
242	Dumpster Gates Labor	\$2,812.50				0.00	0%	2,812.50	0.00
243	<b>DIVISION 6 - WOODS &amp; PLASTICS</b>								
244	Millwork Material	\$5,700.00				0.00	0%	5,700.00	0.00
245	Millwork Labor	\$3,050.00				0.00	0%	3,050.00	0.00
246	<b>DIVISION 7 - THERMAL &amp; MOISTURE PROTECTION</b>								
247	Mobilization	\$4,000.00				0.00	0%	4,000.00	0.00
248	Roof Material	\$63,154.00				0.00	0%	63,154.00	0.00
249	TPO Labor	\$21,000.00				0.00	0%	21,000.00	0.00
250	Metal Material	\$7,000.00				0.00	0%	7,000.00	0.00
251	Metal Labor	\$7,000.00				0.00	0%	7,000.00	0.00
252	Rentals	\$3,000.00				0.00	0%	3,000.00	0.00
253	<b>DAMPROOFING</b>								
254	Mobilization / Submittals	\$5,500.00				0.00	0%	5,500.00	0.00
255	Embedded flashing Material	\$860.40				0.00	0%	860.40	0.00
256	Embedded flashing Labor	\$573.60				0.00	0%	573.60	0.00
257	Thermal Insulation Material	\$10,615.20				0.00	0%	10,615.20	0.00
258	Thermal flashing Labor	\$7,076.80				0.00	0%	7,076.80	0.00
259	Membrane Air Barrier Material	\$10,225.80				0.00	0%	10,225.80	0.00
260	Membrane Air barrier Labor	\$6,817.20				0.00	0%	6,817.20	0.00
261	Flex flashing Material	\$280.80				0.00	0%	280.80	0.00
262	Flex flashing Labor	\$187.20				0.00	0%	187.20	0.00
263	Joint Sealant panel Material	\$2,115.00				0.00	0%	2,115.00	0.00
264	Joint sealant panel Labor	\$1,410.00				0.00	0%	1,410.00	0.00
265	Joint sealant SOG Material	\$760.20				0.00	0%	760.20	0.00
266	Joint sealant SOG Labor	\$506.80				0.00	0%	506.80	0.00
267	Joint sealant sidewalk Material	\$864.60				0.00	0%	864.60	0.00
268	Joint sealant sidewalk Labor	\$576.40				0.00	0%	576.40	0.00
269	<b>DIVISION 8 - DOORS &amp; WINDOWS</b>								
270	H M Frames / Doors material	\$6,025.00				0.00	0%	6,025.00	0.00
271	Wood Doors material	\$7,890.00				0.00	0%	7,890.00	0.00
272	Doors Hardware material	\$12,203.75				0.00	0%	12,203.75	0.00
273	Storefront Glazing Mobilization	\$7,003.00				0.00	0%	7,003.00	0.00
274	Glass Material	\$20,350.00				0.00	0%	20,350.00	0.00
275	Glass Labor	\$7,291.00				0.00	0%	7,291.00	0.00
276	Aluminum Material	\$25,067.00				0.00	0%	25,067.00	0.00
277	Aluminum Labor	\$7,291.00				0.00	0%	7,291.00	0.00
278	<b>METAL STUD / DRYWALL / SAC / CARPENTRY</b>								
279	Metal studs Material	\$10,040.00				0.00	0%	10,040.00	0.00
280	Metal studs Labor	\$6,160.00				0.00	0%	6,160.00	0.00
281	Rough Carpentry Material	\$2,000.00				0.00	0%	2,000.00	0.00
282	Rough Carpentry Labor	\$1,000.00				0.00	0%	1,000.00	0.00
283	Sheating Material	\$8,120.00				0.00	0%	8,120.00	0.00
284	Sheating Labor	\$3,480.00				0.00	0%	3,480.00	0.00
285	Insulation Material	\$13,860.00				0.00	0%	13,860.00	0.00
286	Insulation Labor	\$5,940.00				0.00	0%	5,940.00	0.00
287	Drywall Material	\$19,180.00				0.00	0%	19,180.00	0.00
288	Drywall Labor	\$8,220.00				0.00	0%	8,220.00	0.00

289	Acoustical Panels Material	\$8,000.00				0.00	0%	8,000.00	0.00
290	Acoustical Panels Labor	\$1,900.00				0.00	0%	1,900.00	0.00
291	Ceilings Material	\$40,205.00				0.00	0%	40,205.00	0.00
292	Ceilings Labor	\$32,595.00				0.00	0%	32,595.00	0.00
293	HMF, Doors, Hardware Labor	\$4,000.00				0.00	0%	4,000.00	0.00
294	Bathroom Accessories Labor	\$1,900.00				0.00	0%	1,900.00	0.00
295	<b>DIVISION 9 - FINISHES</b>								
296	Ceramic Tile Material	\$13,590.00				0.00	0%	13,590.00	0.00
297	Ceramic Tile Labor	\$7,000.00				0.00	0%	7,000.00	0.00
298	VCT Material	\$9,030.00				0.00	0%	9,030.00	0.00
299	VCT Labor	\$2,625.00				0.00	0%	2,625.00	0.00
300	Resilient base Materials	\$980.00				0.00	0%	980.00	0.00
301	Resilient base Labor	\$525.00				0.00	0%	525.00	0.00
302	Painting Interior scope Material	\$7,536.00				0.00	0%	7,536.00	0.00
303	Painting Interior scope Labor	\$13,501.00				0.00	0%	13,501.00	0.00
304	Interior rental equipment	\$1,800.00				0.00	0%	1,800.00	0.00
305	Exterior scope Material	\$4,553.00				0.00	0%	4,553.00	0.00
306	Exterior scope Labor	\$6,933.00				0.00	0%	6,933.00	0.00
307	Exterior scope rental	\$2,311.00				0.00	0%	2,311.00	0.00
308	Dumpster Material	\$747.00				0.00	0%	747.00	0.00
309	Dumpster Labor	\$1,519.00				0.00	0%	1,519.00	0.00
310	<b>DIVISION 10 - SPECIALTIES</b>								
311	Bathroom Accessories Material	\$2,020.00				0.00	0%	2,020.00	0.00
312	Bathroom Partitions Material	\$4,930.00				0.00	0%	4,930.00	0.00
313	Exterior Dimensional Lettering Material	\$6,000.00				0.00	0%	6,000.00	0.00
314	Lettering Labor	\$1,500.00				0.00	0%	1,500.00	0.00
315	Building Plaque	\$22,900.00				0.00	0%	22,900.00	0.00
316	Visual Display Signage	\$2,125.00				0.00	0%	2,125.00	0.00
317	FEC Material	\$810.00				0.00	0%	810.00	0.00
318	FEC Labor	\$800.00				0.00	0%	800.00	0.00
319	Folding Panel Partitions Material	\$88,960.00				0.00	0%	88,960.00	0.00
320	Folding Panel Partition Labor	\$37,290.00				0.00	0%	37,290.00	0.00
321	Flag Pole Material	\$6,500.00				0.00	0%	6,500.00	0.00
322	Flag Pole Labor	\$1,000.00				0.00	0%	1,000.00	0.00
323	Marker Board Material	\$15,100.00				0.00	0%	15,100.00	0.00
324	Corner Guards Material	\$700.00				0.00	0%	700.00	0.00
325	Defibrillator Material	\$600.00				0.00	0%	600.00	0.00
326	KnoxBox	\$1,000.00				0.00	0%	1,000.00	0.00
327	<b>DIVISION 11 - EQUIPMENT</b>								
328	Foodservice Equipment	\$65,045.00				0.00	0%	65,045.00	0.00
329	Foodservice Equipment Labor	\$1,475.00				0.00	0%	1,475.00	0.00
330	Video Display Mounts	\$8,200.00				0.00	0%	8,200.00	0.00
331	<b>DIVISION 12 - FURNISHINGS</b>								
332	Louwer Blinds Material and Labor	\$3,150.00				0.00	0%	3,150.00	0.00
333	Furnishing and Accessories Material	\$48,505.00				0.00	0%	48,505.00	0.00
334	<b>DIVISION 22 - PLUMBING</b>								
335	Sanitary Waste, Drain BFF Material	\$16,701.00				0.00	0%	16,701.00	0.00
336	Sanitary Waste, Vent AFF Material	\$3,570.00				0.00	0%	3,570.00	0.00
337	Domestic water Material	\$3,570.00				0.00	0%	3,570.00	0.00
338	Insulation Material	\$3,570.00				0.00	0%	3,570.00	0.00
339	Fixtures Material	\$9,944.00				0.00	0%	9,944.00	0.00

340	Sanitary Waste, Drain, BFF Labor	\$10,100.00				0.00	0%	10,100.00	0.00
341	Sanitary Waste, Vent AFF Labor	\$2,295.00				0.00	0%	2,295.00	0.00
342	Domestic water Labor	\$2,295.00				0.00	0%	2,295.00	0.00
343	Insulation Labor	\$2,295.00				0.00	0%	2,295.00	0.00
344	Fixtures Labor	\$7,649.00				0.00	0%	7,649.00	0.00
345	<b>DIVISION 23 - HVAC</b>								
346	Mobilization	\$3,500.00				0.00	0%	3,500.00	0.00
347	JCI A/C equipment Material	\$68,000.00				0.00	0%	68,000.00	0.00
348	A/C equipment Labor	\$11,800.00				0.00	0%	11,800.00	0.00
349	Metal Duct Material	\$13,500.00				0.00	0%	13,500.00	0.00
350	Metal duct Labor	\$26,900.00				0.00	0%	26,900.00	0.00
351	Mechanical Material	\$2,820.00				0.00	0%	2,820.00	0.00
352	Mechanical Labor	\$2,700.00				0.00	0%	2,700.00	0.00
353	Air devices, exhaust fans Material	\$8,630.00				0.00	0%	8,630.00	0.00
354	Air devices Exhaust fans Labor	\$2,400.00				0.00	0%	2,400.00	0.00
355	Test and Balance	\$3,150.00				0.00	0%	3,150.00	0.00
356	<b>DIVISION 26 - ELECTRICAL</b>								
357	Mobilization/Submittals	\$7,250.00		7,250.00		7,250.00	100%	0.00	362.50
358	Temporary Power	\$2,500.00				0.00	0%	2,500.00	0.00
359	Rough-In Labor	\$55,351.00				0.00	0%	55,351.00	0.00
360	Rough-In Material	\$32,500.00				0.00	0%	32,500.00	0.00
361	Wire Labor	\$28,500.00				0.00	0%	28,500.00	0.00
362	Wire Material	\$15,100.00				0.00	0%	15,100.00	0.00
363	Lighting Labor	\$10,510.00				0.00	0%	10,510.00	0.00
364	Lighting Material	\$46,865.00				0.00	0%	46,865.00	0.00
365	Device Labor	\$6,500.00				0.00	0%	6,500.00	0.00
366	Device Material	\$4,500.00				0.00	0%	4,500.00	0.00
367	Switchboard Labor	\$8,400.00				0.00	0%	8,400.00	0.00
368	Switchboard Material	\$25,300.00				0.00	0%	25,300.00	0.00
369	Generator/ATS Labor	\$7,334.00				0.00	0%	7,334.00	0.00
370	Generator/ATS Material	\$85,400.00				0.00	0%	85,400.00	0.00
371	<b>SPECIAL SYSTEMS</b>								
372	Data Material	\$33,600.00				0.00	0%	33,600.00	0.00
373	Data Labor	\$10,300.00				0.00	0%	10,300.00	0.00
374	A/V Material	\$55,650.00				0.00	0%	55,650.00	0.00
375	A/V Labor	\$13,100.00				0.00	0%	13,100.00	0.00
376	Access control Material	\$8,015.00				0.00	0%	8,015.00	0.00
377	Access control Labor	\$2,350.00				0.00	0%	2,350.00	0.00
378	Intrusion Material	\$3,831.00				0.00	0%	3,831.00	0.00
379	Intrusion Labor	\$3,030.00				0.00	0%	3,030.00	0.00
380	Fire Alarm Material	\$10,500.00				0.00	0%	10,500.00	0.00
381	Fire alarm Labor	\$3,300.00				0.00	0%	3,300.00	0.00
382	<b>DIVISION 31 - EARTHWORK</b>								
383	Mobilization	\$35,000.00	35,000.00			35,000.00	100%	0.00	1,750.00
384	Construction entrance	\$6,500.00		2,800.00		2,800.00	43%	3,700.00	140.00
385	SWPP Plan	\$3,500.00	3,500.00			3,500.00	100%	0.00	175.00
386	Traffic Control	\$4,000.00				0.00	0%	4,000.00	0.00
387	Hauling	\$1,187.00	1,187.00			1,187.00	100%	0.00	59.35
388	Inlet protection	\$3,200.00				0.00	0%	3,200.00	0.00
389	Silt fence	\$6,800.00	5,780.00	1,020.00		6,800.00	100%	0.00	340.00

390	Building Pad A / select fill Material	\$42,442.60		42,442.60		42,442.60	100%	0.00	2,122.13
391	Building Pad A / select fill Labor	\$57,557.39		57,557.39		57,557.39	100%	0.00	2,877.87
392	Building Pad B /select fill Material	\$41,269.25		41,269.25		41,269.25	100%	0.00	2,063.46
393	Building Pad B /select fill Labor	\$53,730.75		53,730.75		53,730.75	100%	0.00	2,686.54
394	Detention pond install	\$10,379.15				0.00	0%	10,379.15	0.00
395	Detention pond Labor	\$11,057.85				0.00	0%	11,057.85	0.00
396	Detention swales Install	\$4,000.00	2,000.00			2,000.00	50%	2,000.00	100.00
397	Detention swales Labor	\$3,076.85				0.00	0%	3,076.85	0.00
398	Site clearing level install	\$29,073.00		14,536.50		14,536.50	50%	14,536.50	726.83
399	Site clearing level Labor	\$61,548.00		30,774.00		30,774.00	50%	30,774.00	1,538.70
400	Concrete washout prep	\$8,436.40				0.00	0%	8,436.40	0.00
401	Concrete washout removal	\$10,500.00				0.00	0%	10,500.00	0.00
402	Demolition/Hauling/Disposal	\$15,000.00	15,000.00			15,000.00	100%	0.00	750.00
403	Demolition Labor	\$20,000.00	20,000.00			20,000.00	100%	0.00	1,000.00
404	<b>DIVISION 32 - EXTERIOR IMPROVEMENTS</b>								
405	Asphalt Materials	\$44,273.59				0.00	0%	44,273.59	0.00
406	Asphalt labor	\$28,533.41				0.00	0%	28,533.41	0.00
407	Liquid lime materials	\$10,400.00				0.00	0%	10,400.00	0.00
408	Liquid lime labor	\$2,343.24				0.00	0%	2,343.24	0.00
409	Caliche materials	\$15,550.05				0.00	0%	15,550.05	0.00
410	Caliche labor	\$21,919.95				0.00	0%	21,919.95	0.00
411	Curb and gutter material	\$18,450.80				0.00	0%	18,450.80	0.00
412	Curb and gutter labor	\$21,789.70				0.00	0%	21,789.70	0.00
413	5" Concrete paving / sidewalks material	\$64,155.38				0.00	0%	64,155.38	0.00
414	5" concrete paving / sidewalks labor	\$71,987.82				0.00	0%	71,987.82	0.00
415	6" Mono curb material	\$1,322.01				0.00	0%	1,322.01	0.00
416	6" Mono curb labor	\$4,553.59				0.00	0%	4,553.59	0.00
417	ADA ramps material	\$1,987.65				0.00	0%	1,987.65	0.00
418	ADA ramps labor	\$5,593.60				0.00	0%	5,593.60	0.00
419	Drain chutes material	\$1,217.58				0.00	0%	1,217.58	0.00
420	Drain chutes labor	\$1,749.27				0.00	0%	1,749.27	0.00
421	4" valley gutter material	\$5,127.83				0.00	0%	5,127.83	0.00
422	4" valley gutter labor	\$829.17				0.00	0%	829.17	0.00
423	Concrete spillway material	\$7,089.30				0.00	0%	7,089.30	0.00
424	Concrete spillway labor	\$4,726.20				0.00	0%	4,726.20	0.00
425	Roof drain covers material	\$920.26				0.00	0%	920.26	0.00
426	Roof drain covers labor	\$769.74				0.00	0%	769.74	0.00
427	<b>LANDSCAPE / IRRIGATION</b>								
428	Mobilization / Submittals	\$7,500.00	3,750.00			3,750.00	50%	3,750.00	187.50
429	Landscape Material	\$35,142.00				0.00	0%	35,142.00	0.00
430	Landscape Labor	\$7,358.00				0.00	0%	7,358.00	0.00
431	Landscape site work	\$7,500.00				0.00	0%	7,500.00	0.00
432	Irrigation Material	\$30,274.00				0.00	0%	30,274.00	0.00
433	Irrigation Labor	\$10,726.00				0.00	0%	10,726.00	0.00
434	Sleeving Material	\$1,280.00				0.00	0%	1,280.00	0.00
435	Sleeving Labor	\$640.00				0.00	0%	640.00	0.00
436	<b>DIVISION 33 - UTILITIES</b>								
437	<b>DOMESTIC WATER</b>								
438	Mobilization	\$8,000.00				0.00	0%	8,000.00	0.00
439	Submittals / Shop drawings	\$6,500.00		6,500.00		6,500.00	100%	0.00	325.00

440	12" Gate VIV Material	\$8,504.92				0.00	0%	8,504.92	0.00
441	12" Gate VIV Labor	\$555.08				0.00	0%	555.08	0.00
442	12" Water Line Material	\$57,564.00				0.00	0%	57,564.00	0.00
443	12" Water Line Labor	\$17,906.00				0.00	0%	17,906.00	0.00
444	12" Cut in Tee Material	\$3,620.96				0.00	0%	3,620.96	0.00
445	12" Cut in Tee Labor	\$309.04				0.00	0%	309.04	0.00
446	18" Steel Casing w/ bore Material	\$5,879.55				0.00	0%	5,879.55	0.00
447	18" Steel Casing w/ bore Labor	\$49,241.25				0.00	0%	49,241.25	0.00
448	4" Water Line to be Cut & Capped	\$10,996.60				0.00	0%	10,996.60	0.00
449	12" x 6" Tee Material	\$3,677.41				0.00	0%	3,677.41	0.00
450	12" x 6" Tee Labor	\$479.59				0.00	0%	479.59	0.00
451	6" Gate VIV Material	\$5,000.00				0.00	0%	5,000.00	0.00
452	6" Gate VIV Labor	\$1,500.00				0.00	0%	1,500.00	0.00
453	6" Water Line @ HYDSD Material	\$8,831.91				0.00	0%	8,831.91	0.00
454	6" Water Line @ HYDSD Labor	\$5,612.97				0.00	0%	5,612.97	0.00
455	Fire Hyds Assys	\$22,050.00				0.00	0%	22,050.00	0.00
456	12" Steel Casing w/ bore Material	\$645.29				0.00	0%	645.29	0.00
457	12" Steel Casing w/ bore Labor	\$9,284.96				0.00	0%	9,284.96	0.00
458	12" x 1.5" Saddle Material	\$1,800.00				0.00	0%	1,800.00	0.00
459	12" x 1.5" Saddle Labor	\$1,647.52				0.00	0%	1,647.52	0.00
460	1.5" Water Line Material	\$3,800.00				0.00	0%	3,800.00	0.00
461	1.5" Water Line Labor	\$2,412.40				0.00	0%	2,412.40	0.00
462	Meter Box Material	\$1,000.00				0.00	0%	1,000.00	0.00
463	Meter Box Labor	\$1,647.52				0.00	0%	1,647.52	0.00
464	1.5" Angle Stop Material	\$3,500.00				0.00	0%	3,500.00	0.00
465	1.5" Angle Stop Install	\$1,647.52				0.00	0%	1,647.52	0.00
466	1.5" Corp Stop Material	\$3,500.00				0.00	0%	3,500.00	0.00
467	1.5" Corp Stop Install	\$1,647.52				0.00	0%	1,647.52	0.00
468	1.5" 45* Elbows Material	\$1,000.00				0.00	0%	1,000.00	0.00
469	1.5" 45* Elbows Inatall	\$1,647.52				0.00	0%	1,647.52	0.00
470	12" 45* Elbows Material	\$1,929.64				0.00	0%	1,929.64	0.00
471	12" 45* Elbows Inatall	\$330.36				0.00	0%	330.36	0.00
472	Connect to Exist Water Service 12" water line Material	\$7,130.00				0.00	0%	7,130.00	0.00
473	Connect to Exist Water Service 12" water line Labor	\$20,180.00				0.00	0%	20,180.00	0.00
474	4" 90* Elbow Material	\$1,219.99				0.00	0%	1,219.99	0.00
475	4" 90* Elbow Install	\$160.01				0.00	0%	160.01	0.00
476	4" Gate VIV Material	\$1,033.88				0.00	0%	1,033.88	0.00
477	4" Gate VIV Install	\$366.12				0.00	0%	366.12	0.00
478	4" x 12" Reducer Material	\$1,310.32				0.00	0%	1,310.32	0.00
479	4" x 12" Reducer Install	\$319.68				0.00	0%	319.68	0.00
480	<b>SANITARY SEWER</b>								
481	6" sanitary sewer connection	\$2,500.00				0.00	0%	2,500.00	0.00
482	6" sanitary sewer connection Labor	\$1,000.00				0.00	0%	1,000.00	0.00
483	6" clean out assembly Materials	\$5,080.00				0.00	0%	5,080.00	0.00
484	6" clean out assembly Labor	\$1,250.00				0.00	0%	1,250.00	0.00
485	6" wye Materials	\$1,000.00				0.00	0%	1,000.00	0.00
486	6" wye Labor	\$500.00				0.00	0%	500.00	0.00
487	6" 45* elbow Material	\$800.00				0.00	0%	800.00	0.00
488	6" 45* elbow Labor	\$370.00				0.00	0%	370.00	0.00
489	Leach field aggregate/soils	\$10,000.00				0.00	0%	10,000.00	0.00

490	Leach field Material	\$20,000.00				0.00	0%	20,000.00	0.00
491	Leach field Labor	\$12,500.00				0.00	0%	12,500.00	0.00
492	5000 septic tank Material	\$32,500.00				0.00	0%	32,500.00	0.00
493	5000 septic tank Labor	\$7,500.00				0.00	0%	7,500.00	0.00
494	4000 septic tanks Material	\$22,500.00				0.00	0%	22,500.00	0.00
495	4000 septic tank Labor	\$7,500.00				0.00	0%	7,500.00	0.00
496	Grease tank Material	\$10,000.00				0.00	0%	10,000.00	0.00
497	Grease tank Labor	\$5,000.00				0.00	0%	5,000.00	0.00
498	<b>STORM SEWER</b>								
499	18" RCP material	\$39,836.17				0.00	0%	39,836.17	0.00
500	18" RCP labor	\$26,703.09				0.00	0%	26,703.09	0.00
501	24" RCP material	\$12,563.00				0.00	0%	12,563.00	0.00
502	24" RCP labor	\$14,871.83				0.00	0%	14,871.83	0.00
503	Open cut storm materail	\$886.14				0.00	0%	886.14	0.00
504	Open cut storm labor	\$4,513.86				0.00	0%	4,513.86	0.00
505	18" dia. Sftye ends	\$2,543.00				0.00	0%	2,543.00	0.00
506	Outlet structure 24" material	\$3,953.33				0.00	0%	3,953.33	0.00
507	Outlet structure 24" labor	\$2,853.67				0.00	0%	2,853.67	0.00
508	24" RCP to curb inlet material	\$455.41				0.00	0%	455.41	0.00
509	24" RCP to curb inlet labor	\$3,624.59				0.00	0%	3,624.59	0.00
510	Storm manhole material	\$15,345.88				0.00	0%	15,345.88	0.00
511	Storm manhole labor	\$7,169.12				0.00	0%	7,169.12	0.00
512	Curb inlet material	\$5,843.04				0.00	0%	5,843.04	0.00
513	Curb inlet labor	\$2,666.96				0.00	0%	2,666.96	0.00
514	<b>ALLOWANCES</b>								
515	Community Resource Center allowance	\$191,000.00				0.00	0%	191,000.00	0.00
516	<b>CRC GRAND TOTAL</b>	\$4,252,000.00	\$238,522.56	\$286,754.22	\$0.00	\$525,276.78	12%	3,726,723.22	26,263.84
517									
518	<b>HC &amp; CRC GRAND TOTAL</b>	\$6,877,000.00	\$369,469.63	\$299,785.36	\$0.00	\$669,254.99	10%	6,207,745.01	33,462.75

**CONTINUATION SHEET**

ATTACHMENT TO PAY APPLICATION

APPLICATION NUMBER: **2-Jan**

**PROJECT:**

APPLICATION DATE: **03/26/24**

Hidalgo County El Paraiso Project  
 1901 N. Los Ebanos Rd.  
 Alton, TX 78573

PERIOD TO: **03/31/24**

A Item No.	B Description of Work	C Scheduled Value	D Work Completed		F Materials Presently Stored (Not In D or E)	G		H Balance To Finish (C - G)
			D From Previous Application (D + E)	E This Period		Total Completed And Stored To Date (D + E + F)	% (G/C)	
	<b>CONTINGENCY ALLOWANCE EXPENDITURE BREAKDOWN</b>							
	<b>HEALTH CLINIC</b>					0.00	0%	0.00
	<b>COMMUNITY RESOURCE CENTER</b>							
<b>THIS PAGE IS FOR REFERENCE PURPOSES ONLY. IT DOES NOT AFFECT TOTAL VALUES.</b>								
	<b>GRAND TOTAL</b>	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	0.00

**PAYROLL**

For contractor's optional use; see instructions at [dol.gov/agencies/whd/forms/wh347](http://dol.gov/agencies/whd/forms/wh347)



Persons are not required to respond to the collection of information unless it displays a currently valid OMB control number.

NAME OF CONTRACTOR  OR SUBCONTRACTOR  ADDRESS 3406 JOYCEE DR, MISSION, TX 78573  
 JR - GARCIA COMPANY LLC OMB No. 1235-0008 Expires 09/30/2026

PAYROLL NO. 1 FOR WEEK ENDING 03/08/2024 PROJECT AND LOCATION HIDALGO COUNTY EL PARAISO HEALTH CLINIC & COMMUNITY RESOURCE CENTER PROJECT PROJECT OR CONTRACT NO. 21087

(1) NAME AND INDIVIDUAL IDENTIFYING NUMBER (e.g., LAST FOUR DIGITS OF SOCIAL SECURITY NUMBER) OF WORKER	(2) NO. OF WITHHOLDING EXEMPTIONS	(3) WORK CLASSIFICATION	OT OR ST	(4) DAY AND DATE							(5) TOTAL HOURS	(6) RATE OF PAY	(7) GROSS AMOUNT EARNED	(8) DEDUCTIONS					(9) NET WAGES PAID FOR WEEK
				F	S	S	M	T	W	T				FICA	WITH-HOLDING TAX	OTHER	TOTAL DEDUCTIONS		
				1	2	3	4	5	6	7									
JOSE LUIS GARCIA 2925	0	MOTOR GRADER OPERATOR	O									\$30.00	\$640.00						
			S			8.00	8.00	8.00	8.00	32.00	20.00		\$48.96	\$101.16				\$150.12	\$489.88
JUAN SALGADO JR 7653	0	COMMON LABOR	O									\$16.50	\$352.00						
			S			8.00	8.00	8.00	8.00	32.00	11.00		\$26.92	\$28.92				\$55.84	\$296.16
			O																
			S																
			O																
			S																
			O																
			S																
			O																
			S																

While completion of Form WH-347 is optional, it is mandatory for covered contractors and subcontractors performing work on Federally financed or assisted construction contracts to respond to the information collection contained in 29 C.F.R. §§ 3.3, 5.5(a). The Copeland Act (40 U.S.C. § 3145) contractors and subcontractors performing work on Federally financed or assisted construction contracts to "furnish weekly a statement with respect to the wages paid each employee during the preceding week." U.S. Department of Labor (DOL) regulations at 29 C.F.R. § 5.5(a)(3)(ii) require contractors to submit weekly a copy of all payrolls to the Federal agency contracting for or financing the construction project, accompanied by a signed "Statement of Compliance" indicating that the payrolls are correct and complete and that each laborer or mechanic has been paid not less than the proper Davis-Bacon prevailing wage rate for the work performed. DOL and federal contracting agencies receiving this information review the information to determine that employees have received legally required wages and fringe benefits.

**Public Burden Statement**

We estimate that it will take an average of 55 minutes to complete this collection, including time for reviewing instructions, searching existing data sources, gathering and maintaining the data needed, and completing and reviewing the collection of information. If you have any comments regarding these estimates or any other aspect of this collection, including suggestions for reducing this burden, send them to the Administrator, Wage and Hour Division, U.S. Department of Labor, Room S3502, 200 Constitution Avenue, N.W. Washington, D.C. 20210



**U.S. Department of Labor**

Wage and Hour Division

**PAYROLL**

For contractor's optional use; see instructions at [dol.gov/agencies/whd/forms/wh347](http://dol.gov/agencies/whd/forms/wh347)

Persons are not required to respond to the collection of information unless it displays a currently valid OMB control number.



WAGE AND HOUR DIVISION

Revised December 2008

NAME OF CONTRACTOR  OR SUBCONTRACTOR  ADDRESS 3406 JOYCEE DR, MISSION, TX 78573  
 JR - GARCIA COMPANY LLC OMB No. 1235-0008 Expires 09/30/2026

PAYROLL NO. 2 FOR WEEK ENDING 03/15/2024 PROJECT AND LOCATION HIDALGO COUNTY EL PARAISO HEALTH CLINIC & COMMUNITY RESOURCE CENTER PROJECT PROJECT OR CONTRACT NO. 21087

(1) NAME AND INDIVIDUAL IDENTIFYING NUMBER (e.g., LAST FOUR DIGITS OF SOCIAL SECURITY NUMBER) OF WORKER	(2) NO. OF WITH-HOLDING EXEMPTIONS	(3) WORK CLASSIFICATION	OT. OR ST.	(4) DAY AND DATE							(5) TOTAL HOURS	(6) RATE OF PAY	(7) GROSS AMOUNT EARNED	(8) DEDUCTIONS					(9) NET WAGES PAID FOR WEEK
				F	S	S	M	T	W	T				FICA	WITH- HOLDING TAX	OTHER	TOTAL DEDUCTIONS		
				8	9	10	11	12	13	14									
JOSE LUIS GARCIA 2925	0	MOTOR GRADER OPERATOR	O									\$30.00	\$800.00	\$61.20	\$126.45			\$187.65	\$612.35
			S	8.00			8.00	8.00	8.00	8.00	40.00	20.00							
JUAN SALGADO JR 7653	0	COMMON LABOR	O									\$16.50	\$440.00	\$33.66	\$36.15			\$69.81	\$370.19
			S	8.00			8.00	8.00	8.00	8.00	40.00	11.00							
			O																
			S																
			O																
			S																
			O																
			S																
			O																
			S																
			O																
			S																

While completion of Form WH-347 is optional, it is mandatory for covered contractors and subcontractors performing work on Federally financed or assisted construction contracts to respond to the information collection contained in 29 C.F.R. §§ 3.3, 5.5(a). The Copeland Act (40 U.S.C. § 3145) contractors and subcontractors performing work on Federally financed or assisted construction contracts to "furnish weekly a statement with respect to the wages paid each employee during the preceding week." U.S. Department of Labor (DOL) regulations at 29 C.F.R. § 5.5(a)(3)(ii) require contractors to submit weekly a copy of all payrolls to the Federal agency contracting for or financing the construction project, accompanied by a signed "Statement of Compliance" indicating that the payrolls are correct and complete and that each laborer or mechanic has been paid not less than the proper Davis-Bacon prevailing wage rate for the work performed. DOL and federal contracting agencies receiving this information review the information to determine that employees have received legally required wages and fringe benefits.

**Public Burden Statement**

We estimate that it will take an average of 55 minutes to complete this collection, including time for reviewing instructions, searching existing data sources, gathering and maintaining the data needed, and completing and reviewing the collection of information. If you have any comments regarding these estimates or any other aspect of this collection, including suggestions for reducing this burden, send them to the Administrator, Wage and Hour Division, U.S. Department of Labor, Room S3502, 200 Constitution Avenue, N.W. Washington, D.C. 20210

Date 03/15/2024

I, ADRIANA N LEAL BOOKKEEPER  
(Name of Signatory Party) (Title)

do hereby state:

(1) That I pay or supervise the payment of the persons employed by  
JR - GARCIA COMPANY LLC on the  
(Contractor or Subcontractor)

HIDALGO COUNTY EL PARAISO; that during the payroll period commencing on the  
(Building or Work)

8 day of MARCH, 2024, and ending the 14 day of MARCH, 2024,

all persons employed on said project have been paid the full weekly wages earned, that no rebates have been or will be made either directly or indirectly to or on behalf of said

JR - GARCIA COMPANY LLC from the full  
(Contractor or Subcontractor)

weekly wages earned by any person and that no deductions have been made either directly or indirectly from the full wages earned by any person, other than permissible deductions as defined in Regulations, Part 3 (29 C.F.R. Subtitle A), issued by the Secretary of Labor under the Copeland Act, as amended (48 Stat. 948, 63 Stat. 108, 72 Stat. 967; 76 Stat. 357; 40 U.S.C. § 3145), and described below:

\_\_\_\_\_  
\_\_\_\_\_  
\_\_\_\_\_

(2) That any payrolls otherwise under this contract required to be submitted for the above period are correct and complete; that the wage rates for laborers or mechanics contained therein are not less than the applicable wage rates contained in any wage determination incorporated into the contract; that the classifications set forth therein for each laborer or mechanic conform with the work he performed.

(3) That any apprentices employed in the above period are duly registered in a bona fide apprenticeship program registered with a State apprenticeship agency recognized by the Bureau of Apprenticeship and Training, United States Department of Labor, or if no such recognized agency exists in a State, are registered with the Bureau of Apprenticeship and Training, United States Department of Labor.

(4) That:

(a) WHERE FRINGE BENEFITS ARE PAID TO APPROVED PLANS, FUNDS, OR PROGRAMS

- in addition to the basic hourly wage rates paid to each laborer or mechanic listed in the above referenced payroll, payments of fringe benefits as listed in the contract have been or will be made to appropriate programs for the benefit of such employees, except as noted in section 4(c) below.

(b) WHERE FRINGE BENEFITS ARE PAID IN CASH

- Each laborer or mechanic listed in the above referenced payroll has been paid, as indicated on the payroll, an amount not less than the sum of the applicable basic hourly wage rate plus the amount of the required fringe benefits as listed in the contract, except as noted in section 4(c) below.

(c) EXCEPTIONS

EXCEPTION (CRAFT)	EXPLANATION

REMARKS

NAME AND TITLE Adriana N. Leal - Bookkeeper SIGNATURE Adriana N. Leal

THE WILLFUL FALSIFICATION OF ANY OF THE ABOVE STATEMENTS MAY SUBJECT THE CONTRACTOR OR SUBCONTRACTOR TO CIVIL OR CRIMINAL PROSECUTION. SEE SECTION 1001 OF TITLE 18 AND SECTION 3729 OF TITLE 31 OF THE UNITED STATES CODE.

PAYROLL

For contractor's optional use; see instructions at [dol.gov/agencies/whd/forms/wh347](http://dol.gov/agencies/whd/forms/wh347)

Persons are not required to respond to the collection of information unless it displays a currently valid OMB control number.



WAGE AND HOUR DIVISION  
Revised December 2008

NAME OF CONTRACTOR  OR SUBCONTRACTOR  JR - GARCIA COMPANY LLC ADDRESS 3406 JOYCEE DR, MISSION, TX 78573  
OMB No. 1235-0008 Expires 09/30/2026

PAYROLL NO. 3 FOR WEEK ENDING 03/22/2024 PROJECT AND LOCATION HIDALGO COUNTY EL PARAISO HEALTH CLINIC & COMMUNITY RESOURCE CENTER PROJECT PROJECT OR CONTRACT NO. 21087

(1) NAME AND INDIVIDUAL IDENTIFYING NUMBER (e.g., LAST FOUR DIGITS OF SOCIAL SECURITY NUMBER) OF WORKER	(2) NO. OF WITH-HOLDING EXEMPTIONS	(3) WORK CLASSIFICATION	OT OR ST.	(4) DAY AND DATE							(5) TOTAL HOURS	(6) RATE OF PAY	(7) GROSS AMOUNT EARNED	(8) DEDUCTIONS					(9) NET WAGES PAID FOR WEEK
				F	S	S	M	T	W	T				FICA	WITH- HOLDING TAX	OTHER	TOTAL DEDUCTIONS		
				15	16	17	18	19	20	21									
JOSE LUIS GARCIA 2925	0	MOTOR GRADER OPERATOR	O									\$30.00	\$320.00	\$24.48	\$50.58		\$75.06	\$244.94	
			S	8.00						8.00	16.00	20.00							
JUAN SALGADO JR 7653	0	COMMON LABOR	O									\$16.50	\$176.00	\$13.46	\$14.46		\$27.92	\$148.08	
			S	8.00						8.00	16.00	11.00							
			O																
			S																
			O																
			S																
			O																
			S																
			O																
			S																
			O																
			S																

While completion of Form WH-347 is optional, it is mandatory for covered contractors and subcontractors performing work on Federally financed or assisted construction contracts to respond to the information collection contained in 29 C.F.R. §§ 3.3, 5.5(a). The Copeland Act (40 U.S.C. § 3145) contractors and subcontractors performing work on Federally financed or assisted construction contracts to "furnish weekly a statement with respect to the wages paid each employee during the preceding week." U.S. Department of Labor (DOL) regulations at 29 C.F.R. § 5.5(a)(3)(ii) require contractors to submit weekly a copy of all payrolls to the Federal agency contracting for or financing the construction project, accompanied by a signed "Statement of Compliance" indicating that the payrolls are correct and complete and that each laborer or mechanic has been paid not less than the proper Davis-Bacon prevailing wage rate for the work performed. DOL and federal contracting agencies receiving this information review the information to determine that employees have received legally required wages and fringe benefits.

Public Burden Statement

We estimate that it will take an average of 55 minutes to complete this collection, including time for reviewing instructions, searching existing data sources, gathering and maintaining the data needed, and completing and reviewing the collection of information. If you have any comments regarding these estimates or any other aspect of this collection, including suggestions for reducing this burden, send them to the Administrator, Wage and Hour Division, U.S. Department of Labor, Room S3502, 200 Constitution Avenue, N.W. Washington, D.C. 20210

