

APPLICATION AND CERTIFICATE FOR PAYMENT

TO OWNER:

The County of Hidalgo Pct. 01
Weslaco Texas 78599

PROJECT:

New Wellness Activity Community Center
Weslaco, Texas 78599

APPLICATION #:

7-May R1
Date: 5/1/2025
Period To: 5/31/2025
Job #: 2143

FROM CONTRACTOR:

NM Contracting, LLC
2022 Orchid Ave.
McAllen, TX 78504

B2Z Engineering, LLC
3700 N. 10th Street, Ste. 205
McAllen, Texas 78501

CONTRACT FOR: New Weslaco Activity Community Center

CONTRACTOR'S APPLICATION FOR PAYMENT

Application is made for payment, as shown below, in connection with the Contract.
Continuation Sheet is attached.

1. ORIGINAL CONTRACT SUM -----	\$	5,948,509.00
2. Net change by Change Orders -----	\$	
3. CONTRACT SUM TO DATE (Line 1 +/- 2)	\$	5,948,509.00
4. TOTAL COMPLETED & STORED TO DATE-\$ (Column G on Continuation Sheet)		1,703,736.67
5. RETAINAGE:		
a. 5.0% of Completed Work (Columns D+E on Continuation Sheet)	\$	85,186.83
b. 5.0% of Stored Material (Column F on Continuation Sheet)	\$	
Total Retainage (Line 5a + 5b or Total in Column 1 of Continuation Sheet)-----	\$	85,186.83
6. TOTAL EARNED LESS RETAINAGE ----- (Line 4 less Line 5 Total)	\$	1,618,549.84
7. LESS PREVIOUS CERTIFICATES FOR PAYMENT (Line 6 from prior Certificate)-----	\$	857,500.71
8. CURRENT PAYMENT DUE -----	\$	761,049.13
9. BALANCE TO FINISH, INCLUDING RETAINAGE (Line 3 less Line 6)	\$	4,329,959.16

CHANGE ORDER SUMMARY	ADDITIONS	DEDUCTIONS
Total changes approved in previous months by Owner		
Total approved this Month		
TOTALS		
NET CHANGES by Change Order		

The undersigned Contractor certifies that to the best of the Contractor's knowledge, information and belief the Work covered by this Application for Payment has been completed in accordance with the Contract Documents, that all amounts have been paid by the Contractor for Work for which previous Certificates for Payment were issued and payments received from the Owner, and that current payment shown therein is now due.

CONTRACTOR:

By: [Signature] Date: 6/6/25

State of: Texas
County of: Hidalgo

Subscribed and sworn to before me this 6th day of June



Notary Public: Carolina Villarreal
My Commission expires: 05/05/2029

CERTIFICATE FOR PAYMENT

In accordance with Contract Documents, based on on-site observations and the data comprising application, the Architect certifies to the Owner that to the best of the Architect's knowledge, information and belief the Work has progressed as indicated, the quality of the Work is in accordance with the Contract Documents, and the Contractor is entitled to payment of the AMOUNT CERTIFIED.

AMOUNT CERTIFIED ----- \$ 761,049.13
(Attach explanation if amount certified differs from the amount applied for. Initial all figures on this application and on the Continuation Sheet that are changed to conform to the amount certified.)

ARCHITECT:

By: [Signature] Date: 06/16/2025

This Certificate is not negotiable. The AMOUNT CERTIFIED is payable only to the Contractor named herein. Issuance, payment and acceptance of payment are without prejudice to any rights of the Owner of Contractor under this Contract.

CONTINUATION SHEET

ATTACHMENT TO PAY APPLICATION

APPLICATION NUMBER: 7-May

APPLICATION DATE: 5/1/2025

PERIOD TO: 5/31/2025

PROJECT:

Hidalgo County Pct. 01 Wellness Activity Community Center
Project No:C-24-02956-10-15

A Item No.	B Description of Work New Wellness Activity Community Center	C Scheduled Value	D Work Completed		F Materials Presently Stored (Not In D or E)	G Total Completed And Stored To Date (D + E + F)	H % (G/C)	I Balance To Finish (C - G)	J Retainage
			From Previous Application (D + E)	This Period					
DIVISION 1- GENERAL REQUIREMENTS									
2	General Conditions	\$140,195.00	\$21,029.25	18,225.35		39,254.60	28%	100,940.40	1,962.73
3	Permit	\$10,800.00	\$10,800.00			10,800.00	100%	0.00	540.00
4	Overhead & Profit	\$217,000.00	\$32,550.00	28,210.00		60,760.00	28%	156,240.00	3,038.00
5	P&P Bonds / Insurance	\$204,933.54	\$204,933.54			204,933.54	100%	0.00	10,246.68
6	Superintendent	\$41,000.00	\$6,150.00	5,330.00		11,480.00	28%	29,520.00	574.00
7	GC Mobilization	\$20,000.00	\$20,000.00			20,000.00	100%	0.00	1,000.00
8	SUBTOTAL	\$633,928.54	\$295,462.79	\$51,765.35	\$0.00	\$347,228.14	55%	\$286,700.40	\$17,361.41
DIVISION 3- CONCRETE									
10	Mobilization	\$30,800.00	\$30,800.00			30,800.00	100%	0.00	1,540.00
11	Foundation excavation perimeter beams	\$15,500.00	\$9,300.00	6,200.00		15,500.00	100%	0.00	775.00
12	Reinforcing/accessories materials	\$65,000.00	\$65,000.00			65,000.00	100%	0.00	3,250.00
13	Reinforcing accessories labor	\$53,000.00	\$13,250.00	26,500.00		39,750.00	75%	13,250.00	1,987.50
14	Concrete placement materials	\$140,000.00		82,600.00		82,600.00	59%	57,400.00	4,130.00
15	Concrete placement labor	\$79,625.00		46,978.75		46,978.75	59%	32,646.25	2,348.94
16	Mezzanine materials	\$6,375.00				0.00	0%	6,375.00	0.00
17	Mezzanine labor	\$15,000.00				0.00	0%	15,000.00	0.00
18	Light pole materials	\$3,000.00				0.00	0%	3,000.00	0.00
19	Light pole labor	\$4,000.00				0.00	0%	4,000.00	0.00
20	Transformer pad materials	\$1,500.00				0.00	0%	1,500.00	0.00
21	Transformer pad labor	\$1,500.00				0.00	0%	1,500.00	0.00
22	Termite treat material	\$5,000.00				0.00	0%	5,000.00	0.00
23	Sidewalk rebar materials	\$1,500.00				0.00	0%	1,500.00	0.00
24	Sidewalk rebar labor	\$2,500.00				0.00	0%	2,500.00	0.00
25	Sidewalk concrete material	\$6,500.00				0.00	0%	6,500.00	0.00
26	Sidewalk concrete labor	\$4,000.00				0.00	0%	4,000.00	0.00
27	Dumpster pad rebar materials	\$1,500.00				0.00	0%	1,500.00	0.00
28	Dumpster pad rebar labor	\$1,000.00				0.00	0%	1,000.00	0.00
29	Dumpster pad concrete materials	\$2,000.00				0.00	0%	2,000.00	0.00
30	Dumpster pad concrete labor	\$2,000.00				0.00	0%	2,000.00	0.00
31	Housekeeping pad / Generator rebar materials	\$1,750.00				0.00	0%	1,750.00	0.00
32	Housekeeping pad / Generator rebar labor	\$1,000.00				0.00	0%	1,000.00	0.00
33	Housekeeping pad / Generator concrete materials	\$2,500.00				0.00	0%	2,500.00	0.00
34	Housekeeping pad / Generator concrete labor	\$4,000.00				0.00	0%	4,000.00	0.00
35	SUBTOTAL	\$450,550.00	\$118,350.00	\$162,278.75	\$0.00	\$280,628.75	62%	\$169,921.25	\$14,031.44

36	DIVISION 4- MASONRY								
37	CMU submittal	\$20,000.00		20,000.00		20,000.00	100%	0.00	1,000.00
38	Masonry CMU mobilization	\$20,000.00		20,000.00		20,000.00	100%	0.00	1,000.00
39	North CMU wall material	\$26,000.00		26,000.00		26,000.00	100%	0.00	1,300.00
40	South CMU wall material	\$26,000.00		26,000.00		26,000.00	100%	0.00	1,300.00
41	East CMU wall material	\$42,000.00		42,000.00		42,000.00	100%	0.00	2,100.00
42	West CMU wall material	\$42,000.00		42,000.00		42,000.00	100%	0.00	2,100.00
43	Interior CMU wall material	\$40,000.00		40,000.00		40,000.00	100%	0.00	2,000.00
44	Split face CMU columns material	\$25,000.00		25,000.00		25,000.00	100%	0.00	1,250.00
45	North CMU wall labor	\$27,000.00				0.00	0%	27,000.00	0.00
46	South CMU wall labor	\$27,000.00				0.00	0%	27,000.00	0.00
47	East CMU wall labor	\$50,000.00				0.00	0%	50,000.00	0.00
48	West CMU wall labor	\$50,000.00				0.00	0%	50,000.00	0.00
49	Interior CMU wall labor	\$60,000.00				0.00	0%	60,000.00	0.00
50	Split face CMU columns labor	\$25,000.00				0.00	0%	25,000.00	0.00
51	Sand material	\$15,000.00				0.00	0%	15,000.00	0.00
52	Masonry cement materials	\$20,000.00				0.00	0%	20,000.00	0.00
53	CMU fill material	\$20,000.00				0.00	0%	20,000.00	0.00
54	Pump rental	\$20,000.00				0.00	0%	20,000.00	0.00
55	Scaffolds	\$40,000.00				0.00	0%	40,000.00	0.00
56	Equipment rental	\$16,000.00		3,200.00		3,200.00	20%	12,800.00	160.00
57	Fuels	\$20,000.00				0.00	0%	20,000.00	0.00
58	Reinforcement	\$54,000.00				0.00	0%	54,000.00	0.00
59	SUBTOTAL	\$685,000.00	\$0.00	\$244,200.00	\$0.00	\$244,200.00	36%	\$440,800.00	\$12,210.00
60	DIVISION 5 - METALS								
61	Structural Steel Materials & Labor								
62	Shop Drawing	\$30,000.00	\$22,500.00	7,500.00		30,000.00	100%	0.00	1,500.00
63	PEMB Steel Materials	\$175,000.00		175,000.00		175,000.00	100%	0.00	8,750.00
64	PEMB Steel Fabrication	\$154,268.00		154,268.00		154,268.00	100%	0.00	7,713.40
65	Structural Steel material	\$55,000.00	\$4,950.00			4,950.00	9%	50,050.00	247.50
66	Steel Bar joist, metal deck, Epic deck material, Bollards, Dumps	\$95,000.00	\$0.00			0.00	0%	95,000.00	0.00
67	Structural Steel Fabrication	\$45,000.00	\$4,950.00			4,950.00	11%	40,050.00	247.50
68	PEMB Structure Erection	\$150,000.00				0.00	0%	150,000.00	0.00
69	Steel Erection - Mezzanine	\$50,000.00				0.00	0%	50,000.00	0.00
70	Equipment	\$45,000.00				0.00	0%	45,000.00	0.00
71	Metal Roof & Wall Panels	\$135,000.00				0.00	0%	135,000.00	0.00
72	SUBTOTAL	\$934,268.00	\$32,400.00	\$336,768.00	\$0.00	\$369,168.00	40%	\$565,100.00	\$18,458.40
73	DIVISION 6 - WOODS & PLASTICS								
74	Millwork								
75	Millwork materials	\$5,000.00				0.00	0%	5,000.00	0.00
76	Millwork installation labor	\$2,500.00				0.00	0%	2,500.00	0.00
77	SUBTOTAL	\$7,500.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$7,500.00	\$0.00
78	DIVISION 7- THERMAL & MOISTURE PROTECTION								
79									
80	Mobilization	\$10,000.00				0.00	0%	10,000.00	0.00
81	Membrane flashing materials	\$19,740.00				0.00	0%	19,740.00	0.00
82	Membrane flashing labor	\$13,160.00				0.00	0%	13,160.00	0.00
83	Dampproofing materials	\$34,360.00				0.00	0%	34,360.00	0.00
84	Dampproofing labor	\$22,400.00				0.00	0%	22,400.00	0.00

85	ISO Board materials	\$23,430.00				0.00	0%	23,430.00	0.00
86	ISO Board labor	\$15,350.00				0.00	0%	15,350.00	0.00
87	Foam in place material	\$25,735.00				0.00	0%	25,735.00	0.00
88	Foam in place labor	\$17,155.00				0.00	0%	17,155.00	0.00
89	Open cell foam material	\$34,215.00				0.00	0%	34,215.00	0.00
90	Open cell foam labor	\$24,775.00				0.00	0%	24,775.00	0.00
91	Caulking CMU, Sidewalk materials	\$6,770.00				0.00	0%	6,770.00	0.00
92	Caulking CMU, Sidewalk labor	\$2,910.00				0.00	0%	2,910.00	0.00
93	SUBTOTAL	\$250,000.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$250,000.00	\$0.00
94	DIVISION 8- DOORS & WINDOWS								
95	Doors								
96	H M Frames / Doors material	\$31,615.00		4,742.25		4,742.25	15%	26,872.75	237.11
97	Wood Doors material	\$19,950.00				0.00	0%	19,950.00	0.00
98	Doors Hardware material	\$100,000.00				0.00	0%	100,000.00	0.00
99	Overhead doors materials	\$16,896.00				0.00	0%	16,896.00	0.00
100	Overhead doors labor	\$3,039.00				0.00	0%	3,039.00	0.00
101	Storefront Glazing								
102	Mobilization	\$3,027.00				0.00	0%	3,027.00	0.00
103	Glass Material	\$8,500.00				0.00	0%	8,500.00	0.00
104	Glass Lab	\$4,500.00				0.00	0%	4,500.00	0.00
105	Aluminum Mat	\$14,494.00				0.00	0%	14,494.00	0.00
106	Aluminum Lab	\$7,500.00				0.00	0%	7,500.00	0.00
107	Metal Stud/Drywall/SAT/Carpentry								
108	Metal stud structural materials	\$33,764.00				0.00	0%	33,764.00	0.00
109	Metal stud structural labor	\$30,894.00				0.00	0%	30,894.00	0.00
110	Metal stud Interior materials	\$35,273.00				0.00	0%	35,273.00	0.00
111	Metal studs Interior labor	\$54,040.00				0.00	0%	54,040.00	0.00
112	Drywall material	\$36,678.00				0.00	0%	36,678.00	0.00
113	Drywall labor	\$41,408.00				0.00	0%	41,408.00	0.00
114	Insulation materials	\$13,476.00				0.00	0%	13,476.00	0.00
115	Insulation labor	\$12,725.00				0.00	0%	12,725.00	0.00
116	Suspended Acoustical ceiling material	\$27,031.00				0.00	0%	27,031.00	0.00
117	Suspended Acoustical ceiling labor	\$24,088.00				0.00	0%	24,088.00	0.00
118	Gypboard ceiling materials	\$3,388.00				0.00	0%	3,388.00	0.00
119	Gypboard ceilings labor	\$4,235.00				0.00	0%	4,235.00	0.00
120	Acoustical panels materials	\$40,936.00				0.00	0%	40,936.00	0.00
121	Acoustical panels labor	\$11,500.00				0.00	0%	11,500.00	0.00
122	General labor	\$13,725.00				0.00	0%	13,725.00	0.00
123	Rough carpentry	\$5,324.00				0.00	0%	5,324.00	0.00
124	SUBTOTAL	\$598,006.00	\$0.00	\$4,742.25	\$0.00	\$4,742.25	1%	\$593,263.75	\$237.11
125	DIVISION 9- FINISHES								
126	Flooring								
127	Admin / insurance	\$3,845.00				0.00	0%	3,845.00	0.00
128	Samples / submittals	\$450.00				0.00	0%	450.00	0.00
129	Materials handling and mobilization	\$900.00				0.00	0%	900.00	0.00
130	Resilient materials	\$7,700.00				0.00	0%	7,700.00	0.00
131	Resilient labor	\$3,000.00				0.00	0%	3,000.00	0.00
132	Ceramic tile materials	\$25,900.00				0.00	0%	25,900.00	0.00
133	Ceramic tile labor	\$15,000.00				0.00	0%	15,000.00	0.00

134	Floor patch / prep materials	\$200.00				0.00	0%	200.00	0.00
135	Floor patch / prep labor	\$200.00				0.00	0%	200.00	0.00
136	Sports flooring	\$209,190.00				0.00	0%	209,190.00	0.00
137	Painting								
138	Tape / float materials	\$6,000.00				0.00	0%	6,000.00	0.00
139	Tape / float labor	\$12,000.00				0.00	0%	12,000.00	0.00
140	Primer materials	\$2,000.00				0.00	0%	2,000.00	0.00
141	Primer labor	\$3,000.00				0.00	0%	3,000.00	0.00
142	Block filler materials	\$12,000.00				0.00	0%	12,000.00	0.00
143	Block filler labor	\$16,000.00				0.00	0%	16,000.00	0.00
144	Paint material	\$12,000.00				0.00	0%	12,000.00	0.00
145	Paint labor	\$17,000.00				0.00	0%	17,000.00	0.00
146	Paint HM frames and doors material	\$2,000.00				0.00	0%	2,000.00	0.00
147	Paint HM Frames and doors labor	\$3,000.00				0.00	0%	3,000.00	0.00
148	Dryfall exposed steel / foam materials	\$5,000.00				0.00	0%	5,000.00	0.00
149	Dryfall exposed steel / foam labor	\$7,000.00				0.00	0%	7,000.00	0.00
150	Ext. block filler materials	\$3,500.00				0.00	0%	3,500.00	0.00
151	Ext. block filler labor	\$4,500.00				0.00	0%	4,500.00	0.00
152	Elastomeric paint material	\$5,750.00				0.00	0%	5,750.00	0.00
153	Elastomeric paint labor	\$8,000.00				0.00	0%	8,000.00	0.00
154	SUBTOTAL	\$385,135.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$385,135.00	\$0.00
155	DIVISION 10- SPECIALTIES								
156	Toilet Partitions material	\$7,580.00				0.00	0%	7,580.00	0.00
157	Bathroom accessories material	\$6,700.00				0.00	0%	6,700.00	0.00
158	Interior Building signage	\$2,049.00				0.00	0%	2,049.00	0.00
159	Dedicatory Signage and Building Plaque	\$18,055.00				0.00	0%	18,055.00	0.00
160	FEC material	\$2,035.00				0.00	0%	2,035.00	0.00
161	Handicap post / signage	\$400.00	\$400.00			400.00	100%	0.00	20.00
162	Tack board	\$1,275.00				0.00	0%	1,275.00	0.00
163	Defibrillator	\$1,983.00				0.00	0%	1,983.00	0.00
164	Bench / Metal Lockers	\$1,992.00				0.00	0%	1,992.00	0.00
165	SUBTOTAL	\$42,069.00	\$400.00	\$0.00	\$0.00	\$400.00	1%	41,669.00	\$20.00
166	DIVISION11 EQUIPMENT								
167	Draper gym equipment	\$128,512.00				0.00	0%	128,512.00	0.00
168	Varsity Sportable scoreboards	\$12,140.00				0.00	0%	12,140.00	0.00
169	DGJD Tip and Roll bleachers	\$23,440.00				0.00	0%	23,440.00	0.00
170	Gym equipment install	\$26,680.00				0.00	0%	26,680.00	0.00
171	Engineering/Project management	\$10,040.00				0.00	0%	10,040.00	0.00
172	Stainless Steel counter	\$9,000.00				0.00	0%	9,000.00	0.00
173	SUBTOTAL	\$209,812.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$209,812.00	\$0.00
174	DIVISION 21- FIRE SPRINKLER SYSTEM								
175	Mobilization	\$2,100.00	\$2,100.00			2,100.00	100%	0.00	105.00
176	Design work	\$2,700.00	\$1,350.00	\$1,350.00		2,700.00	100%	0.00	135.00
177	Submittals	\$300.00	\$300.00			300.00	100%	0.00	15.00
178	Materials	\$51,640.00	\$0.00			0.00	0%	51,640.00	0.00
179	Underground installation	\$13,120.00	\$13,120.00			13,120.00	100%	0.00	656.00
180	Underground labor	\$10,000.00	\$10,000.00			10,000.00	100%	0.00	500.00
181	Riser installation	\$1,114.00	\$1,114.00			1,114.00	100%	0.00	55.70
182	Main lines installation	\$2,228.00				0.00	0%	2,228.00	0.00
183	Branch lines installation	\$3,899.00				0.00	0%	3,899.00	0.00

184	Sprinkler heads installation	\$3,342.00				0.00	0%	3,342.00	0.00	
185	Testing	\$557.00				0.00	0%	557.00	0.00	
186	SUBTOTAL	\$91,000.00	\$27,984.00	\$1,350.00	\$0.00	\$29,334.00	32%	\$61,666.00	\$1,466.70	
187	DIVISION 22- PLUMBING									
188	Submittals	\$1,653.60	\$1,653.60			1,653.60	100%	0.00	82.68	
189	Material									
190	Sanitary Waste, Drain BFF	\$33,072.10	\$33,072.10			33,072.10	100%	0.00	1,653.61	
191	Sanitary Waste, Vent AFF	\$11,575.23	\$0.00			0.00	0%	11,575.23	0.00	
192	Domestic water	\$11,575.23	\$0.00			0.00	0%	11,575.23	0.00	
193	Insulation mat	\$11,575.23	\$0.00			0.00	0%	11,575.23	0.00	
194	Fixtures Mat	\$32,245.29	\$0.00			0.00	0%	32,245.29	0.00	
195	Labor									
196	Sanitary Waste, Drain BFF	\$16,536.05	\$16,536.05			16,536.05	100%	0.00	826.80	
197	Sanitary Waste, Vent AFF	\$7,441.22				0.00	0%	7,441.22	0.00	
198	Domestic water	\$7,441.22				0.00	0%	7,441.22	0.00	
199	Insulation mat	\$7,441.22				0.00	0%	7,441.22	0.00	
200	Fixtures Mat	\$24,804.07				0.00	0%	24,804.07	0.00	
201	SUBTOTAL	\$165,360.46	\$51,261.75	\$0.00	\$0.00	\$51,261.75	31%	\$114,098.71	\$2,563.09	
202	DIVISION 23- HVAC									
203	Mobilization	\$12,000.00	\$2,040.00			2,040.00	17%	9,960.00	102.00	
204	Submittals	\$3,500.00	\$3,500.00			3,500.00	100%	0.00	175.00	
205	Permit	\$1,250.00				0.00	0%	1,250.00	0.00	
206	Equipment rental	\$11,000.00				0.00	0%	11,000.00	0.00	
207	Fabricate Spiral ductwork materials	\$172,306.00	\$22,399.78			22,399.78	13%	149,906.22	1,119.99	
208	Fabricate Spiral labor	\$37,500.00	\$15,000.00			15,000.00	40%	22,500.00	750.00	
209	Ductwork installation	\$112,500.00				0.00	0%	112,500.00	0.00	
210	Ductwork installation materials/accessories	\$24,045.00				0.00	0%	24,045.00	0.00	
211	Air device materials	\$8,891.00				0.00	0%	8,891.00	0.00	
212	Air device labor	\$2,800.00				0.00	0%	2,800.00	0.00	
213	Exhaust fans / heaters materials	\$2,280.00				0.00	0%	2,280.00	0.00	
214	Exhaust fans / heaters labor	\$1,500.00				0.00	0%	1,500.00	0.00	
215	Overhead piping materials	\$3,425.00				0.00	0%	3,425.00	0.00	
216	Overhead piping labor	\$3,630.00				0.00	0%	3,630.00	0.00	
217	RTU / fan coil unit equipment	\$140,067.00				0.00	0%	140,067.00	0.00	
218	RTU / fan coil unit labor	\$2,800.00				0.00	0%	2,800.00	0.00	
219	Controls materials / labor	\$55,160.00				0.00	0%	55,160.00	0.00	
220	Test and Balance	\$6,050.00				0.00	0%	6,050.00	0.00	
221	SUBTOTAL	\$600,704.00	\$42,939.78	\$0.00	\$0.00	\$42,939.78	7%	\$557,764.22	\$2,146.99	
223	DIVISION 26- ELECTRICAL									
224	Mobilization	\$15,000.00	\$15,000.00			15,000.00	100%	0.00	750.00	
225	Underground conduit materials	\$33,000.00	\$33,000.00			33,000.00	100%	0.00	1,650.00	
226	Underground conduit labor	\$53,000.00	\$53,000.00			53,000.00	100%	0.00	2,650.00	
227	Electrical rough-in materials	\$31,000.00				0.00	0%	31,000.00	0.00	
228	Electrical rough-in labor	\$50,000.00				0.00	0%	50,000.00	0.00	
229	Electrical wire materials	\$38,000.00				0.00	0%	38,000.00	0.00	
230	Electrical wire labor	\$55,000.00				0.00	0%	55,000.00	0.00	
231	Electrical gear materials	\$68,000.00				0.00	0%	68,000.00	0.00	
232	Electrical gear labor	\$31,000.00				0.00	0%	31,000.00	0.00	

233	Light fixtures materials	\$51,000.00				0.00	0%	51,000.00	0.00
234	Light fixtures labor	\$36,000.00				0.00	0%	36,000.00	0.00
235	Trim out	\$1,900.00				0.00	0%	1,900.00	0.00
236		\$462,900.00	\$101,000.00	\$0.00	\$0.00	\$101,000.00	22%	\$361,900.00	\$5,050.00
237	DIVISION 31 - EARTHWORK								
238	Mobilization	\$20,000.00	20,000.00			20,000.00	100%	0.00	1,000.00
239	Inlet protection labor	\$270.00				0.00	0%	270.00	0.00
240	Inlet protection material	\$630.00				0.00	0%	630.00	0.00
241	Silt fence labor	\$2,209.00	\$2,209.00			2,209.00	100%	0.00	110.45
242	Silt fence material	\$5,427.00	\$5,427.00			5,427.00	100%	0.00	271.35
243	Remove and spread on site 2' NG labor	\$4,530.00	\$4,530.00			4,530.00	100%	0.00	226.50
244	Remove and spread on site 2' NG material	\$10,570.00	\$10,570.00			10,570.00	100%	0.00	528.50
245	Select fill 2.5 labor	\$21,693.00	\$21,693.00			21,693.00	100%	0.00	1,084.65
246	Select fill 2.5 material	\$50,617.00	\$50,617.00			50,617.00	100%	0.00	2,530.85
247	6" subgrade labor	\$3,876.00	\$3,876.00			3,876.00	100%	0.00	193.80
248	6" subgrade material	\$9,044.00	\$9,044.00			9,044.00	100%	0.00	452.20
249	SUBTOTAL	\$128,866.00	127,966.00	0.00	0.00	127,966.00	99%	900.00	6,398.30
250	DIVISION 32 - EXTERIOR IMPROVEMENTS								
251	Remove and spread on site 8" labor	\$2,955.00	2,955.00			2,955.00	100%	0.00	147.75
252	Remove and spread on site 8" material	\$6,895.00	6,895.00			6,895.00	100%	0.00	344.75
253	6" subgrade prep w/3% lime labor	\$13,211.00	13,211.00			13,211.00	100%	0.00	660.55
254	6" subgrade prep w/3% lime material	\$30,825.00	30,825.00			30,825.00	100%	0.00	1,541.25
255	18" curb and gutter labor	\$6,065.00				0.00	0%	6,065.00	0.00
256	18" curb and gutter material	\$14,153.00				0.00	0%	14,153.00	0.00
257	36" valley gutter	\$900.00				0.00	0%	900.00	0.00
258	36" valley gutter	\$2,100.00				0.00	0%	2,100.00	0.00
259	SUBTOTAL	\$77,104.00	\$53,886.00	\$0.00	\$0.00	\$53,886.00	\$4.00	\$23,218.00	\$2,694.30
260	DIVISION 33 - UTILITIES								
261	Domestic water								
262	Mobilization	\$5,500.00	\$5,500.00			5,500.00	100%	0.00	275.00
263	8" DR PVC water pipe labor	\$8,820.00				0.00	0%	8,820.00	0.00
264	8" DR PVC water pipe material	\$20,580.00	\$20,580.00			20,580.00	100%	0.00	1,029.00
265	8" gate valve labor	\$2,100.00				0.00	0%	2,100.00	0.00
266	8" gate valve material	\$4,900.00				0.00	0%	4,900.00	0.00
267	Tapping sleeve labor	\$1,050.00				0.00	0%	1,050.00	0.00
268	Tapping sleeve material	\$2,450.00				0.00	0%	2,450.00	0.00
269	Fire hydrant assembly labor	\$2,340.00				0.00	0%	2,340.00	0.00
270	Fire hydrant assembly material	\$5,460.00				0.00	0%	5,460.00	0.00
271	2" water service labor	\$600.00				0.00	0%	600.00	0.00
272	2" water service material	\$1,400.00	\$1,400.00			1,400.00	100%	0.00	70.00
273	2" flush valve labor	\$450.00				0.00	0%	450.00	0.00
274	2" flush valve material	\$1,050.00				0.00	0%	1,050.00	0.00
275	Misc fitting labor	\$405.00				0.00	0%	405.00	0.00
276	Misc fitting materials	\$945.00				0.00	0%	945.00	0.00
277	4" casing labor	\$240.00				0.00	0%	240.00	0.00
278	4" casing materials	\$560.00				0.00	0%	560.00	0.00
279	Sanitary sewer								
280	8" sdr 26 SS line labor	\$5,872.00				0.00	0%	5,872.00	0.00
281	8" sdr 26 SS line material	\$13,702.00	\$13,702.00			13,702.00	100%	0.00	685.10

282	48" manhole labor	\$4,200.00	\$0.00			0.00	0%	4,200.00	0.00
283	48" manhole material	\$9,800.00	\$9,800.00			9,800.00	100%	0.00	490.00
284	Clean out	\$1,200.00				0.00	0%	1,200.00	0.00
285	15" pvc casing labor	\$612.00				0.00	0%	612.00	0.00
286	15" pvc casing materials	\$1,428.00				0.00	0%	1,428.00	0.00
287	Storm sewer								
288	24" RCP labor	\$8,040.00				0.00	0%	8,040.00	0.00
289	24" RCP material	\$18,840.00				0.00	0%	18,840.00	0.00
290	30" RCP labor	\$4,788.00				0.00	0%	4,788.00	0.00
291	30" RCP material	\$11,174.00				0.00	0%	11,174.00	0.00
292	36" RCP labor	\$1,740.00				0.00	0%	1,740.00	0.00
293	36" RCP material	\$4,060.00				0.00	0%	4,060.00	0.00
294	Type C inlet labor	\$8,100.00				0.00	0%	8,100.00	0.00
295	Type C inlet material	\$18,900.00				0.00	0%	18,900.00	0.00
296	Stormline tap Material	\$1,500.00				0.00	0%	1,500.00	0.00
297	Stormline tap Labor	\$3,500.00				0.00	0%	3,500.00	0.00
298	SUBTOTAL	\$176,306.00	\$50,982.00	\$0.00	\$0.00	\$50,982.00	29%	\$125,324.00	\$2,549.10
299	ALLOWANCES								
300	Landscaping allowance	\$50,000.00				\$0.00	0%	\$50,000.00	0.00
301	SUBTOTAL	\$50,000.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$50,000.00	\$0.00
302	GRAND TOTALS	\$5,948,509.00	\$902,632.32	\$801,104.35	\$0.00	\$1,703,736.67	29%	\$4,244,772.33	\$85,186.83

PAYROLL

For contractor's optional use; see instructions at dol.gov/agencies/whd/forms/wh347

Persons are not required to respond to the collection of information unless it displays a currently valid OMB control number.

NAME OF CONTRACTOR	OR SUBCONTRACTOR	ADDRESS	OMB No. 1235-0008 Expires 09/30/2026
--------------------	------------------	---------	---

PAYROLL NO.	FOR WEEK ENDING	PROJECT AND LOCATION	PROJECT OR CONTRACT NO.
-------------	-----------------	----------------------	-------------------------

(1) NAME AND INDIVIDUAL IDENTIFYING NUMBER (e.g., LAST FOUR DIGITS OF SOCIAL SECURITY NUMBER) OF WORKER	(2) NO. OF WITHHOLDING EXEMPTIONS	(3) WORK CLASSIFICATION	OT OR ST.	(4) DAY AND DATE							(5) TOTAL HOURS	(6) RATE OF PAY	(7) GROSS AMOUNT EARNED	(8) DEDUCTIONS					(9) NET WAGES PAID FOR WEEK
				HOURS WORKED EACH DAY										FICA	WITH- HOLDING TAX	OTHER	TOTAL DEDUCTIONS		
			O																
			S																
			O																
			S																
			O																
			S																
			O																
			S																
			O																
			S																
			O																
			S																

While completion of Form WH-347 is optional, it is mandatory for covered contractors and subcontractors performing work on Federally financed or assisted construction contracts to respond to the information collection contained in 29 C.F.R. §§ 3.3, 5.5(a). The Copeland Act (40 U.S.C. § 3145) contractors and subcontractors performing work on Federally financed or assisted construction contracts to "furnish weekly a statement with respect to the wages paid each employee during the preceding week." U.S. Department of Labor (DOL) regulations at 29 C.F.R. § 5.5(a)(3)(ii) require contractors to submit weekly a copy of all payrolls to the Federal agency contracting for or financing the construction project, accompanied by a signed "Statement of Compliance" indicating that the payrolls are correct and complete and that each laborer or mechanic has been paid not less than the proper Davis-Bacon prevailing wage rate for the work performed. DOL and federal contracting agencies receiving this information review the information to determine that employees have received legally required wages and fringe benefits.

Public Burden Statement

We estimate that it will take an average of 55 minutes to complete this collection, including time for reviewing instructions, searching existing data sources, gathering and maintaining the data needed, and completing and reviewing the collection of information. If you have any comments regarding these estimates or any other aspect of this collection, including suggestions for reducing this burden, send them to the Administrator, Wage and Hour Division, U.S. Department of Labor, Room S3502, 200 Constitution Avenue, N.W. Washington, D.C. 20210

PAYROLL

For contractor's optional use; see instructions at dol.gov/agencies/whd/forms/wh347

Persons are not required to respond to the collection of information unless it displays a currently valid OMB control number.

NAME OF CONTRACTOR <input type="checkbox"/> OR SUBCONTRACTOR <input checked="" type="checkbox"/>		ADDRESS		OMB No. 1235-0008 Expires 09/30/2026	
JUAN BARRERA PLUMBING, LLC		4109 NOPAL ST MCALLEN TX 78504			
PAYROLL NO. 23 (NO WORK)		FOR WEEK ENDING 05/23/2025		PROJECT AND LOCATION HIDALGO COUNTY PCT 1 WACC 1901 N BRIDGE AVE WESLACO TX 78596	
				PROJECT OR CONTRACT NO. 2143	

(1) NAME AND INDIVIDUAL IDENTIFYING NUMBER (e.g., LAST FOUR DIGITS OF SOCIAL SECURITY NUMBER) OF WORKER	(2) NO. OF WITHHOLDING EXEMPTIONS	(3) WORK CLASSIFICATION	(4) DAY AND DATE							(5) TOTAL HOURS	(6) RATE OF PAY	(7) GROSS AMOUNT EARNED	(8) DEDUCTIONS					(9) NET WAGES PAID FOR WEEK	
			OT. OR ST.	SAT	SUN	MON	TUE	WED	THU				FRI	FICA	WITH- HOLDING TAX	OTHER	TOTAL DEDUCTIONS		
				5/17	5/18	5/19	5/20	5/21	5/22				5/23						HOURS WORKED EACH DAY
			O																
			S																
			O																
			S																
			O																
			S																
			O																
			S																
			O																
			S																
			O																
			S																
			O																
			S																

While completion of Form WH-347 is optional, it is mandatory for covered contractors and subcontractors performing work on Federally financed or assisted construction contracts to respond to the information collection contained in 29 C.F.R. §§ 3.3, 5.5(a). The Copeland Act (40 U.S.C. § 3145) contractors and subcontractors performing work on Federally financed or assisted construction contracts to "furnish weekly a statement with respect to the wages paid each employee during the preceding week." U.S. Department of Labor (DOL) regulations at 29 C.F.R. § 5.5(a)(3)(ii) require contractors to submit weekly a copy of all payrolls to the Federal agency contracting for or financing the construction project, accompanied by a signed "Statement of Compliance" indicating that the payrolls are correct and complete and that each laborer or mechanic has been paid not less than the proper Davis-Bacon prevailing wage rate for the work performed. DOL and federal contracting agencies receiving this information review the information to determine that employees have received legally required wages and fringe benefits.

Public Burden Statement

We estimate that it will take an average of 55 minutes to complete this collection, including time for reviewing instructions, searching existing data sources, gathering and maintaining the data needed, and completing and reviewing the collection of information. If you have any comments regarding these estimates or any other aspect of this collection, including suggestions for reducing this burden, send them to the Administrator, Wage and Hour Division, U.S. Department of Labor, Room S3502, 200 Constitution Avenue, N.W. Washington, D.C. 20210

PAYROLL

For contractor's optional use; see instructions at dol.gov/agencies/whd/forms/wh347

Persons are not required to respond to the collection of information unless it displays a currently valid OMB control number.



WAGE AND HOUR DIVISION
Revised December 2008

NAME OF CONTRACTOR	OR SUBCONTRACTOR	ADDRESS	OMB No. 1235-0008 Expires 09/30/2026
--------------------	------------------	---------	---

PAYROLL NO.	FOR WEEK ENDING	PROJECT AND LOCATION	PROJECT OR CONTRACT NO.
-------------	-----------------	----------------------	-------------------------

(1) NAME AND INDIVIDUAL IDENTIFYING NUMBER (e.g., LAST FOUR DIGITS OF SOCIAL SECURITY NUMBER) OF WORKER	(2) NO. OF WITHHOLDING EXEMPTIONS	(3) WORK CLASSIFICATION	OT OR ST.	(4) DAY AND DATE							(5) TOTAL HOURS	(6) RATE OF PAY	(7) GROSS AMOUNT EARNED	(8) DEDUCTIONS					(9) NET WAGES PAID FOR WEEK
				HOURS WORKED EACH DAY										FICA	WITH- HOLDING TAX	OTHER	TOTAL DEDUCTIONS		
			O																
			S																
			O																
			S																
			O																
			S																
			O																
			S																
			O																
			S																
			O																
			S																

While completion of Form WH-347 is optional, it is mandatory for covered contractors and subcontractors performing work on Federally financed or assisted construction contracts to respond to the information collection contained in 29 C.F.R. §§ 3.3, 5.5(a). The Copeland Act (40 U.S.C. § 3145) contractors and subcontractors performing work on Federally financed or assisted construction contracts to "furnish weekly a statement with respect to the wages paid each employee during the preceding week." U.S. Department of Labor (DOL) regulations at 29 C.F.R. § 5.5(a)(3)(ii) require contractors to submit weekly a copy of all payrolls to the Federal agency contracting for or financing the construction project, accompanied by a signed "Statement of Compliance" indicating that the payrolls are correct and complete and that each laborer or mechanic has been paid not less than the proper Davis-Bacon prevailing wage rate for the work performed. DOL and federal contracting agencies receiving this information review the information to determine that employees have received legally required wages and fringe benefits.

Public Burden Statement

We estimate that it will take an average of 55 minutes to complete this collection, including time for reviewing instructions, searching existing data sources, gathering and maintaining the data needed, and completing and reviewing the collection of information. If you have any comments regarding these estimates or any other aspect of this collection, including suggestions for reducing this burden, send them to the Administrator, Wage and Hour Division, U.S. Department of Labor, Room S3502, 200 Constitution Avenue, N.W. Washington, D.C. 20210

PAYROLL

For contractor's optional use; see instructions at dol.gov/agencies/whd/forms/wh347

Persons are not required to respond to the collection of information unless it displays a currently valid OMB control number.



WAGE AND HOUR DIVISION
Revised December 2008

NAME OF CONTRACTOR	OR SUBCONTRACTOR	ADDRESS	OMB No. 1235-0008 Expires 09/30/2026
--------------------	------------------	---------	---

PAYROLL NO.	FOR WEEK ENDING	PROJECT AND LOCATION	PROJECT OR CONTRACT NO.
-------------	-----------------	----------------------	-------------------------

(1) NAME AND INDIVIDUAL IDENTIFYING NUMBER (e.g., LAST FOUR DIGITS OF SOCIAL SECURITY NUMBER) OF WORKER	(2) NO. OF WITHHOLDING EXEMPTIONS	(3) WORK CLASSIFICATION	OT OR ST.	(4) DAY AND DATE							(5) TOTAL HOURS	(6) RATE OF PAY	(7) GROSS AMOUNT EARNED	(8) DEDUCTIONS					(9) NET WAGES PAID FOR WEEK
				HOURS WORKED EACH DAY										FICA	WITH- HOLDING TAX	OTHER	TOTAL DEDUCTIONS		
			O																
			S																
			O																
			S																
			O																
			S																
			O																
			S																
			O																
			S																
			O																
			S																

While completion of Form WH-347 is optional, it is mandatory for covered contractors and subcontractors performing work on Federally financed or assisted construction contracts to respond to the information collection contained in 29 C.F.R. §§ 3.3, 5.5(a). The Copeland Act (40 U.S.C. § 3145) contractors and subcontractors performing work on Federally financed or assisted construction contracts to "furnish weekly a statement with respect to the wages paid each employee during the preceding week." U.S. Department of Labor (DOL) regulations at 29 C.F.R. § 5.5(a)(3)(ii) require contractors to submit weekly a copy of all payrolls to the Federal agency contracting for or financing the construction project, accompanied by a signed "Statement of Compliance" indicating that the payrolls are correct and complete and that each laborer or mechanic has been paid not less than the proper Davis-Bacon prevailing wage rate for the work performed. DOL and federal contracting agencies receiving this information review the information to determine that employees have received legally required wages and fringe benefits.

Public Burden Statement

We estimate that it will take an average of 55 minutes to complete this collection, including time for reviewing instructions, searching existing data sources, gathering and maintaining the data needed, and completing and reviewing the collection of information. If you have any comments regarding these estimates or any other aspect of this collection, including suggestions for reducing this burden, send them to the Administrator, Wage and Hour Division, U.S. Department of Labor, Room S3502, 200 Constitution Avenue, N.W. Washington, D.C. 20210

PAYROLL

For contractor's optional use; see instructions at dol.gov/agencies/whd/forms/wh347

Persons are not required to respond to the collection of information unless it displays a currently valid OMB control number.

NAME OF CONTRACTOR	OR SUBCONTRACTOR	ADDRESS	OMB No. 1235-0008 Expires 09/30/2026
--------------------	------------------	---------	---

PAYROLL NO.	FOR WEEK ENDING	PROJECT AND LOCATION	PROJECT OR CONTRACT NO.
-------------	-----------------	----------------------	-------------------------

(1) NAME AND INDIVIDUAL IDENTIFYING NUMBER (e.g., LAST FOUR DIGITS OF SOCIAL SECURITY NUMBER) OF WORKER	(2) NO. OF WITHHOLDING EXEMPTIONS	(3) WORK CLASSIFICATION	OT OR ST	(4) DAY AND DATE							(5) TOTAL HOURS	(6) RATE OF PAY	(7) GROSS AMOUNT EARNED	(8) DEDUCTIONS					(9) NET WAGES PAID FOR WEEK
				HOURS WORKED EACH DAY										FICA	WITH- HOLDING TAX	OTHER	TOTAL DEDUCTIONS		
			O																
			S																
			O																
			S																
			O																
			S																
			O																
			S																
			O																
			S																
			O																
			S																

While completion of Form WH-347 is optional, it is mandatory for covered contractors and subcontractors performing work on Federally financed or assisted construction contracts to respond to the information collection contained in 29 C.F.R. §§ 3.3, 5.5(a). The Copeland Act (40 U.S.C. § 3145) contractors and subcontractors performing work on Federally financed or assisted construction contracts to "furnish weekly a statement with respect to the wages paid each employee during the preceding week." U.S. Department of Labor (DOL) regulations at 29 C.F.R. § 5.5(a)(3)(ii) require contractors to submit weekly a copy of all payrolls to the Federal agency contracting for or financing the construction project, accompanied by a signed "Statement of Compliance" indicating that the payrolls are correct and complete and that each laborer or mechanic has been paid not less than the proper Davis-Bacon prevailing wage rate for the work performed. DOL and federal contracting agencies receiving this information review the information to determine that employees have received legally required wages and fringe benefits.

Public Burden Statement

We estimate that it will take an average of 55 minutes to complete this collection, including time for reviewing instructions, searching existing data sources, gathering and maintaining the data needed, and completing and reviewing the collection of information. If you have any comments regarding these estimates or any other aspect of this collection, including suggestions for reducing this burden, send them to the Administrator, Wage and Hour Division, U.S. Department of Labor, Room S3502, 200 Constitution Avenue, N.W. Washington, D.C. 20210

PAYROLL

For contractor's optional use; see instructions at dol.gov/agencies/whd/forms/wh347

Persons are not required to respond to the collection of information unless it displays a currently valid OMB control number.



WAGE AND HOUR DIVISION
Revised December 2008

NAME OF CONTRACTOR	OR SUBCONTRACTOR	ADDRESS	OMB No. 1235-0008 Expires 09/30/2026
--------------------	------------------	---------	---

PAYROLL NO.	FOR WEEK ENDING	PROJECT AND LOCATION	PROJECT OR CONTRACT NO.
-------------	-----------------	----------------------	-------------------------

(1) NAME AND INDIVIDUAL IDENTIFYING NUMBER (e.g., LAST FOUR DIGITS OF SOCIAL SECURITY NUMBER) OF WORKER	(2) NO. OF WITHHOLDING EXEMPTIONS	(3) WORK CLASSIFICATION	OT OR ST.	(4) DAY AND DATE							(5) TOTAL HOURS	(6) RATE OF PAY	(7) GROSS AMOUNT EARNED	(8) DEDUCTIONS					(9) NET WAGES PAID FOR WEEK
				HOURS WORKED EACH DAY										FICA	WITH- HOLDING TAX	OTHER	TOTAL DEDUCTIONS		
			O																
			S																
			O																
			S																
			O																
			S																
			O																
			S																
			O																
			S																
			O																
			S																

While completion of Form WH-347 is optional, it is mandatory for covered contractors and subcontractors performing work on Federally financed or assisted construction contracts to respond to the information collection contained in 29 C.F.R. §§ 3.3, 5.5(a). The Copeland Act (40 U.S.C. § 3145) contractors and subcontractors performing work on Federally financed or assisted construction contracts to "furnish weekly a statement with respect to the wages paid each employee during the preceding week." U.S. Department of Labor (DOL) regulations at 29 C.F.R. § 5.5(a)(3)(ii) require contractors to submit weekly a copy of all payrolls to the Federal agency contracting for or financing the construction project, accompanied by a signed "Statement of Compliance" indicating that the payrolls are correct and complete and that each laborer or mechanic has been paid not less than the proper Davis-Bacon prevailing wage rate for the work performed. DOL and federal contracting agencies receiving this information review the information to determine that employees have received legally required wages and fringe benefits.

Public Burden Statement

We estimate that it will take an average of 55 minutes to complete this collection, including time for reviewing instructions, searching existing data sources, gathering and maintaining the data needed, and completing and reviewing the collection of information. If you have any comments regarding these estimates or any other aspect of this collection, including suggestions for reducing this burden, send them to the Administrator, Wage and Hour Division, U.S. Department of Labor, Room S3502, 200 Constitution Avenue, N.W. Washington, D.C. 20210




May-25

Monthly Rain Day Log

Month	Day	Max	Min	Notes
May	4th			Rain
May	5th			Rain & Mud
May	8th			Rain & Hail
May	9th			Mud
May	21st			Rain
May	27th			Rain
May	28th			Heavy Rain
May	29th			Mud

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	% Complet
1		WAC Pct 1 Schedule 5/30/2025					0%
2		Notice to Proceed	1 day	Tue 11/5/24	Tue 11/5/24		100%
3		Mobilize	10 days	Wed 11/6/24	Tue 11/19/24	2	100%
4		Building Permit	5 days	Wed 11/20/24	Tue 11/26/24	3	0%
5		Permit delays	120 days	Wed 11/27/24	Tue 5/13/25	4	0%
6		Sitework					0%
7		Site clearing/Grading	22 days	Wed 5/14/25	Mon 8/11/25	5	100%
8		Building Pad	20 days	Tue 8/12/25	Mon 9/29/25	7	95%
9		Rough In UG Utilities	20 days	Mon 9/22/25	Fri 10/17/25	8FS-6 days	95%
10		UG Pipe	10 days	Mon 9/22/25	Fri 10/3/25	9SS	100%
11		Cut Parking Lots & Ponds	20 days	Mon 10/6/25	Fri 10/31/25	10	0%
12		Compact SG Place Base	10 days	Mon 11/3/25	Fri 11/14/25	11	0%
13		Concrete Curbs	20 days	Mon 11/17/25	Fri 12/12/25	12	0%
14		Sidewalks & HC Signs	10 days	Mon 12/15/25	Fri 12/26/25	13	0%
15		Paving	10 days	Mon 12/29/25	Fri 1/9/26	14	0%
16		Stripe Parking Lots	2 days	Mon 1/12/26	Tue 1/13/26	15	0%
17		Wheel Stops	3 days	Wed 1/14/26	Fri 1/16/26	16	0%
18		Gym					0%
19		Set Batter Boards	5 days	Wed 5/14/25	Tue 5/20/25	5	100%
20		Trench Grade Beams	3 days	Wed 5/21/25	Fri 5/23/25	19	95%
21		Termite Treat & Poly	1 day	Mon 5/26/25	Mon 5/26/25	20	95%
22		Pour SOG	1 day	Tue 5/27/25	Tue 5/27/25	21	95%
23		Gym					0%
24		Deliver Steel	1 day	Wed 5/28/25	Wed 5/28/25	22	0%
25		Erect Metal Building	30 days	Thu 5/29/25	Wed 7/9/25	24	0%
26		Install Wall Panels & SSR	30 days	Thu 7/10/25	Wed 8/20/25	25	0%
27		Lobby Structural Steel					0%
28		Deliver Steel	1 day	Thu 5/29/25	Thu 5/29/25	24	0%
29		Erect Cols & BJ	20 days	Fri 5/30/25	Thu 6/26/25	28	0%
30		Basket Ball Court 1					0%
31		Install SSR	20 days	Fri 6/27/25	Thu 7/24/25	29	0%
32		Install Exterior Wall Panels	20 days	Fri 7/25/25	Thu 8/21/25	31	0%
33		Install CMU Walls	20 days	Fri 7/25/25	Thu 8/21/25	31	0%
34		Set HM Frames @ Gym	5 days	Fri 8/22/25	Thu 8/28/25	33	0%
35		Lobby					0%
36		Set HM Frames @ Lobby	5 days	Fri 8/29/25	Thu 9/4/25	34	0%
37		Install CMU Walls	20 days	Fri 8/22/25	Thu 9/18/25	33	0%
38		Install Storefront	14 days	Fri 9/19/25	Wed 10/8/25	37	0%
39		Install Roofing system	14 days	Thu 10/9/25	Tue 10/28/25	38	0%
40		Basket ball Court 2					0%

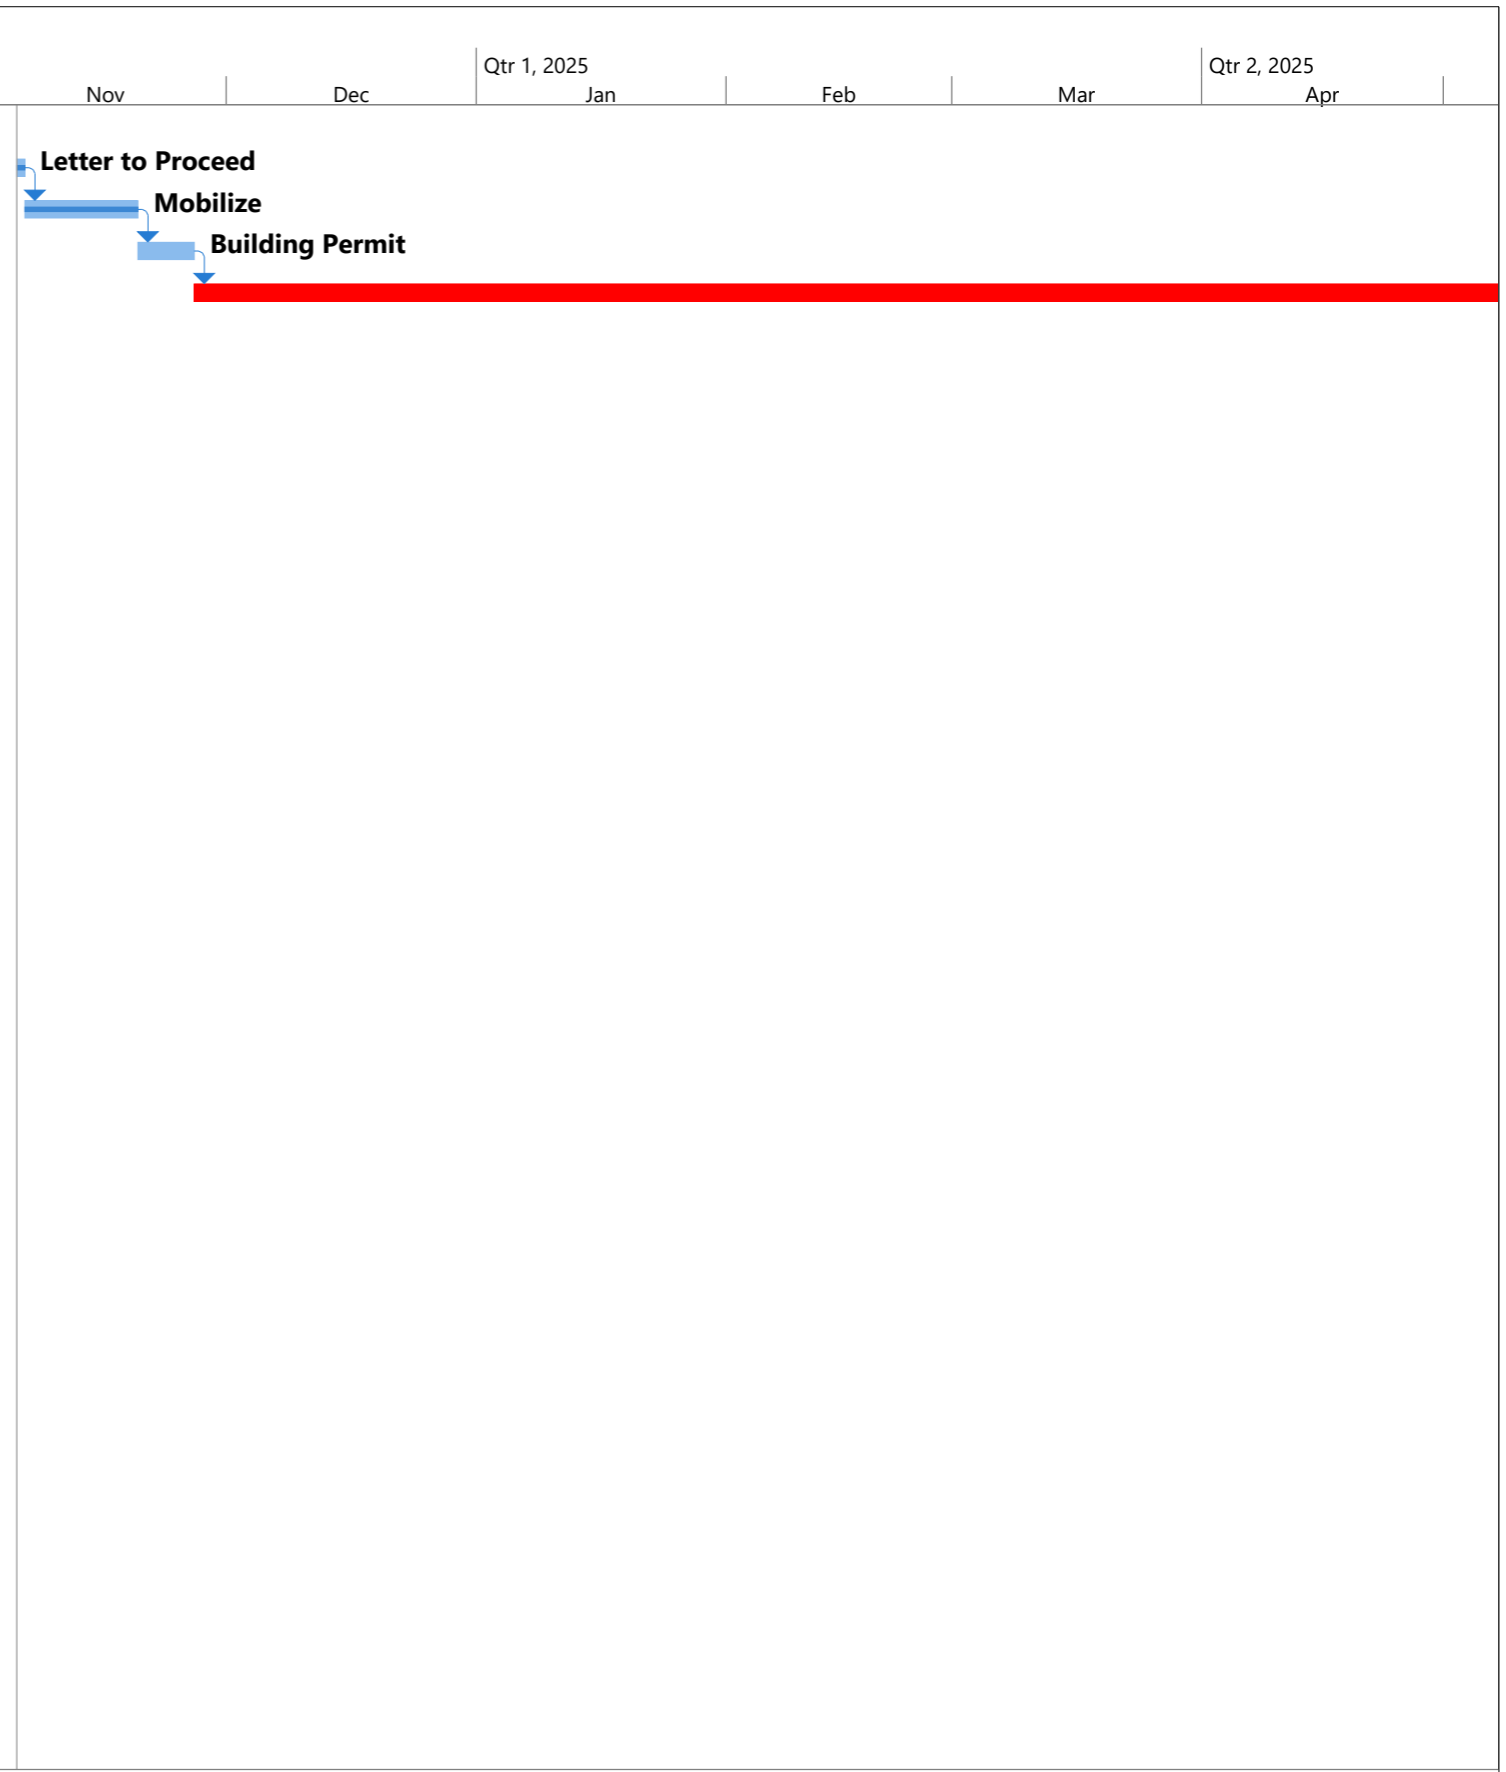

Project: WAC 1
Date: Thu 5/29/25

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	% Complet	Qtr 1, 2025					Qtr 2, 2025		
								Nov	Dec	Jan	Feb	Mar	Apr		
41		Ductwork	20 days	Wed 10/29/25	Tue 11/25/25	39	0%								
42		Meta stud framing	30 days	Fri 9/19/25	Thu 10/30/25	37	0%								
43		RI OH MEP	20 days	Tue 10/28/25	Mon 11/24/25	42FS-3 days	0%								
44		RI MEP in Walls	15 days	Tue 11/25/25	Mon 12/15/25	43	0%								
45		RTU	15 days	Tue 12/16/25	Mon 1/5/26	44	0%								
46		Grilles & Diffusers	15 days	Tue 1/6/26	Mon 1/26/26	45	0%								
47		Connect permanent Power	2 days	Tue 1/6/26	Wed 1/7/26	45	0%								
48		Climatze building	5 days	Thu 1/8/26	Wed 1/14/26	47	0%								
49		In Wall Inspection	1 day	Tue 12/16/25	Tue 12/16/25	44	0%								
50		Install Sheetrock	14 days	Wed 12/17/25	Mon 1/5/26	49	0%								
51		Tape Float Tecture and Paint	10 days	Thu 1/1/26	Wed 1/14/26	50FS-3 days	0%								
52		Install Doors Ext Secure Bldg	3 days	Thu 1/15/26	Mon 1/19/26	51	0%								
53		Install Interior Doors	10 days	Tue 1/20/26	Mon 2/2/26	52	0%								
54		Install Folding Partitions	10 days	Tue 2/3/26	Mon 2/16/26	53	0%								
55		Install Back Stop Supports	5 days	Tue 2/17/26	Mon 2/23/26	54	0%								
56		Deliver Back Stops	1 day	Thu 1/8/26	Thu 1/8/26	47	0%								
57		Install Back Stops	5 days	Fri 1/9/26	Thu 1/15/26	56	0%								
58		Install Scoreboards	10 days	Fri 1/16/26	Thu 1/29/26	57	0%								
59		Install Wall Pads	10 days	Fri 1/30/26	Thu 2/12/26	58	0%								
60		Install Bleachers	5 days	Fri 2/13/26	Thu 2/19/26	59	0%								
61		Weight room					0%								
62		Install Metal Studs & Furr Dwns	20 days	Fri 10/31/25	Thu 11/27/25	42	0%								
63		RI OH MEP	14 days	Fri 11/28/25	Wed 12/17/25	62	0%								
64		RI MEP in Walls	14 days	Thu 12/18/25	Tue 1/6/26	63	0%								
65		In Wall Inspection	5 days	Wed 1/7/26	Tue 1/13/26	64	0%								
66		Install Sheetrock	14 days	Wed 1/14/26	Mon 2/2/26	65	0%								
67		Tape Float Tecture and Paint	10 days	Thu 1/15/26	Wed 1/28/26	51	0%								
68		Install SAC Grid Syst	10 days	Thu 1/29/26	Wed 2/11/26	67	0%								
69		Install Cabinets & Tops	10 days	Thu 1/29/26	Wed 2/11/26	67	0%								
70		Fire Sprinkler System					0%								
71		RI OH	10 days	Tue 11/25/25	Mon 12/8/25	43	0%								
72		RI In Wall Plumbing	10 days	Tue 12/16/25	Mon 12/29/25	44	0%								
73		UG Line 5' to inside	5 days	Wed 1/7/26	Tue 1/13/26	64	0%								
74		Set Fixtures	10 days	Tue 12/30/25	Mon 1/12/26	72,71	0%								
75		FDC Fire Line	5 days	Wed 1/14/26	Tue 1/20/26	73	0%								
76		Install VCT & Base	10 days	Thu 1/15/26	Wed 1/28/26	48	0%								
77		Wood Floor delivery to Climatize	5 days	Thu 1/15/26	Wed 1/21/26	48	0%								
78		Fire Riser	5 days	Wed 1/21/26	Tue 1/27/26	75	0%								
79		Trim Out Plumbing	10 days	Tue 1/13/26	Mon 1/26/26	74	0%								
80		Install Wood Floors	10 days	Thu 1/22/26	Wed 2/4/26	77	0%								


Project: WAC 1
Date: Thu 5/29/25

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	% Complet	Qtr 1, 2025					Qtr 2, 2025		
								Nov	Dec	Jan	Feb	Mar	Apr		
81		RI OH Conduit, Boxes, Fittings	5 days	Thu 1/29/26	Wed 2/4/26	77,76	0%								
82		Run OH Lines Interior	5 days	Thu 2/5/26	Wed 2/11/26	78,80	0%								
83		RI In Wall Conduit and Boxes	5 days	Thu 2/5/26	Wed 2/11/26	81	0%								
84		Make Drops and Install Heads at Gy	5 days	Thu 2/12/26	Wed 2/18/26	82	0%								
85		Panels & Service	5 days	Tue 2/10/26	Mon 2/16/26	83FS-2 days	0%								
86		Make Drops and Install Heads at Lobby	5 days	Thu 2/19/26	Wed 2/25/26	84,85FS-2 days	0%								
87		Set Light Fixtures	5 days	Mon 2/23/26	Fri 2/27/26	85,86FS-3 days	0%								
88		Trim Out Electrical	5 days	Wed 2/25/26	Tue 3/3/26	87FS-3 days	0%								
89		GC Punch List	7 days	Thu 2/26/26	Fri 3/6/26	88FS-4 days	0%								
90		Final & Close Out Project					0%								
91		A & E Punch List	5 days	Mon 3/2/26	Fri 3/6/26	89FS-5 days	0%								
92		Final Clean	3 days	Mon 3/9/26	Wed 3/11/26	89	0%								
93		Final Punchlist	10 days	Thu 3/12/26	Wed 3/25/26	91,92	0%								
94		Substantial completion	1 day	Thu 3/26/26	Thu 3/26/26	93	0%								


Project: WAC 1
Date: Thu 5/29/25

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

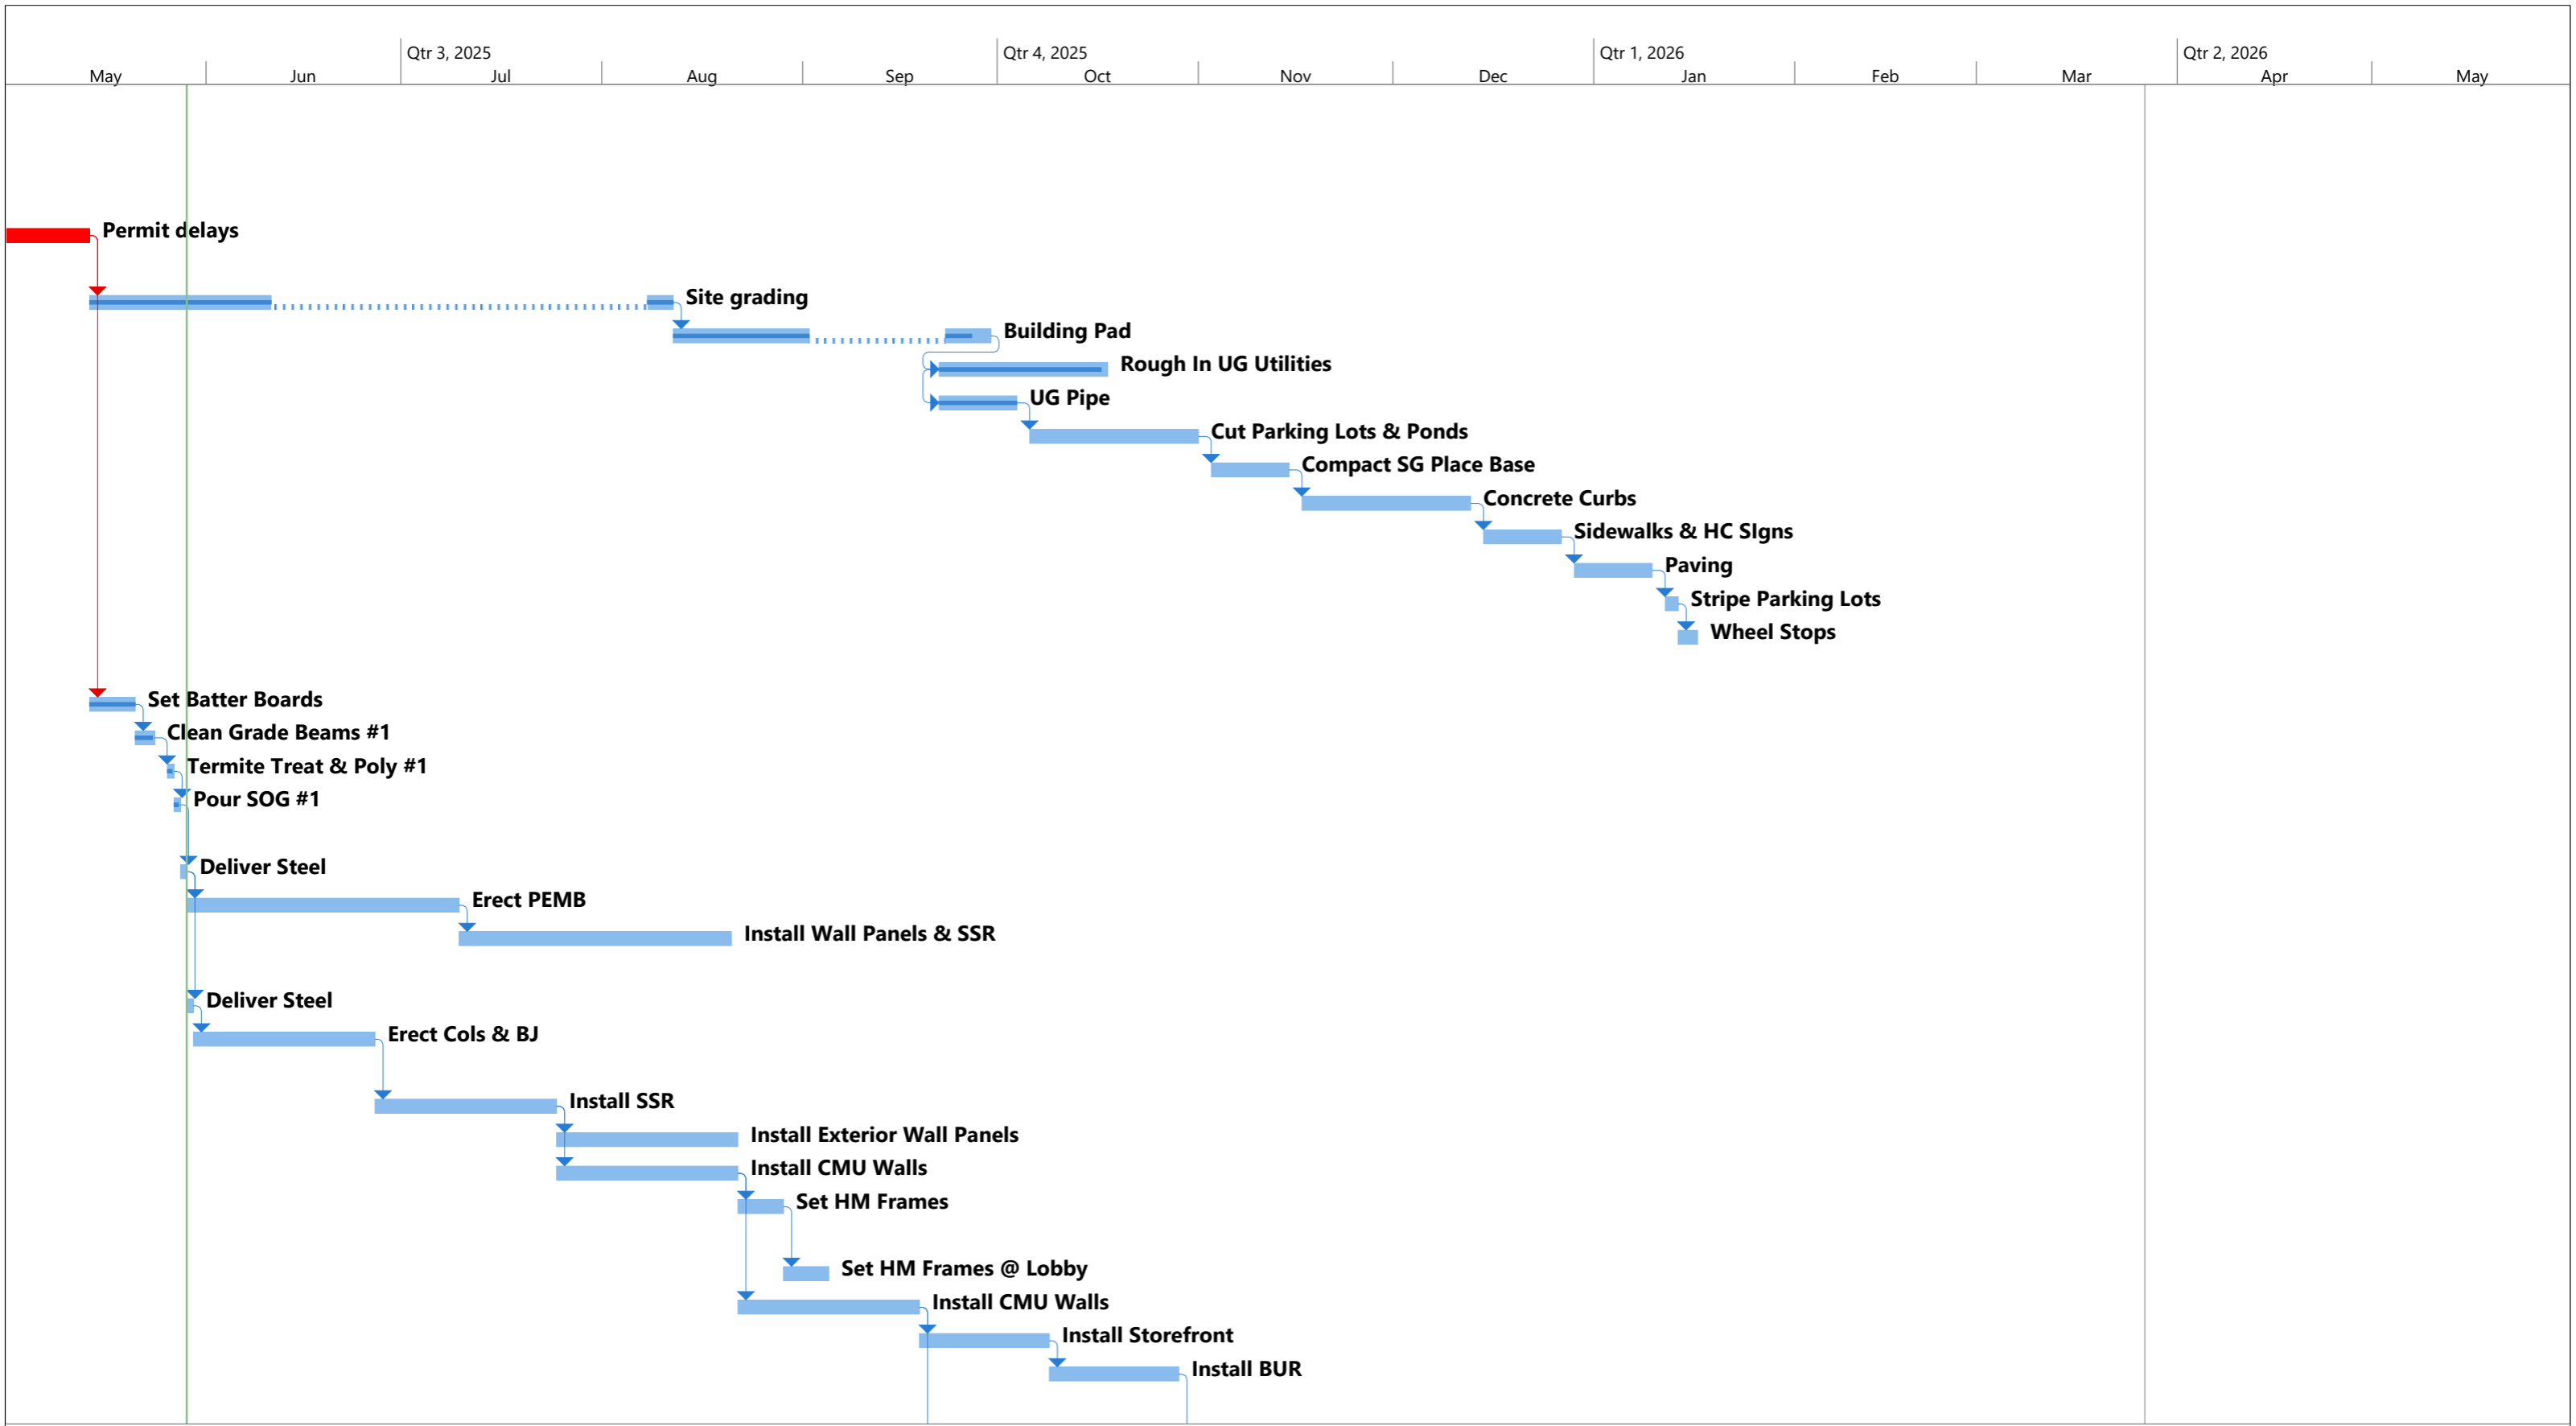


Project: WAC 1
Date: Thu 5/29/25

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

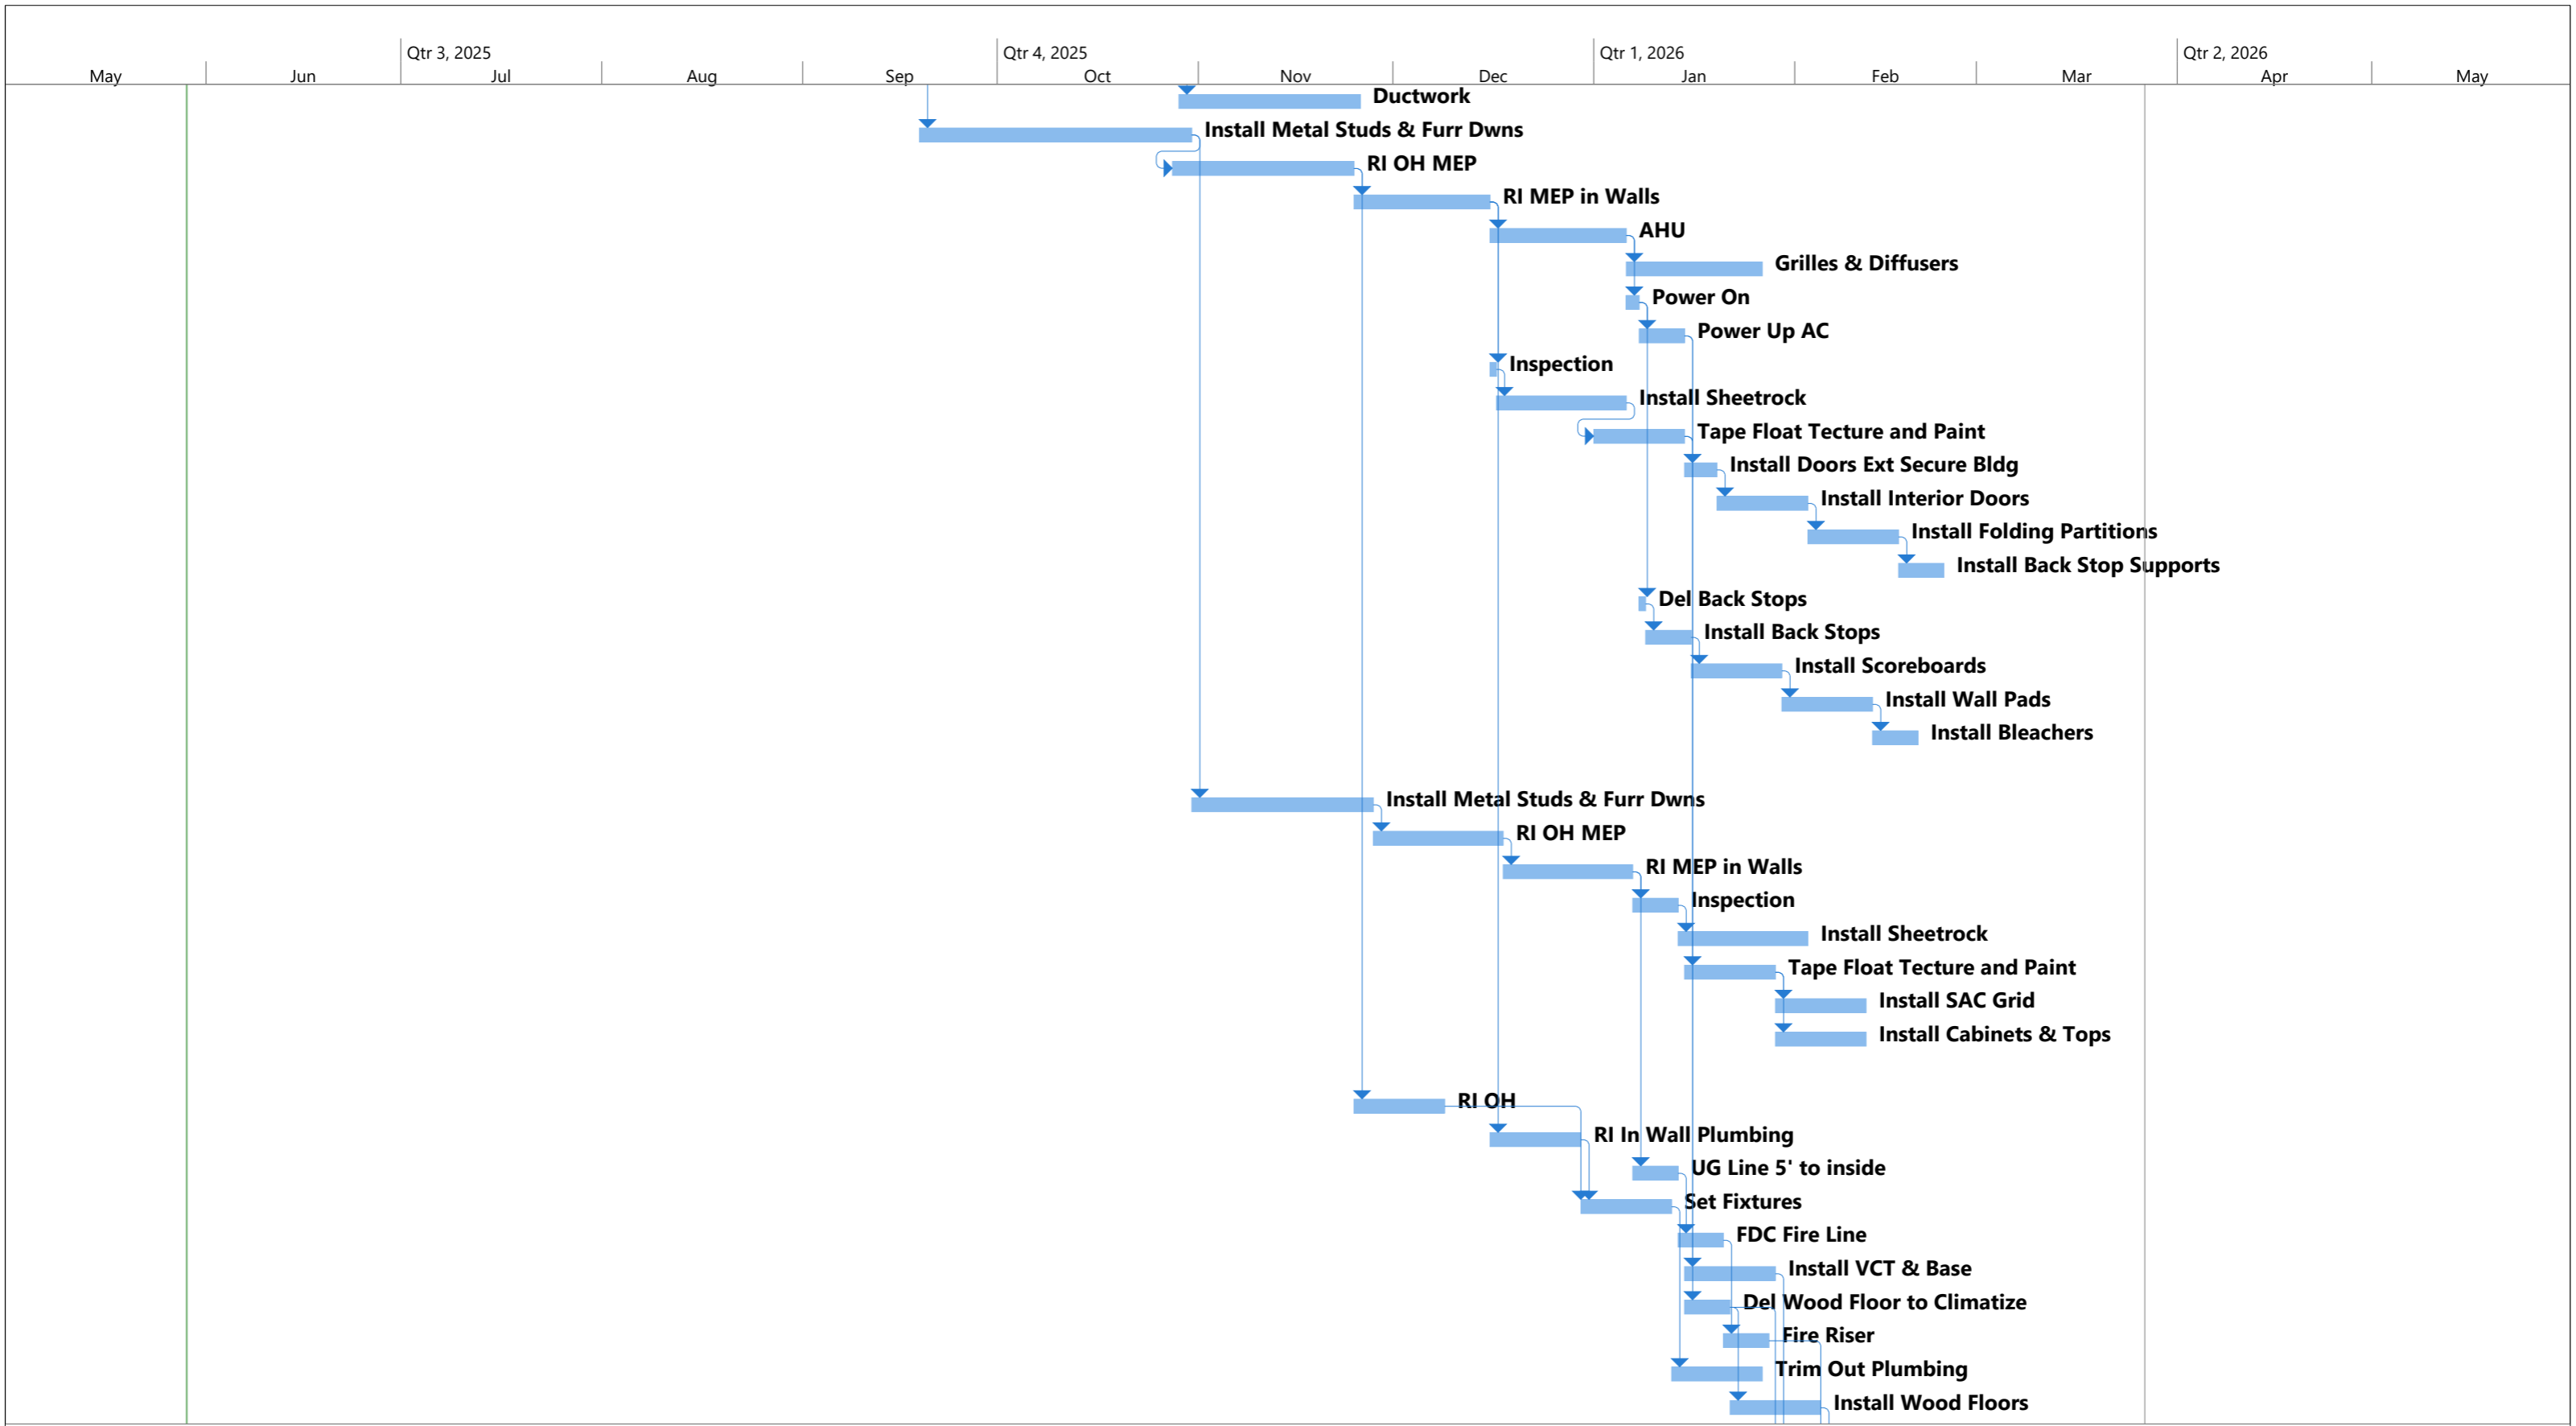

Project: WAC 1
Date: Thu 5/29/25

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

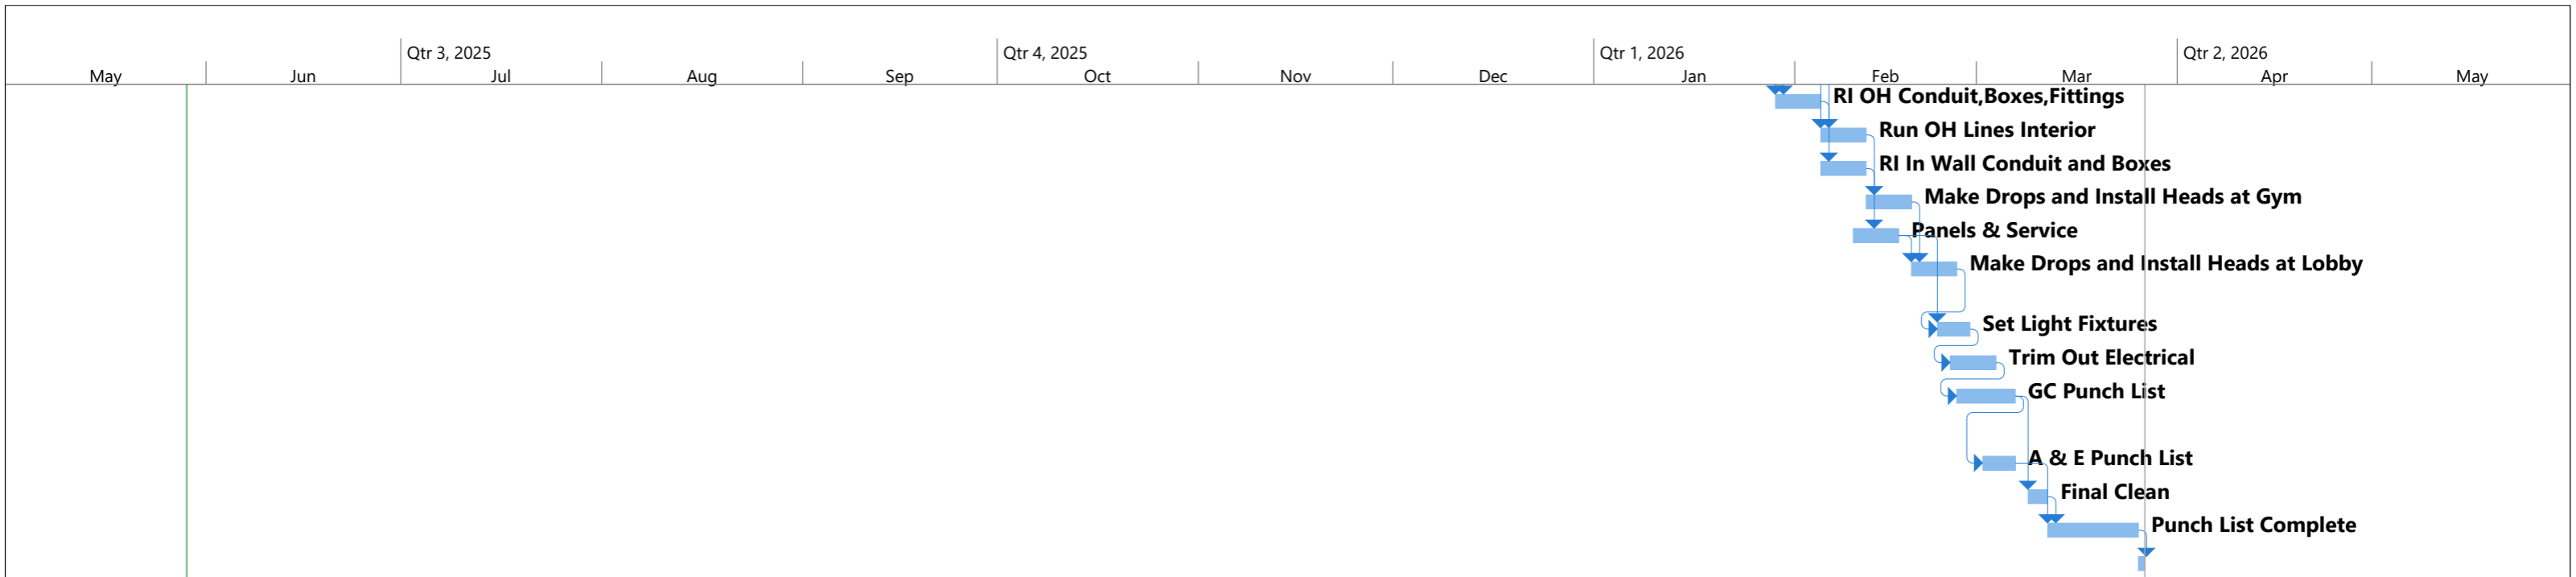

Project: WAC 1
Date: Thu 5/29/25

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
