



ROAD BOND & PASS THROUGH FINANCING

Construction Summary Report


County Judge
Dan Gattis

Commissioners
Lisa Birkman
Cynthia Long
Valerie Covey
Ron Morrison

November 2008

WWW.WILCOGOV.ORG/BONDS/ROAD/

Volume VII - Issue No. 11

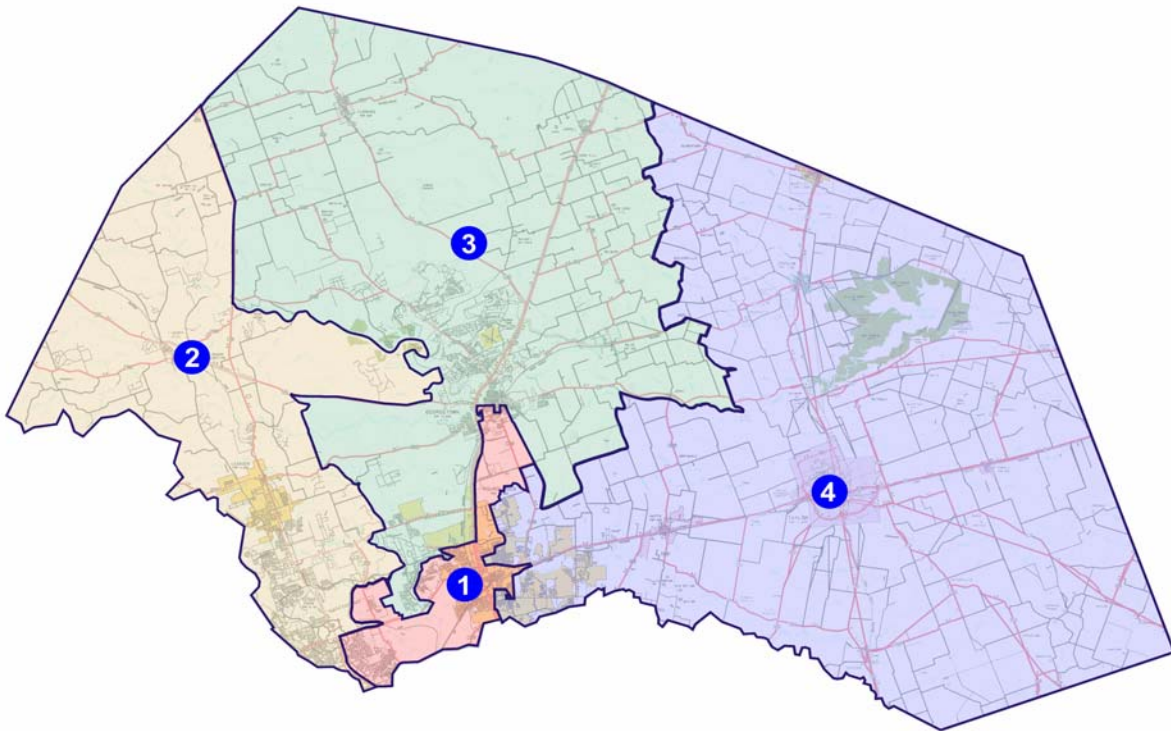

Presented By:



PRIME
STRATEGIES,
INC.

HNTB

Table of Contents



Completed Projects.....	1
PRECINCT No. 1 – Commissioner Lisa Birkman.....	2
RM 620, Ph. 1 Intersections (Wyoming Springs, Oaklands and Deepwood)	3
CR 111 – Westinghouse Rd (Hewlett Loop to FM 1460)	4
PRECINCT No. 2 – Commissioner Cynthia Long	6
San Gabriel Pkwy, Phase 1 (Halsey Drive to CR 273 Extension)	7
Ronald W. Reagan Blvd. South, Ph. 2 (FM 2243 to SH 29)	8
PRECINCT No. 3 – Commissioner Valerie Covey	11
Ronald W. Reagan Blvd North, Ph. 2 (FM 3405 to RM 2338)	12
Pass Through: IH-35 at SH 29 Turnaround Structures	14
SH 29 @ CR 104, Ph. 1 Improvements	16
PRECINCT No. 4 – Commissioner Ron Morrison	17
Limmer Loop, Ph. 1B (Haybarn Ln. to CR 119).....	18
Limmer Loop, Ph. 1C (CR 110 to SH 130)	19
Pass Through: US 79, Section 5B (FM 1063 to Milam County Line).....	21

WILLIAMSON COUNTY

ROAD BOND PROGRAM

COMPLETED PROJECTS

SUBSTANTIAL CONSTRUCTION COMPLETE/OPEN TO TRAFFIC - AS OF OCTOBER 2008

Precinct 1

- Pond Springs Road (signal) – July 2002
- McNeil Road, Phase 1 – Jan 2005
- McNeil Road, Phase 2 – Feb 2007
- Lakeline Blvd – July 2007
- RM 620, Phase 1 – September 2008

Precinct 2

- Cedar Hollow at SH 29 (signal) – Aug 2002
- FM 1869 at SH 29 (signal) – Aug 2002
- County Road 175 – June 2003
- River Bend Oaks – Aug 2003
- County Road 200 – Sept 2003
- Ronald Reagan Blvd, South Ph. 1 – Dec 2004
- County Road 214 – Feb 2005
- County Road 258 – Sept 2006
- San Gabriel Pkwy, Ph. 1 – Feb 2007
- Ronald Reagan Blvd North Ph. 1 – Sept 2007
- Ronald Reagan Blvd South, Ph. 2 – Feb 2008
- US 183 @ San Gabriel Pkwy – Feb 2008

Precinct 3

- DB Wood/Cedar Breaks – June 2004
- Cedar Breaks Road – June 2004
- Georgetown Inner Loop East Extension – Aug 2004
- CR 152 Bridge Replacement – Sept 2004
- Inner Loop East (CR 151 to Bus 35) – Oct 2005
- Ronald Reagan Blvd North, Ph. 2 – May 2008
- 12" Water Main Relocation for SH 29 Widening – June 2008
- SH 29 / CR 104, Ph. 1 – July 2008
- IH 35 @ SH 29 Turnarounds (Pass Through Financing) – August 2008

Precinct 4


- Wooden Bridges (CR 390, 406 & 427) – Nov 2002
- County Road 412 – Aug 2003
- CR 368 & 369 – Aug 2003
- County Road 300 – Dec 2003
- CR 424 Bridge Replacement – Jan 2004
- Chandler Rd. Extension, Ph. 1 – March 2005
- County Road 112, Ph. 1 – Aug 2005
- County Road 137 – Oct 2005
- Limmer Loop, Ph. 1A – July 2006
- Chandler Rd, Ph. 2 – Dec 2007
- Limmer Loop, Ph. 1B – March 2008
- Limmer Loop, Ph. 1C – October 2008

PRECINCT 1

COMMISSIONER BIRKMAN

Completed/Open to Traffic

- 1.01 Anderson Mill Rd.
- 1.02 Avery Ranch Blvd
- 1.03 Lake Creek Drainage – Phase 1
- 1.04 Lake Creek Drainage – Phase 2
- 1.05 Lakeline Blvd.
- 1.06 McNeil Road – Phase 1
- 1.07 McNeil Road – Phase 2
- 1.08 Pond Springs at Turtle Rock Signal
- 1.09 RM 620 Feasibility Study
- 1.10 Wyoming Springs North Study
- 1.11 RM 620 Interim Improvements – Phase 1

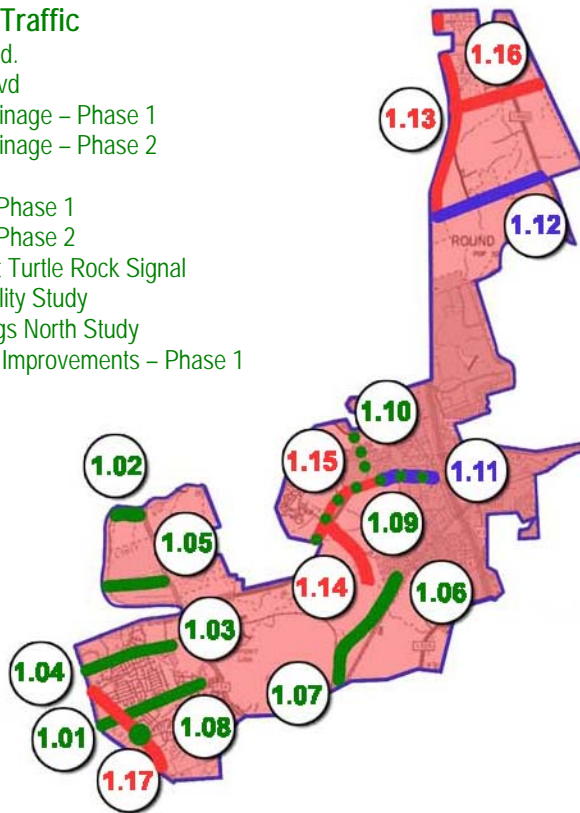

Under Construction

- 1.12 CR 111 (Westinghouse Rd)

In Design

- 1.13 IH-35 Northbound Frontage Rd and Ramps
- 1.14 O'Connor Extension
- 1.15 RM 620 Interim Improvements – Phase 2
- 1.16 Georgetown SE Inner Loop
- 1.17 Pond Springs Road

RM 620, Ph. 1 (Intersections of Wyoming Springs, Oaklands and Deepwood)
Project No. 08WC605

Original Contract Price = \$780,644.01

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantially Complete</u>	<u>Work Accepted</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
2/13/2008	3/4/2008	5/23/2008	6/2/2008	10/24/2008		120	28	148

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoice Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time</u>	<u>Liquidated Damages</u>	<u>Total Liq Damages</u>
1	6/2/2008	8/31/2008	91	\$456,146.87	\$456,146.87	\$24,007.73	\$24,007.73	61	61	\$0.00	\$0.00

5/26/2008 Comments - The NTP was issued on Friday, 5/23/08. Aaron is ordering materials and is scheduled to begin construction on 6/2/08.

4/28/2008 Comments - The Pre-Construction Conference was held on 4/25/08. The Contractor has requested Notice to Proceed to be issued in mid-May to allow their signal subcontractor adequate mobilization time.

4/14/2008 Comments - The executed contract documents were received from the Contractor on 4/14/08. The Pre-Construction Conference has been scheduled for Friday, 4/25/08.

3/24/2008 Comments - The construction contract was awarded to the low bidder Aaron Concrete Contractors at the 3/4/08 Commissioners Court meeting. Contract documents are being prepared by the Engineer. TxDOT concurrence on the bid award was received on 3/26/08.


<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
01	10/30/2008	11,869.20	11,869.20

2I: Differing Site Conditions. Additional safety needs (unforeseeable). Commissioner Birkman requested additional safety measures at the western HEB entrance to reduce the risk of accidents. Flexible Delineator Posts were therefore added to address the safety concerns. Twenty-eight (28) days were added to the Contract schedule.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
02	10/30/2008	-19,537.50	-7,668.30

1A: Design Error or Omission. Other. The proposed 18" RCP was changed to 24" RCP to match field conditions for the pipe extensions at Deep Wood Dr. 3: County Convenience. 3M: Other. Removes additional items that went with the In Pavement Lighting, which was removed from the Contract prior to Execution of the Contract Documents. 3L: Revising safety work/measures desired by the County. Upgrades the existing flashing beacon at the hike & bike trail crossing.

Adjusted Price = \$772,975.71

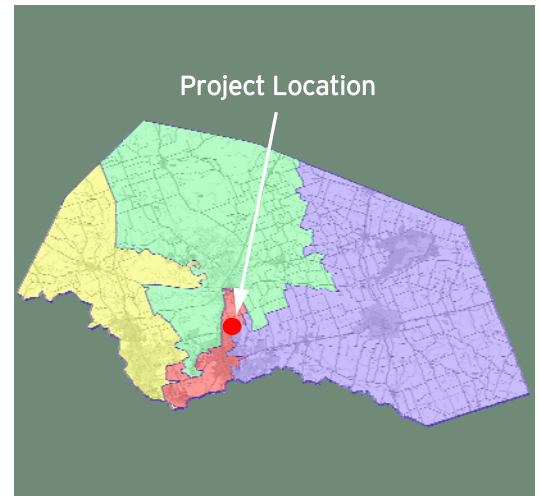

CR 111 (WESTINGHOUSE ROAD) (Hewlett Loop to FM 1460)

Project Length: 1.99 Miles
Roadway Classification: Minor Arterial
Roadway Section: Transitions from four-lane w/ center two-way turn lane on the west end to four-lane divided on the east end

Project Schedule: June 2008 - June 2010
Estimated Construction Cost: \$5.9 Million



OCTOBER 2008 IN REVIEW

10/6/2008 - JC Evans began formwork on the wingwalls for culvert structures located on the west end of project.

10/13/2008 - JC Evans continues the formwork on the wingwalls for culvert structures located on the west end of project. They are also currently working on subgrade just east of Park Central to just west of FM 1460 on the proposed eastbound lanes.

10/20/2008 - JC Evans is continuing to work on subgrade just west of Park Central to just west of FM 1460.

10/27/2008 - JC Evans poured the wingwalls for the culvert structures located on the west end of project near Park Central last week and is working on the surface finish on the wingwalls and headwalls. JC Evans continues to work on subgrade from just west of Park Central to just west of FM 1460.



Design Engineer: Huggins/Seiler & Associates
Contractor: J.C. Evans Construction
Construction Observation:
Benny Cloud, Williamson County

Williamson County
Road Bond Program

CR 111 - Westinghouse Rd. (Hewlett Loop to FM 1460)
Project No. 08WC608

Original Contract Price = \$5,864,053.94

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Anticipated Work Complete</u>	<u>Work Accepted</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
4/2/2008	4/15/2008	6/6/2008	6/16/2008	6/15/2010		730	0	730

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoice Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time Used</u>	<u>Liquidated Damages</u>	<u>Total Liq Damages</u>
1	6/16/2008	6/30/2008	15	\$273,125.71	\$273,125.71	\$14,375.04	\$14,375.04	5	2	\$0.00	\$0.00
2	7/1/2008	7/31/2008	31	\$690,458.44	\$963,584.15	\$36,339.92	\$50,714.96	17	6	\$0.00	\$0.00
3	8/1/2008	8/31/2008	31	\$405,777.61	\$1,369,361.76	\$21,356.71	\$72,071.67	25	11	\$0.00	\$0.00
4	9/1/2008	9/30/2008	30	\$410,275.17	\$1,779,636.93	\$21,593.43	\$93,665.10	31	15	\$0.00	\$0.00

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
01	09/23/2008	6,660.00	6,660.00

4D: Third Party Accommodation. Other. The Contractor installed permanent fencing along the ROW per an agreement made with the Property owner of Parcel 21 (NNP-Terra Vista. LP) and Williamson County prior to construction. The Contractor was also directed to install temporary fencing on Parcel 3 to keep the property owners cows off of the ROW.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
02	10/07/2008	100,144.67	106,804.67

6B: Untimely ROW/Utilities. Right-of-Way not clear (County responsibility for ROW). The property owner agreed to donate the ROW in exchange for the work associated with this Change Order: the installation of steel sleeve encasements for future utilities, the upgrade of existing driveways, and the addition of new driveways.

Adjusted Price = \$5,970,858.61

PRECINCT 2

COMMISSIONER LONG

Under Construction


2.20 Kauffman Loop

In Design

2.21 CR 175 Extension
 2.22 CR 179
 2.23 San Gabriel Parkway – Phase 2
 2.24 CR 214 – Phase 1
 2.25 CR 214 – Phase 2
 2.26 SH 29 Corridor Study
 2.27 US 183 (PTF)

Completed/Open to Traffic

2.01 Vista Ridge Blvd.
 2.02 Avery Ranch Road
 2.03 Brushy Creek Road
 2.04 Cedar Hollow at SH 29
 2.05 Cypress Creek Road
 2.06 Lakeline Blvd.
 2.07 River Bend Oaks Subdivision
 2.08 Ronald W. Reagan South – Phase 1
 2.09 Ronald W. Reagan North – Phase 1
 2.10 CR 175 (FM 1431 to Regional Park)
 2.11 CR 185
 2.12 CR 200 (CR 201 to Lackey Creek)
 2.13 CR 214 (SH 2 to Rolling Hills Dr.)
 2.14 CR 258 (US 183 to Sunset Ridge)
 2.15 SH 29 at FM 1869
 2.16 Lakeline Blvd.
 2.17 San Gabriel Parkway – Phase 1
 2.18 US 183 Widening at CR 274
 2.19 Ronald W. Reagan South – Phase 2
 2.28 CR 272
 2.29 CR 273

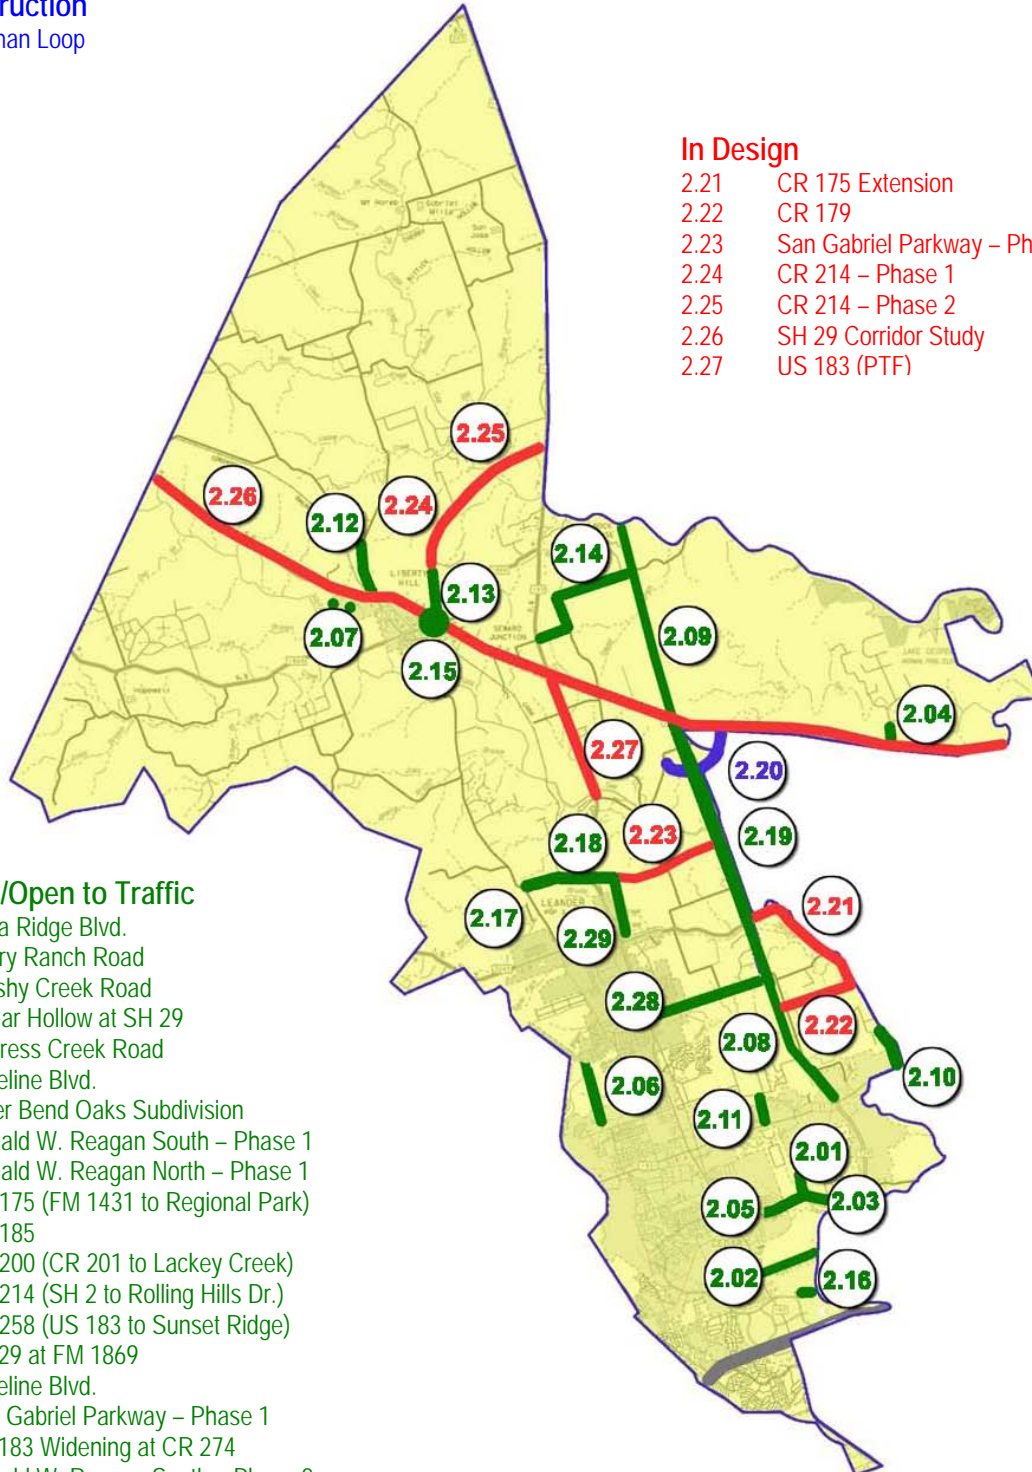

San Gabriel Pkwy, Ph. 1 (Future Halsey Dr. to Future CR 273)
Project No. 05WC321

Original Contract Price = \$2,291,679.53

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantially Complete</u>	<u>Work Accepted</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
6/22/2005	7/12/2005	5/1/2006	5/8/2006	2/15/2007		244	39	283

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoice Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time Used</u>	<u>Liquidated Damages</u>	<u>Total Liq Damages</u>
1	5/8/2006	5/31/2006	24	\$424,768.73	\$424,768.73	\$47,196.53	\$47,196.53	19	8	\$0.00	\$0.00
2	6/1/2006	6/30/2006	30	\$138,345.52	\$563,114.25	\$15,371.72	\$62,568.25	25	19	\$0.00	\$0.00
3	7/1/2006	7/31/2006	31	\$279,550.44	\$842,664.69	\$31,061.16	\$93,629.41	38	30	\$0.00	\$0.00
4	8/1/2006	8/31/2006	31	\$228,153.27	\$1,070,817.96	\$25,350.36	\$118,979.77	48	41	\$0.00	\$0.00
5	9/1/2006	9/30/2006	30	\$249,149.78	\$1,319,967.74	\$27,683.31	\$146,663.08	59	52	\$0.00	\$0.00
6	10/1/2006	10/31/06	31	\$319,298.06	\$1,639,265.80	\$35,477.56	\$182,140.64	74	63	\$0.00	\$0.00
7	11/1/2006	11/30/06	30	\$377,676.64	\$2,016,942.44	\$41,964.08	\$224,104.72	91	73	\$0.00	\$0.00
8	12/1/2006	1/31/2007	62	\$35,795.41	\$2,052,737.85	\$3,977.26	\$228,081.98	92	95	\$0.00	\$0.00
9	2/1/2007	2/28/2007	15	\$47,813.82	\$2,100,551.67	\$5,312.65	\$233,394.63	94	100	\$0.00	\$0.00
10	3/1/2007	3/31/2007	N/A	\$186,715.71	\$2,287,267.38	\$-186,715.70	\$46,678.93	94	-	\$0.00	\$0.00

- 10/27/08 Comments - HNTB has issued a letter to JC Evans with items that need to be corrected concerning the Railroad Crossing. HNTB is awaiting a schedule of work from J.C. Evans.
- 9/29/2008 Comments - GEC coordinating with CapMetro for final approval of the Railroad Crossing. HNTB has issued a letter to JC Evans with items that need to be corrected concerning the Railroad Crossing.
- 8/25/2008 Comments - HNTB continues coordinating with CapMetro for final approval of the Railroad Crossing. A meeting is being scheduled for Thursday, 8/28/08.
- 4/28/2008 Comments - HNTB is working to coordinate with Capital Metro for final approval of the Railroad Crossing. Once Capital Metro has approved the crossing, final project close-out can begin.
- 3/24/2008 Comments - PEC completed installation of power to the intersection on 1/11/08. Awaiting CMTA verification of power supply and working condition of the railroad crossing signal.
- 1/28/2008 Comments - PEC completed installation of power to the intersection on 1/11/08. The Contractor is currently in the process of requesting CMTA verification of power supply and working condition of the railroad crossing signal.
- 11/26/2007 Comments A meeting was held on 9/19/07 with PEC, TxDOT, Waterstone Development, Capital Metro and Cobb Fendley to discuss the plan for electric service to the railroad crossing. PEC will run power along the east side of the tracks from the CMTA Park & Ride facility to the railroad control house. Upon official approval from CMTA for the plan to bore under the tracks, electric service should be provided within 30 days. Currently awaiting update from CMTA regarding approval of the plan.
- 8/27/2007 Comments - PEC has developed the exhibit for their easement requirements, which has been submitted to CMTA for approval. The pole locations have been staked in the field. PEC is working with TxDOT to obtain an easement to cross US 183 with the power lines. The Contractor has completed all of the Punch List items on the project. The sub-contractor has completed the crack sealing of the asphalt and repair of the thermoplastic markings.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
01	03/21/2006	180,012.38	180,012.38

5E: Contractor Convenience. The project was let in July 2005. Due to delays with acquisition of easements for the project, construction was postponed for approximately 6 months. As a result of the extensive delays, the Contractor was unable to honor the original unit costs bid and awarded for selected contract items and requested revised contract prices for those items.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
02	09/20/2006	2,719.00	182,731.38

1B: Design Error (Other) - Item of work in plans was not identified in original bid. New item is being added (valley gutter).

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
03	02/23/2007	16,716.25	199,447.63

2E: Differing Site Conditions. Miscellaneous difference in site conditions (unforeseeable). The section of Halsey Drive included in the project was widened and striping was added to match conditions on the existing Halsey Drive. 38 days were added to the contract schedule.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
04	02/23/2007	12,377.65	211,825.28

1A: Design Error or Omission. Incorrect PS&E. The elevations at the existing railroad did not match those on the plans. Elevations were revised to meet field conditions, resulting in additional quantities. The vegetative watering quantity has been revised to meet the contract watering requirements. 3M: County Convenience. Other. County opted to revise the project limits in order to better coordinate the future work to be done at the US 183 intersection.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
5	08/16/2007	0.00	211,825.28

5E: Contractor Convenience. Other. The Owner may elect to reduce the contract retainage to 5% upon completion of 50% of the value of the work in keeping with current industry standard practice. The Owner may elect to further reduce the contract retainage to 2% upon issuance of the Certificate of Substantial Completion.

Adjusted Price = \$2,503,504.81

Ronald Reagan Blvd. South, Ph. 2 (FM 2243 to SH 29)
Project No. 05WC324

Original Contract Price = \$15,857,326.54

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantially Complete</u>	<u>Work Accepted</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
8/17/2005	9/27/2005	1/13/2006	1/23/2006	2/13/2008		540	212	752

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoice Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time Used</u>	<u>Liquidated Damages</u>	<u>Total Liq Damages</u>
1	11/1/2005	11/30/05	0	\$74,925.00	\$74,925.00	\$8,325.00	\$8,325.00	1	0	\$0.00	\$0.00
2	12/1/2005	12/31/05	0	\$103,696.20	\$178,621.20	\$11,521.80	\$19,846.80	1	0	\$0.00	\$0.00
3	1/1/2006	1/9/2006	9	\$750,735.00	\$929,356.20	\$83,415.00	\$103,261.80	7	1	\$0.00	\$0.00
4	2/1/2006	2/28/2006	28	\$444,184.20	\$1,373,540.40	\$49,353.80	\$152,615.60	11	5	\$0.00	\$0.00
5	3/1/2006	3/31/2006	31	\$291,523.10	\$1,665,063.50	\$32,391.46	\$185,007.06	13	9	\$0.00	\$0.00
6	4/1/2006	4/30/2006	30	\$399,662.07	\$2,064,725.57	\$44,406.89	\$229,413.95	17	13	\$0.00	\$0.00
7	5/1/2006	5/31/2006	31	\$655,292.34	\$2,720,017.91	\$72,810.26	\$302,224.21	22	17	\$0.00	\$0.00
8	6/1/2006	6/30/2006	30	\$455,018.26	\$3,175,036.17	\$50,557.59	\$352,781.80	25	21	\$0.00	\$0.00
9	7/1/2006	7/31/2006	31	\$40,437.00	\$3,215,473.17	\$4,493.00	\$357,274.80	26	25	\$0.00	\$0.00
10	8/1/2006	8/31/2006	31	\$285,902.35	\$3,501,375.52	\$31,766.92	\$389,041.72	27	29	\$0.00	\$0.00
11	9/1/2006	9/30/2006	30	\$528,814.84	\$4,030,190.36	\$58,757.21	\$447,798.93	32	33	\$0.00	\$0.00
12	10/1/2006	10/31/200	31	\$311,641.77	\$4,341,832.13	\$34,626.86	\$482,425.79	34	38	\$0.00	\$0.00
13	11/1/2006	11/30/200	30	\$478,315.80	\$4,820,147.93	\$53,146.20	\$535,571.99	38	41	\$0.00	\$0.00
14	12/1/2006	3/31/2007	121	\$1,317,936.47	\$6,138,084.40	\$146,437.39	\$682,009.38	48	58	\$0.00	\$0.00
15	4/1/2007	4/30/2007	30	\$447,058.65	\$6,585,143.05	\$49,673.18	\$731,682.56	51	62	\$0.00	\$0.00
16	5/1/2007	5/31/2007	31	\$250,755.70	\$6,835,898.75	\$27,861.77	\$759,544.33	53	66	\$0.00	\$0.00
17	6/1/2007	7/31/2007	61	\$892,102.41	\$7,728,001.16	\$99,122.49	\$858,666.82	60	74	\$0.00	\$0.00
18	8/1/2007	8/31/2007	31	\$625,810.47	\$8,353,811.63	\$69,534.49	\$928,201.31	65	78	\$0.00	\$0.00
19	9/1/2007	9/30/2007	30	\$804,499.07	\$9,158,310.70	\$89,388.79	\$1,017,590.10	71	82	\$0.00	\$0.00
20	10/1/2007	10/31/200	31	\$1,258,832.28	\$10,417,142.98	\$-469,076.61	\$548,513.49	77	86	\$0.00	\$0.00
21	11/1/2007	11/30/200	30	\$785,594.47	\$11,202,737.45	\$41,347.08	\$589,860.57	83	90	\$0.00	\$0.00
22	12/1/2007	12/31/200	31	\$453,813.77	\$11,656,551.22	\$23,884.94	\$613,745.51	86	94	\$0.00	\$0.00
23	1/1/2008	1/31/2008	31	\$701,577.47	\$12,358,128.69	\$36,925.13	\$650,670.64	91	98	\$0.00	\$0.00
24	2/1/2008	2/13/2008	13	\$789,217.12	\$13,147,345.81	\$-381,980.87	\$268,689.77	94	100	\$0.00	\$0.00
25	3/1/2008	3/31/2008	N/A	\$168,372.53	\$13,315,718.34	\$3,436.18	\$272,125.95	95	-	\$0.00	\$0.00
26	4/1/2008	4/30/2008	N/A	\$123,532.38	\$13,439,250.72	\$2,521.06	\$274,647.01	96	-	\$0.00	\$0.00
27	5/1/2008	5/31/2008	N/A	\$158,393.86	\$13,597,644.58	\$3,232.53	\$277,879.54	97	-	\$0.00	\$0.00

10/27/2008 Comments Ranger's sub is currently working on watering the sodded and seeded areas of the project. The GEC has received concurrence from Tesch on design of the low water crossing at the South San Gabriel River. Ranger has completed all punch list items except the low water crossing and the chip seal on the south side of the South San Gabriel River.

9/29/2008 Comments - Ranger is working to finish the punch list items. A meeting was held on 9/12/09 with the GEC, Ranger and Mr. Tesch, a property owner, to discuss his low water crossing issues.

8/25/2008 Comments - Ranger's sub has currently completed the sod installation on the project. The GEC is scheduling a meeting with Ranger this week to determine when they will have the punch list completed.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
01	02/14/2006	-2,114,062.05	-2,114,062.05

3C - County Convenience. Implementation of a Value Engineering finding. Pavement design was changed to a 2.5" TY C HMA over a 15" Flexible Base section for the main lanes. Due to change in pavement design, excavation & embankment quantities were also revised.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
02	02/14/2006	-192,122.88	-2,306,184.93

3C - County Convenience. Implementation of a Value Engineering finding. As a result of the value engineering process, unit prices for the 6x3 and 7x3 box culvert items were adjusted as mutually agreed to by Williamson County and Ranger Excavating.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
03	05/18/2006	12,444.00	-2,293,740.93

2J - Differing Site Conditions (unforeseeable) (other). A residence within the ROW that was scheduled for demolition was found to have asbestos. Extra expenses were incurred by the Contractor for asbestos removal.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
04	07/11/2006	128,440.00	-2,165,300.93

6D. Untimely ROW/Utilities. Other. Steel encasement pipe for future waterline for the City of Leander added at sta. 227+10, sta. 241+70, sta. 262+00, sta. 262+10. Utility plans were not incorporated into PS&E at the time of letting.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
05	09/05/2006	111,179.80	-2,054,121.13

1A: Design error or Omission. Incorrect PS&E. Original plans did not account for the channel crossing at the proposed driveway location. A box culvert was added for the drainage design. 15 days were added to the contract schedule.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
06	08/17/2006	8,493.37	-2,045,627.76

2C: New Development - Conditions changing after PS&E completed. 2D: Environmental Remediation. During the clearing and grubbing of ROW, two abandoned water wells and one abandoned septic tank were discovered and needed to be properly removed.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
07	08/29/2006	59,041.60	-1,986,586.16
4B: Third Party requested work. Per the terms of the real estate contract agreement, the County must provide a driveway for the landowner. 6D: Untimely ROW. The real estate contract agreement was not finalized until after the contract plans were complete and the project was let. 15 days were added to the contract schedule.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
08	09/05/2006	218,894.00	-1,767,692.16
6D: Untimely ROW/Utilities. 6D-Other. Chisholm Trail waterline relocations were not incorporated into the plans prior to contract award. 30 days were added to the contract schedule.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
09	02/07/2007	8,360.00	-1,759,332.16
4B: Third Party Accommodation - Third party requested work. The County and the property owner agreed to temporary fencing at the driveways and culvert locations to facilitate the construction of the roadway. This change order provides compensation to the property owner for installation of temporary special fencing around the easements, and its removal once the driveway and culvert construction is complete, allowing the permanent fencing to be installed.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
10	03/27/2007	205,000.00	-1,554,332.16
3M: County Convenience. Other. The one-course surface treatment will be added due to the deletion of the 4.5" of Type B asphalt requested by Williamson County as part of the pavement design section revision.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
11	03/21/2007	10,577.00	-1,543,755.16
6C: Untimely ROW/Utilities. Utilities not Clear. The location of water lines on the plans did not match actual field conditions. Additional effort was required to perform exploratory work and additional water line relocations.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
12	04/20/2007	2,530.00	-1,541,225.16
6B: Untimely ROW/Utilities. Right-of-Way not clear (County responsibility for ROW). New fencing was added for the drainage easement on the north and south sides of Hwy 29 for the stock pass extension.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
13	07/05/2007	-12,050.34	-1,553,275.50
4B: Third Party Accommodation. Third Party requested work. Realigned driveway to avoid taking out unnecessary trees on the Lamb property. 6D: Untimely ROW/Utilities. Other. Move Densford's driveway back to CL Sta. of 279+00 to avoid power pole in the proposed driveway location of Sta. 280+00.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
14	07/12/2007	81,502.00	-1,471,773.50
4B: Third Party Accommodation. Third Party requested work. Installation of steel sleeves for future utilities at property owner's request, per terms of the real estate contract agreement. Twenty-five (25) days were added to the project schedule.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
15	09/17/2007	4,010.38	-1,467,763.12
4B: Third Party Accommodation. Third party requested work. Driveways relocated and a drainage pipe added to one location. Twenty (20) days were added to the Contract schedule.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
16	08/15/2007	29,117.00	-1,438,646.12
2J: Differing Site Conditions. Other. Existing groundwater within the strata below the proposed roadway is resulting in soft subgrade conditions. A geotechnical investigation was completed to assess the problem and a rock filter system was developed to mitigate the groundwater problem. This change order provides compensation for the extra time and work associated with the revision. Ninety-three (93) days were added to the Contract schedule.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
17	10/31/2007	7,424.20	-1,431,221.92
1B: Design Error or Emission. Other. Metal Beam Guard Fence transitions were not included as a bid item even though they show to be installed on plans. This change order provides payment for the transitions. 2E: Differing Site Conditions. Miscellaneous Difference in Site Conditions. In order to construct certain driveways, a small amount of fencing was removed while various amounts of temporary and permanent fencing will need to be installed. Five (5) days were added to the Contract schedule.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
18	11/19/2007	0.00	-1,431,221.92
5E: Contractor Convenience. Other. The Owner may elect to reduce the contract retainage to 5% upon completion of 50% of the value of the work in keeping with current industry standard practice. The Owner may elect to further reduce the contract retainage to 2% upon issuance of the Certificate of Substantial Completion			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
19	01/08/2008	15,628.50	-1,415,593.42
1B: Design Error or Emission. Other. Signal layout information for FM 2243 intersection was excluded from plans. Contractor had to remove and replace existing traffic detectors and pull boxes in order to construct a portion of roadway. Two (2) days were added to the Contract schedule.			

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
20	01/30/2008	24,887.96	-1,390,705.46

2J: Differing Site Conditions. Other. This change order provides compensation for the extra time and work associated with revisions to mitigate the groundwater problem in the northbound lanes of Reagan Blvd, following the same strategy developed for the southbound lanes of Reagan Blvd under Change Order No. 16.
 4B: Third Party Accommodation. Third Party Requested Work. Provides compensation for the removal of entrance walls and capping gate columns on the Fisher property. 3F: County Convenience. Additional work required by the County. Provides compensation for removal of Parmer Ln sign at the intersection of Reagan Blvd and RM 2243. Seven (7) days were added to the Contract schedule.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
21	01/29/2008	106,465.66	-1,284,239.80

2J: Differing Site Conditions. Other. Change Order #16 (attached) added ninety-three (93) days to the Contract schedule. The change in the Contract schedule delayed the Contractor's planned paving schedule. As a result of the delay, the Contractor was unable to hold the bid prices for asphalt materials. This Change Order provides for a fair and equitable price increase for asphalt material items.


<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
22	07/08/2008	8,930.00	-1,275,309.80

3M: County Convenience. Other. Property owner's fence was located in the middle of the new ditch line. To prevent future damage to the fence, it was moved into the County's ROW and a water gap was installed. 2E: Differing Site Conditions (unforeseeable). Miscellaneous difference in site conditions. In order to maintain the proper slope at certain driveways, the Contractor demoed SET's and extended driveway pipes to accommodate wider driveways.

Adjusted Price = \$14,582,016.74

PRECINCT 3

COMMISSIONER COVEY

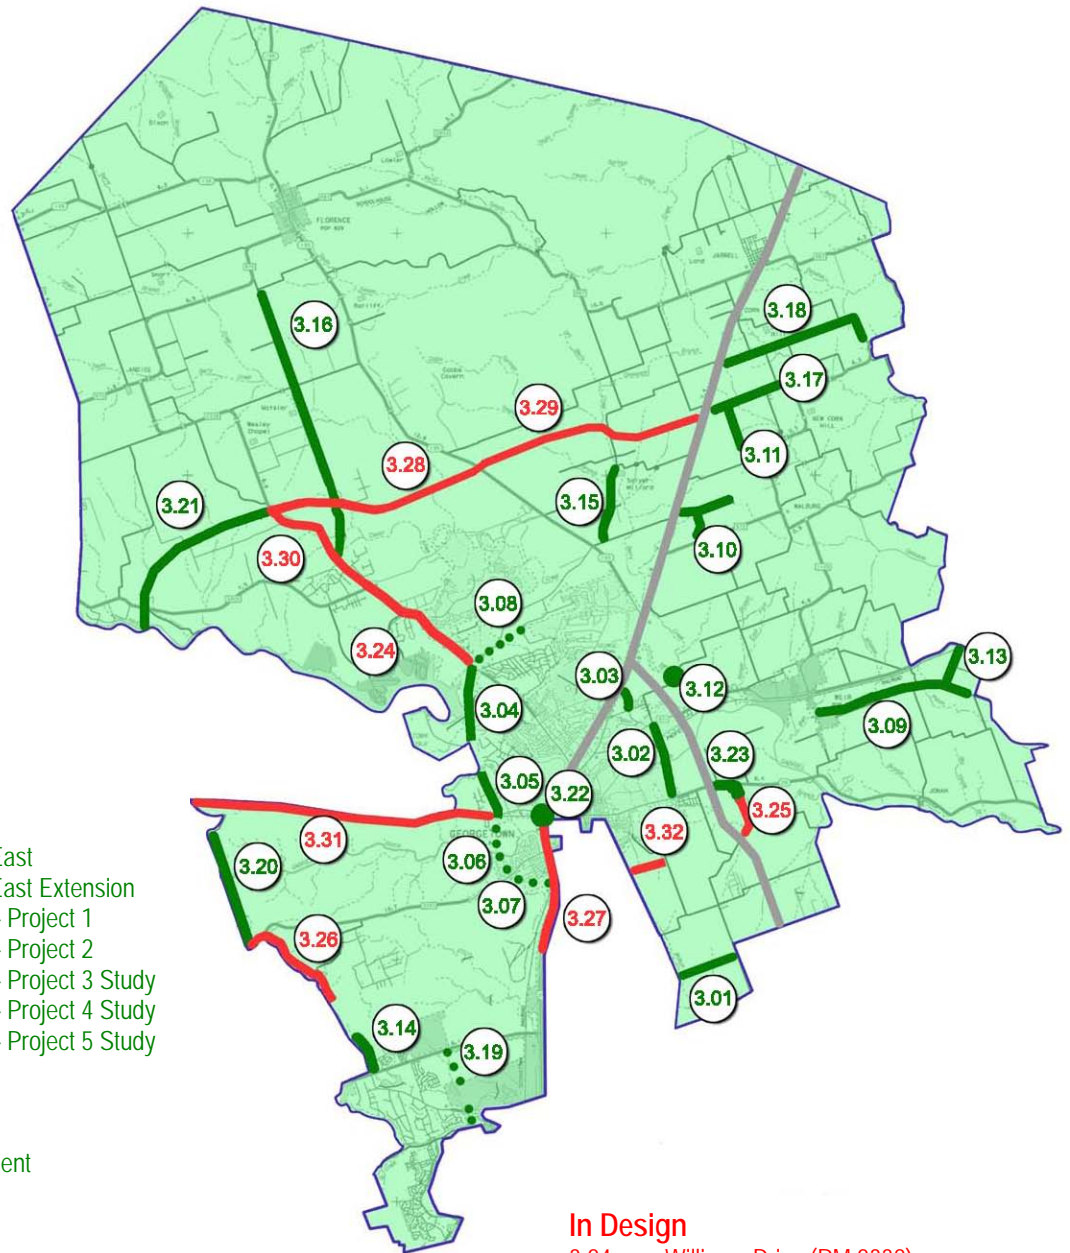

Completed/Open to Traffic

- 3.01 Chandler Rd. – Phase 1
- 3.02 Georgetown Inner Loop East
- 3.03 Georgetown Inner Loop East Extension
- 3.04 Georgetown Inner Loop – Project 1
- 3.05 Georgetown Inner Loop – Project 2
- 3.06 Georgetown Inner Loop – Project 3 Study
- 3.07 Georgetown Inner Loop – Project 4 Study
- 3.08 Georgetown Inner Loop – Project 5 Study
- 3.09 CR 124
- 3.10 CR 142
- 3.11 CR 145
- 3.12 CR 152 Bridge Replacement
- 3.13 CR 157
- 3.14 CR 175
- 3.15 CR 234
- 3.16 CR 245
- 3.17 CR 311
- 3.18 CR 314
- 3.19 Wyoming Springs North – Study
- 3.20 Ronald W. Reagan South Phase 2
- 3.21 Ronald W. Reagan North Phase 2
- 3.23 SH 29/CR 104 – Phase 1
- 3.22 IH-35 @ SH 29 Turnarounds (PTF)

In Design

- 3.24 Williams Drive (RM 2338)
- 3.25 CR 104 – Phase 2
- 3.26 CR 175 Extension
- 3.27 IH-35 Northbound Frontage Rd and Ramps
- 3.28 Ronald W. Reagan North Phase 3
- 3.29 Ronald W. Reagan North Phase 4
- 3.30 RM 2338 (PTF)
- 3.31 SH 29 Corridor Study
- 3.32 Georgetown SE Inner Loop Widening

Ronald Reagan Blvd North, Ph. 2 (FM 3405 to RM 2338)
Project No. 07WC502

Original Contract Price = \$9,757,296.99

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantially Complete</u>	<u>Work Accepted</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
11/1/2006	11/28/2006	3/7/2007	3/12/2007	5/23/2008		450	0	450

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoice Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time</u>	<u>Liquidated Damages</u>	<u>Total Liq Damages</u>
1	3/12/2007	3/31/2007	20	\$356,220.00	\$356,220.00	\$39,580.00	\$39,580.00	4	4	\$0.00	\$0.00
2	4/1/2007	4/30/2007	30	\$607,947.95	\$964,167.95	\$67,549.77	\$107,129.77	11	11	\$0.00	\$0.00
3	5/1/2007	5/31/2007	31	\$250,364.38	\$1,214,532.33	\$27,818.27	\$134,948.04	14	18	\$0.00	\$0.00
4	6/1/2007	6/30/2007	30	\$524,013.80	\$1,738,546.13	\$58,223.75	\$193,171.79	20	25	\$0.00	\$0.00
5	7/1/2007	7/31/2007	31	\$256,470.21	\$1,995,016.34	\$28,496.69	\$221,668.48	23	32	\$0.00	\$0.00
6	8/1/2007	8/31/2007	31	\$675,412.47	\$2,670,428.81	\$75,045.83	\$296,714.31	30	38	\$0.00	\$0.00
7	9/1/2007	9/30/2007	30	\$975,098.54	\$3,645,527.35	\$108,344.28	\$405,058.59	41	45	\$0.00	\$0.00
8	10/1/2007	10/31/07	31	\$1,034,884.68	\$4,680,412.03	\$114,987.19	\$520,045.78	53	52	\$0.00	\$0.00
9	11/1/2007	11/30/07	30	\$897,356.66	\$5,577,768.69	\$99,706.30	\$619,752.08	63	59	\$0.00	\$0.00
10	12/1/2007	12/31/07	31	\$491,751.45	\$6,069,520.14	\$-300,303.65	\$319,448.43	65	66	\$0.00	\$0.00
11	1/1/2008	1/31/2008	31	\$600,627.39	\$6,670,147.53	\$31,611.97	\$351,060.40	72	72	\$0.00	\$0.00
12	2/1/2008	2/29/2008	29	\$933,260.56	\$7,603,408.09	\$49,118.97	\$400,179.37	82	79	\$0.00	\$0.00
13	3/1/2008	3/31/2008	31	\$534,479.40	\$8,137,887.49	\$28,130.50	\$428,309.87	88	86	\$0.00	\$0.00
14	4/1/2008	4/30/2008	30	\$505,128.78	\$8,643,016.27	\$26,585.72	\$454,895.59	93	92	\$0.00	\$0.00
15	5/1/2008	5/23/2008	23	\$123,657.52	\$8,766,673.79	\$6,508.29	\$461,403.88	94	98	\$0.00	\$0.00
16	6/1/2008	6/30/2008	N/A	\$114,594.93	\$8,881,268.72	\$6,031.32	\$467,435.20	100	-	\$0.00	\$0.00
17	7/1/2008	7/31/2008	N/A	\$326,467.91	\$9,207,736.63	\$-279,522.21	\$187,912.99	100	-	\$0.00	\$0.00

10/27/2008 Comments The Contractor has revegetated some bare areas on the project and is currently watering to establish the vegetation. The GEC met with County staff on 10/13/08 and it was determined that the additional fencing will be placed on all four sides of Tributary #2. This work was completed during the week of 10/20/08.

9/29/2008 Comments - The GEC has notified the Contractor of areas that need revegetated on the project. Watering continues for vegetation establishment.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
01	05/25/2007	24,640.00	24,640.00

4D: Third Party Accommodation. Other. Item added as obligation to Seller (property owner) by Purchaser (Williamson County) in Real Estate Contract to furnish and install pipe sleeves of sufficient size to contain utility lines across property from North to South. Real estate contract provision was inadvertently left out of the contract as a bid item.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
02	08/10/2007	-5,041.39	19,598.61

4B: Third Party Accommodation. Third Party Requested Work. The County agreed to property owner's request to eliminate construction of the proposed cul-de-sac at CR 248 and construct a driveway for access into the property. This change order will add and adjust bid item quantities associated with the construction changes in this area.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
03	08/10/2007	8,420.00	28,018.61

4D: Third Party Accommodation. Other. Item added as obligated to Seller (Elvin and Donna Hall - property owner Parcel 23) by Purchaser (Williamson County) on Real Estate Contract to construct driveway at Station 746 RT. The change order will reflect the additional cost for construction of this drive using existing contract items and unit rates.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
04	08/28/2007	28,133.90	56,152.51

5B: Contractor Convenience. Contractor requested change in the sequence and/or method of work. 3D: County Convenience. Achievement of an early project completion. The County agreed to Contractor's request to modify the construction strategy at the FM 3405 intersection. This change order accounts for the extra work associated with the revised construction strategy.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
05	01/14/2008	11,623.50	67,776.01

4B: Third Party Accommodation. Third party requested work. Williamson County agreed to accommodate a property owner's request to construct an additional driveway which allows access from the Thomlinson Family property (Parcel 38) to Ronald Reagan Blvd.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
06	12/11/2007	289,372.00	357,148.01

4B: Third Party Accommodation. Third party requested work. 6C: Untimely ROW/Utilities. Utilities not clear. The County agreed to Chisholm Trail Utility District's request for assistance with the relocation of their 18" water line that conflicts with construction of intersection at FM 3405. This change order will add bid item quantities associated with the relocation of the water line.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
07	07/31/2008	-718,831.29	-361,683.28

3H: County Convenience. Cost savings opportunity discovered during construction. The ultimate alignment for the Reagan Blvd / RM 2338 intersection will be constructed as part of the Reagan North, Ph. 3 project. Rather than construct the interim intersection as originally planned, the County opted for a simpler tie-in which reduced the amount of new construction to be removed during the Reagan North, Ph. 3 construction.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
08	10/30/2008	22,536.50	-339,146.78

5B: Contractor Convenience. Contractor requested change in the sequence and/or method of work. 2E: Differing Site Conditions. Miscellaneous difference in site conditions (unforeseeable). The County agreed to Contractor's request to modify the construction strategy at the FM 3405 (via CO #4) and CR 289 intersections (via RFI #15). This change order accounts for the extra work associated with the revised construction strategy at CR 289, as well as extra quantities associated with unexpected field conditions at FM 3405 to create a smooth tie-in.

Adjusted Price = \$9,418,150.21

PASS THROUGH FINANCING: IH-35 at SH 29 (Turnaround Structures)
Wilco Project No. 07WC513 TxDOT CSJ: 015-08-122

Original Contract Price = \$3,673,982.79

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantially Complete</u>	<u>Work Accepted</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
7/25/2007	8/7/2007	9/28/2007	10/29/2007	8/25/2008		209	3	212

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoice Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time Used</u>	<u>Liquidated Damages</u>	<u>Total Liq Damages</u>
1	10/29/200	10/31/07	3	\$296,803.30	\$296,803.30	\$0.00	\$0.00	8	1	\$0.00	\$0.00
2	11/1/2007	11/30/07	19	\$430,321.76	\$727,125.06	\$0.00	\$0.00	20	10	\$0.00	\$0.00
3	12/1/2007	12/31/07	18	\$238,722.18	\$965,847.24	\$0.00	\$0.00	26	19	\$0.00	\$0.00
4	1/1/2008	1/31/2008	22	\$655,758.48	\$1,621,605.72	\$0.00	\$0.00	44	29	\$0.00	\$0.00
5	2/1/2008	2/29/2008	21	\$419,178.90	\$2,040,784.62	\$0.00	\$0.00	56	39	\$0.00	\$0.00
6	3/1/2008	3/31/2008	21	\$221,080.63	\$2,261,865.25	\$0.00	\$0.00	62	49	\$0.00	\$0.00
7	4/1/2008	4/30/2008	22	\$292,046.55	\$2,553,911.80	\$0.00	\$0.00	70	59	\$0.00	\$0.00
8	5/1/2008	5/31/2008	21	\$112,337.87	\$2,666,249.67	\$0.00	\$0.00	73	69	\$0.00	\$0.00
9	6/1/2008	6/30/2008	21	\$129,096.35	\$2,795,346.02	\$0.00	\$0.00	76	79	\$0.00	\$0.00
10	7/1/2008	7/31/2008	22	\$259,428.07	\$3,054,774.09	\$0.00	\$0.00	83	90	\$0.00	\$0.00
11	8/1/2008	8/31/2008	18	\$479,658.20	\$3,534,432.29	\$0.00	\$0.00	96	98	\$0.00	\$0.00
12	9/1/2008	9/30/2008	N/A	\$37,186.78	\$3,571,619.07	\$0.00	\$0.00	97	-	\$0.00	\$0.00

10/27/2008 Comments - The Contractor continues watering for establishment of grass growth on the project.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
01	12/06/2007	25,000.00	25,000.00

3F: County Convenience. Additional work desired by the County. Revising safety work/measures desired by the County. This change order establishes an item to pay for off duty police and their vehicles that are required to work in lane closures according General Note to Item 502. Payment will be made based on invoices submitted by the Contractor.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
02	12/06/2007	750.00	25,750.00

3F: County Convenience. Additional work desired by the County. This change order establishes an item to pay for Drill Shaft cores according to Item 416.5C

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
03	02/07/2008	-52,500.00	-26,750.00

5B: Contractor Convenience. Contractor requested change in the sequence and/or method of work. The work item for Portable Concrete Traffic Barrier (CTB) is being revised, at the Contractor's request, from being furnished by the Contractor to being furnished from a TXDOT stockpile.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
04	02/18/2008	-4,434.15	-31,184.15

5B: Contractor Convenience. Contractor requested change in the sequence and/or method of work. The Contractor requested and received permission from the Design Engineer and TxDOT to delete the epoxy coating on the rebar for the bridge slabs. This Change Order credits the County for the deletion of the epoxy coating.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
05	03/27/2008	0.00	-31,184.15

4D: Third Party Accommodation. Other. 5E: Contractor Convenience. Other. This change order adds three (3) working days to the contract to account for time charged between Christmas and New Years holidays. TxDOT regulations restricted work on state roads during this time period.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
06	07/16/2008	20,000.00	-11,184.15

2E: Differing Site Conditions. Miscellaneous differences in sight conditions (unforeseeable). This change order sets up a force account for \$20,000.00 to remove and replace coping on retaining wall 6 due to a redesign of the roadway and retaining wall profile.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
07	05/14/2008	10,000.00	-1,184.15

3M: County Convenience. Other. This change order sets up a force account pay item to pay the contractor for repairing damage to safety appurtenances on the project.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
08	10/01/2008	-5,592.10	-6,776.25

3L: County Convenience. Revising safety work/measures desired by the County. This change order deletes work on the guard rail that is attached to the existing SH 29 bridge, as approved by TXDOT, and installs a crash cushion and guard rail at NBSB Sta. 15+60 at the end of wall 7.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
09	10/01/2008	18,998.55	12,222.30

3L: County Convenience. Revising safety work/measures desired by the County. This change order pays the Contractor to place PCTB which protects the work zone and allows the Contractor to perform excavation adjacent to IH 35, relocate an illumination pole, and replace conduit in the excavated area that fed the illumination assemblies.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
10	10/30/2008	-39,812.00	-27,589.70
1B: Design Error or Omission. Incorrect PS&E. This change order decreases the retaining wall Plan Quantity square footage due a revision in the height of the wall at the Abutments.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
11	10/30/2008	4,200.00	-23,389.70
3E: County Convenience. Reduction of future maintenance. This change order adds rock berms to the contract to control erosion at the backless inlets.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
12	10/30/2008	5,159.00	-18,230.70
3F: County Convenience. Additional work desired by County. This change order pays the contractor to construct a drill shaft foundation, provide and install an illumination pole to be used as a mount for a future for the traffic counting device.			
			Adjusted Price = \$3,655,752.09

SH 29 / CR 104, Ph. 1 Improvements
Project No. 08WC602

Original Contract Price = \$1,977,963.60

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantially Complete</u>	<u>Work Accepted</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
1/16/2008	1/29/2008	2/15/2008	3/1/2008	7/28/2008		150	0	150

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoice Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time Used</u>	<u>Liquidated Damages</u>	<u>Total Liq Damages</u>
1	3/1/2008	3/31/2008	31	\$430,637.70	\$430,637.70	\$0.00	\$0.00	22	21	\$0.00	\$0.00
2	4/1/2008	4/30/2008	30	\$295,203.00	\$725,840.70	\$0.00	\$0.00	37	41	\$0.00	\$0.00
3	5/1/2008	5/31/2008	31	\$306,661.50	\$1,032,502.20	\$0.00	\$0.00	52	61	\$0.00	\$0.00
4	6/1/2008	6/30/2008	30	\$803,127.78	\$1,835,629.98	\$0.00	\$0.00	92	81	\$0.00	\$0.00
5	7/1/2008	7/31/2008	28	\$45,171.89	\$1,880,801.87	\$0.00	\$0.00	95	100	\$0.00	\$0.00

10/27/2008 Comments Watering continues for establishment of grass growth at various locations on project.

9/29/2008 Comments - The Contractor is watering seed for establishment of grass growth at various locations on project.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
01	07/08/2008	10,000.00	10,000.00

3M: County Convenience. Other. This change order sets up a force account pay item to pay the contractor for repairing damage to safety appurtenances on the project.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
02	08/13/2008	4,550.00	14,550.00

2: Differing Site Conditions (unforeseeable). 2G: Unadjusted Utility. This change order will provide payment for adjustment of valve risers located behind the curb on CR 104, over existing Jonah water line. 2E: Miscellaneous difference in site conditions. This change order will also pay the Contractor to modify Driveway #10 to address a drainage problem located behind the curb located on the south end of CR 104. 2I: Additional safety needs. The change order will pay for removal and relocation of mailboxes on the north side of SH 29 (requested by the rural postal carrier).

Adjusted Price = \$1,992,513.60

PRECINCT 4


COMMISSIONER MORRISON

Completed/Open to Traffic

- 4.01 Bridge Replacements Phase 1
(CR 406, CR 390, CR 427)
- 4.02 Bridge Replacements Ph. 2A (CR 424)
- 4.03 Chandler Rd. – Phase 1
- 4.04 CR 100
- 4.05 CR 112 – Phase 1
- 4.06 CR 119
- 4.07 CR 122 at US 79
- 4.08 CR 124
- 4.09 CR 132
- 4.10 CR 136
- 4.11 CR 137
- 4.12 CR 138 & CR 139 Alignment Study
- 4.13 CR 300 & CR 301
- 4.14 CR 302
- 4.15 CR 347 & CR 348
- 4.16 CR 368 & CR 369 (CR 101 to CR 366)
- 4.17 CR 404
- 4.18 CR 412
- 4.19 CR 466
- 4.20 FM 37 at SH 95 Signal
- 4.21 Gattis School Rd. ROW
- 4.22 Limmer Loop – Phase 1A
- 4.23 Thrall School Zone
- 4.24 US 79 – Section 1
- 4.25 US 79 – Section 2
- 4.26 US 79 – Section 3A
- 4.27 Chandler Rd. – Phase 2
- 4.28 Limmer Loop – Phase 1B
- 4.30 Limmer Loop – Phase 1C

In Design

- 4.31 Arterial A – Phase 1
- 4.32 Arterial A – Phase 2
- 4.33 Chandler Rd. – Phase 3A
- 4.34 Chandler Rd. – Phase 3B
- 4.35 FM 1660 (PTF)
- 4.36 Gattis School Road
- 4.37 US 79 Section 3 (PTF)
- 4.38 BUS 79/2nd Street Improvements
- 4.39 BUS 79 Drainage Improvements
- 4.40 US 79 Section 5A (PTF)
- 4.42 Bridge Replacements Phase 2B
(CR 351 & CR 434)

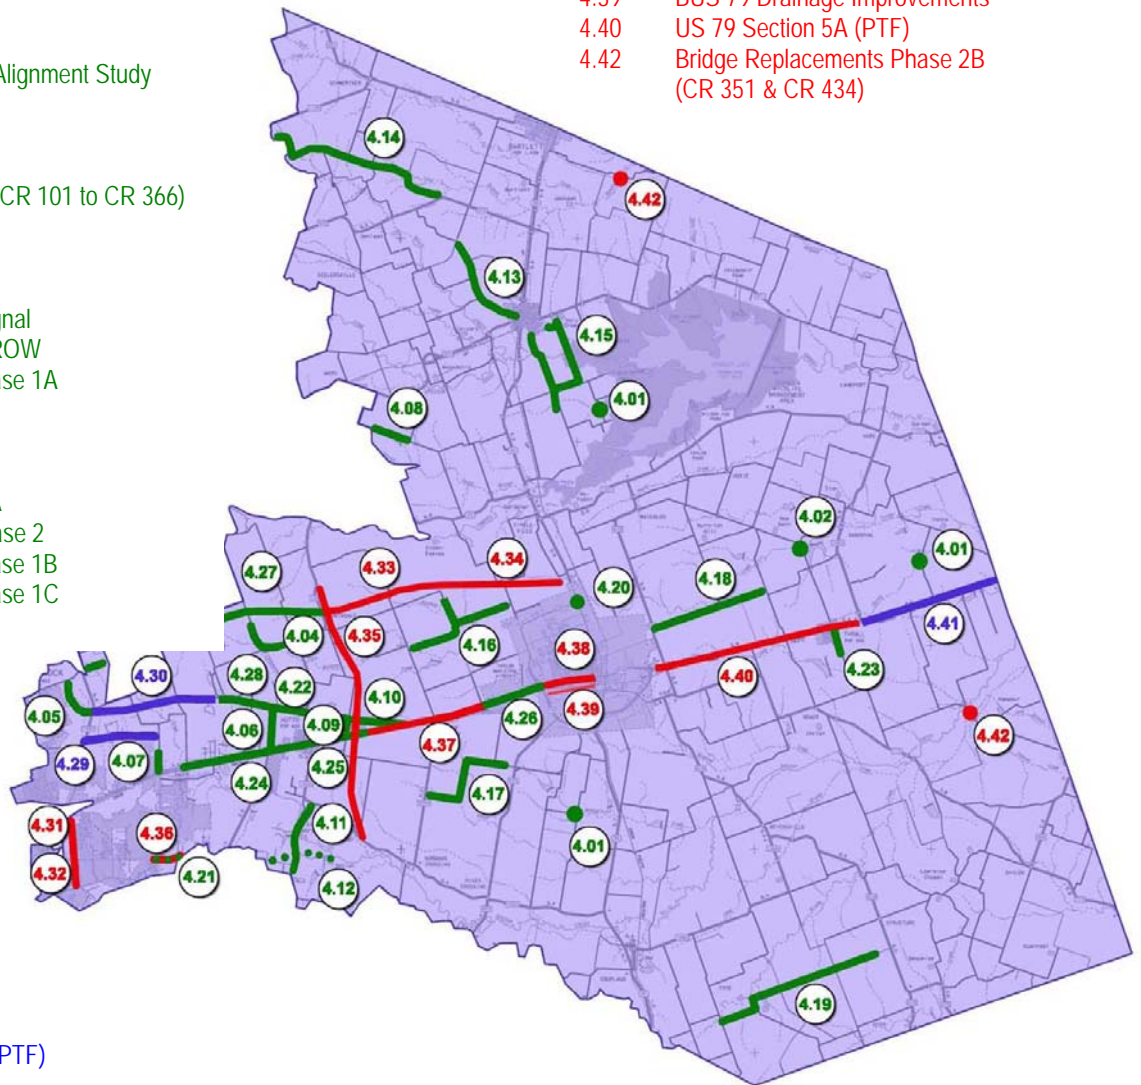

Under Construction

- 4.29 CR 113
- 4.41 US 79 Section 5B (PTF)

Limmer Loop, Ph. 1B (Haybarn Lane to CR 119)
Project No. 06WC420

Original Contract Price = \$2,010,629.65

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Work Completed</u>	<u>Work Accepted</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
9/20/2006	10/3/2006	3/8/2007	3/12/2007	4/7/2008	10/31/2008	270	92	362

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoice Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time</u>	<u>Liquidated Damages</u>	<u>Total Liq Damages</u>
1	3/12/2007	5/31/2007	81	\$62,486.40	\$62,486.40	\$6,942.93	\$6,942.93	3	22	\$0.00	\$0.00
2	6/1/2007	6/30/2007	30	\$22,599.00	\$85,085.40	\$2,511.00	\$9,453.93	5	31	\$0.00	\$0.00
3	7/1/2007	7/31/2007	31	\$59,346.00	\$144,431.40	\$6,594.00	\$16,047.93	8	39	\$0.00	\$0.00
4	8/1/2007	8/31/2007	31	\$271,091.70	\$415,523.10	\$30,121.30	\$46,169.23	23	48	\$0.00	\$0.00
5	9/1/2007	9/30/2007	30	\$351,959.13	\$767,482.23	\$39,106.57	\$85,275.80	42	56	\$0.00	\$0.00
6	10/1/2007	10/31/07	31	\$239,598.00	\$1,007,080.23	\$26,622.00	\$111,897.80	55	65	\$0.00	\$0.00
7	11/1/2007	11/30/07	30	\$383,864.29	\$1,390,944.52	\$-38,690.19	\$73,207.61	72	73	\$0.00	\$0.00
8	12/1/2007	12/31/07	31	\$350,494.81	\$1,741,439.33	\$18,447.09	\$91,654.70	88	81	\$0.00	\$0.00
9	1/1/2008	1/31/2008	31	\$203,731.42	\$1,945,170.75	\$10,722.71	\$102,377.41	95	90	\$0.00	\$0.00
10	2/1/2008	2/29/2008	29	\$180,435.58	\$2,125,606.33	\$-58,997.69	\$43,379.72	97	98	\$0.00	\$0.00
11	3/1/2008	3/31/2008	0	\$54,234.17	\$2,179,840.50	\$1,106.82	\$44,486.54	100	-	\$0.00	\$0.00
12	Retainage Release		0	\$44,486.54	\$2,224,327.04	\$-44,486.54	\$0.00	100	-	\$0.00	\$0.00

10/27/2008 Comments Project is complete, with the exception of the Contractor's responsibility under the Maintenance Bond.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
01	07/13/2007	0.00	0.00

2H: Differing Site Conditions (unforeseeable). Unacquired Right-of-Way (unforeseeable). Negotiations with a landowner impeded the start of construction on the west side of the project. 6C: Untimely ROW/Utilities. Utilities Not Clear. Overhead lines in conflict with beginning construction. 3M: County Convenience. Other. A time extension was negotiated in lieu of renegotiated contract prices. Fifty-two (52) days were added to the project schedule.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
02	11/19/2007	23,331.00	23,331.00

2E: Differing Site Conditions. Miscellaneous differences in site conditions (unforeseeable). An area of roadway is experiencing a groundwater issue resulting in soft and unsuitable subgrade conditions. Raba-Kistner (Geotechnical Engineer) recommended the use of an edge drain system to remediate the problem. Thirty (30) days were added to the Contract schedule.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
03	11/19/2007	15,050.00	38,381.00

2E: Differing Site Conditions. Miscellaneous difference in site conditions. Box Culvert 'C's original alignment did not line up with the existing channel. Design Engineer reduced the skew from 45° to 30° thus creating the need for re-staking the box culvert. 2C: Differing Site Conditions. New Development (conditions changing after PS&E completed). Property owners added driveways after original PS&E were completed. In order to restore access, Design Engineer added 4 new driveways to the plans.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
04	01/17/2008	38,278.10	76,659.10

1A: Design Error or Emission. Incorrect PS&E. CR108/Limmer intersection construction plan was omitted from the original construction documents. Revised plans are attached with the Engineer's proposal for an expedited construction utilizing asphalt base. The extra work will include the installation of drainage cross culverts at the intersection and the relocation of an existing 2" water line. Ten (10) days were added to the Contract schedule.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
05	01/14/2008	3,500.00	80,159.10

2C: Differing Site Conditions. New development (conditions changing after PS&E completed). After PS&E was completed, SH 130 contractor installed cross culverts (rcp's) that are now in conflict for channel grading. Contractor has removed culverts w/ SET's in order to complete grading.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
06	04/01/2008	81,276.60	161,435.70

2E: Differing Site Conditions (unforeseeable). Miscellaneous difference in site conditions. Quantities for the listed items were exceeded.


<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
07	09/23/2008	88,131.00	249,566.70

3E: County Convenience. Reduction of future maintenance. In an effort to reduce future erosion issues, the County directed the Contractor to place additional concrete riprap in various areas throughout the project. 1A: Design Error or Omission. Incorrect PS&E. Several existing driveways were not included in the original plans, this change order accounts for those additional quantities. 6D: Untimely ROW/Utilities. Other. This Change Order also accounts for a driveway added after the project was bid. The delay was due to stalled negotiations with the property owner.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
08	10/17/2008	-35,869.31	213,697.39

2E: Differing Site Conditions. Miscellaneous difference in site conditions (unforeseeable). Adjustment of quantities to meet field conditions.

Adjusted Price = \$2,224,327.04

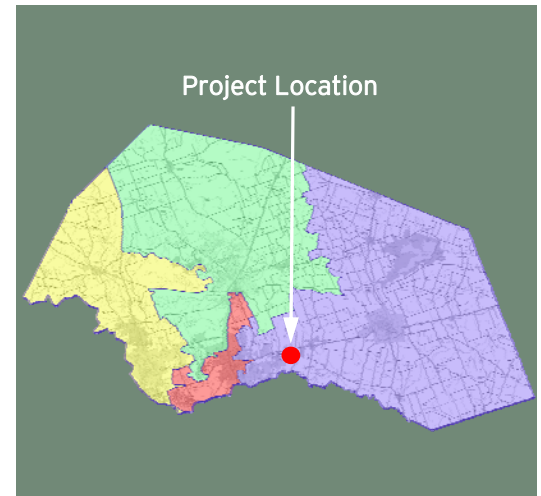

LIMMER LOOP, PHASE 1C

(CR 110 to SH 130)

Project Length: 1.2 Miles
 Roadway Classification: Minor Arterial
 Roadway Section: Transitions from two-lane undivided with center two way turn lane in the west end to two-lane undivided on east end

Project Schedule: April 2008 - October 2008
 Estimated Construction Cost: \$1.5 Million



OCTOBER 2008 IN REVIEW

10/6/08 - The Contractor is currently working on punch list items and watering seed for establishment of grass. The ribbon cutting ceremony was held on Thursday, 10/2/08.

10/27/2008 - Substantial Completion was granted on Thursday, October 2, 2008, almost 8 weeks ahead of schedule. The Contractor continues with watering seed on project for establishment of grass.



Design Engineer: Pate Engineers
 Contractor: J.C. Evans Construction
 Construction Observation:
 Jerry Jansen, Williamson County

Williamson County
 Road Bond Program

Limmer Loop, Ph. 1C (CR 110 to SH 130)
Project No. 08WC603

Original Contract Price = \$1,504,753.60

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantially Complete</u>	<u>Work Accepted</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
2/6/2008	2/19/2008	4/21/2008	4/30/2008	10/2/2008		210	0	210

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoice Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time Used</u>	<u>Liquidated Damages</u>	<u>Total Liq Damages</u>
1	4/1/2008	4/30/2008	1	\$120,168.90	\$120,168.90	\$13,352.10	\$13,352.10	9	0	\$0.00	\$0.00
2	5/1/2008	5/31/2008	31	\$201,787.20	\$321,956.10	\$22,420.80	\$35,772.90	24	15	\$0.00	\$0.00
3	6/1/2008	6/30/2008	30	\$211,777.20	\$533,733.30	\$23,530.80	\$59,303.70	39	30	\$0.00	\$0.00
4	7/1/2008	7/31/2008	31	\$265,662.00	\$799,395.30	\$29,518.00	\$88,821.70	59	44	\$0.00	\$0.00
5	8/1/2008	9/30/2008	61	\$585,041.28	\$1,384,436.58	\$65,004.59	\$153,826.29	96	73	\$0.00	\$0.00


<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
01	10/17/2008	17,888.18	17,888.18

3: County Convenience. 3F: Additional work desired by the County. This change order will provide payment for construction of an additional driveway on the 1B section of Limmer Loop, located on the SH 130 Frontage Road - Sta 34+38. 3I: Implementation of improved technology or better process. This change order will provide payment for a combined seed mix that the Contractor will place in lieu of two seeding operations to obtain both permanent and temporary cool weather grass coverage. 1A: Design Error or Omission. Incorrect PS&E. This change order will provide payment for construction of two concrete drives in lieu of asphalt as indicated in the plans at Sta 53+21 (RT) and Sta 54+82 (RT).

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
02	10/28/2008	80,498.92	98,387.10

3: County Convenience. 3L: Revising safety work/measures desired by the County. 3D: Achievement of an early project completion. This change order provides payment for adjustment to width of roadway and construction to accommodate a continuous two way turn lane on the west end of project from CR 110 to the school entrance as directed by the County. This change order also accounts for additional costs incurred by the Contractor to accelerate road construction on the west end of the project in order to have the road open prior to the beginning of the school year.

Adjusted Price = \$1,603,140.70



PASS THROUGH FINANCING PROJECT US 79, SECTION 5B

(East of FM 1063 to Milam County Line)

Project Length: 4 Miles

Roadway Classification: Major Arterial

Roadway Section: Four-lane Divided with Shoulders

Structures: Bridge Class Culvert

Project Schedule: July 2008 - July 2010

Estimated Construction Cost: \$17 Million



OCTOBER 2008 IN REVIEW

10/6/2008 - Excavation and embankment operations on the proposed westbound lanes continue. Installation of driveway pipes on the north side of the proposed westbound lanes will begin this week.

10/13/2008 - Excavation and embankment operations on the proposed westbound lanes continue. Utility relocation and coordination efforts continue. Fugro is currently taking samples to determine the amount of sulfates in the subgrade material at various locations on the project.

10/27/2008 - Fugro continues with sulfate testing on embankment material on the proposed westbound lanes. The Contractor set portable concrete traffic barrier along the outside edge of the westbound lanes and began box culvert installation at site #1, #2 & #3 located on the west end of project.



Design Engineer: HNTB Corporation
Contractor: J.C. Evans Construction
Construction Inspection: Huitt-Zollars

Williamson County
Pass Through Financing Program



PRIME
STRATEGIES,
INC.

PASS THROUGH FINANCING: US 79, Section 5B (FM 1063 to Milam County Line)**Project No. 08WC607 TxDOT CSJ: 0204-04-042**

Original Contract Price = \$16,986,053.49

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Anticipated Work Complete</u>	<u>Work Accepted</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
4/16/2008	4/29/2008	7/11/2008	7/23/2008	7/13/2010		499	0	499

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoice Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$) Used</u>	<u>% Time Used</u>	<u>Liquidated Damages</u>	<u>Total Liq Damages</u>
1	7/23/2008	7/31/2008	8	\$57,547.25	\$57,547.25	\$0.00	\$0.00	0	2	\$0.00	\$0.00
2	8/1/2008	8/31/2008	23	\$1,486,551.50	\$1,544,098.75	\$0.00	\$0.00	9	6	\$0.00	\$0.00
3	9/1/2008	9/30/2008	24	\$321,941.62	\$1,866,040.37	\$0.00	\$0.00	11	11	\$0.00	\$0.00

Adjusted Price = \$16,986,053.49
