

Williamson County Commissioners Court

Road Bond Program November 19, 2019








Precinct 1





Anticipated Completion
Spring 2020

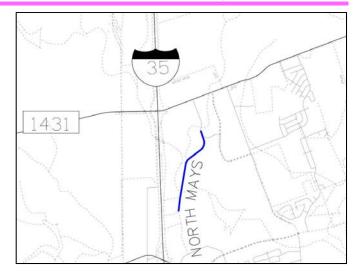

Original Contract Price = \$10,775,835.75

Total Change Orders to Date = \$0.00


Adjusted Contract Price = \$10,775,835.75

Expenditures to Date = \$5,580,335.04 (52%)







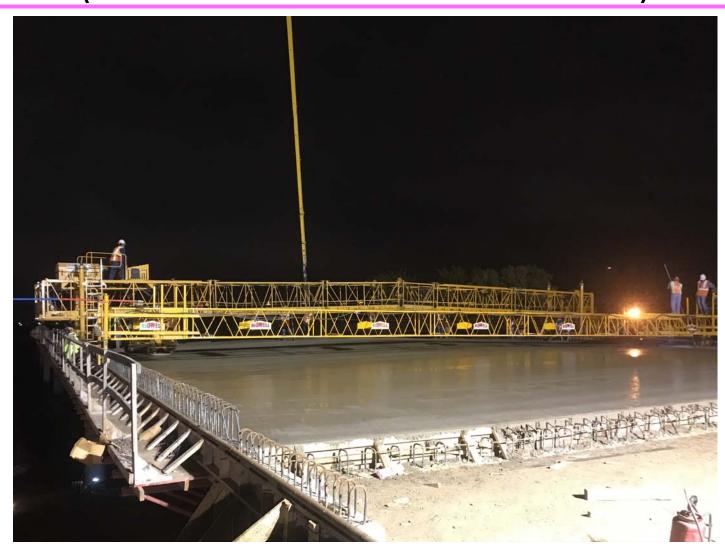








Pearson Ranch Road at Iveans Way (Pedestrian Crossing)

Substantially Complete

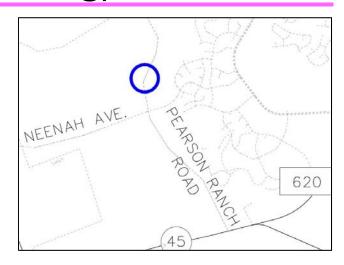

Partnership with the City of Austin

WilCo Contribution = 100% of the total project cost, not to exceed \$130,000.00

Construction is managed by the City of Austin




Pearson Ranch Road at Iveans Way (Pedestrian Crossing)






Precinct 2

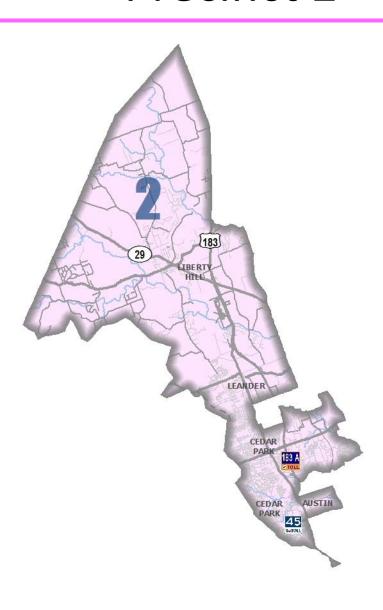



Anticipated Completion Early 2020

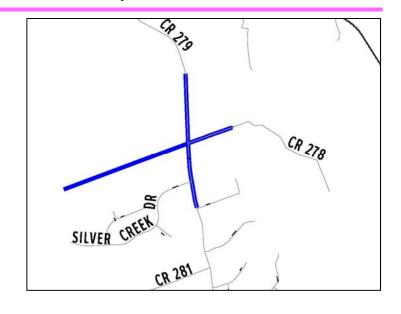

Original Contract Price = \$2,959,000.00

Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$2,959,000.00

Expenditures to Date = \$1,710,798.36 (58%)
















San Gabriel Ranch Road Bridge at Lackey Creek

Anticipated Completion Early 2020

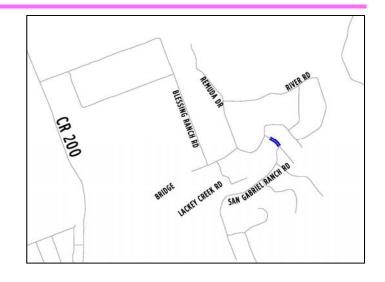

Original Contract Price = \$1,425,301.90

Total Change Orders to Date = \$16,166.09

Adjusted Contract Price = \$1,441,467.99

Expenditures to Date = \$874,985.43 (61%)






San Gabriel Ranch Road Bridge at Lackey Creek





Anticipated Completion Late 2020

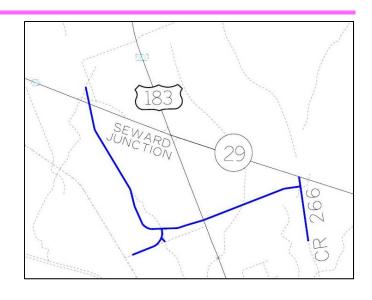

Original Contract Price = \$13,270,258.10

Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$13,270,258.10

Expenditures to Date = \$3,689,253.07 (28%)
















Precinct 3





Anticipated Completion Early 2020

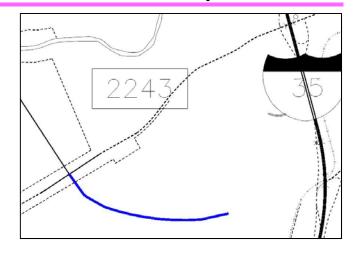

Original Contract Amount = \$8,087,943.77

Total Change Orders = \$0.00

Adjusted Contract Price = \$8,087,943.77

Expenditures to Date = \$5,347,545.24 (66%)
















Anticipated Completion Late 2019

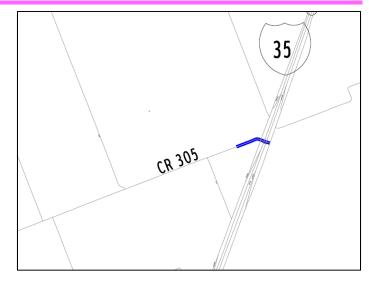

Partnership with TxDOT

Original Contract Amount = \$6,748,948.60

Construction is managed by TxDOT
















IH 35 Ramp Reversals and Frontage Road Conversion

Anticipated Completion Fall 2020

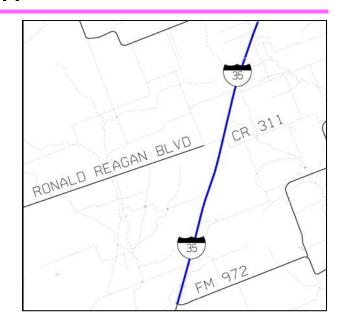

Partnership with TxDOT


Original Contract Amount = \$13,145,762.51

Construction is managed by TxDOT





IH 35 Ramp Reversals and Frontage Road ³⁰ Conversion

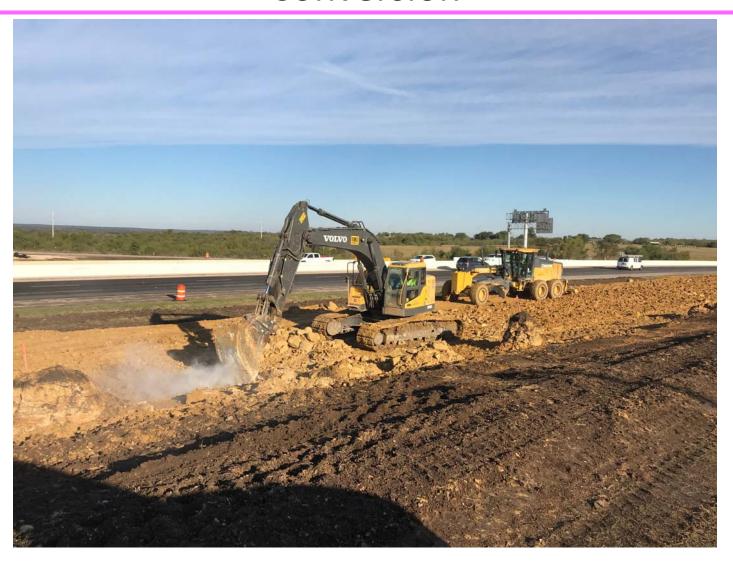





IH 35 Ramp Reversals and Frontage Road ³¹ Conversion








IH 35 Ramp Reversals and Frontage Road ³² Conversion





Anticipated Completion
Summer 2020

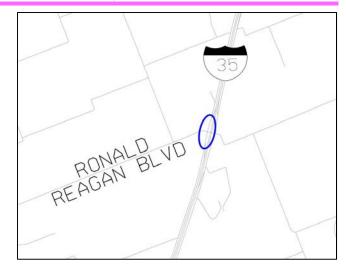

Partnership with TxDOT

Original Contract Amount = \$15,048,229.93

Construction is managed by TxDOT
















Anticipated Completion
Spring 2020

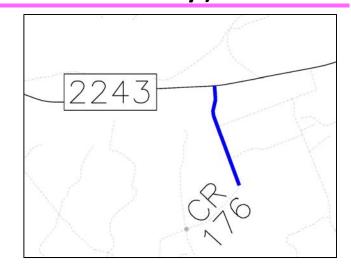


Original Contract Amount = \$2,447,560.00 Total Change Orders = \$0.00 Adjusted Contract Price = \$2,447,560.00 Expenditures to Date = \$567,710.26 (23%)







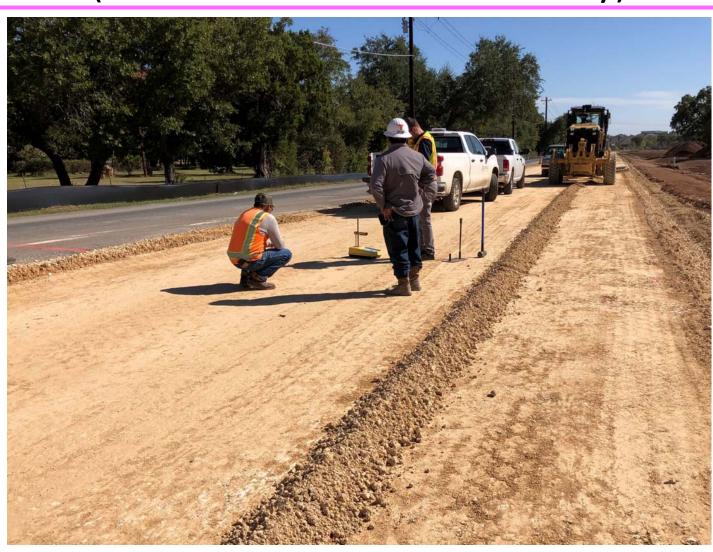









Anticipated Completion Spring 2020

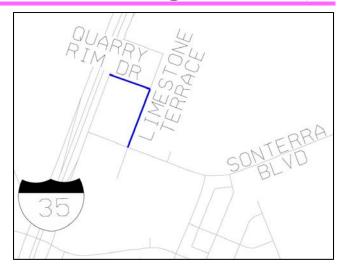

Original Contract Amount = \$1,060,707.70 Total Change Orders = \$0.00 Adjusted Contract Price = \$1,060,707.70 Expenditures to Date = \$201,666.91 (19%)





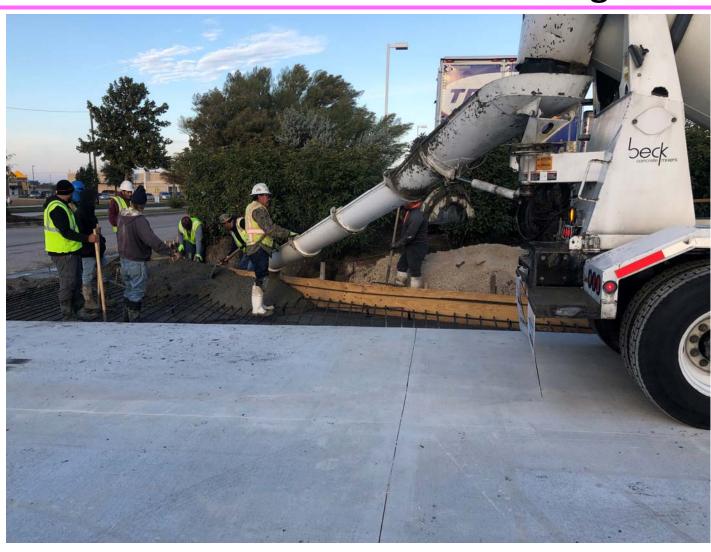

















Precinct 4

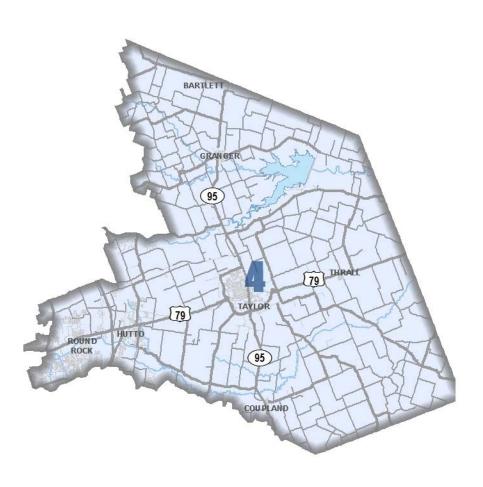



CR 110 Middle (Limmer Loop to CR 107)

Anticipated Completion
Spring 2020

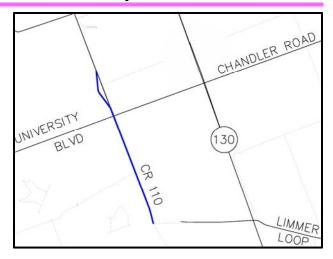

Original Contract Amount = \$8,910,862.73

Total Change Orders = \$66,291.83

Adjusted Contract Price = \$8,977,154.56

Expenditures to Date = \$2,476,168.11 (28%)



CR 110 Middle (Limmer Loop to CR 107)





CR 110 Middle (Limmer Loop to CR 107)





CR 110 Middle (Limmer Loop to CR 107)

