



# Williamson County Commissioners Court

---

Road Bond Program

May 18, 2021



# Precinct 1






## RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)

---

3

Anticipated Completion  
Summer 2022

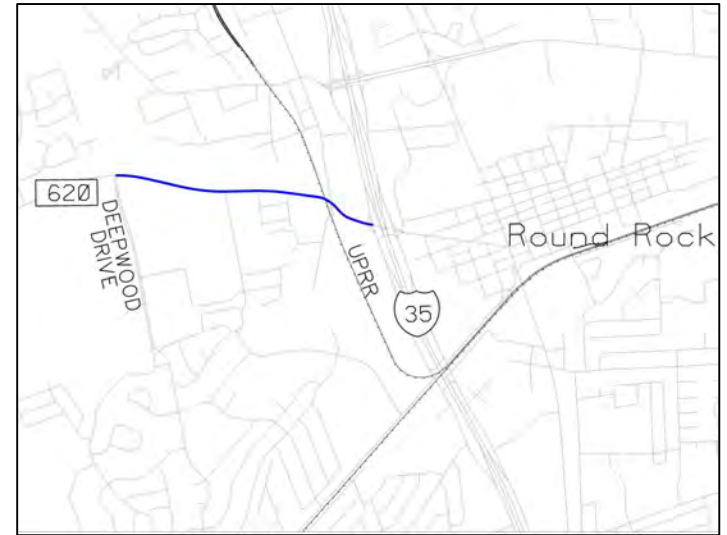

Partnership with TxDOT and the City of Round Rock  
Original Contract Amount = \$27,468,703.67  
Construction is managed by TxDOT



# RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)

4





# RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)

5





# RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)

6






# Forest North Phase 3 Drainage Improvements

7

Anticipated Completion  
Early 2022

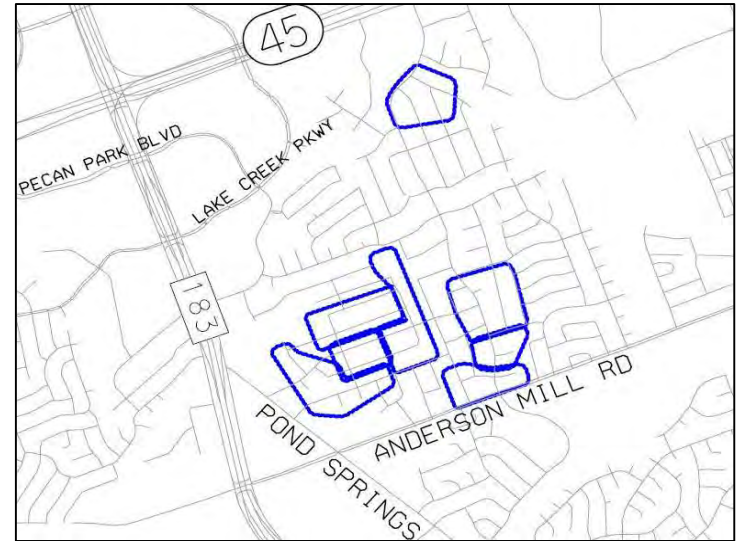

Original Contract Price = \$4,793,058.15

Total Change Orders to Date = \$87,744.37

Adjusted Contract Price = \$4,880,802.52

Expenditures to Date = \$3,042,957.22 (62%)



# Forest North Phase 3 Drainage Improvements





## Forest North Phase 3 Drainage Improvements





## Forest North Phase 3 Drainage Improvements

10








## O'Connor Traffic Signals

11

(Morgan Hill Trail, Liberty Walk, Great Oaks)

---

Anticipated Completion  
Spring 2021

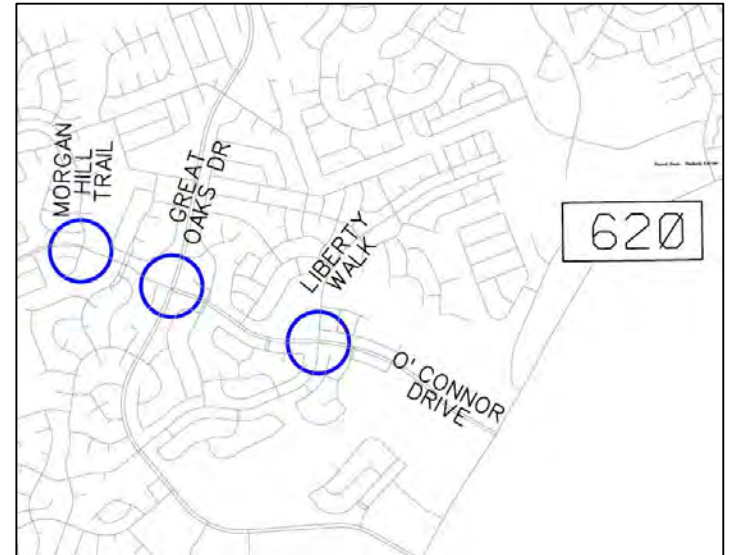

Original Contract Price = \$853,503.50

Total Change Orders to Date = \$131,055.38

Adjusted Contract Price = \$984,558.88

Expenditures to Date = \$611,860.08 (62%)

# O'Connor Traffic Signals (Morgan Hill Trail, Liberty Walk, Great Oaks)





# O'Connor Traffic Signals (Morgan Hill Trail, Liberty Walk, Great Oaks)





# O'Connor Traffic Signals (Morgan Hill Trail, Liberty Walk, Great Oaks)







## Corridor H – Sam Bass Road (Interim Traffic Signals)

---

15

Anticipated Completion  
Spring 2021



Original Contract Price = \$319,866.00

Total Change Orders to Date = \$28,476.86

Adjusted Contract Price = \$348,342.86

Expenditures to Date = \$233,518.86 (67%)

## Corridor H – Sam Bass Road (Interim Traffic Signals)

16





## Corridor H – Sam Bass Road (Interim Traffic Signals)

17





## Corridor H – Sam Bass Road (Interim Traffic Signals)

18








# Hairy Man Road / Brushy Creek Road Safety Improvements

---

19

Anticipated Completion  
Winter 2021

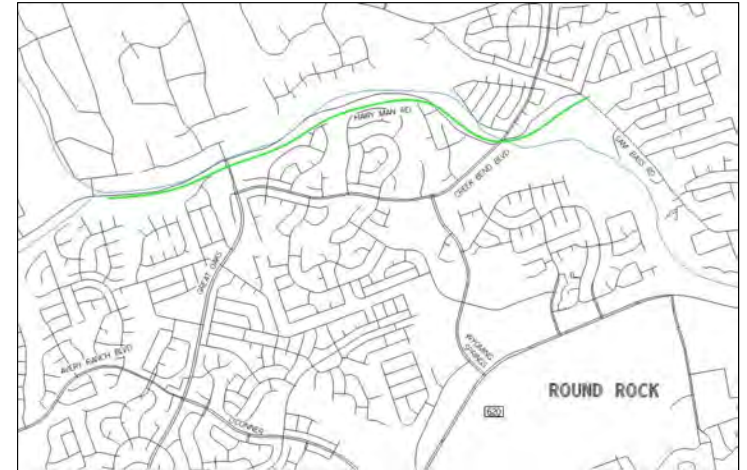

Original Contract Price = \$3,964,380.00

Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$3,964,380.00

Expenditures to Date = \$647,914.84 (16%)

# Hairy Man Road / Brushy Creek Road Safety Improvements





# Hairy Man Road / Brushy Creek Road Safety Improvements





## Hairy Man Road / Brushy Creek Road Safety Improvements








# University Boulevard Widening (IH 35 to Sunrise Road)

23

Anticipated Completion  
Early 2022

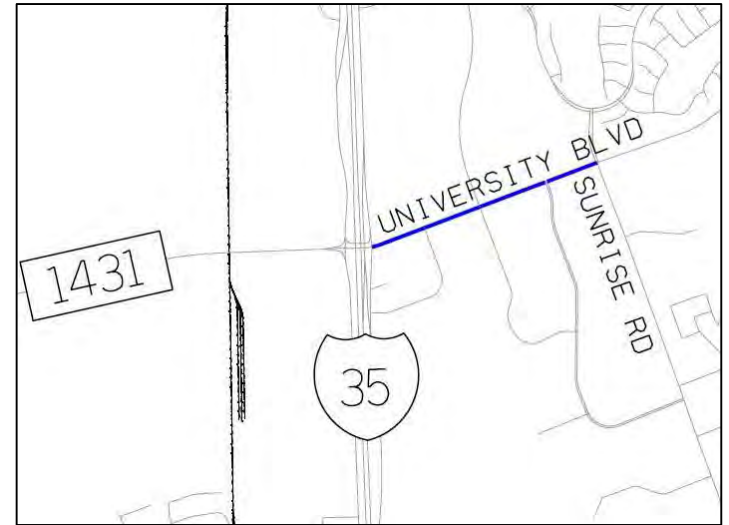

Partnership with the City of Round Rock

Original Contract Amount = \$12,135,410.45

Construction is managed by the City of Round Rock



# University Boulevard Widening (IH 35 to Sunrise Road)

24





# University Boulevard Widening (IH 35 to Sunrise Road)

25






# University Boulevard Widening (IH 35 to Sunrise Road)

26






# Precinct 2

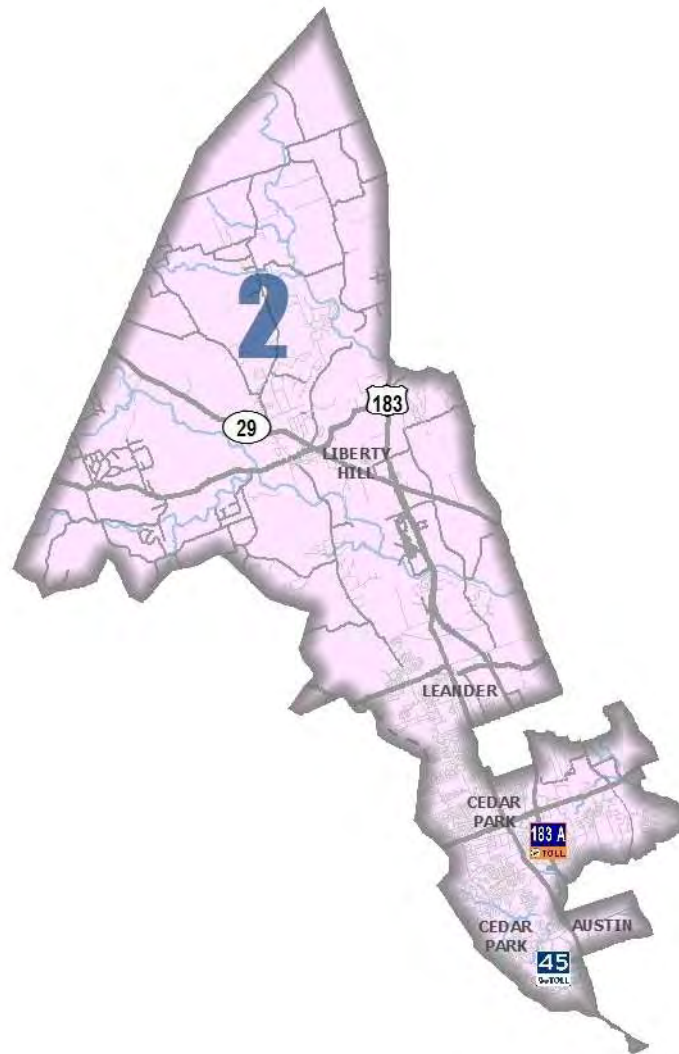

# Seward Junction Improvements

---

Substantially Complete  
March 15, 2021

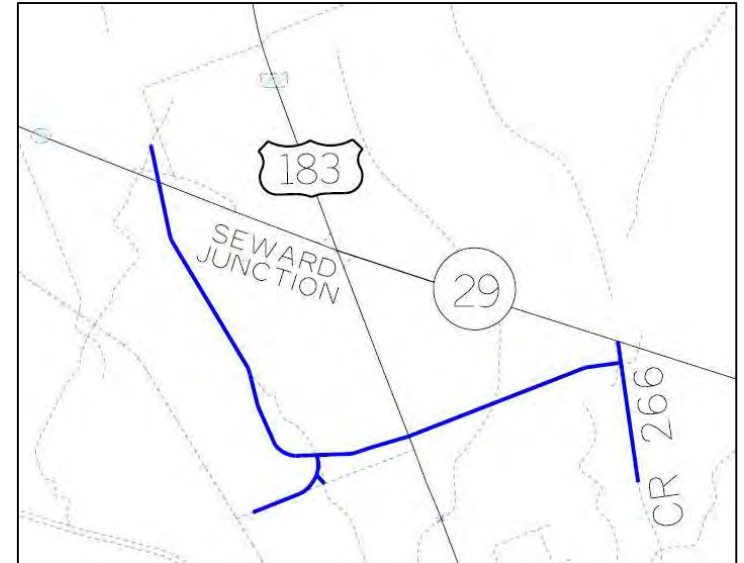

Original Contract Price = \$13,270,258.10


Total Change Orders to Date = \$611,059.17

Adjusted Contract Price = \$13,881,317.27

Expenditures to Date = \$12,618,645.87 (91%)



# Precinct 3

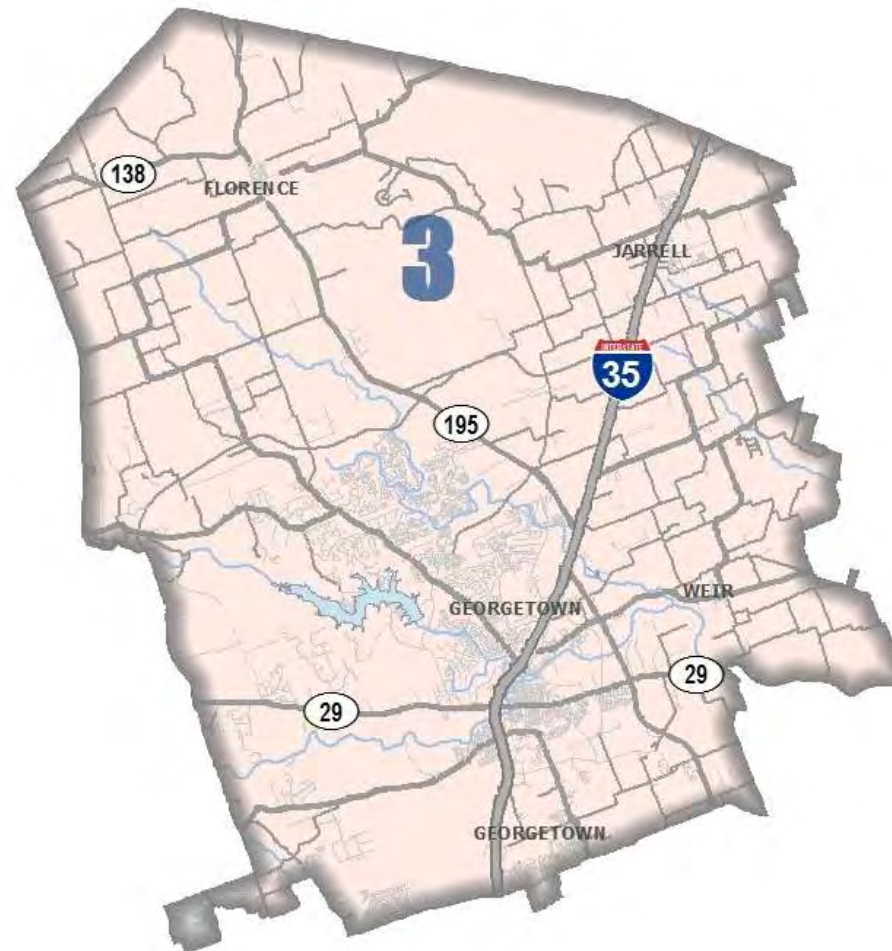




# Ronald Reagan Boulevard at IH 35 (Bridge Replacement)

---

30

Anticipated Completion  
Fall 2021

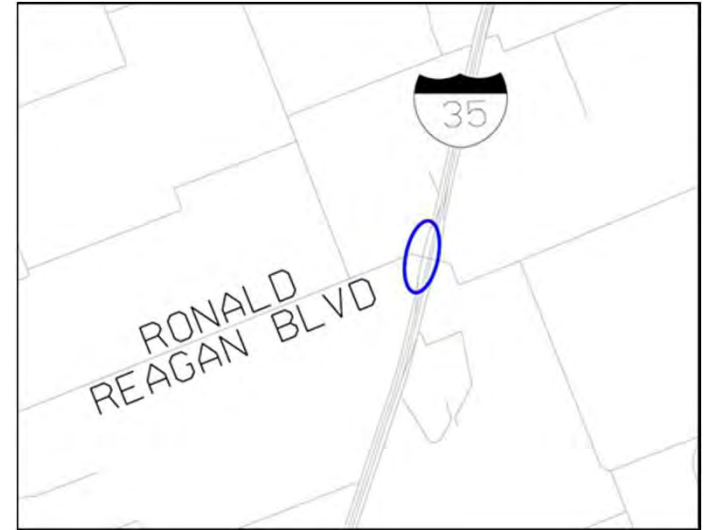

Partnership with TxDOT

Original Contract Amount = \$15,048,229.93

Construction is managed by TxDOT



# Ronald Reagan Boulevard at IH 35 (Bridge Replacement)

31





# Ronald Reagan Boulevard at IH 35 (Bridge Replacement)

32





# Ronald Reagan Boulevard at IH 35 (Bridge Replacement)

33






# Ronald Reagan at Silver Spur

## Ronald Reagan at Sun City

---

34

Anticipated Completion  
Spring 2021

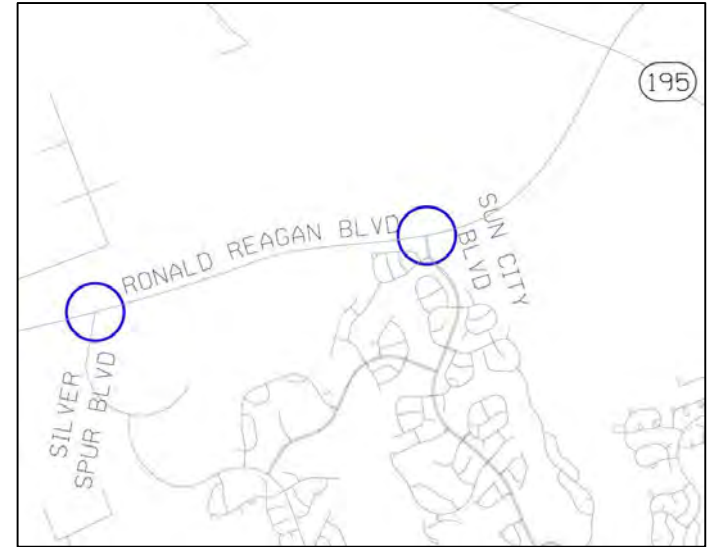

Original Contract Price = \$875,350.00

Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$875,350.00

Expenditures to Date = \$253,336.03 (29%)



# Ronald Reagan at Silver Spur Ronald Reagan at Sun City

35





# Ronald Reagan at Silver Spur Ronald Reagan at Sun City

36





# Ronald Reagan at Silver Spur Ronald Reagan at Sun City

37



# Precinct 4








## CR 101

39

(US 79 to North of Chandler Road)

---

Anticipated Completion  
Winter 2021

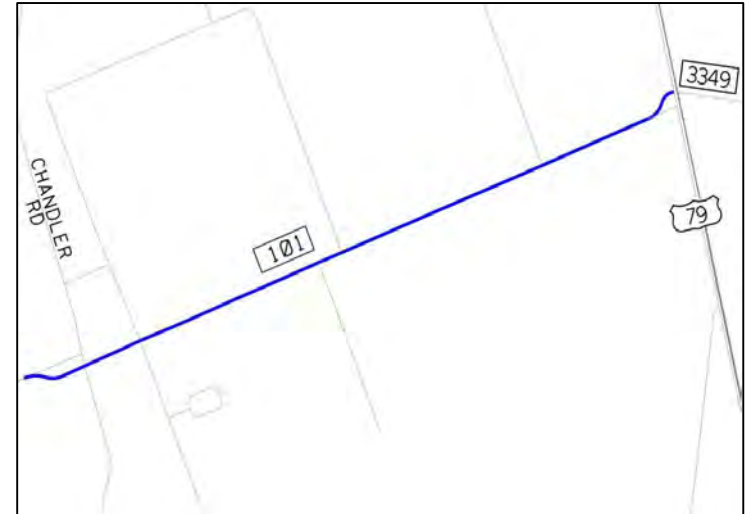

Original Contract Amount = \$13,092,842.00

Total Change Orders = \$0.00

Adjusted Contract Price = \$13,092,842.00

Expenditures to Date = \$6,164,729.30 (47%)

# CR 101 (US 79 to North of Chandler Road)





## CR 101 (US 79 to North of Chandler Road)





## CR 101 (US 79 to North of Chandler Road)

