

MTECC PROJECT STATUS REPORT- FEBRUARY 2026

LYONS ROAD PEDESTRIAN SAFETY PROJECT (B23-CP-FL0383), City of Coconut Creek

- **Project Summary:** Pedestrian Lighting along west side of Lyons Road, Atlantic Blvd. to Sawgrass Expressway
- **Design Schedule:** Final sealed plans received November 2025.
- **Key Activities since September 2025:**
 - Design plans finalized.
 - Broward County permitting review completed.
 - Pole/Luminaire contract drafted, advertised, and executed in December 2025. Poles/luminaires ordered on January 15, 2026 with 14-week delivery expected.
 - CEI procurement process- advertise, review submittals, rank, and selection in January 2026.
 - Initial drafting of Construction procurement package in early 2026. City meeting in January 2026 discussed current/expected project funding in place to proceed.
- **Upcoming Major Milestone:** CEI contract negotiation & construction advertisement in February 2026.
- **Project Critical Path:** Construction advertisement by end of February to start construction in April 2026.
- **Anticipated Construction Start:** April 2026
- **Anticipated Project Completion:** Twelve months after Construction Contract or approximately March 2027.
- **Project Grant Budget:** \$3,510,000




PEMBROKE MOBILITY HUB (#4334293), City of Pembroke Pines

- **Project Summary:** Mobility Hub improvements within Pembroke Pines City Center to include transit bus stops, new shared use path, new bike lanes, path lighting, and crosswalks.
- **Design Schedule:** Began 4/18/25, 60% plans submitted 1/30/26, final plans due 4/29/2026
- **Key Activities since September 2025:**
 - Public meeting on 11/5/2025 with no major comments.
 - Pre-Final (60% Plans) submitted to 4 permitting agencies in early February with 30 day review period.
 - MTECC reviewed grant funding with estimated construction estimate.
- **Upcoming Major Milestone:** Final permit approvals and Final plans- April 2026.
- **Project Critical Path:** Permitting comments from 4 agencies.
- **Anticipated Construction Start:** July 2026
- **Anticipated Project Completion:** December 2017
- **Project Grant Budget:** \$2,608,752



SE 17th STREET MOBILITY HUB, City of Fort Lauderdale

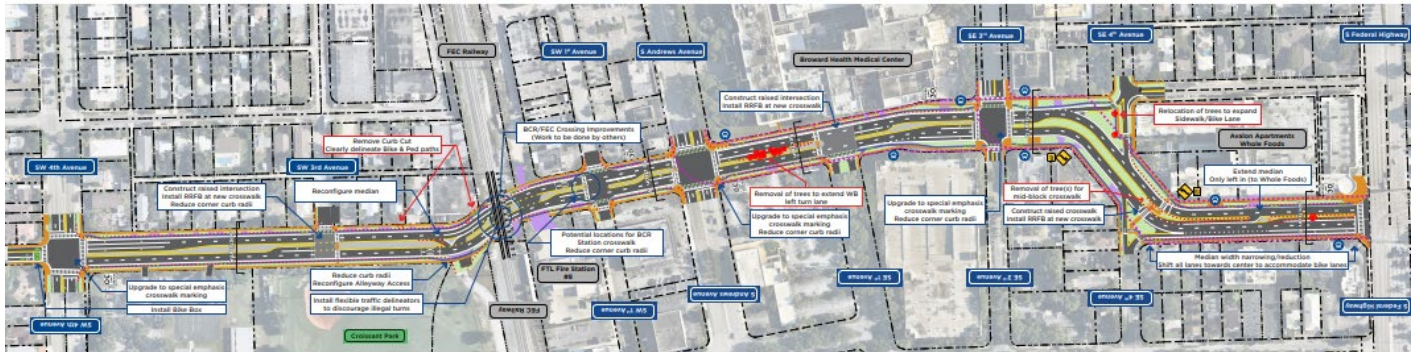

- **Project Summary:** 1-mile of complete streets improvements on SE 17th Street, from SE 9th Avenue to US1/Federal Highway to support pedestrian and bike connectivity with existing transit services.
- **Design Schedule:** Began 9/2025, 30% Plans 3/31/26, 60% Plans 6/15/2026, and final plans 10/30/2026
- **Key Activities since September 2025:**
 - Design started in September 2025.
 - Survey completed in early December 2025.
 - Railroad coordination with Brightline for gate upgrades on-going.
 - Public involvement plan being finalized to include 2 public meetings and 3 commission updates. Consultant has all data collection needed to proceed on schedule.
 - City working with County to discuss opportunity for mast arm signalization upgrades for all three main intersections from old span wire signals.
- **Upcoming Major Milestone:** 30% submittal, 3/31/2026
- **Project Critical Path:** FEC Railroad Design review/FRC updated design in early 2026
- **Anticipated Construction Start:** Spring 2027
- **Anticipated Project Completion:** Spring 2029
- **Project Grant Budget:** \$6,804,000

PEMBROKE ROAD, DOUGLAS ROAD to SR-817/UNIVERSITY DRIVE, City of Pembroke Pines & City of Miramar – FDOT LAP Project

- **MTECC** – unofficial request for MTECC support during construction phase, project is in fiscal year 2027-28.
- **Project Summary:** 1-mile of widening and reconstruction
- **Upcoming Major Milestone:** Design completed by FDOT. ROW Acquisition on-going by FDOT.
- **Project Critical Path:** ROW acquisition
- **Anticipated Construction Start:** Summer 2027
- **Anticipated Project Completion:** Summer 2029
- **Project Funding:** \$14.3 million
