



HD King Property Interim Source Removal - 2015

Project Update - April 2015





HD King Property Interim Source Removal 2015

Project Description: The project entails the removal of contaminated soil from the former electric power generation plant property and backfilling with clean fill material. Restoration goals are to bring the site into compliance with the higher set standards of residential living.

Project Status: The work scheduled for fiscal year 2015 has been completed. Cardno Construction mobilized to the site in February and completed this phase of work by the third week of March. A total of 9,611 tons of contaminated material was removed and hauled to the Okeechobee landfill for disposal. Approximately 16,020 cy of clean fill material was trucked to the site, graded and compacted.

Cardno will continue monitoring the site as required by FDEP and submit all necessary reports by November 2015.


Remaining Work: It is estimated that 10,000 cubic yards of contaminated material remains to be excavated in 2016. The proposed cost for the 2016 work totals \$1,160,000.

Engineering is currently exploring methods and funding sources in order to stock necessary fill material as required for the 2016 backfilling. The material will come from the Phase II portion of the Indian Hills Recreation Area project which is proposed to begin within the next 60 days.



HD King Property Interim Source Removal 2015

2015/2016 Excavation Areas

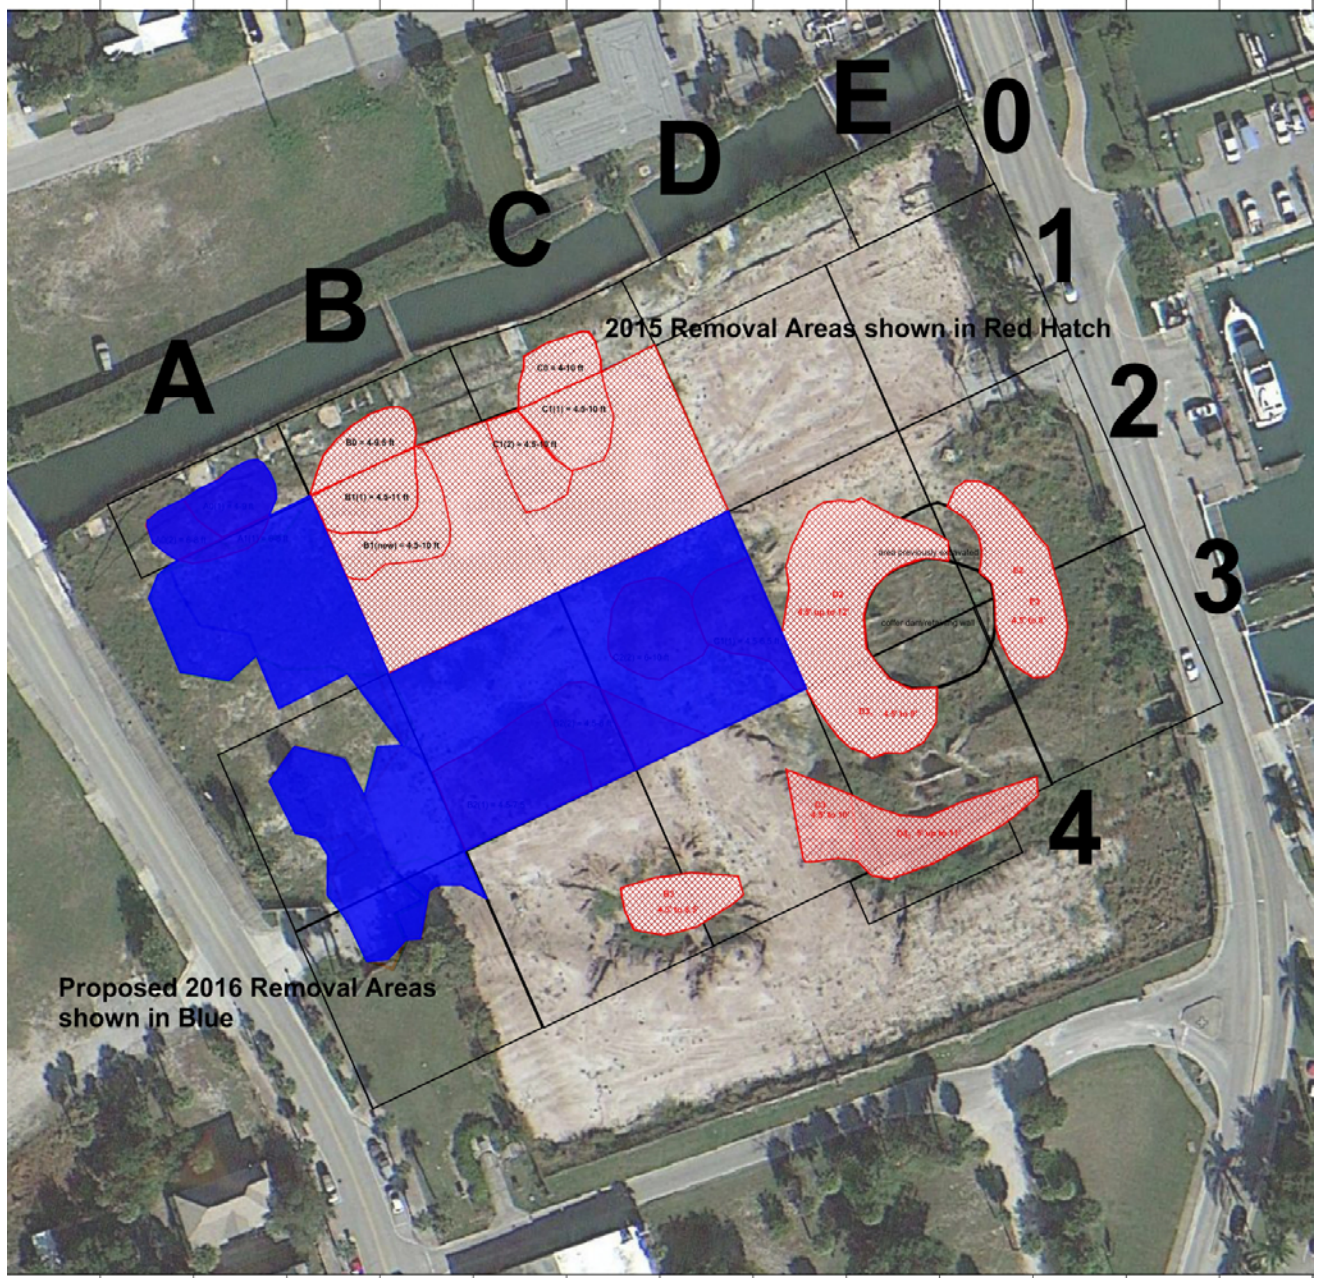

2015 Removal Areas shown in Red Hatch

Proposed 2016 Removal Areas shown in Blue

FORMER HD KING SITE
Prepared by Cardno



HD King Property Interim Source Removal 2015



HD King Property - 2015 Area Finished Backfill - March 25, 2015
