



HD KING PROPERTY


PROJECT UPDATE – JULY 2015

*Prepared By:
Fort Pierce Engineering Department*

HD KING PROPERTY PROJECT UPDATE - JULY 2015

Work completed in 2015

- 9,610 tons of contaminated soil removed
- 31,000 cubic yards of clean material imported from Indian Hills Recreation project.
 - 16,000 utilized to backfill 2015 removal
 - 15,000 stock piled for 2016 work
- Semi-annual test results from ground water monitoring show no significant changes. Requesting FDEP to discontinue monitoring and abandon wells.

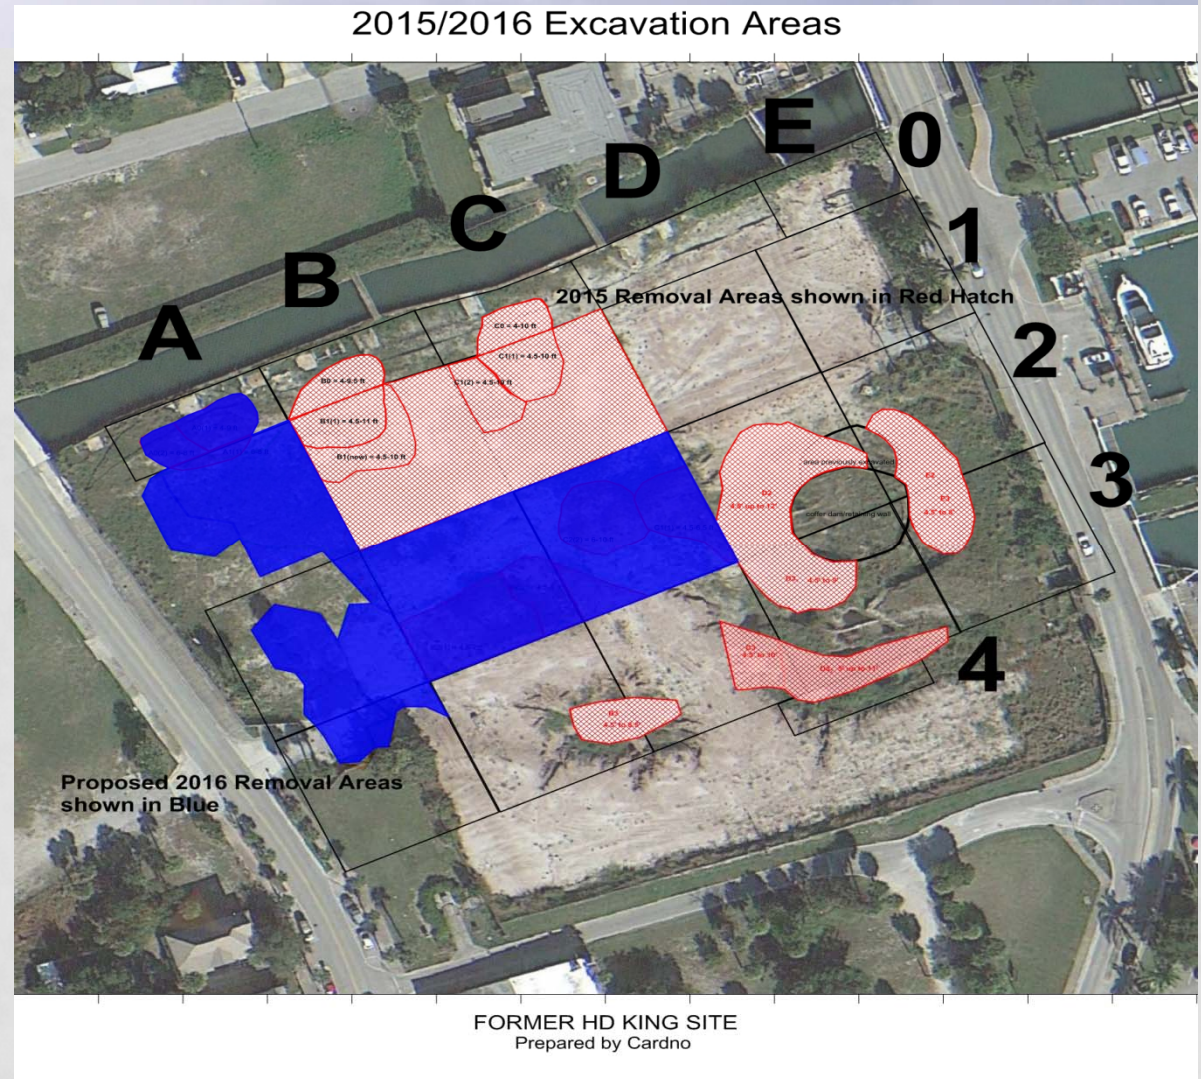

HD KING PROPERTY

PROJECT UPDATE - JULY 2015

Work completed in 2015

- Stock piled material graded to a low profile and seeded to prevent wind blown dust in the downtown area.




HD KING PROPERTY PROJECT UPDATE - JULY 2015

Proposed Work 2016

- An estimated 10,000 tons of material (shown in blue) is planned to be removed in 2016
- The estimated cost for the 2016 work is **\$1,159,389**

Schedule

- Notice to Proceed - **January 2016**
- Mobilization and Source Removal Activities - **January - April 2016**
- Preparation and Submittal of Final Source Removal Report - **June 2016**
- FDEP Approval of ISR Report - **August 2016**
- Preparation of DRC Package - **September 2016**
- Final FDEP Approval and Issuance of SRCO - **November 2016**
- VCTC Preparation - **November/December 2016**

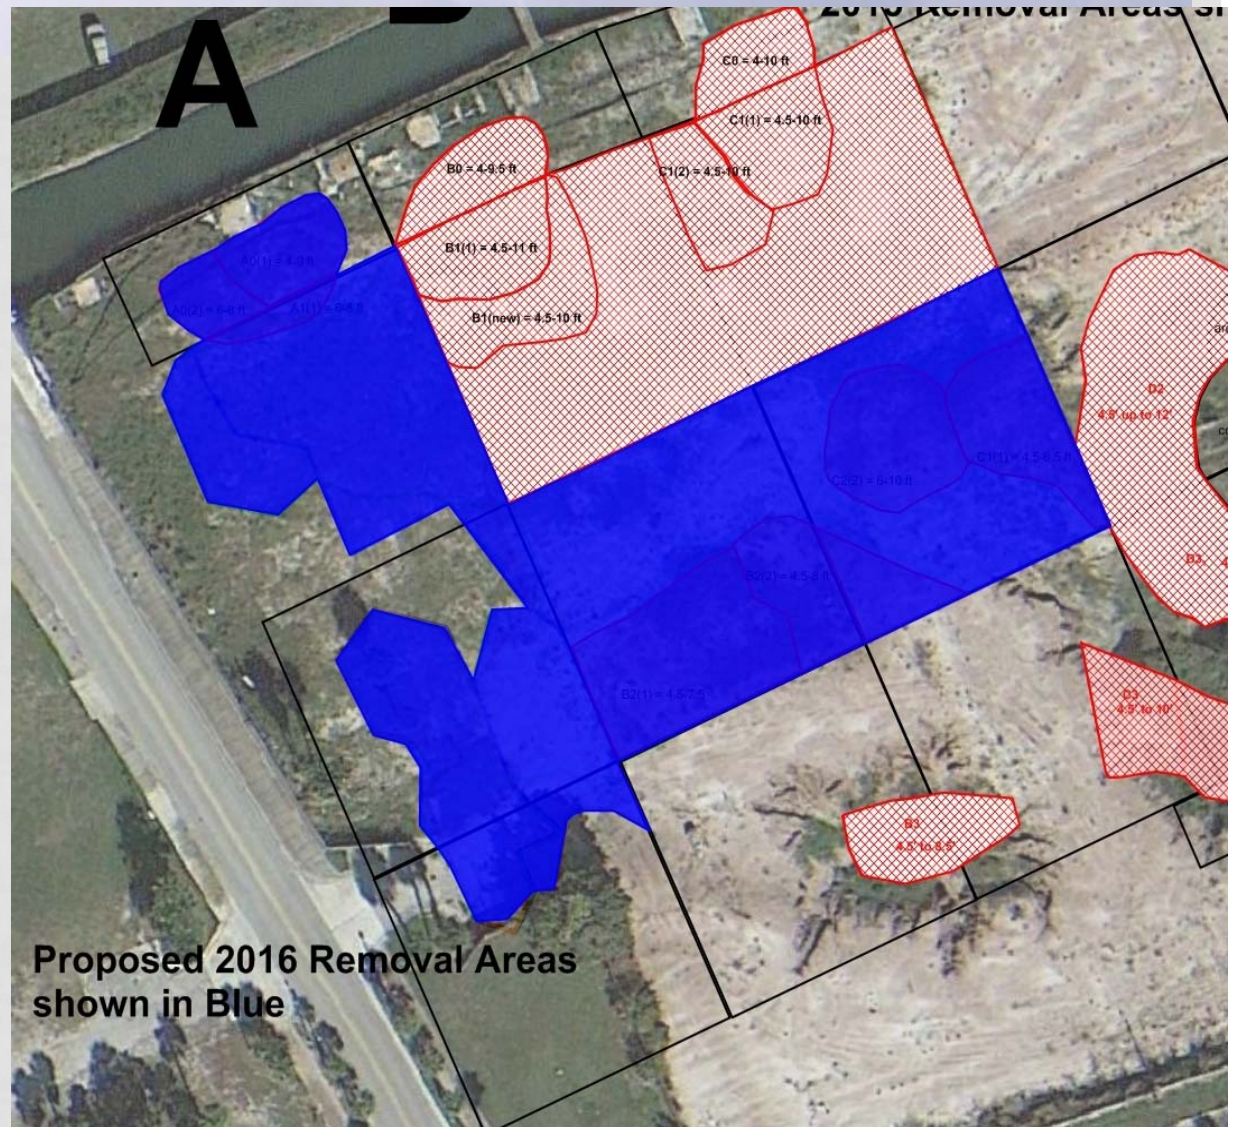



HD KING PROPERTY

PROJECT UPDATE - JULY 2015

Seawall Replacement

- Cardno is currently preparing a proposal for a “Design/Build” contract for replacement of the failing seawall to be constructed concurrently with the 2016 remediation work
