


ID	Task Mode	Task Name	Duration	Start	Finish	Timeline																											
						Apr '24	May '24	Jun '24	Jul '24	Aug '24	Sep '24	Oct '24	Nov '24	Dec '24	Jan																		
1		The Highwaymen Museum	160 days	Fri 5/17/24	Thu 12/26/24	[Red bar spanning from May 17 to Dec 26, 2024]																											
2		CoFP Department Permitting	57 days	Tue 12/19/23	Wed 3/6/24	[Blue bar spanning from Dec 19, 2023 to Mar 6, 2024]																											
3		COA Application Approval	12 days	Tue 12/19/23	Wed 1/3/24	[Blue bar spanning from Dec 19, 2023 to Jan 3, 2024]																											
4		DPCR Application Approval	1 day	Thu 1/4/24	Thu 1/4/24	[Blue bar at Jan 4, 2024]																											
5		Planning Department Prescreen Review	3 days	Thu 1/4/24	Mon 1/8/24	[Blue bar spanning from Jan 4 to Jan 8, 2024]																											
6		DPCR Application Resubmission request from City	0 days	Thu 1/4/24	Thu 1/4/24	[Blue bar at Jan 4, 2024]																											
7		AOR resubmit drawings per 2023 FBC & ASCE codes	9 days	Thu 1/18/24	Tue 1/30/24	[Blue bar spanning from Jan 18 to Jan 30, 2024]																											
8		Planning Department Review/Approval	4 days	Thu 2/8/24	Tue 2/13/24	[Blue bar spanning from Feb 8 to Feb 13, 2024]																											
9		Building Department Permit Forms Intake	16 days	Wed 2/14/24	Wed 3/6/24	[Blue bar spanning from Feb 14 to Mar 6, 2024]																											
10		Low Voltage Permitting	154 days	Fri 3/15/24	Wed 10/16/24	[Black bar spanning from Mar 15 to Oct 16, 2024]																											
11		Low Voltage Scope Coordination	36 days	Fri 3/15/24	Fri 5/3/24	[Blue bar spanning from Mar 15 to May 3, 2024]																											
12		Low Voltage Drawing Submission	50 days	Mon 5/6/24	Fri 7/12/24	[Blue bar spanning from May 6 to Jul 12, 2024]																											
13		Low Voltage Drawing Review/Approval	10 days	Thu 10/3/24	Wed 10/16/24	[Blue bar spanning from Oct 3 to Oct 16, 2024]																											
14		Building Department Permitting	92 days	Thu 3/7/24	Fri 7/12/24	[Black bar spanning from Mar 7 to Jul 12, 2024]																											
15		Permit Review/Approval	50 days	Thu 3/7/24	Wed 5/15/24	[Red bar spanning from Mar 7 to May 15, 2024]																											
16		Owner Fee payment	1 day	Thu 5/16/24	Thu 5/16/24	[Blue bar at May 16, 2024]																											
17		Building Permit Review Revisions	34 days	Fri 5/17/24	Wed 7/3/24	[Blue bar spanning from May 17 to Jul 3, 2024]																											
18		Permit Review/Approval	6 days	Fri 7/5/24	Fri 7/12/24	[Blue bar spanning from Jul 5 to Jul 12, 2024]																											
19		Fire Department Permitting	79 days	Thu 3/21/24	Tue 7/9/24	[Black bar spanning from Mar 21 to Jul 9, 2024]																											
20		Owner Permit Check Payment	21 days	Fri 3/22/24	Fri 4/19/24	[Blue bar spanning from Mar 22 to Apr 19, 2024]																											
21		Building Drawing Submission	1 day	Thu 3/21/24	Thu 3/21/24	[Blue bar at Mar 21, 2024]																											
22		Fire Sprinkler Drawing Submission	1 day	Thu 3/21/24	Thu 3/21/24	[Blue bar at Mar 21, 2024]																											
23		Fire Alarm Drawing Review/Approval	23 days	Mon 5/6/24	Wed 6/5/24	[Blue bar spanning from May 6 to Jun 5, 2024]																											
24		Fire Alarm Permit Resubmission	4 days	Thu 6/6/24	Tue 6/11/24	[Blue bar spanning from Jun 6 to Jun 11, 2024]																											
25		Fire Alarm Permit Review/Approval	15 days	Wed 6/12/24	Tue 7/2/24	[Blue bar spanning from Jun 12 to Jul 2, 2024]																											
26		Fire Sprinkler Permit Review/Approval	20 days	Wed 6/12/24	Tue 7/9/24	[Blue bar spanning from Jun 12 to Jul 9, 2024]																											
27		Low Voltage Permitting	10 days	Thu 10/17/24	Wed 10/30/24	[Black bar spanning from Oct 17 to Oct 30, 2024]																											
28		Low Voltage Drawing Submission	10 days	Thu 10/17/24	Wed 10/30/24	[Blue bar spanning from Oct 17 to Oct 30, 2024]																											

Project: Highwaymen Museum
Date: Thu 9/26/24

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			


ID	Task Mode	Task Name	Duration	Start	Finish	Apr '24	May '24	Jun '24	Jul '24	Aug '24	Sep '24	Oct '24	Nov '24	Dec '24	Jan
29		RFI Directives	43 days	Wed 7/31/24	Fri 9/27/24										
30		RFI #2 - Exterior wall sconces (Pending Owner approval)	43 days	Wed 7/31/24	Fri 9/27/24										
31		RFI #4 - Electrical track lighting (Pending EOR approval)	29 days	Tue 8/20/24	Fri 9/27/24										
32		Change Order Approvals	25 days	Wed 8/21/24	Tue 9/24/24										
33		CO #4 - Bathroom Renovation	23 days	Wed 8/21/24	Fri 9/20/24										
34		CO #5 - Concrete removal & reinstall sidewalk	16 days	Wed 8/21/24	Wed 9/11/24										
35		CO #6 - Repair second floor joists	16 days	Wed 8/21/24	Wed 9/11/24										
36		CO #7 - Sanitary line relocation	1 day	Tue 9/24/24	Tue 9/24/24										
37		Exterior Finishes	52 days	Tue 8/6/24	Wed 10/16/24										
38		Demo exterior concrete stairs / railing - 2nd FL	3 days	Tue 8/6/24	Thu 8/8/24										
39		Remove concrete slab - East	1 day	Tue 9/17/24	Tue 9/17/24										
40		Build exterior stairs & railing - East	2 days	Thu 10/3/24	Fri 10/4/24										
41		Install concrete pad for Generator	2 days	Thu 10/3/24	Fri 10/4/24										
42		Inspection	2 days	Mon 10/7/24	Tue 10/8/24										
43		CO #5 - Concrete removal & reinstall sidewalk	5 days	Thu 9/26/24	Wed 10/2/24										
44		CO #7 - Sanitary line relocation	1 day	Wed 9/25/24	Wed 9/25/24										
45		Relocate domestic water line - East	5 days	Thu 9/26/24	Wed 10/2/24										
46		Stucco	2 days	Mon 10/7/24	Tue 10/8/24										
47		Paint	3 days	Wed 10/9/24	Fri 10/11/24										
48		Awning	3 days	Mon 10/14/24	Wed 10/16/24										
49		Exterior Openings	9 days	Mon 10/7/24	Thu 10/17/24										
50		Remove exterior door & frames	2 days	Mon 10/7/24	Tue 10/8/24										
51		Demo exterior wall for new openings	3 days	Wed 10/9/24	Fri 10/11/24										
52		Frame and set new impact doors / windows	3 days	Mon 10/14/24	Wed 10/16/24										
53		Inspection	1 day	Thu 10/17/24	Thu 10/17/24										
54		Interior Finishes	73 days	Thu 9/12/24	Mon 12/23/24										
55		Water Damage Repairs / Select Demo work	17 days	Thu 9/12/24	Fri 10/4/24										
56		Demo existing AHU system - 1st FL	4 days	Mon 9/30/24	Thu 10/3/24										

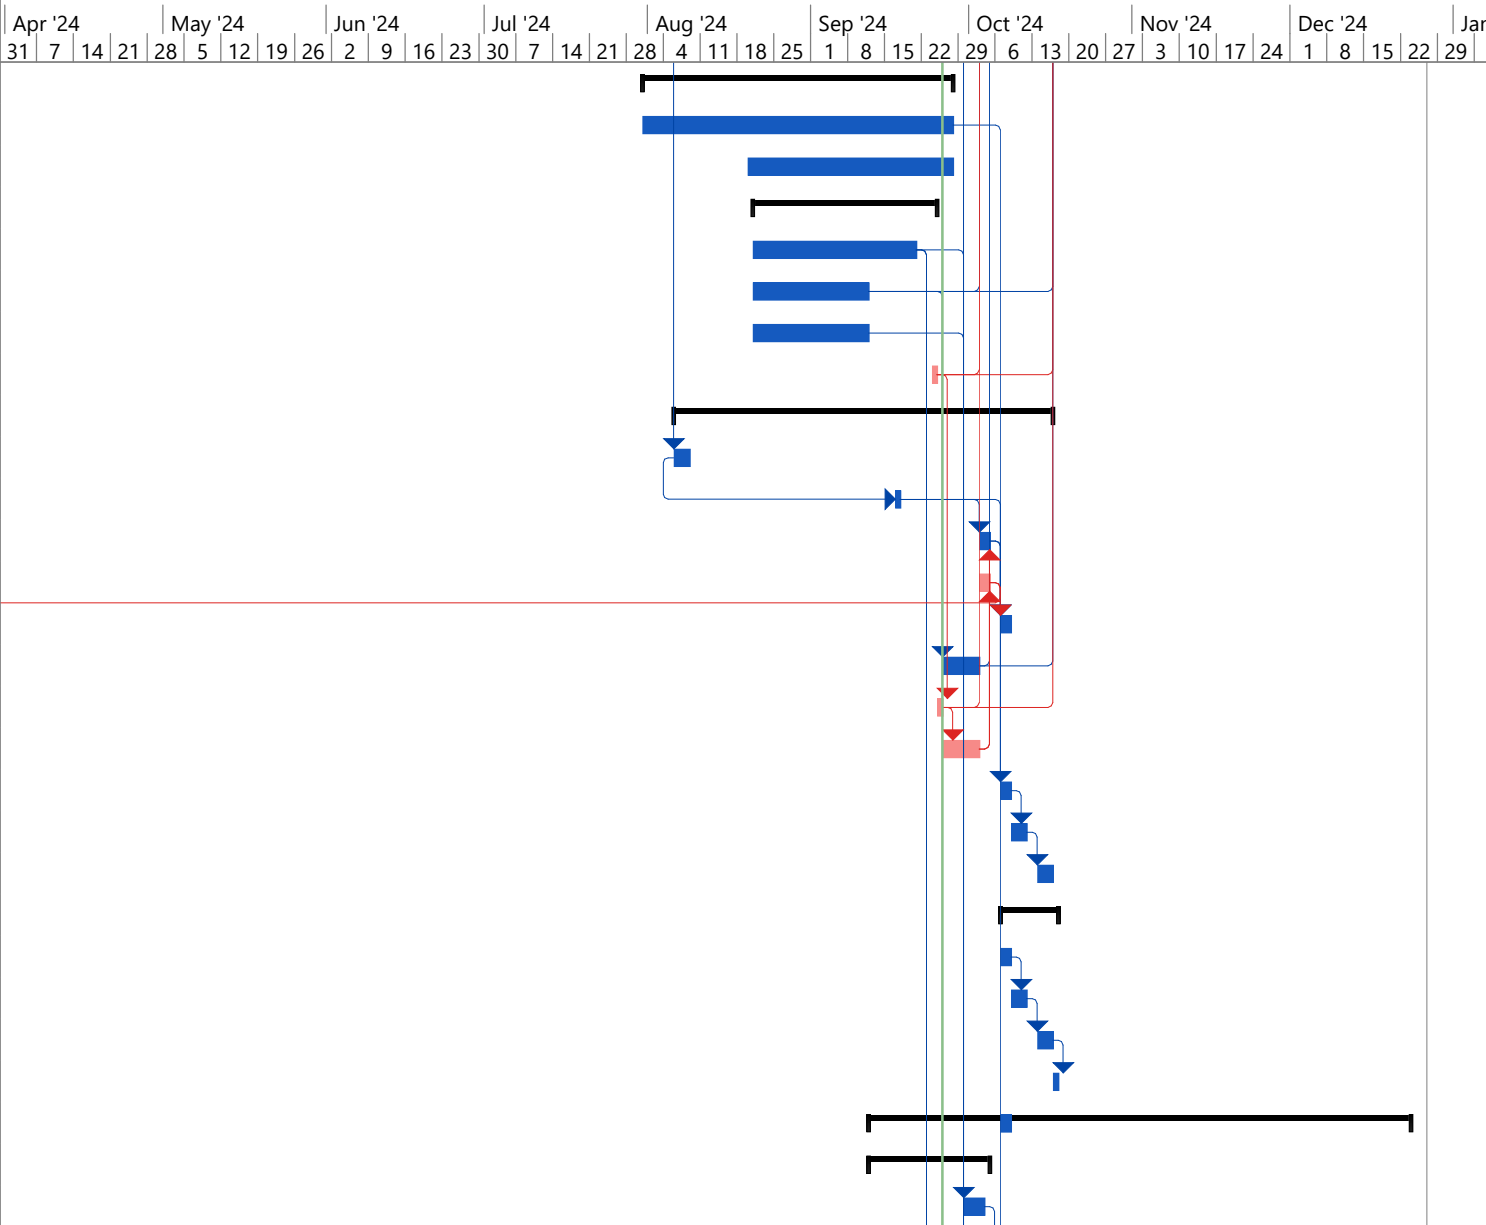

Project: Highwaymen Museum
Date: Thu 9/26/24

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			

ID	Task Mode	Task Name	Duration	Start	Finish	Apr '24	May '24	Jun '24	Jul '24	Aug '24	Sep '24	Oct '24	Nov '24	Dec '24	Jan
85		Frame and insulate new Electrical room - 1st FL	2 days	Mon 10/21/24	Tue 10/22/24										
86		Inspection	1 day	Wed 10/23/24	Wed 10/23/24										
87		Fire Protection/Sprinkler	7 days	Mon 9/30/24	Tue 10/8/24										
88		Re-route O/H Fire Sprinkler -1st FL	5 days	Mon 9/30/24	Fri 10/4/24										
89		Inspection	2 days	Mon 10/7/24	Tue 10/8/24										
90		Electrical	6 days	Mon 10/7/24	Mon 10/14/24										
91		Generator 80W connection	2 days	Mon 10/7/24	Tue 10/8/24										
92		Inspection	1 day	Wed 10/9/24	Wed 10/9/24										
93		Electrical Trim - 2nd FL	3 days	Mon 10/7/24	Wed 10/9/24										
94		Electrical Trim -1st FL	3 days	Thu 10/10/24	Mon 10/14/24										
95		Low Voltage installations	5 days	Mon 10/7/24	Fri 10/11/24										
96		Inspection	1 day	Mon 10/14/24	Mon 10/14/24										
97		Drywall	34 days	Wed 10/9/24	Mon 11/25/24										
98		Install drywall walls and ceilings - 2nd FL	3 days	Thu 10/24/24	Mon 10/28/24										
99		Frame new soffits - 1st FL	2 days	Wed 10/9/24	Thu 10/10/24										
100		Install drywall walls and ceilings - 1st FL	4 days	Tue 10/29/24	Fri 11/1/24										
101		Screw Inspection	1 day	Tue 11/5/24	Tue 11/5/24										
102		Tape and float drywall - 2nd FL	6 days	Wed 11/6/24	Wed 11/13/24										
103		Tape and float drywall - 1st FL	6 days	Thu 11/14/24	Thu 11/21/24										
104		Electrical room racks - 1st FL	2 days	Fri 11/22/24	Mon 11/25/24										
105		Flooring	12 days	Thu 11/14/24	Fri 11/29/24										
106		Install Tile - 2nd FL	6 days	Thu 11/14/24	Thu 11/21/24										
107		Install Tile - 1st FL	6 days	Fri 11/22/24	Fri 11/29/24										
108		Interior Doors and Trim	10 days	Mon 12/2/24	Fri 12/13/24										
109		Install Interior Door Frames	3 days	Mon 12/2/24	Wed 12/4/24										
110		Inspection	1 day	Thu 12/5/24	Thu 12/5/24										
111		Install Doors	2 days	Fri 12/6/24	Mon 12/9/24										
112		Install Door Hardware	1 day	Tue 12/10/24	Tue 12/10/24										

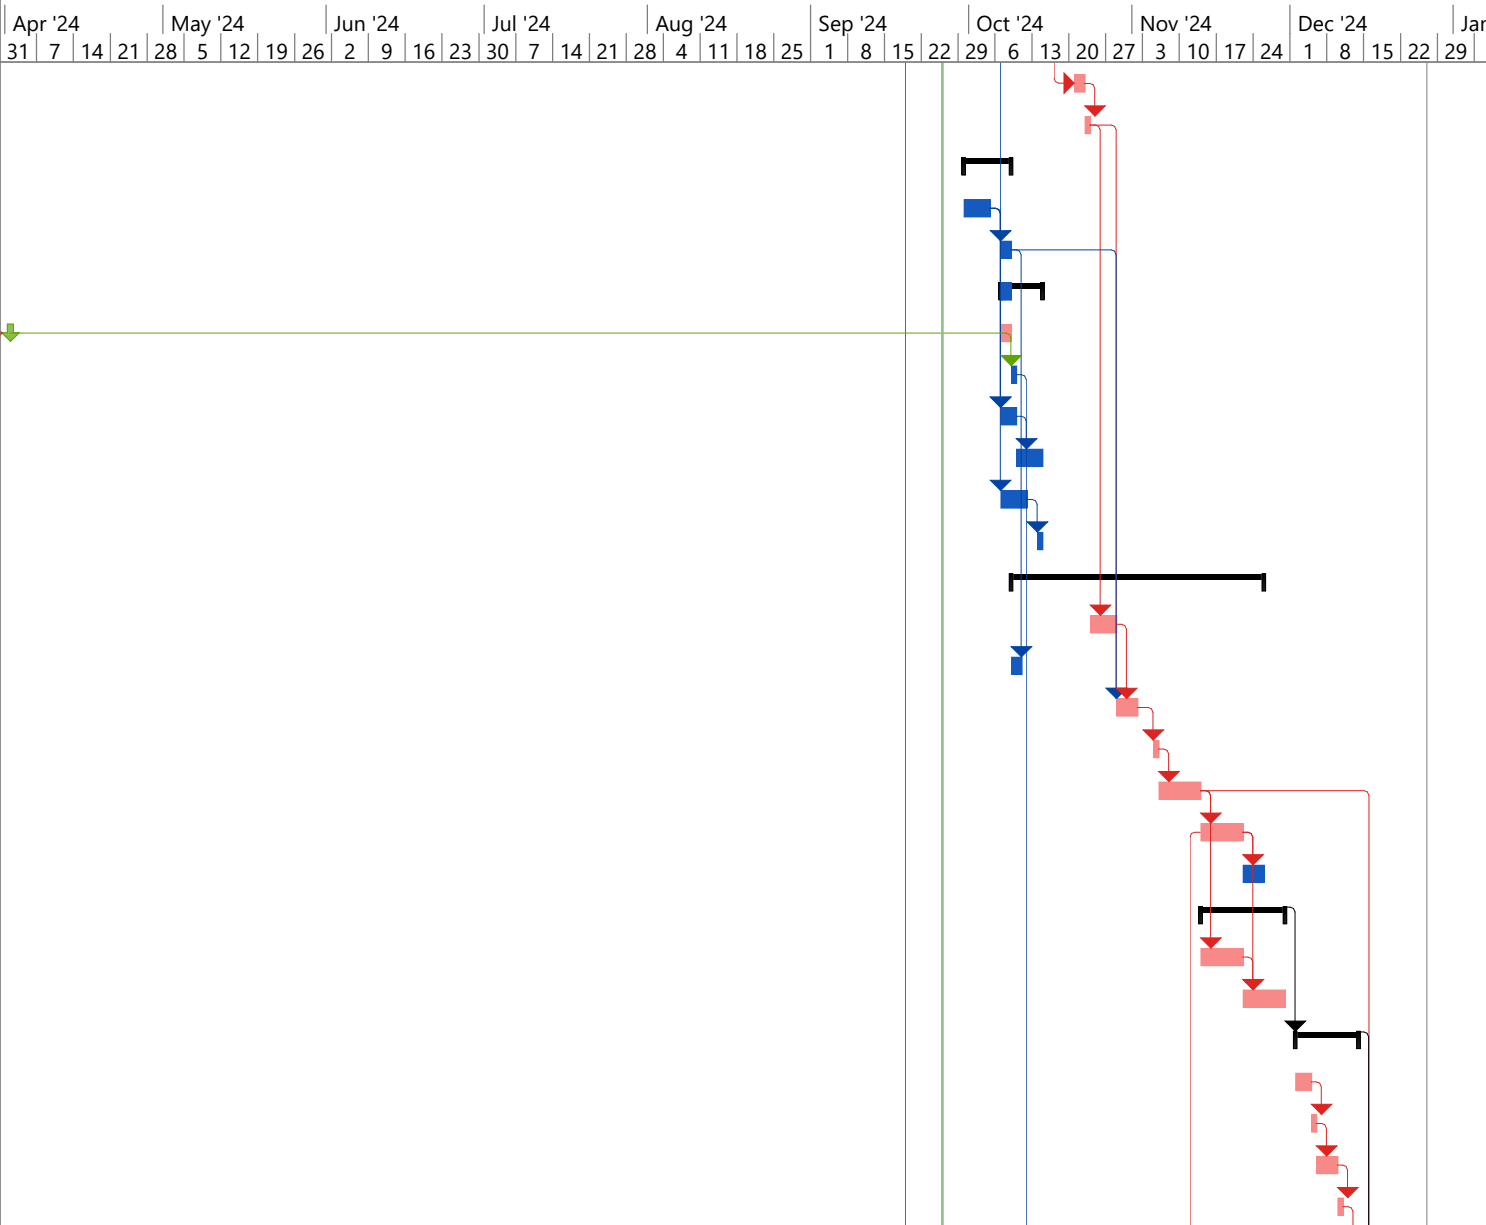

Project: Highwaymen Museum
Date: Thu 9/26/24

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			

ID	Task Mode	Task Name	Duration	Start	Finish	Apr '24	May '24	Jun '24	Jul '24	Aug '24	Sep '24	Oct '24	Nov '24	Dec '24	Jan
113		Install Trim	3 days	Wed 12/11/24	Fri 12/13/24										
114		Interior Paint	5 days	Mon 12/16/24	Fri 12/20/24										
115		Prime all walls and ceilings - 2nd FL	5 days	Mon 12/16/24	Fri 12/20/24										
116		Paint all walls and ceilings - 1st FL	5 days	Mon 12/16/24	Fri 12/20/24										
117		Cabinets	70 days	Tue 9/17/24	Mon 12/23/24										
118		Measure and Fabricate Countertops	10 days	Tue 9/17/24	Mon 9/30/24										
119		Install Kitchen countertops & cabinets - 1st FL	4 days	Tue 10/1/24	Fri 10/4/24										
120		Install Kitchen appliances	1 day	Mon 12/23/24	Mon 12/23/24										
121		Sitework	11 days	Thu 10/10/24	Thu 10/24/24										
122		Install gates & fencing	5 days	Mon 10/14/24	Fri 10/18/24										
123		Fence inspection	1 day	Mon 10/21/24	Mon 10/21/24										
124		New CMU wall for generator- North	2 days	Thu 10/10/24	Fri 10/11/24										
125		Pour new concrete stairs - East	3 days	Mon 10/14/24	Wed 10/16/24										
126		Inspection	2 days	Thu 10/17/24	Fri 10/18/24										
127		Paint CMU wall for generator	1 day	Mon 10/21/24	Mon 10/21/24										
128		Install brick paving	3 days	Tue 10/22/24	Thu 10/24/24										
129		Final Acceptance	4 days	Mon 12/23/24	Thu 12/26/24										
130		Perform final walk-through inspection	1 day	Mon 12/23/24	Mon 12/23/24										
131		Complete punch list items	2 days	Tue 12/24/24	Wed 12/25/24										
132		Final cleanup	1 day	Thu 12/26/24	Thu 12/26/24										

Project: Highwaymen Museum
Date: Thu 9/26/24

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			
