



ROAD BOND & PASS THROUGH FINANCING

Construction Summary Report


County Judge
Dan Gattis

Commissioners
Lisa Birkman
Cynthia Long
Valerie Covey
Ron Morrison

February 2010

WWW.ROADBOND.ORG

Volume IX - Issue No. 2

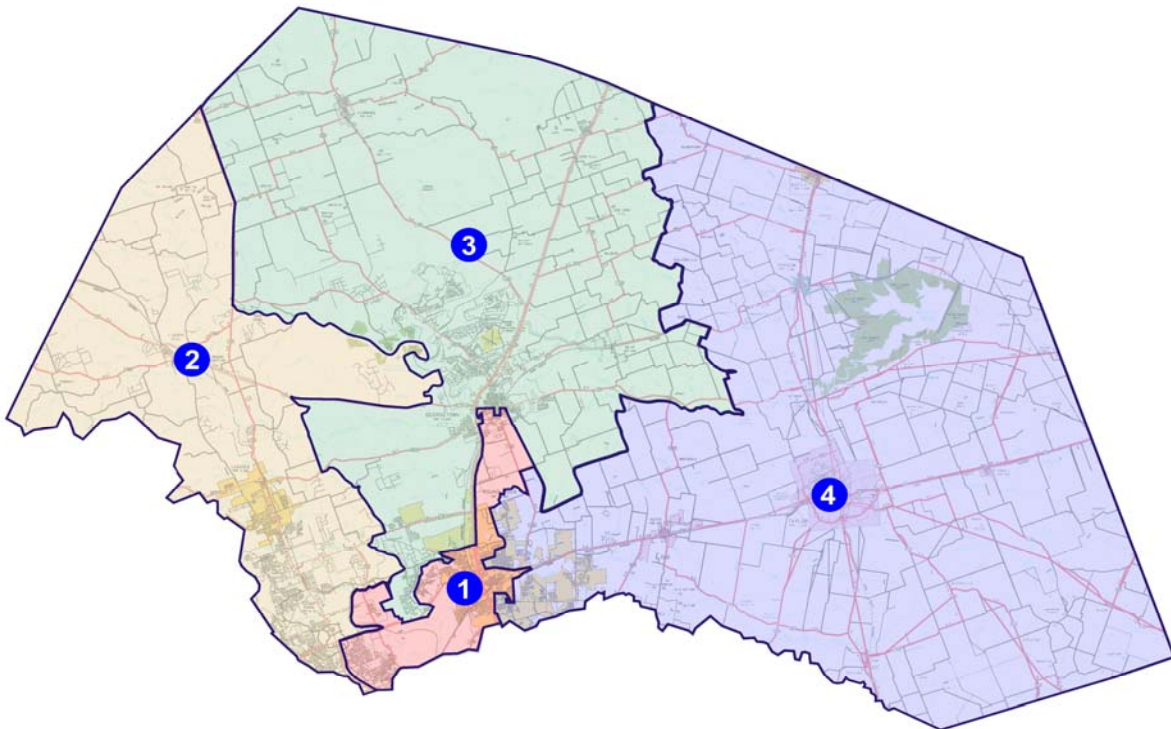

Presented By:



PRIME
STRATEGIES,
INC.

HNTB

Table of Contents



Completed Projects.....	1
PRECINCT No. 1 – Commissioner Lisa Birkman.....	2
CR 111 – Westinghouse Rd (Hewlett Loop to FM 1460)	3
S.E. Inner Loop at FM 1460	6
Pond Springs Widening (McNeil Rd to US 183)	7
PRECINCT No. 2 – Commissioner Cynthia Long	10
San Gabriel Pkwy, Phase 1 (Halsey Drive to CR 273 Extension)	11
Ronald W. Reagan Blvd. South, Ph. 2 (FM 2243 to SH 29)	12
CR 175, Phase 2A Extension (Regional Park to Creekside Meadows)	15
US 183 at FM 3405 (Traffic Signal Construction).....	17
Pass Through: US 183 (Riva Ridge Rd to SH 29)	19
CR 214, Phase 2A (Rolling Hills to San Gabriel Ranch Road).....	21
US 183 at FM 3405 (Intersection Improvements).....	23
PRECINCT No. 3 – Commissioner Valerie Covey	24
Williams Drive (DB Wood Rd to FM 3405).....	25
Pass Through: RM 2338 Phase 2 (FM 3405 to Ronald Reagan Blvd).....	27
PRECINCT No. 4 – Commissioner Ron Morrison	28
Pass Through: US 79, Section 5B (FM 1063 to Milam County Line).....	29
Pass Through: US 79, Section 5A (East of Taylor to FM 1063).....	31
Chandler Road, Phase 3B (CR 368/369 to SH 95)	33
Business 79 Drainage Improvements	35

WILLIAMSON COUNTY

ROAD BOND PROGRAM

COMPLETED PROJECTS

SUBSTANTIAL CONSTRUCTION COMPLETE/OPEN TO TRAFFIC - AS OF JANUARY 2010

Precinct 1

- Pond Springs Road (signal) – July 2002
- McNeil Road, Phase 1 – Jan 2005
- McNeil Road, Phase 2 – Feb 2007
- Lakeline Blvd – July 2007
- RM 620, Phase 1 – January 2009
- SE Inner Loop @ FM 1460 – November 2009

Precinct 2

- Cedar Hollow at SH 29 (signal) – Aug 2002
- FM 1869 at SH 29 (signal) – Aug 2002
- County Road 175 – June 2003
- River Bend Oaks – Aug 2003
- County Road 200 – Sept 2003
- Ronald Reagan Blvd, South Ph. 1 – Dec 2004
- County Road 214 – Feb 2005
- County Road 258 – Sept 2006
- San Gabriel Pkwy, Ph. 1 – Feb 2007
- Ronald Reagan Blvd North Ph. 1 – Sept 2007
- Ronald Reagan Blvd South, Ph. 2 – Feb 2008
- US 183 @ San Gabriel Pkwy – Feb 2008
- CR 175 Phase 2A – Jan 2010

Precinct 3

- DB Wood/Cedar Breaks – June 2004
- Cedar Breaks Road – June 2004
- Georgetown Inner Loop East Extension – Aug 2004
- CR 152 Bridge Replacement – Sept 2004
- Inner Loop East (CR 151 to Bus 35) – Oct 2005
- Ronald Reagan Blvd North, Ph. 2 – May 2008
- 12" Water Main Relocation for SH 29 Widening – June 2008
- SH 29 / CR 104, Ph. 1 – July 2008
- IH 35 @ SH 29 Turnarounds (Pass Through Financing) – August 2008

Precinct 4


- Wooden Bridges (CR 390, 406 & 427) – Nov 2002
- County Road 412 – Aug 2003
- CR 368 & 369 – Aug 2003
- County Road 300 – Dec 2003
- CR 424 Bridge Replacement – Jan 2004
- Chandler Rd. Extension, Ph. 1 – March 2005
- County Road 112, Ph. 1 – Aug 2005
- County Road 137 – Oct 2005
- Limmer Loop, Ph. 1A – July 2006
- Chandler Rd, Ph. 2 – Dec 2007
- Limmer Loop, Ph. 1B – March 2008
- Limmer Loop, Ph. 1C – October 2008

PRECINCT 1

COMMISSIONER BIRKMAN

Completed/Open to Traffic

- 1.01 Anderson Mill Rd.
- 1.02 Avery Ranch Blvd
- 1.03 Lake Creek Drainage – Phase 1
- 1.04 Lake Creek Drainage – Phase 2
- 1.05 Lakeline Blvd.
- 1.06 McNeil Road – Phase 1
- 1.07 McNeil Road – Phase 2
- 1.08 Pond Springs at Turtle Rock Signal
- 1.09 RM 620 Feasibility Study
- 1.10 Wyoming Springs North Study
- 1.11 RM 620 Interim Improvements – Phase 1
- 1.16 SE Inner Loop @ FM 1460

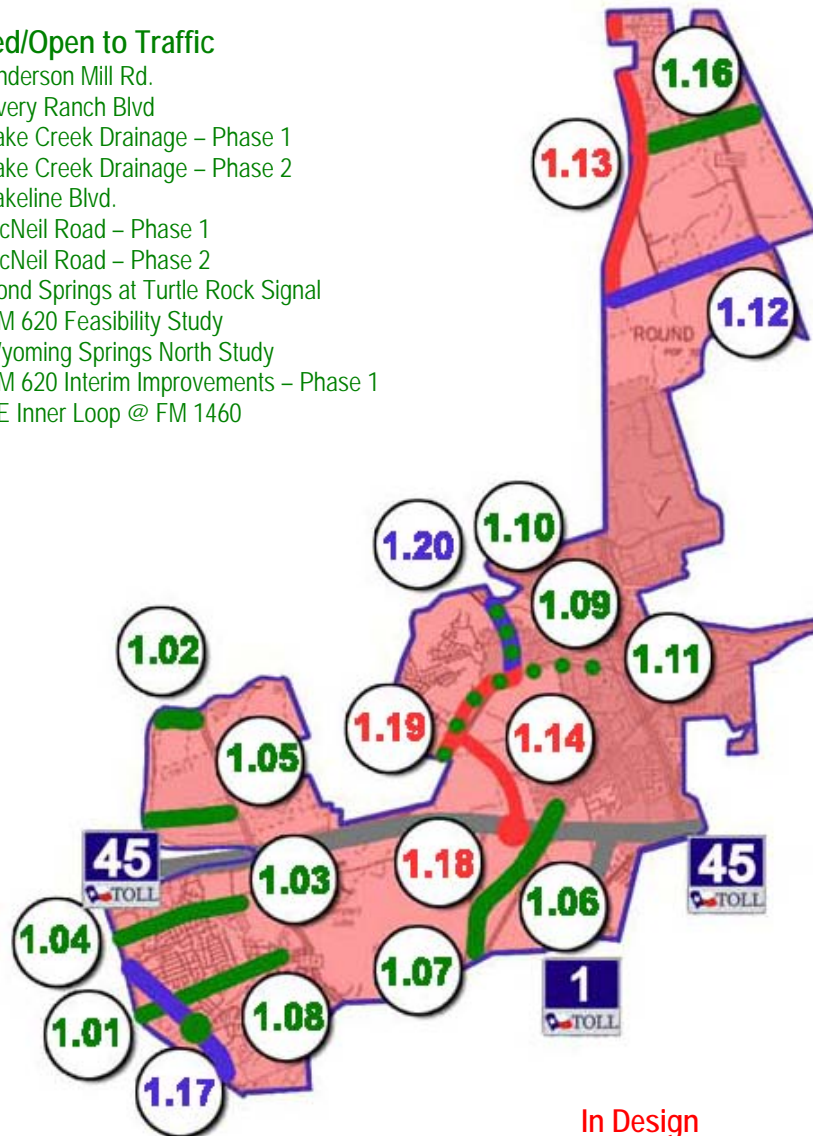


Under Construction / Bidding

- 1.12 CR 111 (Westinghouse Rd)
- 1.17 Pond Springs Road
- 1.20 Wyoming Springs

In Design

- 1.13 IH-35 Northbound Frontage Rd and Ramps
- 1.14 O'Connor Extension
- 1.18 O'Connor Overpass at SH 45
- 1.19 RM 620: Cornerwood Dr to Wyoming Springs

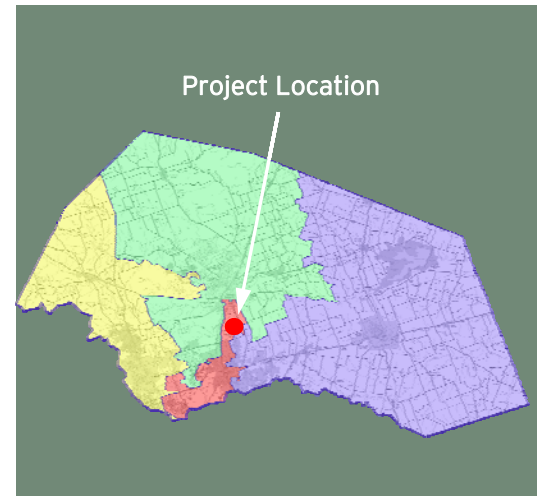

CR 111 (WESTINGHOUSE ROAD) (Hewlett Loop to FM 1460)

Project Length: 1.99 Miles
Roadway Classification: Minor Arterial
Roadway Section: Transitions from four-lane w/ center two-way turn lane on the west end to four-lane divided on the east end

Project Schedule: June 2008 - August 2010
Estimated Construction Cost: \$6.6 Million



JANUARY 2010 IN REVIEW

1/8/2010 - The Contractor is currently working on processing the first course of flex base on the proposed westbound lanes of CR 111 from just east of Scenic Lake to FM 1460. They have completed the installation of the triple barrel 36-inch RCP at FM 1460. They have also started excavating to subgrade on the proposed southbound lanes of FM 1460.

1/22/2010 - The Contractor processed flex base on the proposed southbound lanes of FM 1460 and on the westbound lanes of CR 111 from FM 1460 to Scenic Lake. They are scheduled to start on the west half of the culvert extension the last week of January, weather permitting.

1/29/2010 - The Contractor worked on processing the final course of flex base on the proposed southbound lanes of FM 1460 from the north end to the cemetery driveway and from CR 111 to the south tie-in. They also worked on the final course of flex base on the westbound lanes of CR 111 from FM 1460 to Scenic Lake. They have completed the west half extension of the box culvert on FM 1460. The last of the curb and gutter placement on CR 111 is scheduled for next week.



Design Engineer: Huggins/Seiler & Associates
Contractor: J.C. Evans Construction
Construction Observation:
Kenneth Marak, Williamson County

Williamson County
Road Bond Program

CR 111 - Westinghouse Rd. (Hewlett Loop to FM 1460)
Project No. 08WC608

Original Contract Price = \$5,864,053.94

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Anticipated Work Complete</u>	<u>Work Accepted</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
4/2/2008	4/15/2008	6/6/2008	6/16/2008	8/14/2010		730	60	790

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoice Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time</u>	<u>Liquidated Damages</u>	<u>Total Liq Damages</u>
1	6/16/2008	6/30/2008	15	\$273,125.71	\$273,125.71	\$14,375.04	\$14,375.04	5	2	\$0.00	\$0.00
2	7/1/2008	7/31/2008	31	\$690,458.44	\$963,584.15	\$36,339.92	\$50,714.96	17	6	\$0.00	\$0.00
3	8/1/2008	8/31/2008	31	\$405,777.61	\$1,369,361.76	\$21,356.71	\$72,071.67	25	10	\$0.00	\$0.00
4	9/1/2008	9/30/2008	30	\$410,275.17	\$1,779,636.93	\$21,593.43	\$93,665.10	31	14	\$0.00	\$0.00
5	10/1/2008	10/31/08	31	\$170,855.60	\$1,950,492.53	\$8,992.40	\$102,657.50	34	17	\$0.00	\$0.00
6	11/1/2008	11/30/08	30	\$328,636.79	\$2,279,129.32	\$17,296.67	\$119,954.17	40	21	\$0.00	\$0.00
7	12/1/2008	12/31/08	31	\$183,573.77	\$2,462,703.09	\$9,661.78	\$129,615.95	43	25	\$0.00	\$0.00
8	1/1/2009	1/31/2009	31	\$85,656.15	\$2,548,359.24	\$4,508.22	\$134,124.17	45	29	\$0.00	\$0.00
9	2/1/2009	2/28/2009	28	\$199,204.04	\$2,747,563.28	\$10,484.42	\$144,608.59	48	33	\$0.00	\$0.00
10	3/1/2009	3/31/2009	31	\$148,110.31	\$2,895,673.59	\$7,795.28	\$152,403.87	51	37	\$0.00	\$0.00
11	4/1/2009	4/30/2009	30	\$516,671.71	\$3,412,345.30	\$27,193.25	\$179,597.12	60	40	\$0.00	\$0.00
12	5/1/2009	5/31/2009	31	\$226,555.61	\$3,638,900.91	\$11,923.98	\$191,521.10	65	44	\$0.00	\$0.00
13	6/1/2009	6/30/2009	30	\$249,244.85	\$3,888,145.76	\$13,118.15	\$204,639.25	69	48	\$0.00	\$0.00
14	7/1/2009	7/31/2009	31	\$332,593.17	\$4,220,738.93	\$17,504.90	\$222,144.15	75	52	\$0.00	\$0.00
15	8/1/2009	8/31/2009	31	\$245,723.19	\$4,466,462.12	\$12,932.80	\$235,076.95	79	56	\$0.00	\$0.00
16	9/1/2009	9/30/2009	30	\$296,925.12	\$4,763,387.24	\$15,627.64	\$250,704.59	84	60	\$0.00	\$0.00
17	10/1/2009	10/31/09	31	\$135,901.82	\$4,899,289.06	\$7,152.73	\$257,857.32	78	64	\$0.00	\$0.00
18	11/1/2009	11/30/09	30	\$144,217.19	\$5,043,506.25	\$7,590.38	\$265,447.70	80	67	\$0.00	\$0.00
19	12/1/2009	12/31/09	31	\$77,935.90	\$5,121,442.15	\$4,101.89	\$269,549.59	81	71	\$0.00	\$0.00
20	1/1/2010	1/31/2010	31	\$54,006.73	\$5,175,448.88	\$2,842.46	\$272,392.05	82	75	\$0.00	\$0.00

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
01	09/23/2008	6,660.00	6,660.00

4D: Third Party Accommodation. Other. The Contractor installed permanent fencing along the ROW per an agreement made with the Property owner of Parcel 21 (NNP-Terra Vista. LP) and Williamson County prior to construction. The Contractor was also directed to install temporary fencing on Parcel 3 to keep the property owners cows off of the ROW.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
02	10/07/2008	100,144.67	106,804.67

6B: Untimely ROW/Utilities. Right-of-Way not clear (County responsibility for ROW). The property owner agreed to donate the ROW in exchange for the work associated with this Change Order: the installation of steel sleeve encasements for future utilities, the upgrade of existing driveways, and the addition of new driveways.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
03	03/10/2009	42,796.26	149,600.93

3F: County Convenience. Additional work desired by the County. An additional turn lane/median opening and a street stub-out is being added at the Terra Vista Track. 1B: Design Error or Omission. Other. Erosion control items are being added that were left out of the original plan sheets. These items include topsoil, seeding, and rip rap for the median noses in all of the proposed median islands.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
04	03/30/2009	2,760.00	152,360.93

2J: Differing Site Conditions (unforeseeable). Other. In order to complete the driveway installation at sta. 77+50, it was necessary to remove an existing entrance with gates. This change order accounts for costs incurred by the Contract to replace the entrance.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
05	04/03/2009	-92,636.54	59,724.39

5B: Contractor Convenience. Contractor requested change in the sequence and/or method of work. 3H: County Convenience. Cost savings opportunity discovered during construction. After additional testing on the existing subgrade, it was determined that the lime treatment original specified was not necessary. With the Engineer's and the County's concurrence, the Contractor opted to undercut the existing subgrade by 8 inches and placed flex base in lieu of the 8 inches of lime treated subgrade.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
06	05/08/2009	16,730.56	76,454.95

4B: Third Party Accommodation. Third party requested work: The Developer requested the installation of additional driveways and gates on the Madison Property. The Developer has submitted payment to Williamson County.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
07	05/08/2009	2,400.00	78,854.95

2G: Differing Site Conditions. Unadjusted Utility. The Contractor relocated an existing Flush Valve Hydrant that was in conflict with the proposed rip rap slope on the NW corner of Park Central Drive.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
08	10/20/2009	686,352.92	765,207.87

3F: County Convenience. Additional work desired by the County. This Change Order accounts for additional costs associated with widening and realigning the FM 1460 Intersection at Westinghouse Rd. Sixty (60) days were added to the Contract schedule.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
09	02/12/2010	5,000.00	770,207.87
3E: County Convenience. Reduction of future maintenance. This Change Order accounts for cost associated the construction of an underdrain from the median nose just east of Park Central to the south side of the roadway, including a tie-in the storm drain system.			
			Adjusted Price = \$6,634,261.81

S.E. Inner Loop @ FM 1460
Project No. 09WC708

Original Contract Price = \$889,492.48

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantially Complete</u>	<u>Work Accepted</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
3/25/2009	4/21/2009	5/22/2009	6/1/2009	11/5/2009		163	0	163


<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoice Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time Used</u>	<u>Liquidated Damages</u>	<u>Total Liq Damages</u>
1	6/1/2009	6/30/2009	30	\$102,851.51	\$102,851.51	\$11,427.95	\$11,427.95	13	18	\$0.00	\$0.00
2	7/1/2009	7/31/2009	31	\$79,130.70	\$181,982.21	\$8,792.30	\$20,220.25	23	37	\$0.00	\$0.00
3	8/1/2009	8/31/2009	31	\$161,496.94	\$343,479.15	\$17,944.10	\$38,164.35	43	56	\$0.00	\$0.00
4	9/1/2009	9/30/2009	30	\$178,603.64	\$522,082.79	\$19,844.85	\$58,009.20	65	75	\$0.00	\$0.00
5	10/1/2009	10/31/09	31	\$302,954.22	\$825,037.01	\$-41,171.71	\$16,837.49	95	94	\$0.00	\$0.00
6	11/1/2009	11/30/09	5	\$40,139.30	\$865,176.31	\$819.17	\$17,656.66	99	97	\$0.00	\$0.00

1/29/2010 Comments - Contractor continues to work on completing punch list items, including establishing vegetative cover.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
01	10/27/2009	-77.88	-77.88

2G: Differing Site Conditions. Unadjusted utility (unforeseeable): The plans originally called for 3-inch PVC Conduit. However, the proposed 3-inch PVC Conduit will not fit into the electrical service and, at the Contractor's request, is being revised to 2-inch PVC Conduit.

Adjusted Price = \$889,414.60

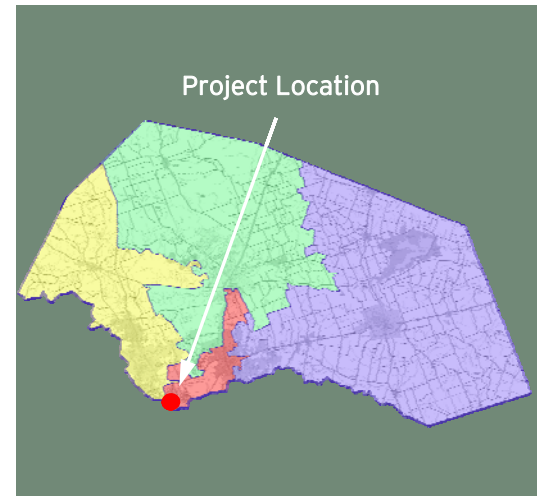

POND SPRINGS WIDENING

(McNeil Road to US 183)

Project Length: 1.84 Miles

Roadway Classification: Minor Arterial

Roadway Section: Two-lane w/ a center two-way turn lane

Project Schedule: June 2009 - March 2010

Estimated Construction Cost: \$3.5 Million



JANUARY 2010 IN REVIEW

1/8/2010 - Subgrade and flex base work continues on the southbound lane widening starting from the north end working south. All cross culvert widening is complete. Sidewalk excavation and installation continues throughout on the east side of the project, and is approximately 85% complete. Driveway pipe and ditch work continues on the west side of Pond Springs. Paving has begun which includes driveways and the road widening on the east side of the project.

1/22/2010 - Riprap placement has begun throughout the project. Level up paving on the proposed northbound lane is complete. Driveways on the east side should all have the first course of paving complete next week.

1/29/2010 - Riprap placement continues throughout the project. Driveway pipe and ditch work continues on the west side of Pond Springs. The first course of paving is complete on the east side driveways. Subgrade and flex base work continues on the proposed southbound lane.



Design Engineer: URS Corporation
Contractor: RGM Constructors
Construction Observation:
Jerry Batten, Williamson County

Williamson County
Road Bond Program

Pond Springs Widening (McNeil Rd to US 183)
Project No. 09WC710

Original Contract Price = \$3,167,595.05

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Anticipated Work Complete</u>	<u>Work Accepted</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
5/6/2009	5/12/2009	6/3/2009	6/12/2009	3/20/2010		150	120	270

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoice Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time Used</u>	<u>Liquidated Damages</u>	<u>Total Liq Damages</u>
1	6/24/2009	6/30/2009	7	\$152,121.44	\$152,121.44	\$16,902.38	\$16,902.38	5	3	\$0.00	\$0.00
2	7/1/2009	7/31/2009	31	\$214,799.85	\$366,921.29	\$23,866.65	\$40,769.03	13	14	\$0.00	\$0.00
3	8/1/2009	8/31/2009	31	\$218,310.42	\$585,231.71	\$24,256.72	\$65,025.75	20	26	\$0.00	\$0.00
4	9/1/2009	9/30/2009	30	\$185,674.01	\$770,905.72	\$20,630.44	\$85,656.19	27	37	\$0.00	\$0.00
5	10/1/2009	10/31/09	31	\$77,230.62	\$848,136.34	\$8,581.18	\$94,237.37	29	48	\$0.00	\$0.00
6	11/1/2009	11/30/09	30	\$235,853.77	\$1,083,990.11	\$26,205.98	\$120,443.35	38	59	\$0.00	\$0.00
7	12/1/2009	12/31/09	31	\$231,299.76	\$1,315,289.87	\$25,699.97	\$146,143.32	46	71	\$0.00	\$0.00
8	1/1/2010	1/31/2010	31	\$145,428.65	\$1,460,718.52	\$16,158.74	\$162,302.06	51	82	\$0.00	\$0.00

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
01	07/23/2009	15,313.65	15,313.65
1A: Design Error or Omission. Incorrect PS&E. This change order adds line items for temporary work zone pavement markers and the elimination of the same.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
02	09/11/2009	2,869.98	18,183.63
4C: Third Party Accommodation. Compliance requirements of new laws and/or policies (impacting third party). Per City of Austin specs, prior to any work beginning, the contractor has to place message boards at the project limits to inform public of road construction. This change order is for the message board rental.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
03	09/11/2009	15,000.00	33,183.63
6D: Untimely ROW/Utilities. Other. Contractor has damaged unmarked utilities while constructing the roadway. This change order is for the repair of all damaged utilities that were unmarked by utility locators.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
04	09/22/2009	111,840.00	145,023.63
1A: Design Error or Omission. Incorrect PS&E. An incorrect quantity for rip-rap was given on the bid set of plans. Since then a revised quantity has been added to the plans.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
05	10/27/2009	9,428.82	154,452.45
1A: Design Error or Omission. Incorrect PS&E. Original plan and profile sheets show a Type H inlet to be installed but the PS&E did not include a line item for payment of this work. This change order accounts for all work associated with the installation of the inlet. Two (2) days were added to the Contract schedule.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
06	12/04/2009	4,296.00	158,748.45
2G: Differing Site Conditions. Unadjusted utility (unforeseeable). In order to avoid existing and unadjusted utilities, the contractor utilized pre-fabbed pipe fittings (such as 45° and 30° angle fittings) which were not a part of the original bid documents.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
07	12/04/2009	-4,019.95	154,728.50
4B: Third Party Accommodation. Third party requested work. Due to driveway slopes and culvert coverage issues, City of Austin requested that the driveway pavement design be re-worked with a more flexible material. Fifteen (15) days were added to the contract schedule.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
08	12/04/2009	14,250.00	168,978.50
2J: Differing Site Conditions. Other. Soil Retention blankets were not included the original plans. The Design Engineer has since reevaluated their necessity and has added the blankets to reduce erosion and minimize long-term maintenance issues. This change order is for the installation of soil retention blankets throughout the project.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
09	12/08/2009	189,547.62	358,526.12
2G: Differing Site Conditions. Unadjusted utility (unforeseeable). 4B: Third Party Accommodation. Third party requested work. In order to complete the project, the contractor will need to adjust and/or relocate existing City of Austin utilities in and outside the proposed roadway pavement section. The City of Austin will reimburse the County in full for the final quantities of this work.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
10	12/04/2009	18,800.00	377,326.12
1A: Design Error or Omission. Incorrect PS&E. 4D: Third Party Accommodation. Other. 2J: Differing Site Conditions. Other. Due to design issues, unexpected/differing site conditions, and a lengthy City of Austin review process regarding driveways, culverts, and side streets, additional days are being added to the Contract schedule to account for the delay to the Contractor. 103 days were added to the contract schedule.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
11	01/01/2010	0.00	377,326.12
Change Order No. 11 is still under review.			

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
12	02/12/2010	2,196.50	379,522.62
1A: Design Error or Omission. Incorrect PS&E. Due to the Advance Landscape Design driveway slope being out of spec, gate adjustments are needed in order to construct a driveway past the ROW limit to meet City requirements.			
			Adjusted Price = \$3,547,117.67

PRECINCT 2

COMMISSIONER LONG

Under Construction / Bidding


- 2.27 US 183 (PTF)
- 2.35 US 183 @ FM 3405 Traffic Signal
- 2.24 CR 214 – Phase 2A
- 2.32 RM 1431
- 2.36 US 183 @ FM 3405 Left Turn Lanes

In Design

- 2.22 CR 179
- 2.23 San Gabriel Parkway – Phase 2
- 2.25 CR 214 – Phase 2B
- 2.29 CR 273
- 2.30 CR 175 Extension, Phase 2B
- 2.31 Brushy Creek Road
- 2.33 CR 185 (Cottonwood Trail)
- 2.34 Hero Way
- 2.37 SH 29 (CR 277 to CR 200)
- 2.38 SH 29 at CR 260
- 2.39 SH 29 at Park Place Dr & Jack Nicklaus Blvd

Completed/Open to Traffic

- 2.01 Vista Ridge Blvd.
- 2.02 Avery Ranch Blvd.
- 2.03 Brushy Creek Road
- 2.04 Cedar Hollow at SH 29
- 2.05 Cypress Creek Road
- 2.06 Lakeline Blvd.
- 2.07 River Bend Oaks Subdivision
- 2.08 Ronald W. Reagan South – Phase 1
- 2.09 Ronald W. Reagan North – Phase 1
- 2.10 CR 175 (FM 1431 to Regional Park)
- 2.11 CR 185
- 2.12 CR 200 (CR 201 to Lackey Creek)
- 2.13 CR 214 (SH 2 to Rolling Hills Dr.)
- 2.14 CR 258 (US 183 to Sunset Ridge)
- 2.15 SH 29 at FM 1869
- 2.16 Lakeline Blvd.
- 2.17 San Gabriel Parkway – Phase 1
- 2.18 US 183 Widening at CR 274
- 2.19 Ronald W. Reagan South – Phase 2
- 2.20 Kauffman Loop
- 2.21 CR 175 Extension Phase 2A
- 2.26 SH 29 Improvements Study & Schematic
- 2.28 CR 272

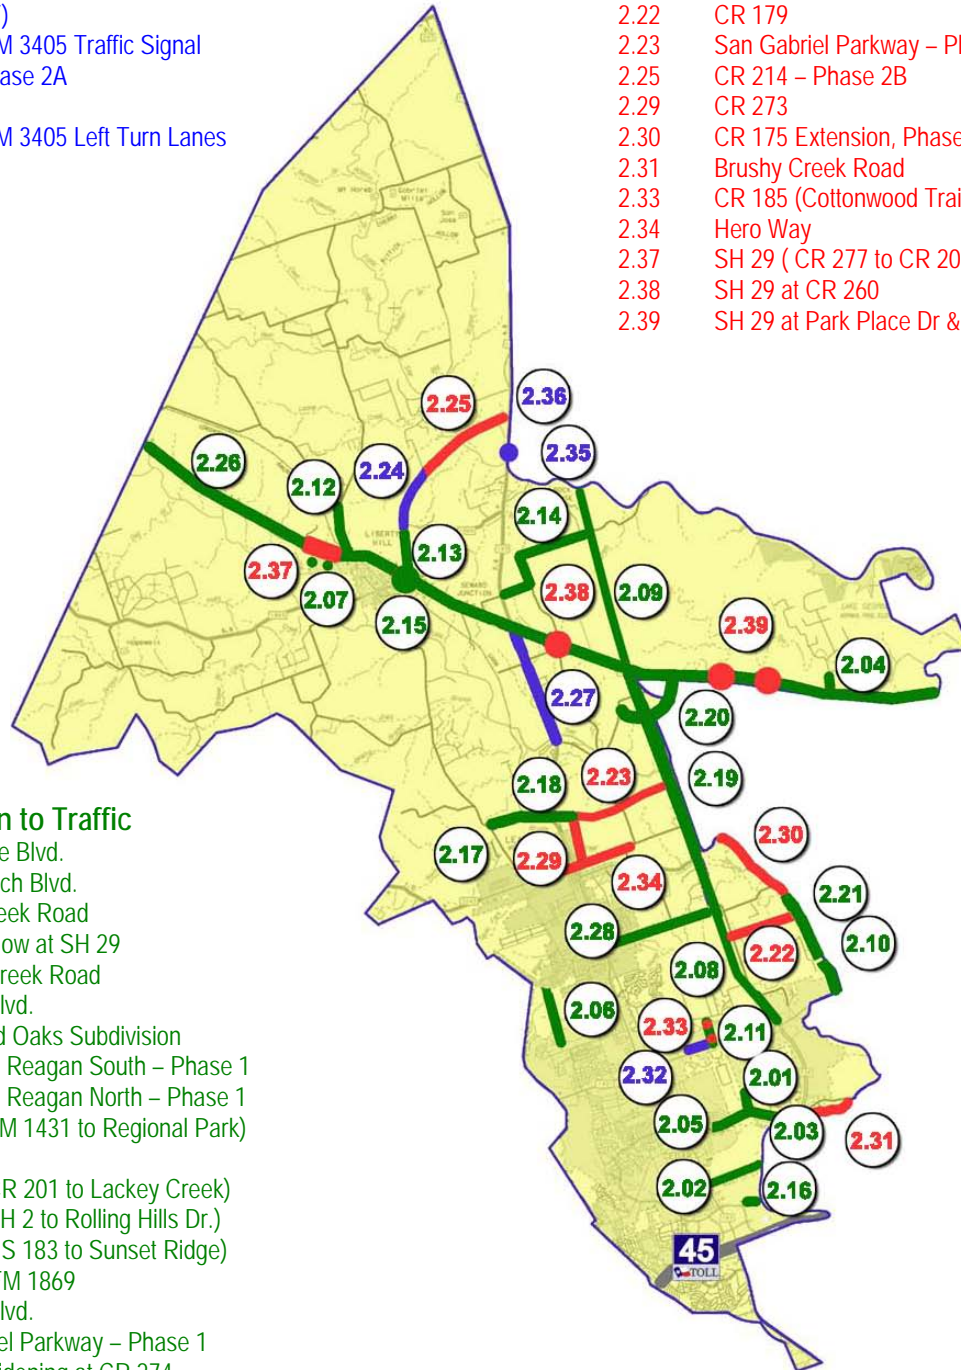

San Gabriel Pkwy, Ph. 1 (Future Halsey Dr. to Future CR 273)
Project No. 05WC321

Original Contract Price = \$2,291,679.53

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Work Completed</u>	<u>Work Accepted</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
6/22/2005	7/12/2005	5/1/2006	5/8/2006	2/15/2007		244	39	283

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoice Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time Used</u>	<u>Liquidated Damages</u>	<u>Total Liq Damages</u>
1	5/8/2006	5/31/2006	24	\$424,768.73	\$424,768.73	\$47,196.53	\$47,196.53	19	8	\$0.00	\$0.00
2	6/1/2006	6/30/2006	30	\$138,345.52	\$563,114.25	\$15,371.72	\$62,568.25	25	19	\$0.00	\$0.00
3	7/1/2006	7/31/2006	31	\$279,550.44	\$842,664.69	\$31,061.16	\$93,629.41	38	30	\$0.00	\$0.00
4	8/1/2006	8/31/2006	31	\$228,153.27	\$1,070,817.96	\$25,350.36	\$118,979.77	48	41	\$0.00	\$0.00
5	9/1/2006	9/30/2006	30	\$249,149.78	\$1,319,967.74	\$27,683.31	\$146,663.08	59	52	\$0.00	\$0.00
6	10/1/2006	10/31/06	31	\$319,298.06	\$1,639,265.80	\$35,477.56	\$182,140.64	74	63	\$0.00	\$0.00
7	11/1/2006	11/30/06	30	\$377,676.64	\$2,016,942.44	\$41,964.08	\$224,104.72	91	73	\$0.00	\$0.00
8	12/1/2006	1/31/2007	62	\$35,795.41	\$2,052,737.85	\$3,977.26	\$228,081.98	92	95	\$0.00	\$0.00
9	2/1/2007	2/28/2007	15	\$47,813.82	\$2,100,551.67	\$5,312.65	\$233,394.63	94	100	\$0.00	\$0.00
10	3/1/2007	3/31/2007	N/A	\$186,715.71	\$2,287,267.38	\$-186,715.70	\$46,678.93	94	-	\$0.00	\$0.00
11	9/1/2009	9/30/2009	N/A	\$16,138.15	\$2,303,405.53	\$329.35	\$47,008.28	94	-	\$0.00	\$0.00
12	Final Billing	N/A	N/A	\$73,721.09	\$2,377,126.62	\$1,504.51	\$48,512.79	97	-	\$0.00	\$0.00
13	Retainage Release	N/A	N/A	\$48,512.79	\$2,425,639.41	\$-48,512.79	\$0.00	97	-	\$0.00	\$0.00

1/29/2010 Comments - The Contractor has submitted all required close-out paperwork. The pay estimate for release of retainage is being processed for payment.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
01	03/21/2006	180,012.38	180,012.38

5E: Contractor Convenience. The project was let in July 2005. Due to delays with acquisition of easements for the project, construction was postponed for approximately 6 months. As a result of the extensive delays, the Contractor was unable to honor the original unit costs bid and awarded for selected contract items and requested revised contract prices for those items.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
02	09/20/2006	2,719.00	182,731.38

1B: Design Error (Other) - Item of work in plans was not identified in original bid. New item is being added (valley gutter).

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
03	02/23/2007	16,716.25	199,447.63

2E: Differing Site Conditions. Miscellaneous difference in site conditions (unforeseeable). The section of Halsey Drive included in the project was widened and striping was added to match conditions on the existing Halsey Drive. 39 days were added to the contract schedule.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
04	02/23/2007	12,377.65	211,825.28

1A: Design Error or Omission. Incorrect PS&E. The elevations at the existing railroad did not match those on the plans. Elevations were revised to meet field conditions, resulting in additional quantities. The vegetative watering quantity has been revised to meet the contract watering requirements. 3M: County Convenience. Other. County opted to revise the project limits in order to better coordinate the future work to be done at the US 183 intersection.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
05	08/16/2007	0.00	211,825.28

5E: Contractor Convenience. Other. The Owner may elect to reduce the contract retainage to 5% upon completion of 50% of the value of the work in keeping with current industry standard practice. The Owner may elect to further reduce the contract retainage to 2% upon issuance of the Certificate of Substantial Completion.

Adjusted Price = \$2,503,504.81

Ronald Reagan Blvd. South, Ph. 2 (FM 2243 to SH 29)
Project No. 05WC324

Original Contract Price = \$15,857,326.54

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Work Completed</u>	<u>Work Accepted</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
8/17/2005	9/27/2005	1/13/2006	1/23/2006	9/17/2008		540	212	752

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoice Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time Used</u>	<u>Liquidated Damages</u>	<u>Total Liq Damages</u>
1	11/1/2005	10/31/05	0	\$74,925.00	\$74,925.00	\$8,325.00	\$8,325.00	1	0	\$0.00	\$0.00
2	12/1/2005	11/30/05	0	\$103,696.20	\$178,621.20	\$11,521.80	\$19,846.80	1	0	\$0.00	\$0.00
3	1/1/2006	1/9/2006	9	\$750,735.00	\$929,356.20	\$83,415.00	\$103,261.80	7	1	\$0.00	\$0.00
4	2/1/2006	2/28/2006	28	\$444,184.20	\$1,373,540.40	\$49,353.80	\$152,615.60	11	5	\$0.00	\$0.00
5	3/1/2006	3/31/2006	31	\$291,523.10	\$1,665,063.50	\$32,391.46	\$185,007.06	13	9	\$0.00	\$0.00
6	4/1/2006	4/30/2006	30	\$399,662.07	\$2,064,725.57	\$44,406.89	\$229,413.95	17	13	\$0.00	\$0.00
7	5/1/2006	5/31/2006	31	\$655,292.34	\$2,720,017.91	\$72,810.26	\$302,224.21	22	17	\$0.00	\$0.00
8	6/1/2006	6/30/2006	30	\$455,018.26	\$3,175,036.17	\$50,557.59	\$352,781.80	25	21	\$0.00	\$0.00
9	7/1/2006	7/31/2006	31	\$40,437.00	\$3,215,473.17	\$4,493.00	\$357,274.80	26	25	\$0.00	\$0.00
10	8/1/2006	8/31/2006	31	\$285,902.35	\$3,501,375.52	\$31,766.92	\$389,041.72	27	29	\$0.00	\$0.00
11	9/1/2006	9/30/2006	30	\$528,814.84	\$4,030,190.36	\$58,757.21	\$447,798.93	32	33	\$0.00	\$0.00
12	10/1/2006	10/31/06	31	\$311,641.77	\$4,341,832.13	\$34,626.86	\$482,425.79	34	38	\$0.00	\$0.00
13	11/1/2006	11/30/06	30	\$478,315.80	\$4,820,147.93	\$53,146.20	\$535,571.99	38	41	\$0.00	\$0.00
14	12/1/2006	3/31/2007	121	\$1,317,936.47	\$6,138,084.40	\$146,437.39	\$682,009.38	48	58	\$0.00	\$0.00
15	4/1/2007	4/30/2007	30	\$447,058.65	\$6,585,143.05	\$49,673.18	\$731,682.56	51	62	\$0.00	\$0.00
16	5/1/2007	5/31/2007	31	\$250,755.70	\$6,835,898.75	\$27,861.77	\$759,544.33	53	66	\$0.00	\$0.00
17	6/1/2007	7/31/2007	61	\$892,102.41	\$7,728,001.16	\$99,122.49	\$858,666.82	60	74	\$0.00	\$0.00
18	8/1/2007	8/31/2007	31	\$625,810.47	\$8,353,811.63	\$69,534.49	\$928,201.31	65	78	\$0.00	\$0.00
19	9/1/2007	9/30/2007	30	\$804,499.07	\$9,158,310.70	\$89,388.79	\$1,017,590.10	71	82	\$0.00	\$0.00
20	10/1/2007	10/31/07	31	\$1,258,832.28	\$10,417,142.98	\$-469,076.61	\$548,513.49	77	86	\$0.00	\$0.00
21	11/1/2007	11/30/07	30	\$785,594.47	\$11,202,737.45	\$41,347.08	\$589,860.57	83	90	\$0.00	\$0.00
22	12/1/2007	12/31/07	31	\$453,813.77	\$11,656,551.22	\$23,884.94	\$613,745.51	86	94	\$0.00	\$0.00
23	1/1/2008	1/31/2008	31	\$701,577.47	\$12,358,128.69	\$36,925.13	\$650,670.64	91	98	\$0.00	\$0.00
24	2/1/2008	2/28/2008	13	\$789,217.12	\$13,147,345.81	\$-381,980.87	\$268,689.77	94	100	\$0.00	\$0.00
25	3/1/2008	3/31/2008	N/A	\$168,372.53	\$13,315,718.34	\$3,436.18	\$272,125.95	95	-	\$0.00	\$0.00
26	4/1/2008	5/31/2008	N/A	\$123,532.38	\$13,439,250.72	\$2,521.06	\$274,647.01	96	-	\$0.00	\$0.00
27	6/1/2008	6/30/2008	N/A	\$158,393.86	\$13,597,644.58	\$3,232.53	\$277,879.54	97	-	\$0.00	\$0.00
28	7/1/2009	7/31/2009	N/A	\$246,514.59	\$13,844,159.17	\$5,030.91	\$282,910.45	99	-	\$0.00	\$0.00
29	9/1/2009	10/31/09	N/A	\$247,467.35	\$14,091,626.52	\$-141,224.56	\$141,685.89	100	-	\$0.00	\$0.00
30	11/1/2009	11/30/09	N/A	\$174,653.12	\$14,266,279.64	\$-125,358.86	\$16,327.03	100	-	\$0.00	\$0.00

1/29/2010 Comments - The Contractor is continuing to work to complete all items added under Change Order No. 24. Project Close-out will resume once the work is complete. The Record Drawings have been received from the Contractor, reviewed, and found to be complete and accurate.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
01	02/14/2006	-2,114,062.05	-2,114,062.05

3C - County Convenience. Implementation of a Value Engineering finding. Pavement design was changed to a 2.5" TY C HMA over a 15" Flexible Base section for the main lanes. Due to change in pavement design, excavation & embankment quantities were also revised.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
02	02/14/2006	-192,122.88	-2,306,184.93

3C - County Convenience. Implementation of a Value Engineering finding. As a result of the value engineering process, unit prices for the 6x3 and 7x3 box culvert items were adjusted as mutually agreed to by Williamson County and Ranger Excavating.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
03	05/18/2006	12,444.00	-2,293,740.93

2J - Differing Site Conditions (unforeseeable) (other). A residence within the ROW that was scheduled for demolition was found to have asbestos. Extra expenses were incurred by the Contractor for asbestos removal.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
04	07/11/2006	128,440.00	-2,165,300.93

6D. Untimely ROW/Utilities. Other. Steel encasement pipe for future waterline for the City of Leander added at sta. 227+10, sta. 241+70, sta. 262+00, sta. 262+10. Utility plans were not incorporated into PS&E at the time of letting.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
05	09/05/2006	111,179.80	-2,054,121.13

1A: Design error or Omission. Incorrect PS&E. Original plans did not account for the channel crossing at the proposed driveway location. A box culvert was added for the drainage design. 15 days were added to the contract schedule.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
06	08/17/2006	8,493.37	-2,045,627.76

2C: New Development - Conditions changing after PS&E completed. 2D: Environmental Remediation. During the clearing and grubbing of ROW, two abandoned water wells and one abandoned septic tank were discovered and needed to be properly removed.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
07	08/29/2006	59,041.60	-1,986,586.16
4B: Third Party requested work. Per the terms of the real estate contract agreement, the County must provide a driveway for the landowner. 6D: Untimely ROW. The real estate contract agreement was not finalized until after the contract plans were complete and the project was let. 15 days were added to the contract schedule.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
08	09/05/2006	218,894.00	-1,767,692.16
6D: Untimely ROW/Utilities. 6D-Other. Chisholm Trail waterline relocations were not incorporated into the plans prior to contract award. 30 days were added to the contract schedule.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
09	02/07/2007	8,360.00	-1,759,332.16
4B: Third Party Accommodation - Third party requested work. The County and the property owner agreed to temporary fencing at the driveways and culvert locations to facilitate the construction of the roadway. This change order provides compensation to the property owner for installation of temporary special fencing around the easements, and its removal once the driveway and culvert construction is complete, allowing the permanent fencing to be installed.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
10	03/27/2007	205,000.00	-1,554,332.16
3M: County Convenience. Other. The one-course surface treatment will be added due to the deletion of the 4.5" of Type B asphalt requested by Williamson County as part of the pavement design section revision.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
11	03/21/2007	10,577.00	-1,543,755.16
6C: Untimely ROW/Utilities. Utilities not Clear. The location of water lines on the plans did not match actual field conditions. Additional effort was required to perform exploratory work and additional water line relocations.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
12	04/20/2007	2,530.00	-1,541,225.16
6B: Untimely ROW/Utilities. Right-of-Way not clear (County responsibility for ROW). New fencing was added for the drainage easement on the north and south sides of Hwy 29 for the stock pass extension.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
13	07/05/2007	-12,050.34	-1,553,275.50
4B: Third Party Accommodation. Third Party requested work. Realigned driveway to avoid taking out unnecessary trees on the Lamb property. 6D: Untimely ROW/Utilities. Other. Move Densford's driveway back to CL Sta. of 279+00 to avoid power pole in the proposed driveway location of Sta. 280+00.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
14	07/12/2007	81,502.00	-1,471,773.50
4B: Third Party Accommodation. Third Party requested work. Installation of steel sleeves for future utilities at property owner's request, per terms of the real estate contract agreement. Twenty-five (25) days were added to the project schedule.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
15	09/17/2007	4,010.38	-1,467,763.12
4B: Third Party Accommodation. Third party requested work. Driveways relocated and a drainage pipe added to one location. Twenty (20) days were added to the Contract schedule.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
16	08/15/2007	29,117.00	-1,438,646.12
2J: Differing Site Conditions. Other. Existing groundwater within the strata below the proposed roadway is resulting in soft subgrade conditions. A geotechnical investigation was completed to assess the problem and a rock filter system was developed to mitigate the groundwater problem. This change order provides compensation for the extra time and work associated with the revision. Ninety-three (93) days were added to the Contract schedule.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
17	10/31/2007	7,424.20	-1,431,221.92
1B: Design Error or Emission. Other. Metal Beam Guard Fence transitions were not included as a bid item even though they show to be installed on plans. This change order provides payment for the transitions. 2E: Differing Site Conditions. Miscellaneous Difference in Site Conditions. In order to construct certain driveways, a small amount of fencing was removed while various amounts of temporary and permanent fencing will need to be installed. Five (5) days were added to the Contract schedule.			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
18	11/19/2007	0.00	-1,431,221.92
5E: Contractor Convenience. Other. The Owner may elect to reduce the contract retainage to 5% upon completion of 50% of the value of the work in keeping with current industry standard practice. The Owner may elect to further reduce the contract retainage to 2% upon issuance of the Certificate of Substantial Completion			
<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
19	01/08/2008	15,628.50	-1,415,593.42
1B: Design Error or Emission. Other. Signal layout information for FM 2243 intersection was excluded from plans. Contractor had to remove and replace existing traffic detectors and pull boxes in order to construct a portion of roadway. Two (2) days were added to the Contract schedule.			

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
20	01/30/2008	24,887.96	-1,390,705.46

2J: Differing Site Conditions. Other. This change order provides compensation for the extra time and work associated with revisions to mitigate the groundwater problem in the northbound lanes of Reagan Blvd, following the same strategy developed for the southbound lanes of Reagan Blvd under Change Order No. 16.
 4B: Third Party Accommodation. Third Party Requested Work. Provides compensation for the removal of entrance walls and capping gate columns on the Fisher property.
 3F: County Convenience. Additional work required by the County. Provides compensation for removal of Parmer Lane sign at the intersection of Reagan Blvd and RM 2243. Seven (7) days were added to the Contract schedule.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
21	01/29/2008	106,465.66	-1,284,239.80

2J: Differing Site Conditions. Other. Change Order #16 (attached) added ninety-three (93) days to the Contract schedule. The change in the Contract schedule delayed the Contractor's planned paving schedule. As a result of the delay, the Contractor was unable to hold the bid prices for asphalt materials. This Change Order provides for a fair and equitable price increase for asphalt material items.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
22	07/08/2008	8,930.00	-1,275,309.80

3M: County Convenience. Other. Property owner's fence was located in the middle of the new ditch line. To prevent future damage to the fence, it was moved into the County's ROW and a water gap was installed.
 2E: Differing Site Conditions (unforeseeable). Miscellaneous difference in site conditions. In order to maintain the proper slope at certain driveways, the Contractor demoed SET's and extended driveway pipes to accommodate wider driveways.


<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
23	09/30/2009	0.00	-1,275,309.80

This Change Order (the balancing change order) will be revised and processed after all work added under Change Order No. 24 is completed.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
24	09/22/2009	158,657.05	-1,116,652.75

3F: County Convenience. Additional Work Desired by the County. Additional erosion control work is required at the South Fork of the San Gabriel River. The revised plans will meet TCEQ guidelines.

Adjusted Price = \$14,740,673.79

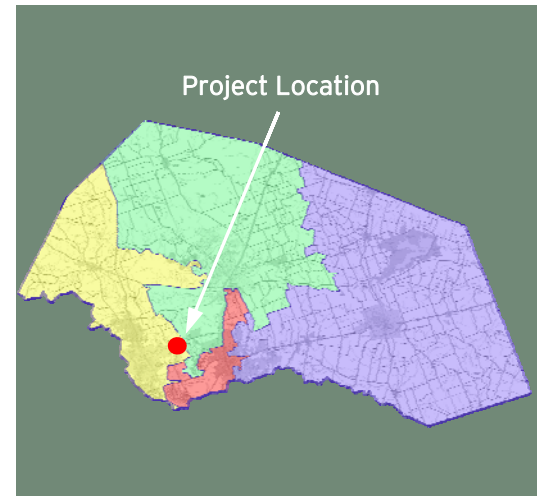

CR 175, PHASE 2A EXTENSION (Regional Park to Creekside Meadows)

Project Length: 1.01 Miles
Roadway Classification: Urban Collector
Roadway Section: Four-lane divided

Project Schedule: April 2009 - January 2010
Estimated Construction Cost: \$1.9 Million



JANUARY 2010 IN REVIEW

1/8/2010 - RGM continues working on topsoil around both Culverts #1 and #2. They have also completed the MBGF, mow strips, and the rip rap on the median noses in the islands. Subcontractor Wheeler Coatings completed the surface paving for the northbound lanes and they are scheduled to complete the southbound lanes next week.

1/22/2010 - RGM has completed the topsoil work around the culverts. Subcontractor Wheeler Coatings completed the surface Ty C mix on the proposed southbound lanes. RGM has submitted a punch list to the GEC. The GEC and WilCo are scheduled to walk through the project early next week and add any additional items to the punch list.

1/29/2010 - The GEC and WilCo issued additional punch list items to RGM on 1/26/10. RGM has completed all items except grass growth. Subcontractor ATS has also completed the installation of the additional signal head at the Perry Mayfield intersection. Highway Technologies has also completed the final pavement markings. Substantial completion was granted on 1/28/10. A Ribbon Cutting Ceremony is scheduled for 2/12/10.



Design Engineer: Haynie Consulting
Contractor: RGM Constructors
Construction Observation:
Jerry Jansen, Williamson County

Williamson County
Road Bond Program

CR 175, Ph. 2A Extension (Regional Park to Creekside Meadows)
Project No. 09WC707

Original Contract Price = \$1,854,291.16

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Anticipated Work Complete</u>	<u>Work Accepted</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
1/21/2009	2/3/2009	4/20/2009	7/6/2009	1/28/2010		180	27	207

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoice Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time Used</u>	<u>Liquidated Damages</u>	<u>Total Liq Damages</u>
1	4/20/2009	4/19/2009	0	\$43,970.99	\$43,970.99	\$4,885.67	\$4,885.67	3	0	\$0.00	\$0.00
2	5/12/2009	5/11/2009	0	\$396,055.07	\$440,026.06	\$44,006.11	\$48,891.78	26	0	\$0.00	\$0.00
3	7/1/2009	7/26/2009	26	\$213,429.04	\$653,455.10	\$23,714.34	\$72,606.12	39	13	\$0.00	\$0.00
4	8/1/2009	8/31/2009	31	\$250,681.21	\$904,136.31	\$27,853.47	\$100,459.59	54	28	\$0.00	\$0.00
5	9/1/2009	9/30/2009	30	\$162,098.59	\$1,066,234.90	\$-44,341.96	\$56,117.63	61	42	\$0.00	\$0.00
6	10/1/2009	10/31/09	31	\$53,846.74	\$1,120,081.64	\$2,834.03	\$58,951.66	64	57	\$0.00	\$0.00
7	11/1/2009	11/30/09	30	\$244,706.53	\$1,364,788.17	\$12,879.30	\$71,830.96	77	71	\$0.00	\$0.00
8	12/1/2009	12/31/09	31	\$55,411.74	\$1,420,199.91	\$2,916.40	\$74,747.36	81	86	\$0.00	\$0.00
9	1/1/2010	1/31/2010	27	\$344,508.49	\$1,764,708.40	\$-38,732.90	\$36,014.46	97	100	\$0.00	\$0.00

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
01	07/23/2009	-4,029.24	-4,029.24

3: County Convenience. 3E: Reduction of future maintenance. 3H: Cost savings opportunity discovered during construction. At both proposed culverts, the rip rap item has been changed from common rock rip rap to concrete rip rap.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
02	07/23/2009	17,615.43	13,586.19

4B: Third Party Accommodation. Third party requested work: Adding 6 4 IN conduits at a total of 1320 LF for PEC, AT&T, and Time Warner.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
03	09/11/2009	2,700.00	16,286.19

2J: Differing Site Conditions. Other: This change order accounts for adding removable striping to the project for the detour just south of the actual proposed roadway tie-in. This striping application can be removed without damaging the existing pavement surface.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
04	10/27/2009	1,881.40	18,167.59


4B: Third Party Accommodation. Third party requested work: This Change Order accounts costs associated with the installation 300 feet of 4-inch PVC sleeves for future irrigation for the Parkside subdivision.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
05	02/12/2010	1,947.84	20,115.43

1A: Design Error or Omission. Incorrect PS&E. A signal head was added at the intersection of CR 175 and Perry Mayfield for the northbound traffic.

Twenty-seven (27) days were added to the Contract schedule to account for the delay encountered while the Engineer developed a solution for the lack of cover over Culverts #1 and #2 on the northbound lanes.

Adjusted Price = \$1,874,406.59

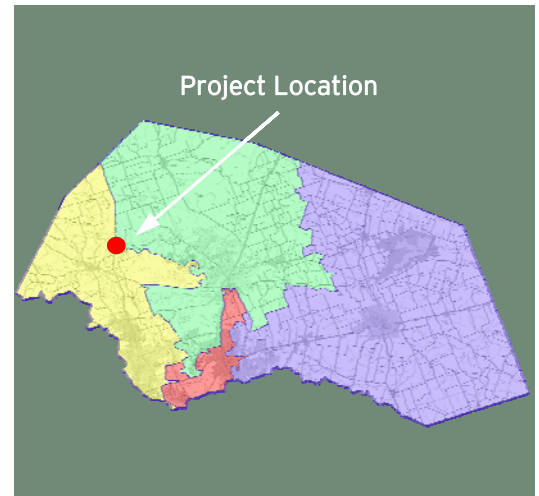

US 183 at FM 3405 (Traffic Signal Construction)

Project Length: 0.10 Miles

Project Schedule: November 2009 - February 2010
Estimated Construction Cost: \$102,499.00



JANUARY 2010 IN REVIEW

1/8/2010 - RTI is working on installing conduit and pull boxes.

1/22/2010 - RTI has set all four signal poles and the two advanced flashing beacons. They continue to install conduit to the pull boxes and the control cabinet. They are scheduled to place the pull box aprons and the control cabinet pad on 1/26/10.

1/29/2010 - RTI has completed the installation of all conduit and the poured all pull box aprons and the control cabinet pad. They are scheduled to set the cabinet, pull wires, and hang mast arms next week.



Design Engineer: Brown & Gay
Contractor: Republic ITS
Construction Observation:
Kenneth Marak, Williamson County

Williamson County
Road Bond Program


US 183 at FM 3405 (Traffic Signal Construction)
Project No. 09WC713

Original Contract Price = \$102,499.00

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Anticipated Work Complete</u>	<u>Work Accepted</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
7/22/2009	8/11/2009	11/10/2009	11/19/2009	2/16/2010		90	0	90

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoice Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time Used</u>	<u>Liquidated Damages</u>	<u>Total Liq Damages</u>
1	11/19/2009	1/31/2010	74	\$71,957.03	\$71,957.03	\$7,995.23	\$7,995.23	78	82	\$0.00	\$0.00

Adjusted Price = \$102,499.00

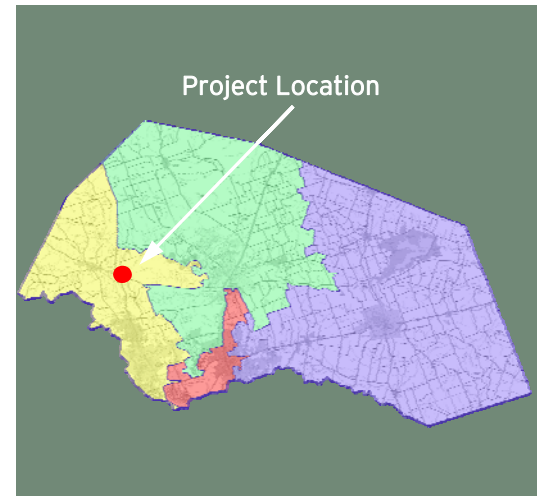

PASS THROUGH FINANCING PROJECT US 183

(Riva Ridge Road to SH 29)

Project Length: 4.3 Miles

Roadway Classification: Principal Arterial

Roadway Section: Four-lane divided with shoulders and a wide median for future transportation corridor

Structures: Two four-lane bridges and bridge class culverts

Project Schedule: December 2009 - Fall 2012

Estimated Construction Cost: \$14.7 Million



JANUARY 2010 IN REVIEW

1/8/2010 - Clearing and placement of erosion control measures continues on the south end of project. The ground breaking ceremony for this project was held on Wednesday, 01/06/10.

1/22/2010 - Dan Williams completed foundation drill shaft placement and began construction of columns on bent #3 for the northbound San Gabriel River bridge. They continue to excavate material from water quality pond #4 and began importing material from a TxDOT project in Cedar Park for embanking on the north and south side of the bridge. Relocation of the existing High Gabriel waterline is scheduled to begin next week.

1/29/2010 - Dan Williams continues with embankment activities for Phase 1 construction and to clear, grub and strip topsoil in areas north and south of the San Gabriel River. Construction of bridge columns continues. The relocation of the existing High Gabriel waterline began this week.



Design Engineer: Dannenbaum
Contractor: Dan Williams Company
Construction Inspection: HDR

Williamson County
Pass Through Financing Program


PASS THROUGH FINANCING: US 183 (Riva Ridge Rd to SH 29)
Project No. 09WC720 TxDOT CSJ: 0151-04-063

Original Contract Price = \$14,677,727.84

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Anticipated Work Complete</u>	<u>Work Accepted</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
8/24/2009	8/25/2009	12/21/2009	12/23/2009	Fall 2012		627	0	627

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoice Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time Used</u>	<u>Liquidated Damages</u>	<u>Total Liq Damages</u>
1	12/21/200	12/31/10	0	\$135,503.26	\$135,503.26	\$0.00	\$0.00	1	0	\$0.00	\$0.00
2	1/1/2010	1/31/2010	0	\$519,553.82	\$655,057.08	\$0.00	\$0.00	4		\$0.00	\$0.00

Adjusted Price = \$14,677,727.84

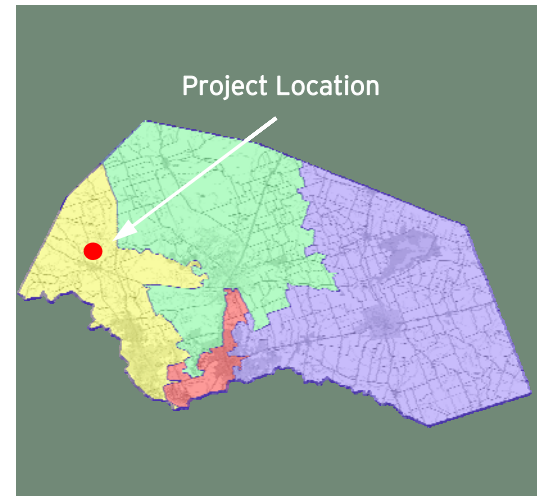

CR 214, Phase 2A

(Rolling Hills to San Gabriel Ranch Road)

Project Length: 1.3 Miles

Roadway Classification: Rural Collector

Roadway Section: Two-lane undivided with shoulders

Project Schedule: December 2009 - September 2010

Estimated Construction Cost: \$1.2 Million



JANUARY 2010 IN REVIEW

1/8/2010 - FT Woods began clearing ROW from the south end of the project heading north.

1/22/2010 - FT Woods continues to clear the ROW along the east half of the project. They have also begun stripping topsoil in various locations. Subcontractor Austin Wood Recycling is onsite grinding the trees and hauling off the mulch. Pike is continuing to install the new poles and hang cable for the PEC relocations.

1/29/2010 - FT Woods continues to clear the ROW along the east half of the project. They have also continue stripping topsoil in various locations and stockpiling it.



Design Engineer: Rogers Design
Contractor: FT Woods Constructors
Construction Observation:
Kenneth Marak, Williamson County

Williamson County
Road Bond Program

CR 214 Phase 2A (Rolling Hills to San Gabriel Ranch Road)
Project No. 09WC723

Original Contract Price = \$1,183,999.03

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Anticipated Work Complete</u>	<u>Work Accepted</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
9/30/2009	10/13/2009	12/8/2009	12/8/2009	Fall 2010		227	0	227

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoice Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time Used</u>	<u>Liquidated Damages</u>	<u>Total Liq Damages</u>
1	11/1/2009	11/30/09	0	\$2,126.46	\$2,126.46	\$236.27	\$236.27	0	0	\$0.00	\$0.00
2	12/1/2009	12/31/09	0	\$10,980.83	\$13,107.29	\$1,220.10	\$1,456.37	1	0	\$0.00	\$0.00
3	1/1/2010	1/31/2010	0	\$36,651.83	\$49,759.12	\$4,072.42	\$5,528.79	5	0	\$0.00	\$0.00

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
01	02/12/2010	-16,500.00	-16,500.00

5E: Contractor Convenience. Other. 3H: County Convenience. Cost savings opportunity discovered during construction. The Contractor requested to use temporary sediment control fence instead of biodegradable erosion control logs in various locations on the Project. Due to the significant savings, the County agreed.

Adjusted Price = \$1,167,499.03

US 183 at FM 3405 Intersection Improvements
Project No. 10WC805

Original Contract Price = \$379,185.10

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Anticipated Work Complete</u>	<u>Work Accepted</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
11/19/2009	12/1/2009	Pending	Pending			90	0	90

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoice Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$ Used)</u>	<u>% Time Used</u>	<u>Liquidated Damages</u>	<u>Total Liq Damages</u>
-----------------------	-----------------------	--------------------	---------------------	------------------------	----------------------	--------------------------	------------------------	--------------------	--------------------	---------------------------	--------------------------

1/29/2010 Comments - Bids were opened on 11/19/09. Six (6) bids were received, and the contract was awarded on 12/1/09 to Aaron Concrete Contractors in the amount of \$379,185.10. A pre-construction meeting is scheduled for 2/11/2010.

Adjusted Price = \$379,185.10

PRECINCT 3

COMMISSIONER COVEY

Under Construction / Bidding

3.24 Williams Drive (RM 2338)


3.30 RM 2338 (PTF)


Completed/Open to Traffic

- 3.01 Chandler Rd. – Phase 1
- 3.02 Georgetown Inner Loop East
- 3.03 Georgetown Inner Loop East Extension
- 3.04 Georgetown Inner Loop – Project 1
- 3.05 Georgetown Inner Loop – Project 2
- 3.06 Georgetown Inner Loop – Project 3 Study
- 3.07 Georgetown Inner Loop – Project 4 Study
- 3.08 Georgetown Inner Loop – Project 5 Study
- 3.09 CR 124
- 3.10 CR 142
- 3.11 CR 145
- 3.12 CR 152 Bridge Replacement
- 3.13 CR 157
- 3.14 CR 175
- 3.15 CR 234
- 3.16 CR 245
- 3.17 CR 311
- 3.18 CR 314
- 3.19 Wyoming Springs North – Study
- 3.20 Ronald W. Reagan South Phase 2
- 3.21 Ronald W. Reagan North Phase 2
- 3.22 IH-35 @ SH 29 Turnarounds (PTF)
- 3.23 SH 29/CR 104 – Phase 1
- 3.26 CR 175 Extension Phase 2A
- 3.31 SH 29 Improvements Study & Schematic

In Design

- 3.25 CR 104 – Phase 2
- 3.27 IH-35 Northbound Frontage Rd and Ramps
- 3.28 Ronald W. Reagan North Phase 3
- 3.29 Ronald W. Reagan North Phase 4
- 3.32 Georgetown SE Inner Loop Widening
- 3.33 CR 175 Extension, Phase 2B
- 3.34 SH 195 ROW and Utilities
- 3.35 SH 29 at Park Place Dr & Jack Nicklaus Blvd

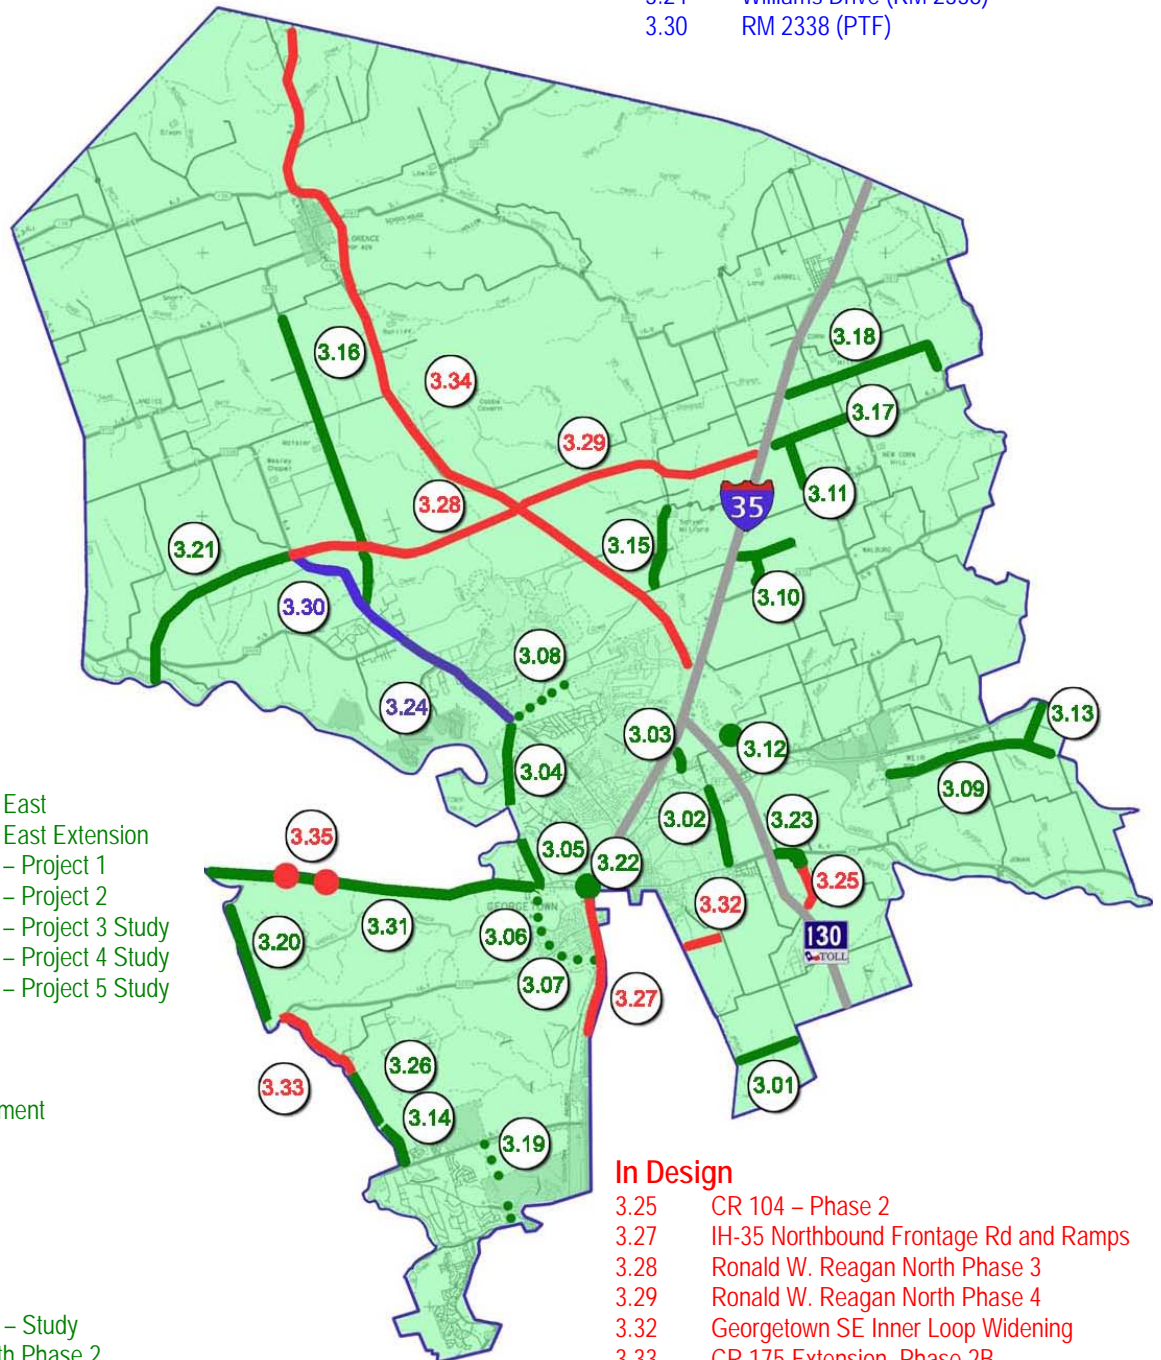

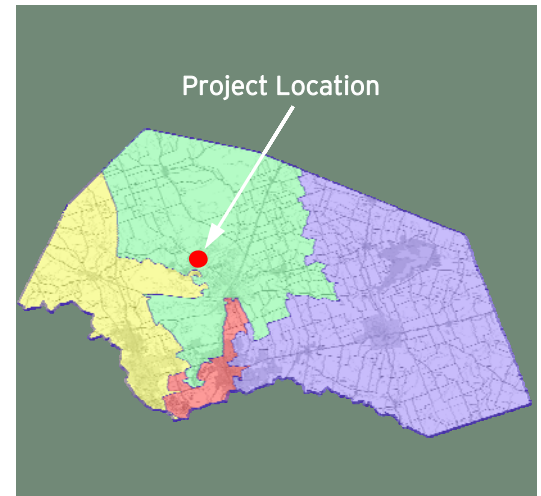

WILLIAMS DRIVE

(DB Wood Road to FM 3405)

Project Length: 3.4 Miles

Roadway Classification: Major Arterial

Roadway Section: Four-lane w/ center two-way turn lane and shoulders

Structures: None

Project Schedule: March 2009 - November 2010

Estimated Construction Cost: \$12.3 Million



JANUARY 2010 IN REVIEW

1/8/2010 - JC Evans began work on crossing Old Oak with waterline encasement pipe. They are also working on excavating, investigating, and preparing for the water tie-ins to transmission mains. They installed a pressure release valve vault along 4T Ranch Road. JC Evans continues to place rip rap on the backslope of the ditch along the south ROW across from N. Lakewood Dr. They are scheduled to make final waterline tie-ins to transmission mains overnight on 1/11/10 and 1/13/10.

1/22/2010 - JC Evans completed the installation of the 24-inch waterline pipe and the 42-inch encasement across Old Oak. They also completed the box culvert end treatments at Del Webb. The Contractor continues to place rip rap along the south ROW west of Jim Hogg on the back slope.

1/29/2010 - JC Evans completed the installation of the remaining 24-inch waterline pipe at Wildwood along the south ROW. They continue to restore the waterline easement to original condition in various locations. JC Evans continues to work on excavation and embankment to subgrade along the north ROW from Jim Hogg to Del Webb and they are working on excavating for the proposed ditchline west of Del Webb along the north ROW. They are also working on grading for concrete rip rap east of Old Oak along the south ROW.



Design Engineer: KBR
Contractor: J.C. Evans Construction
Construction Inspection: PBS&J

Williamson County
Road Bond Program

Williams Drive (DB Wood Rd to FM 3405)
Project No. 09WC706

Original Contract Price = \$11,464,068.41

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Anticipated Work Complete</u>	<u>Work Accepted</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
12/17/2008	1/20/2009	3/2/2009	3/16/2009	11/8/2010		570	33	603

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoice Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time</u>	<u>Liquidated Damages</u>	<u>Total Liq Damages</u>
1	3/16/2009	3/31/2009	16	\$409,766.45	\$409,766.45	\$0.00	\$0.00	4	3	\$0.00	\$0.00
2	4/1/2009	4/30/2009	30	\$275,352.93	\$685,119.38	\$0.00	\$0.00	6	8	\$0.00	\$0.00
3	5/1/2009	5/31/2009	31	\$780,300.96	\$1,465,420.34	\$0.00	\$0.00	13	13	\$0.00	\$0.00
4	6/1/2009	6/30/2009	30	\$409,988.45	\$1,875,408.79	\$0.00	\$0.00	16	18	\$0.00	\$0.00
5	7/1/2009	7/31/2009	31	\$439,814.28	\$2,315,223.07	\$0.00	\$0.00	20	23	\$0.00	\$0.00
6	8/1/2009	8/31/2009	31	\$748,866.19	\$3,064,089.26	\$0.00	\$0.00	27	28	\$0.00	\$0.00
7	9/1/2009	9/30/2009	30	\$1,044,554.30	\$4,108,643.56	\$0.00	\$0.00	36	33	\$0.00	\$0.00
8	10/1/2009	10/31/09	31	\$560,440.65	\$4,669,084.21	\$0.00	\$0.00	41	38	\$0.00	\$0.00
9	11/1/2009	11/30/09	28	\$489,651.00	\$5,158,735.21	\$0.00	\$0.00	45	43	\$0.00	\$0.00
10	12/1/2009	12/31/09	30	\$347,909.60	\$5,506,644.81	\$0.00	\$0.00	48	48	\$0.00	\$0.00
11	1/1/2010	1/31/2010	30	\$236,560.28	\$5,743,205.09	\$0.00	\$0.00	50	53	\$0.00	\$0.00

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
01	06/09/2009	-22,295.80	-22,295.80

3H: County Convenience. Cost savings opportunity discovered during construction. This change order adds Item 351, Flexible Pavement Structure Repair (4") to the contract, which will be in lieu of the original Item 351, Flexible Structure Repair (10"). The pavement condition of Williams Drive does not warrant the 10" repair and can be accomplished with a 4" repair.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
02	09/15/2009	818,430.82	796,135.02

4B: Third Party Accommodation. Third party requested work. This change order upgrades the proposed Chisholm Trail Special Utility District waterline (Segments A and C) from an 18 inch waterline to a 24 inch waterline. This will be funded in full by Chisholm Trail. Thirty-three (33) days were added to the Contract schedule.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
03	10/27/2009	6,018.38	802,153.40

4B: Third Party Accommodation. Third party requested work. 6C: Untimely ROW/Utilities. Utilities not clear. This change order pays the contractor for various items of extra work necessary to install the Chisholm Trail waterline and for one day of idle equipment due to a request by Chisholm Trail Special Utility District not to work on in the vicinity of their waterline.

Adjusted Price = \$12,266,221.81

PASS THROUGH FINANCING: RM 2338 Phase 2 (FM 3405 to Ronald Reagan Blvd)**Project No. 09WC722A TxDOT CSJ: 2211-01-023**

Original Contract Price = \$8,700,198.56

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Anticipated Work Complete</u>	<u>Work Accepted</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
1/13/2010	2/2/2010	Pending	Pending			540	0	540

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoice Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$ Used)</u>	<u>% Time Used</u>	<u>Liquidated Damages</u>	<u>Total Liq Damages</u>
-----------------------	-----------------------	--------------------	---------------------	------------------------	----------------------	--------------------------	------------------------	--------------------	--------------------	---------------------------	--------------------------

1/29/2010 Comments - Seven bids were received on 1/13/2010. The Contract was awarded to Joe Bland Construction on 2/2/2010 for the alternate bid price of \$8,700,198.56.

Adjusted Price = \$8,700,198.56

PRECINCT 4


COMMISSIONER MORRISON

Completed/Open to Traffic

- 4.01 Bridge Replacements Phase 1
(CR 406, CR 390, CR 427)
- 4.02 Bridge Replacements Ph. 2A (CR 424)
- 4.03 Chandler Rd. – Phase 1
- 4.04 CR 100
- 4.05 CR 112 – Phase 1
- 4.06 CR 119
- 4.07 CR 122 at US 79
- 4.08 CR 124
- 4.09 CR 132
- 4.10 CR 136
- 4.11 CR 137
- 4.12 CR 138 & CR 139 Alignment Study
- 4.13 CR 300 & CR 301
- 4.14 CR 302
- 4.15 CR 347 & CR 348
- 4.16 CR 368 & CR 369 (CR 101 to CR 366)
- 4.17 CR 404
- 4.18 CR 412
- 4.19 CR 466
- 4.20 FM 37 at SH 95 Signal
- 4.21 Gattis School Rd. ROW
- 4.22 Limmer Loop – Phase 1A
- 4.23 Thrall School Zone
- 4.24 US 79 – Section 1
- 4.25 US 79 – Section 2
- 4.26 US 79 – Section 3A
- 4.27 Chandler Rd. – Phase 2
- 4.28 Limmer Loop – Phase 1B
- 4.29 CR 113
- 4.30 Limmer Loop – Phase 1C


In Design

- 4.31 Arterial A – Phase 1
- 4.32 Arterial A – Phase 2
- 4.33 Chandler Rd. – Phase 3A
- 4.35 FM 1660 (PTF)
- 4.37 US 79 Section 3 (PTF)
- 4.38 BUS 79/2nd Street Improvements
- 4.43 FM 1460 Section 2
- 4.42 Bridge Replacements Phase 2B
(CR 351 & CR 434)
- 4.44 CR 138
- 4.45 CR 170

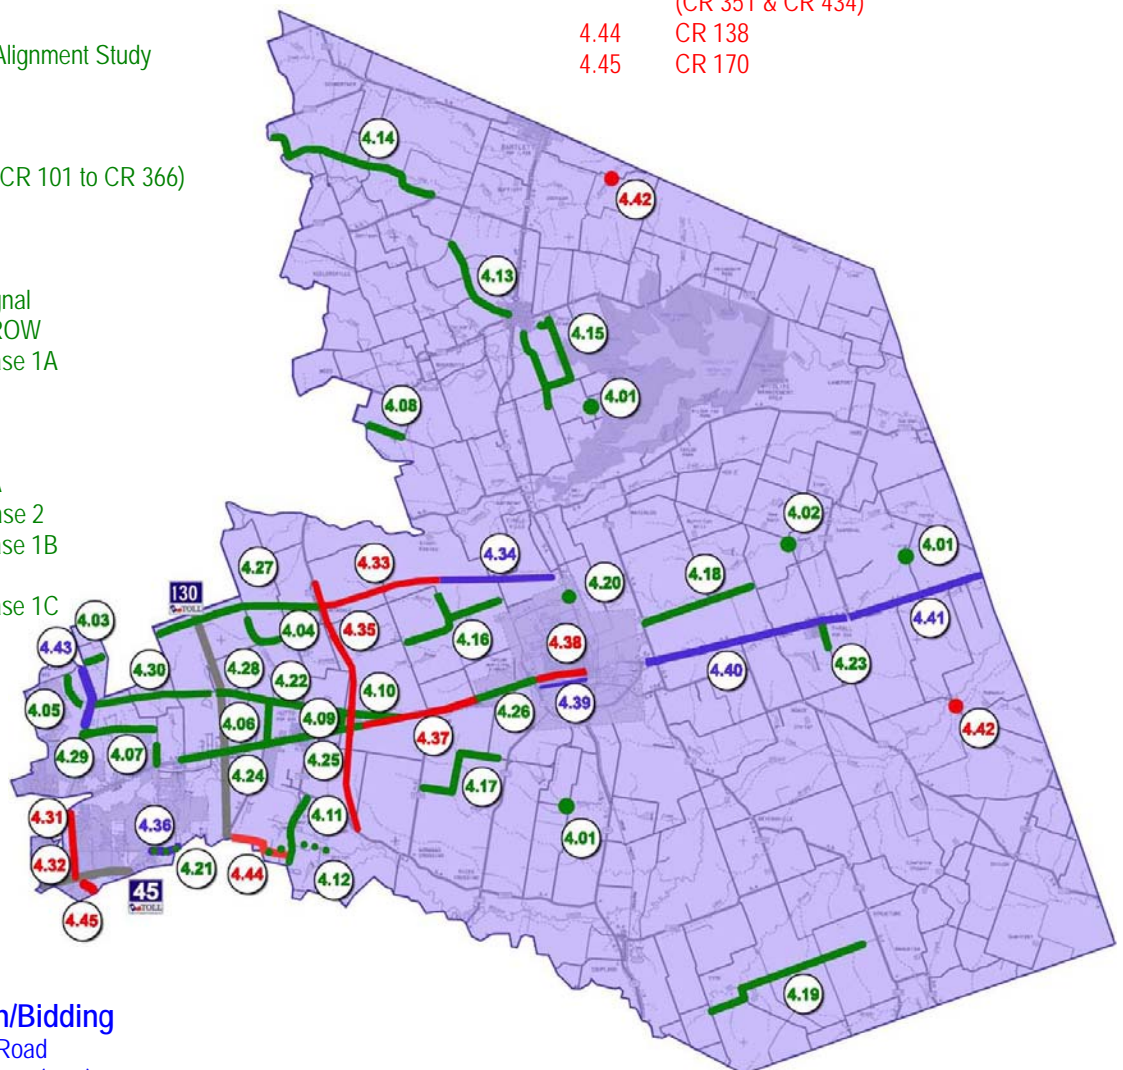

Under Construction/Bidding

- 4.36 Gattis School Road
- 4.40 US 79 Section 5A (PTF)
- 4.41 US 79 Section 5B (PTF)
- 4.34 Chandler Rd. – Phase 3B
- 4.39 BUS 79 Drainage Improvements

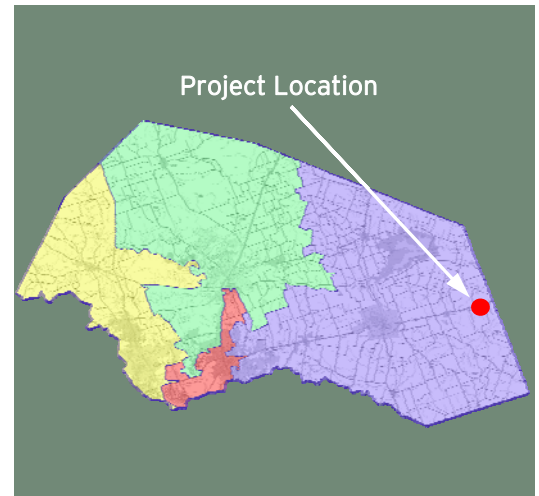

PASS THROUGH FINANCING PROJECT US 79, SECTION 5B

(East of FM 1063 to Milam County Line)

Project Length: 4 Miles

Roadway Classification: Major Arterial

Roadway Section: Four-lane Divided with Shoulders

Structures: Bridge Class Culvert

Project Schedule: July 2008 - May 2010

Estimated Construction Cost: \$16.8 Million



JANUARY 2010 IN REVIEW

1/8/2010 - JC Evans completed processing, re-mixing and curing lime in the full-depth reconstruction area on the eastbound lanes over Culvert #7 and Culvert #10. They began processing flex base over Culvert #10 and continue with subgrade prep for turn lanes at various locations.

1/22/2010 - JC Evans continues to place and process flex base in the full depth and left turn widening areas at various locations on project. They began placement of asphalt in the milled and widening area on the east end of project over Culvert #11.

1/29/2010 - JC Evans continues to place and process flex base in the full depth and left turn widening areas at various locations on project. They completed milling on the existing eastbound lanes. Level-up with asphalt is scheduled to begin next week.



Design Engineer: LAN
Contractor: J.C. Evans Construction
Construction Inspection: Huitt~Zollars

Williamson County
Pass Through Financing Program



PRIME
STRATEGIES,
INC.

PASS THROUGH FINANCING: US 79, Section 5B (FM 1063 to Milam County Line)**Project No. 08WC607 TxDOT CSJ: 0204-04-042****Original Contract Price = \$16,986,053.49**

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Anticipated Work Complete</u>	<u>Work Accepted</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
4/16/2008	4/29/2008	7/11/2008	7/23/2008	5/26/2010		499	0	499

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoice Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time</u>	<u>Liquidated Damages</u>	<u>Total Liq Damages</u>
1	7/23/2008	7/31/2008	8	\$57,547.25	\$57,547.25	\$0.00	\$0.00	0	2	\$0.00	\$0.00
2	8/1/2008	8/31/2008	23	\$1,486,551.50	\$1,544,098.75	\$0.00	\$0.00	9	6	\$0.00	\$0.00
3	9/1/2008	9/30/2008	24	\$321,941.62	\$1,866,040.37	\$0.00	\$0.00	11	11	\$0.00	\$0.00
4	10/1/2008	10/31/08	23	\$308,687.50	\$2,174,727.87	\$0.00	\$0.00	13	16	\$0.00	\$0.00
5	11/1/2008	11/30/08	20	\$473,119.00	\$2,647,846.87	\$0.00	\$0.00	16	20	\$0.00	\$0.00
6	12/1/2008	12/31/08	24	\$147,566.05	\$2,795,412.92	\$0.00	\$0.00	16	24	\$0.00	\$0.00
7	1/1/2009	1/31/2009	26	\$502,757.37	\$3,298,170.29	\$0.00	\$0.00	19	30	\$0.00	\$0.00
8	2/1/2009	2/28/2009	24	\$1,005,695.63	\$4,303,865.92	\$0.00	\$0.00	25	34	\$0.00	\$0.00
9	3/1/2009	3/31/2009	25	\$227,189.19	\$4,531,055.11	\$0.00	\$0.00	27	39	\$0.00	\$0.00
10	4/1/2009	4/30/2009	24	\$349,811.28	\$4,880,866.39	\$0.00	\$0.00	29	44	\$0.00	\$0.00
11	5/1/2009	5/31/2009	23	\$2,262,161.67	\$7,143,028.06	\$0.00	\$0.00	42	49	\$0.00	\$0.00
12	6/1/2009	6/30/2009	24	\$383,195.52	\$7,526,223.58	\$0.00	\$0.00	44	54	\$0.00	\$0.00
13	7/1/2009	7/31/2009	23	\$230,817.15	\$7,757,040.73	\$0.00	\$0.00	45	58	\$0.00	\$0.00
14	8/1/2009	8/31/2009	22	\$289,357.32	\$8,046,398.05	\$0.00	\$0.00	47	63	\$0.00	\$0.00
15	9/1/2009	9/30/2009	21	\$691,746.05	\$8,738,144.10	\$0.00	\$0.00	52	67	\$0.00	\$0.00
16	10/1/2009	10/31/09	23	\$203,663.89	\$8,941,807.99	\$0.00	\$0.00	54	72	\$0.00	\$0.00
17	11/1/2009	11/30/09	19	\$106,411.20	\$9,048,219.19	\$0.00	\$0.00	54	75	\$0.00	\$0.00
18	12/1/2009	12/31/09	22	\$76,843.68	\$9,125,062.87	\$0.00	\$0.00	55	80	\$0.00	\$0.00
19	1/1/2010	1/31/2010	20	\$323,448.24	\$9,448,511.11	\$0.00	\$0.00	57	84	\$0.00	\$0.00

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
01	01/23/2009	25,000.00	25,000.00

3M: County Convenience. Other. This change order sets up a force account pay item to pay the contractor for repairing damage to safety appurtenances on the project. 1A: Design Error or Omission. Incorrect PS&E. This change order revises Bid Item #48 from 467-2303 SET (TY II)(24 IN)(CMP)(6:1)(P) to 467-2288 SET (TY II)(24 IN)(RCP)(6:1)(P).

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
02	06/09/2009	0.00	25,000.00

1A: Design Error or Omission. Incorrect PS&E. This change order revises Bid Item #15 from 340-2014 D-GR HMA (METH) TY-B PG70-22 to 341-2014 D-GR HMA (QC/QA) TY-B PG70-22.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
03	07/09/2009	22,350.00	47,350.00

1A: Design Error or Omission: Incorrect PS&E. This change order allows the contractor to relocate an existing 8" waterline which is in conflict with proposed ditch grades, per revised cross sections. Waterline was lowered before construction based on original cross sections, which were incorrect.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
04	07/21/2009	55,234.06	102,584.06

3M: County Convenience. Other. This change order allows Williamson County to adjust the amount of compensation to be paid to the contractor in proportion to the quality of the asphalt pavement produced and placed on the project.


<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
05	07/21/2009	91,768.04	194,352.10

4B: Third Party Accommodation. Third party requested work. TxDOT requested that Culvert #11 be replaced due to its current condition. 1B: Design Error or Omission. Other. Before beginning construction on Culvert #11 it was discovered that a portion of the bottom of the top slab of the three boxes was deteriorated and the box needed to be replaced rather than just extended at each end. 3E: County Convenience. Reduction of future maintenance. Rock riprap is being added in ditches and on slopes to reduce erosion.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
06	09/11/2009	-386,598.20	-192,246.10

3H: County Convenience. Cost savings opportunity discovered during construction. It was determined that a large portion of the eastbound full-depth reconstruction areas could be constructed by simply overlaying the existing pavement with new asphalt. 1A: Design error or omission. Incorrect PS&E. The proposed pavement grades were designed to be lower than the existing grades in an area that called for asphalt level-up and overlay only. Therefore, the contractor was required to revise the method of construction in this area.

Adjusted Price = \$16,793,807.39

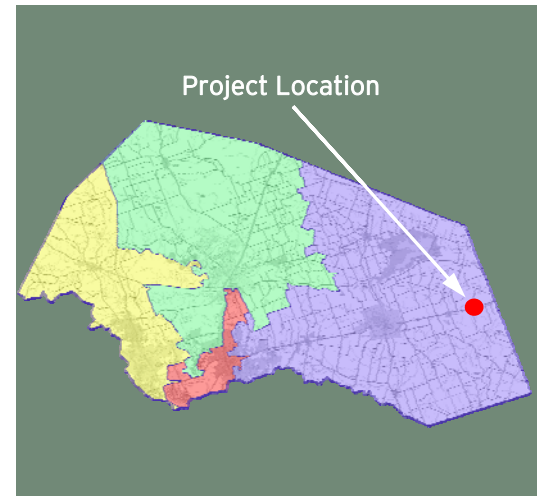

PASS THROUGH FINANCING PROJECT US 79, SECTION 5A

(East of Taylor to FM 1063)

Project Length: 6.1 Miles

Roadway Classification: Major Arterial

Roadway Section: Four-lane Divided with Shoulders

Structures: Bridge Class Culverts

Project Schedule: January 2009 - May 2011

Estimated Construction Cost: \$19.6 Million



JANUARY 2010 IN REVIEW

1/8/2010 - Hunter continues with formwork and pouring concrete on the tops of curb inlets in Thrall. They also continued with excavation of the north ditch to grade and resumed placement of topsoil. Construction continues on the detour pavement located near FM 619.

1/22/2010 - Hunter continues with construction of driveways and is pouring the concrete curb and gutter transitions to inlets in Thrall. Asphalt is being placed on the east end of Thrall and on the west end of project. Electrical construction (laying conduit & connection of wiring) continues for the illumination in Thrall and intersection area at FM 619.

1/29/2010 - Hunter completed Phase 1 milling and paving in Thrall. They continue to pour concrete on drives, sidewalk and riprap in Thrall. Flex base is being placed on driveways and mailbox turnouts at various locations on project. The drainage pipes were installed under the Tomecek service road. Hunter began installation of small sign bases.



Design Engineer: Jacobs
Contractor: Hunter Industries
Construction Inspection: Huitt~Zollars

Williamson County
Pass Through Financing Program

PASS THROUGH FINANCING: US 79, Section 5A (East of Taylor to FM 1063)
Project No. 08WC619 TxDOT CSJ: 0204-04-040

Original Contract Price = \$20,021,693.92

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Anticipated Work Complete</u>	<u>Work Accepted</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
10/29/2009	11/18/2008	1/12/2009	7/27/2009	5/18/2011		593	0	593

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoice Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time</u>	<u>Liquidated Damages</u>	<u>Total Liq Damages</u>
1	1/27/2009	1/31/2009	4	\$1,072,701.94	\$1,072,701.94	\$0.00	\$0.00	5	1	\$0.00	\$0.00
2	2/1/2009	2/28/2009	20	\$1,522,944.68	\$2,595,646.62	\$0.00	\$0.00	13	4	\$0.00	\$0.00
3	3/1/2009	3/31/2009	22	\$788,518.66	\$3,384,165.28	\$0.00	\$0.00	17	8	\$0.00	\$0.00
4	4/1/2009	4/30/2009	21	\$502,872.77	\$3,887,038.05	\$0.00	\$0.00	19	11	\$0.00	\$0.00
5	5/1/2009	5/31/2009	22	\$757,178.89	\$4,644,216.94	\$0.00	\$0.00	23	15	\$0.00	\$0.00
6	6/1/2009	6/30/2009	22	\$711,613.42	\$5,355,830.36	\$0.00	\$0.00	27	19	\$0.00	\$0.00
7	7/1/2009	7/31/2009	22	\$635,205.99	\$5,991,036.35	\$0.00	\$0.00	30	22	\$0.00	\$0.00
8	8/1/2009	8/31/2009	21	\$1,677,078.01	\$7,668,114.36	\$0.00	\$0.00	38	26	\$0.00	\$0.00
9	9/1/2009	9/30/2009	21	\$1,431,729.03	\$9,099,843.39	\$0.00	\$0.00	45	30	\$0.00	\$0.00
10	10/1/2009	10/31/09	22	\$538,454.63	\$9,638,298.02	\$0.00	\$0.00	48	33	\$0.00	\$0.00
11	11/1/2009	11/30/09	19	\$1,169,970.14	\$10,808,268.16	\$0.00	\$0.00	54	36	\$0.00	\$0.00
12	12/1/2009	12/231/09	20	\$535,790.54	\$11,344,058.70	\$0.00	\$0.00	57	40	\$0.00	\$0.00
13	1/1/2010	1/31/2010	21	\$545,272.91	\$11,889,331.61	\$0.00	\$0.00	59	43	\$0.00	\$0.00

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
01	06/09/2009	5,534.58	5,534.58

2E: Differing Site Conditions(unforeseeable). Miscellaneous difference in site conditions (unforeseeable). This change order compensates the Contractor for the additional costs associated with plugging three (3) existing hand dug water wells discovered within the ROW limits.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
02	07/28/2009	79,075.00	84,609.58

2G: Differing Site Conditions. Unadjusted utility (unforeseeable). This change order allows for the relocation of a waterline that was in conflict with proposed ditch grades and was also under proposed pavement in some areas.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
03	07/13/2009	1,546.07	86,155.65

6C: Untimely ROW/Utilities. Utilities not clear. This change order allows for the contractor to cut, and cap as necessary, existing utility lines that currently run from the Lumpkin property onto the ROW.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
04	09/30/2009	-55,081.50	31,074.15

6C: Untimely ROW/Utilities. Utilities not clear. This change order allows for the contractor to relocate an existing 8" waterline in Thrall that is in conflict with proposed storm sewer pipe. 3H: County Convenience. Cost savings opportunity discovered during construction. Due to a revised paving plan through the City of Thrall, several waterline crossings will not need to be constructed in town.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
05	09/30/2008	-448,146.46	-417,072.31

5B: Contractor Convenience. Contractor requested change in the sequence and/or method of work. Contractor noted it would be difficult to construct the pavement through Thrall utilizing the original traffic control plans. 3H: County Convenience. Cost savings opportunity discovered during construction. Revising the pavement design through Thrall also allowed for a revised traffic control plan which in turn reduced the overall cost to the project.


<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
06	09/30/2009	-48,155.70	-465,228.01

3H: County Convenience. Cost savings opportunity discovered during construction. Place topsoil in lieu of compost manufactured topsoil.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total CO</u>
07	10/27/2009	3,000.00	-462,228.01

3L: County Convenience. Revising safety work/measures desired by the County. Allows the contractor to use off-duty police officers or other traffic safety measures to assist in traffic safety during traffic switches, night work, etc.

Adjusted Price = \$19,559,465.91

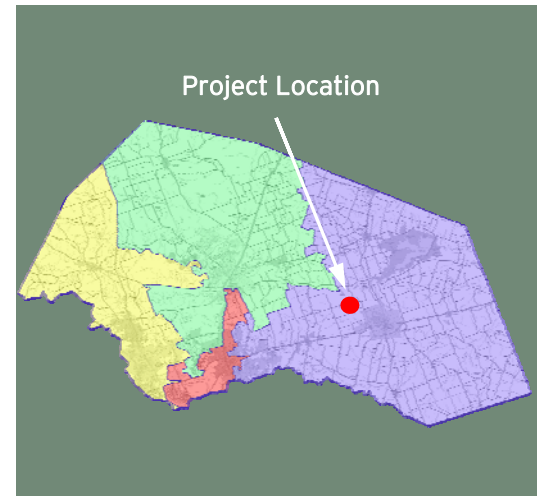

CHANDLER ROAD, PHASE 3B (CR 368/369 to SH 95)

Project Length: 4.1 Miles
Roadway Classification: Rural Arterial
Roadway Section: Westbound 2 lanes of an ultimate 4-lane divided arterial

Project Schedule: October 2009 - September 2010
Estimated Construction Cost: \$5.6 Million



JANUARY 2010 IN REVIEW

1/8/2010 - Chasco completed formwork and poured concrete on the downstream wings for Culvert G and footing for Culvert J1. They began placement of driveway pipes on the east side of SH 95 and continue with embankment activities for the section of roadway located west of CR 365.

1/22/2010 - Chasco poured the deck and wings on Culvert J1 (west of CR 365). They formed and poured concrete for the wing footing and walls on Culvert H2 and began installation of the steel pipe encasement across the ROW at Station 298+71 (east of CR 366). Embankment and ditch excavation continues for the section of roadway located west of CR 365.

1/29/2010 - Chasco completed construction of Culvert H2, installed RC pipe for drainage structure G20 (across median ditch to the north), and poured the concrete footing for Culvert J2 (east of CR 365). Embankment and ditch excavation continues for the section of roadway located west of CR 365. They began backfilling around drainage culvert J1 (west of CR 365) and embanking material starting at this culvert and working the lift toward the west.



Design Engineer: Jacobs
Contractor: Chasco Constructors
Construction Observation:
Jerry Jansen, Williamson County

Williamson County
Road Bond Program

Chandler Road Phase 3B (CR 368/369 to SH 95)
Project No. 09WC717

Original Contract Price = \$5,649,034.60

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Anticipated Work Complete</u>	<u>Work Accepted</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
6/24/2009	7/14/2009	9/21/2009	10/1/2009	9/30/2010		365	0	365

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoice Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time Used</u>	<u>Liquidated Damages</u>	<u>Total Liq Damages</u>
1	10/1/2009	10/31/09	31	\$78,713.10	\$78,713.10	\$8,745.90	\$8,745.90	2	8	\$0.00	\$0.00
2	11/1/2009	11/30/09	30	\$82,998.00	\$161,711.10	\$9,222.00	\$17,967.90	3	17	\$0.00	\$0.00
3	12/1/2009	12/31/09	31	\$844,282.66	\$1,005,993.76	\$93,809.18	\$111,777.08	20	25	\$0.00	\$0.00
4	1/1/2010	1/31/2010	31	\$208,681.20	\$1,214,674.96	\$23,186.80	\$134,963.88	24	34	\$0.00	\$0.00

Adjusted Price = \$5,649,034.60

Business 79 Drainage Improvements
Project No. 09WC712

Original Contract Price = \$3,735,873.35

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Anticipated Work Complete</u>	<u>Work Accepted</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
11/19/2009	12/15/2009	Pending	Pending			304	0	304

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoice Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$ Used)</u>	<u>% Time Used</u>	<u>Liquidated Damages</u>	<u>Total Liq Damages</u>
-----------------------	-----------------------	--------------------	---------------------	------------------------	----------------------	--------------------------	------------------------	--------------------	--------------------	---------------------------	--------------------------

1/29/2010 Comments - The contract was awarded to Austin Engineering for \$3,735,873.35 on 12/15/09. A pre-construction meeting will be scheduled in February.

Adjusted Price = \$3,735,873.35
