




Williamson County Commissioners Court

Road Bond Program

June 16, 2020




Precinct 1

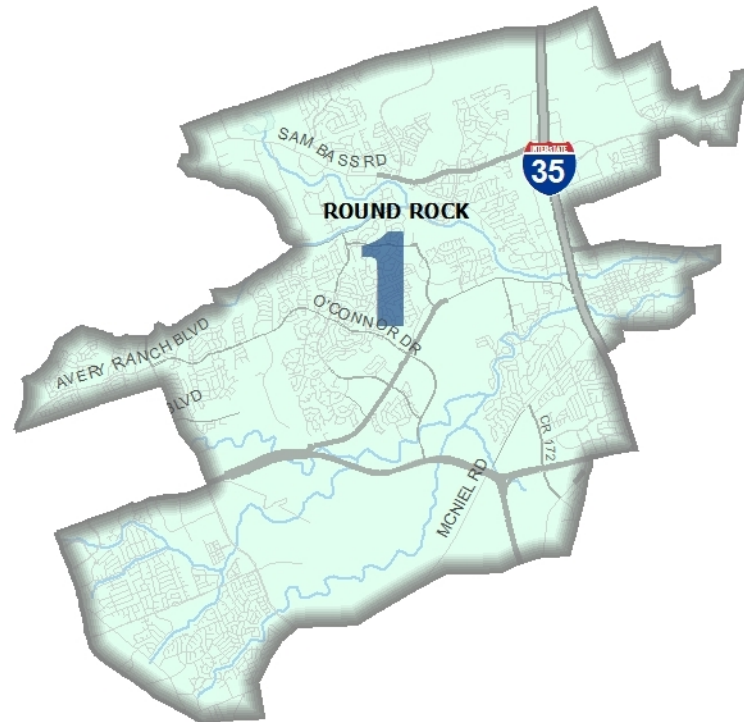

North Mays Extension (Paloma Drive to Oakmont Drive)

3

Anticipated Completion
Summer 2020

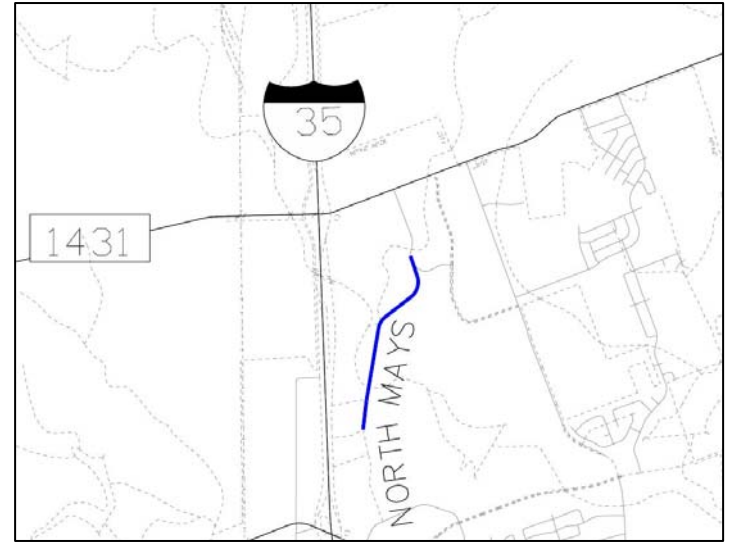

Original Contract Price = \$10,775,835.75

Total Change Orders to Date = \$24,898.18

Adjusted Contract Price = \$10,800,733.93

Expenditures to Date = \$8,321,946.91 (77%)

North Mays Extension (Paloma Drive to Oakmont Drive)



North Mays Extension (Paloma Drive to Oakmont Drive)

5



North Mays Extension (Paloma Drive to Oakmont Drive)






RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)

7

Anticipated Completion
Summer 2022

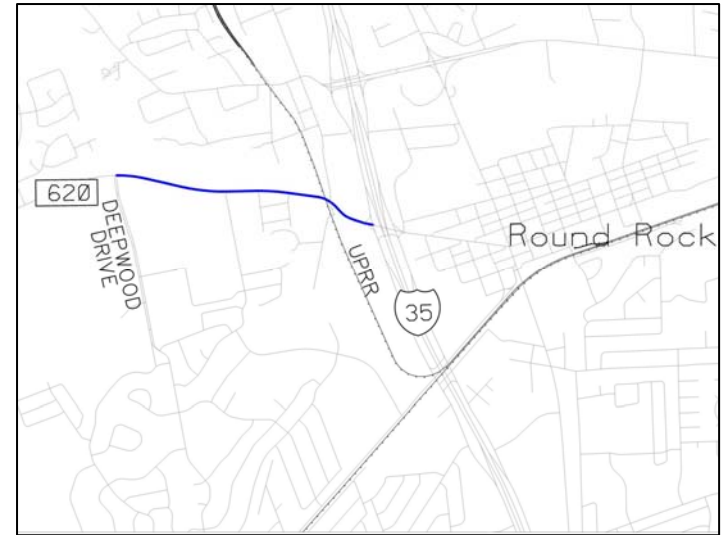

Partnership with TxDOT and the City of Round
Rock

Original Contract Amount = \$27,468,703.67

Construction is managed by TxDOT

RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)

8



RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)

9




RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)



Great Oaks Drive Water Line Replacements

11

Anticipated Completion
Spring 2020

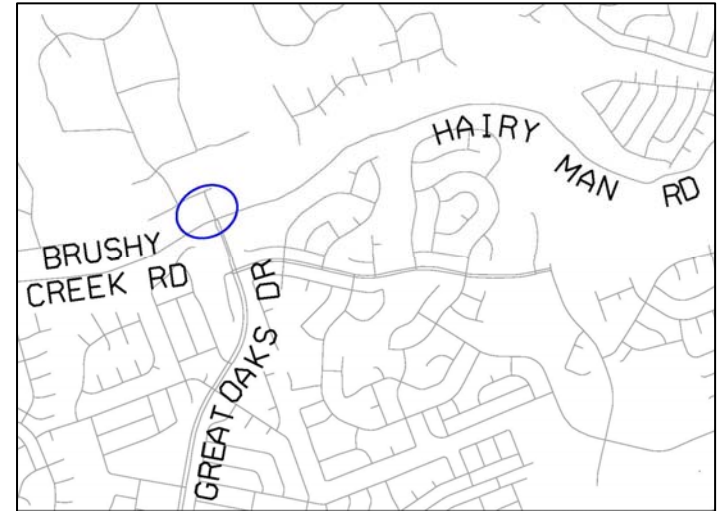

Original Contract Price = \$1,325,000.00

Total Change Orders to Date = \$170,929.84

Adjusted Contract Price = \$1,495,929.84

Expenditures to Date = \$1,322,498.36 (89%)

Great Oaks Drive Water Line Replacements




Great Oaks Drive Water Line Replacements



Great Oaks Drive Water Line Replacements




Precinct 2

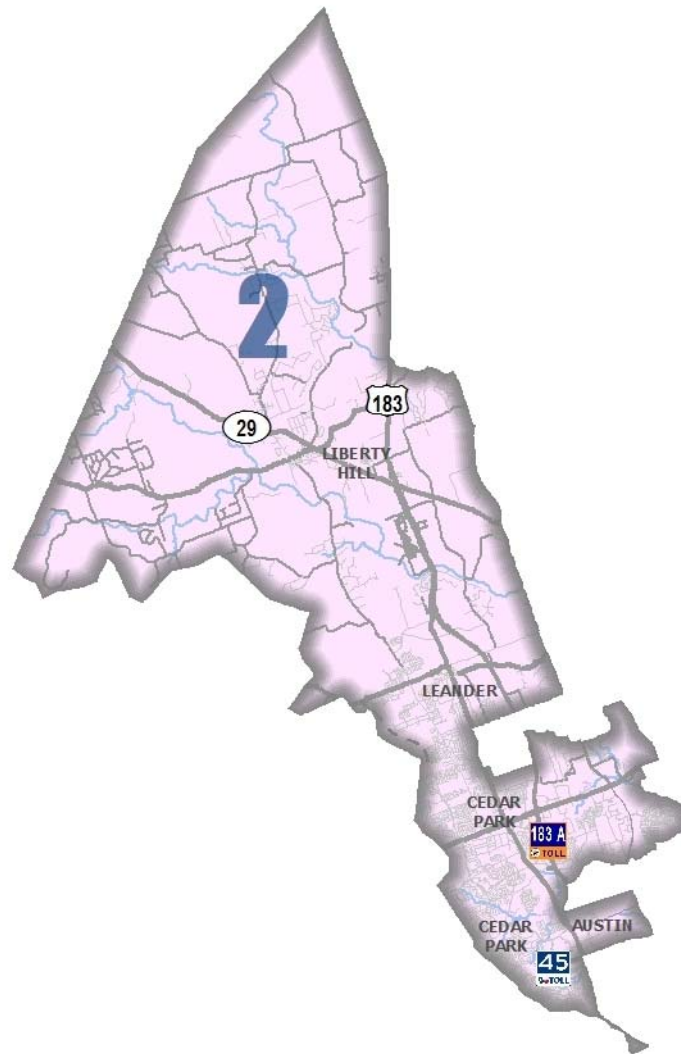

Seward Junction Improvements

Anticipated Completion
Late 2020

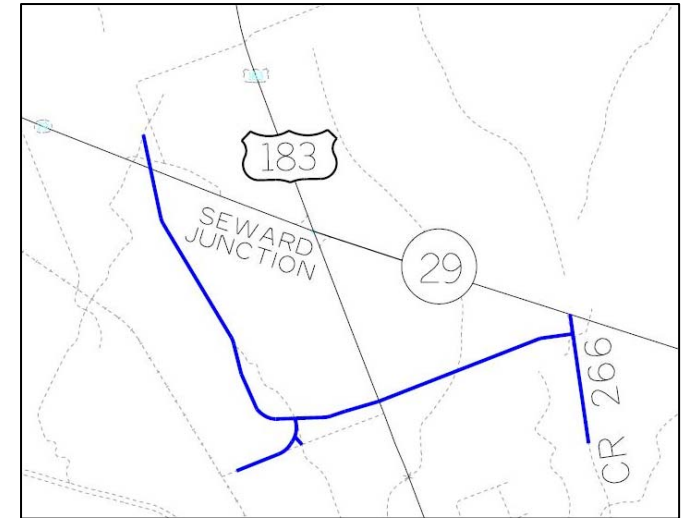

Original Contract Price = \$13,270,258.10

Total Change Orders to Date = \$112,306.36

Adjusted Contract Price = \$13,382,564.46

Expenditures to Date = \$9,355,665.78 (70%)

Seward Junction Improvements




Seward Junction Improvements



Seward Junction Improvements




Precinct 3

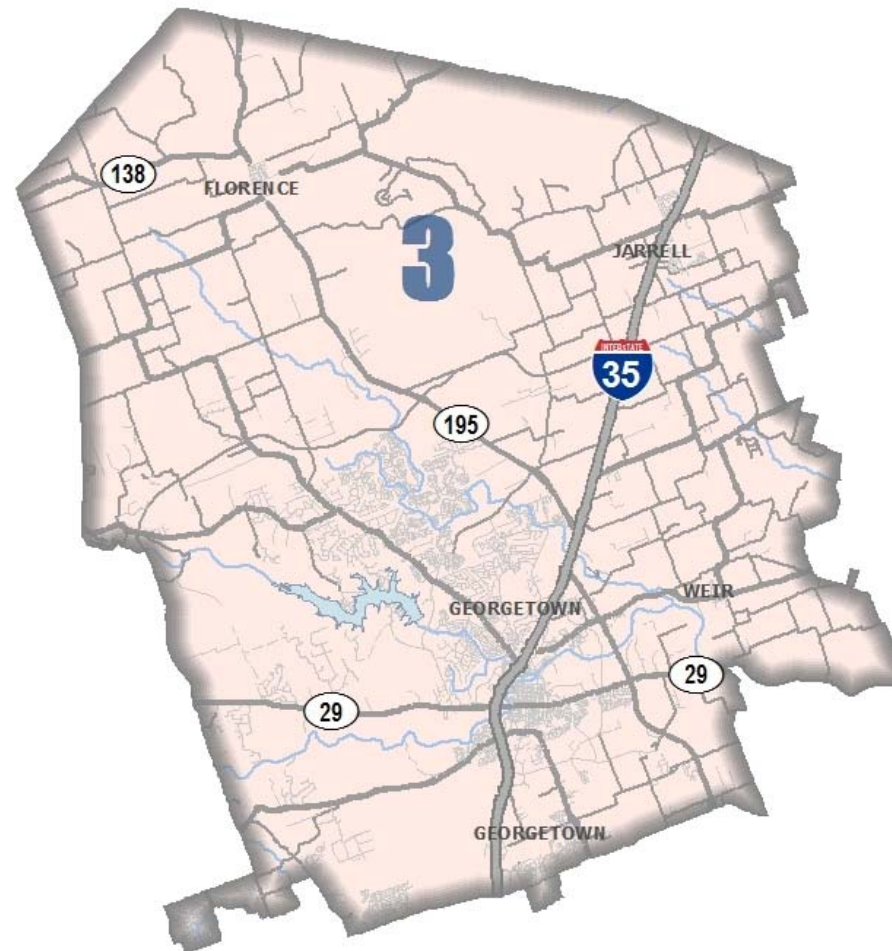

Southwest Bypass Segment 2 (Southbound IH 35 to RM 2243)

21

Substantially Complete

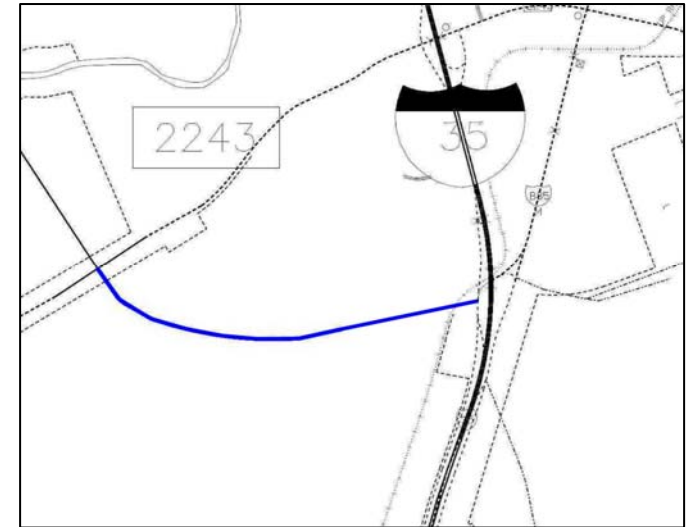

Original Contract Amount = \$8,087,943.77

Total Change Orders = \$503,379.40

Adjusted Contract Price = \$8,591,323.17

Expenditures to Date = \$8,207,602.92 (96%)

Southwest Bypass Segment 2 (Southbound IH 35 to RM 2243)

22



Southwest Bypass Segment 2 (Southbound IH 35 to RM 2243)

23



Southwest Bypass Segment 2 (Southbound IH 35 to RM 2243)


24





IH 35 Ramp Reversals and Frontage Road Conversion ²⁵

Anticipated Completion
Late 2020

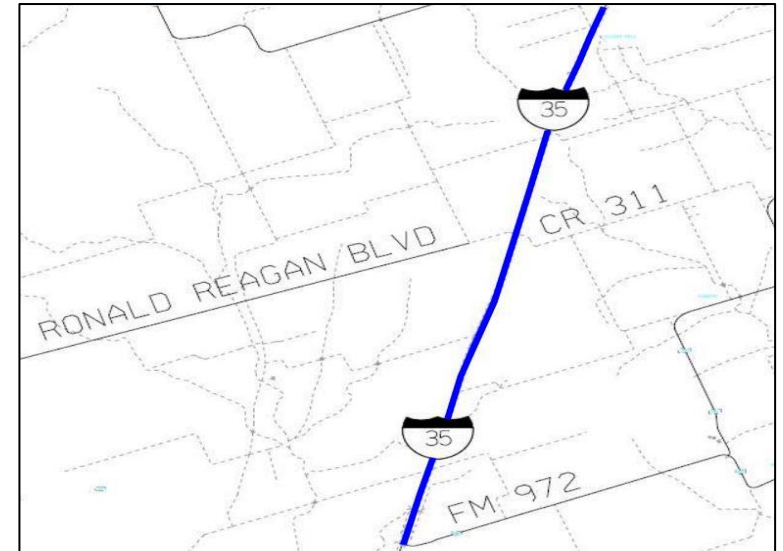

Partnership with TxDOT

Original Contract Amount = \$13,145,762.51

Construction is managed by TxDOT

IH 35 Ramp Reversals and Frontage Road²⁶ Conversion



IH 35 Ramp Reversals and Frontage Road Conversion ²⁷




IH 35 Ramp Reversals and Frontage Road Conversion²⁸



Ronald Reagan Boulevard at IH 35 (Bridge Replacement)

29

Anticipated Completion
Summer 2021

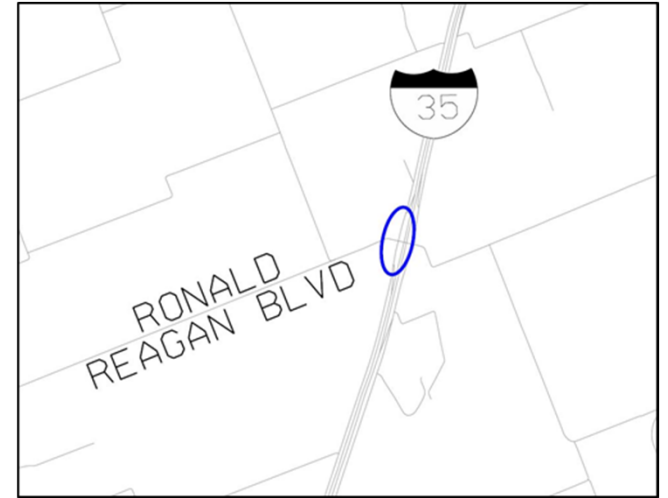

Partnership with TxDOT

Original Contract Amount = \$15,048,229.93

Construction is managed by TxDOT

Ronald Reagan Boulevard at IH 35 (Bridge Replacement)

30



Ronald Reagan Boulevard at IH 35 (Bridge Replacement)

31



Ronald Reagan Boulevard at IH 35 (Bridge Replacement)


32



CR 176 at RM 2243 (RM 2243 to Parkside Parkway)

33

Anticipated Completion
Summer 2020

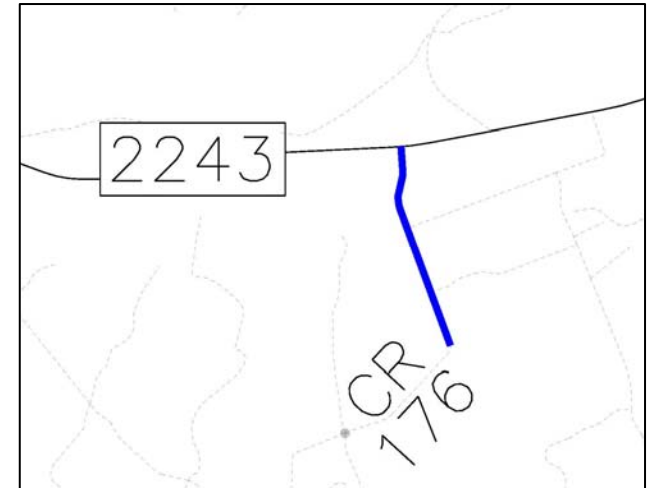

Original Contract Amount = \$2,447,560.00

Total Change Orders = \$208,869.67

Adjusted Contract Price = \$2,656,429.67

Expenditures to Date = \$1,994,292.26 (75%)

CR 176 at RM 2243 (RM 2243 to Parkside Parkway)




CR 176 at RM 2243 (RM 2243 to Parkside Parkway)



CR 176 at RM 2243 (RM 2243 to Parkside Parkway)




Precinct 4



CR 110 Middle (Limmer Loop to CR 107)

38

Anticipated Completion
Fall 2020

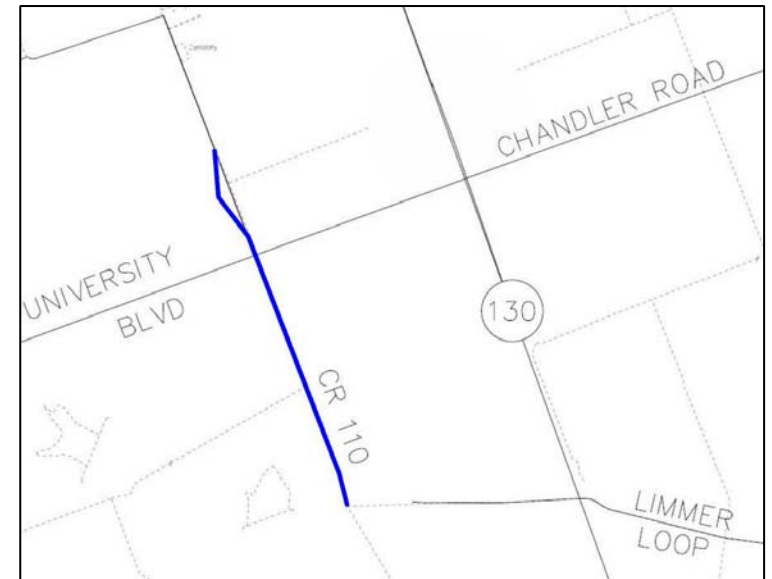

Original Contract Amount = \$8,910,862.73

Total Change Orders = \$98,172.70

Adjusted Contract Price = \$9,009,035.70

Expenditures to Date = \$5,532,279.83 (61%)

CR 110 Middle (Limmer Loop to CR 107)






CR 110 Middle (Limmer Loop to CR 107)



Oak Bluff and Greenfield Drainage Improvements

42

Anticipated Completion
Early 2021

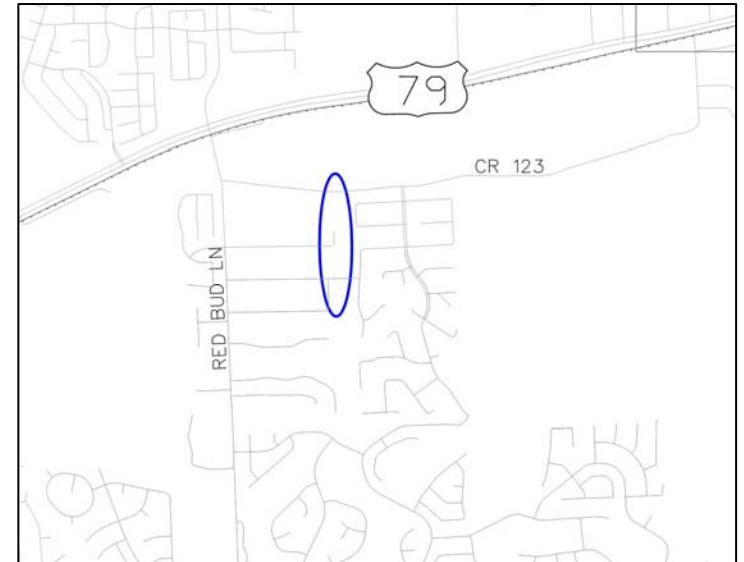

Partnership with City of Round Rock

Original Contract Amount = \$1,770,012.25

Construction is managed by City of Round Rock

Oak Bluff and Greenfield Drainage Improvements

43



Oak Bluff and Greenfield Drainage Improvements

44



Oak Bluff and Greenfield Drainage Improvements

45

