



Williamson County Commissioners Court

Road Bond Program

April 20, 2021



Precinct 1






RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)

3

Anticipated Completion
Summer 2022

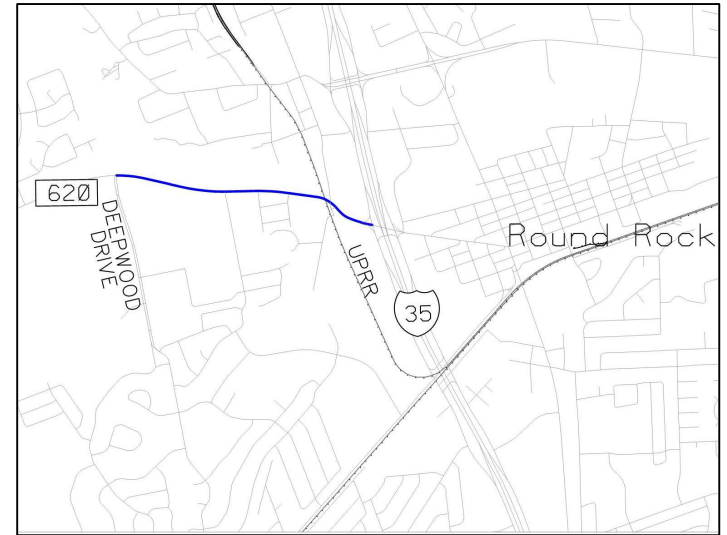

Partnership with TxDOT and the City of Round Rock

Original Contract Amount = \$27,468,703.67

Construction is managed by TxDOT

RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)

4



RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)

5



RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)

6






Forest North Phase 3 Drainage Improvements

7

Anticipated Completion
Early 2022

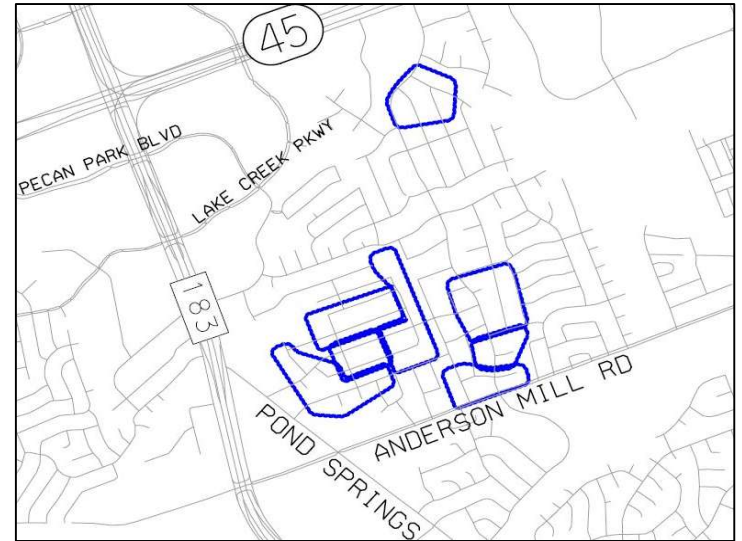

Original Contract Price = \$4,793,058.15

Total Change Orders to Date = \$87,744.37

Adjusted Contract Price = \$4,880,802.52

Expenditures to Date = \$2,921,816.48 (60%)

Forest North Phase 3 Drainage Improvements



Forest North Phase 3 Drainage Improvements



Forest North Phase 3 Drainage Improvements






O'Connor Traffic Signals

11

(Morgan Hill Trail, Liberty Walk, Great Oaks)

Anticipated Completion
Spring 2021

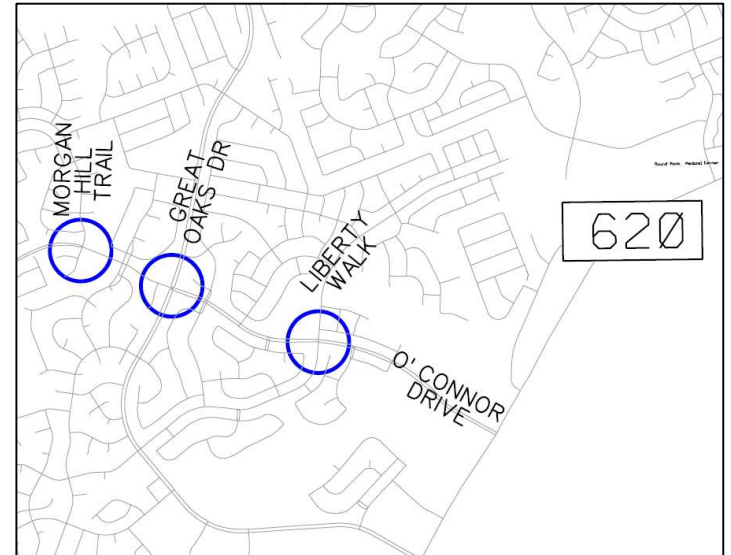

Original Contract Price = \$853,503.50

Total Change Orders to Date = \$131,055.38

Adjusted Contract Price = \$984,558.88

Expenditures to Date = \$611,860.08 (62%)

O'Connor Traffic Signals (Morgan Hill Trail, Liberty Walk, Great Oaks)

12



O'Connor Traffic Signals (Morgan Hill Trail, Liberty Walk, Great Oaks)



O'Connor Traffic Signals (Morgan Hill Trail, Liberty Walk, Great Oaks)

14






Corridor H – Sam Bass Road (Interim Traffic Signals)

15

Anticipated Completion
Spring 2021

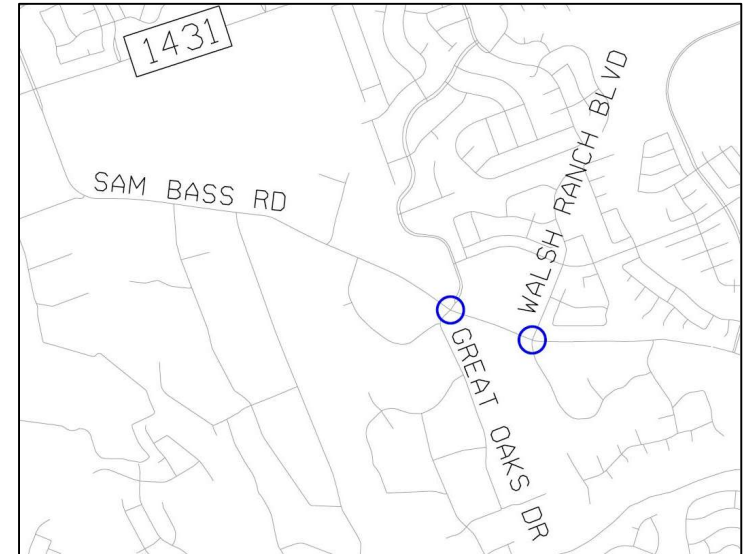

Original Contract Price = \$319,866.00

Total Change Orders to Date = \$28,476.86

Adjusted Contract Price = \$348,342.86

Expenditures to Date = \$77,562.00 (22%)

Corridor H – Sam Bass Road (Interim Traffic Signals)

16



Corridor H – Sam Bass Road (Interim Traffic Signals)



Corridor H – Sam Bass Road (Interim Traffic Signals)

18



Hairy Man Road / Brushy Creek Road Safety Improvements

19

Anticipated Completion
Winter 2021



Original Contract Price = \$3,964,380.00

Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$0.00

Expenditures to Date = \$465,113.84 (12%)

Hairy Man Road / Brushy Creek Road Safety Improvements



Hairy Man Road / Brushy Creek Road Safety Improvements

21




Hairy Man Road / Brushy Creek Road Safety Improvements



University Boulevard Widening (IH 35 to Sunrise Road)

23

Anticipated Completion
Early 2022

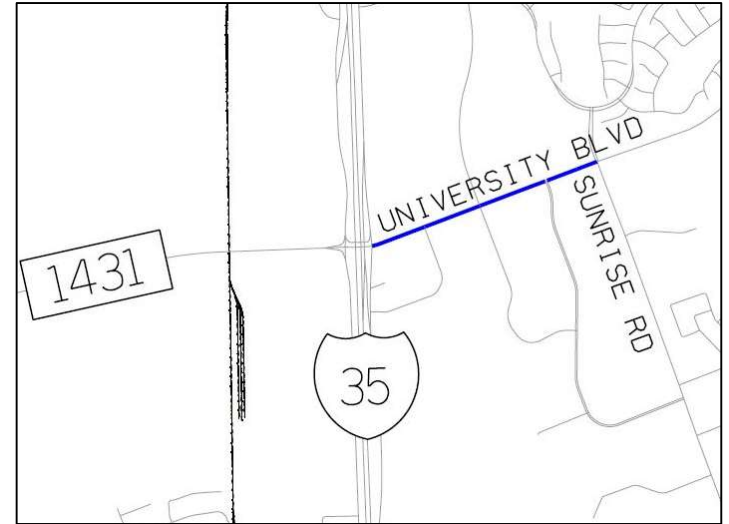

Partnership with the City of Round Rock

Original Contract Amount = \$12,135,410.45

Construction is managed by the City of Round Rock

University Boulevard Widening (IH 35 to Sunrise Road)

24



University Boulevard Widening (IH 35 to Sunrise Road)

25




University Boulevard Widening (IH 35 to Sunrise Road)

26




Precinct 2

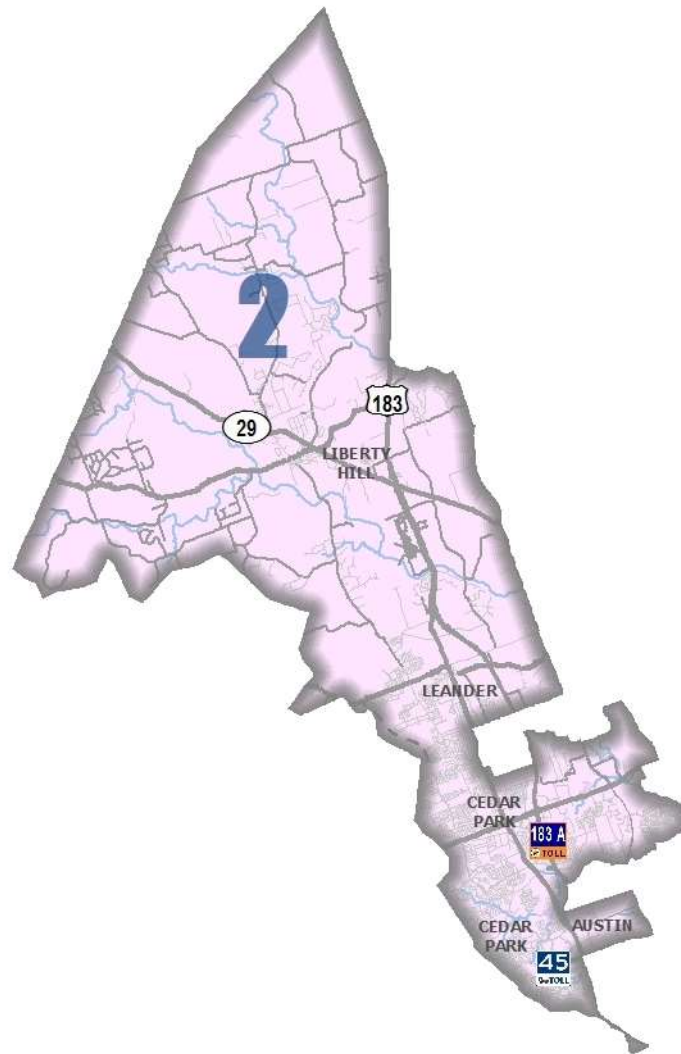

Seward Junction Improvements

Substantially Complete
March 15, 2021

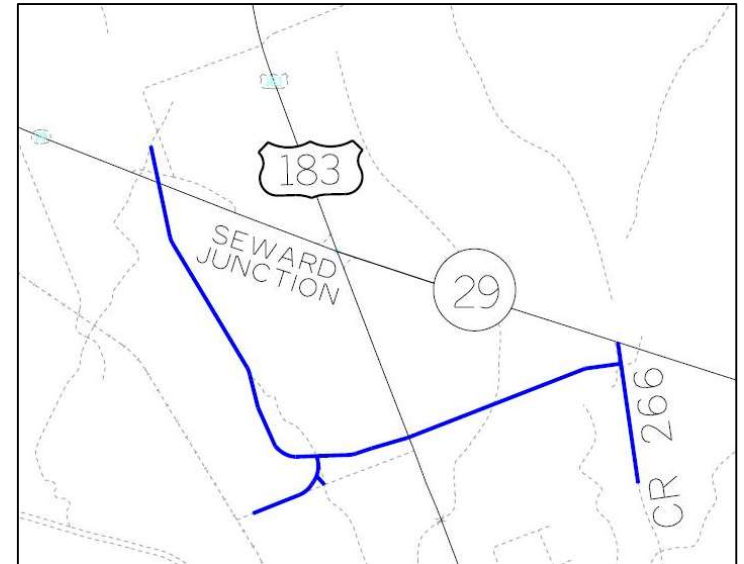

Original Contract Price = \$13,270,258.10

Total Change Orders to Date = \$611,059.17

Adjusted Contract Price = \$13,881,317.27

Expenditures to Date = \$12,503,329.95 (90%)

Seward Junction Improvements




Seward Junction Improvements



Seward Junction Improvements



Precinct 3






Ronald Reagan Boulevard at IH 35 (Bridge Replacement)

33

Anticipated Completion
Fall 2021

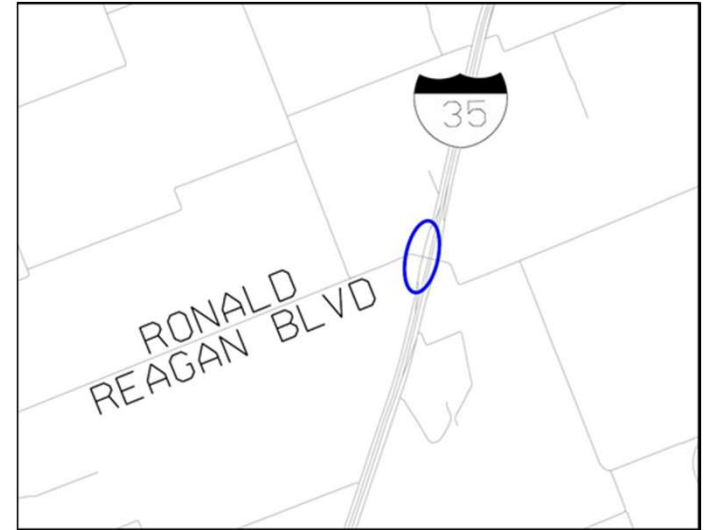

Partnership with TxDOT

Original Contract Amount = \$15,048,229.93

Construction is managed by TxDOT

Ronald Reagan Boulevard at IH 35 (Bridge Replacement)

34



Ronald Reagan Boulevard at IH 35 (Bridge Replacement)

35



Ronald Reagan Boulevard at IH 35 (Bridge Replacement)

36




Ronald Reagan at Silver Spur

Ronald Reagan at Sun City

37

Anticipated Completion
Spring 2021

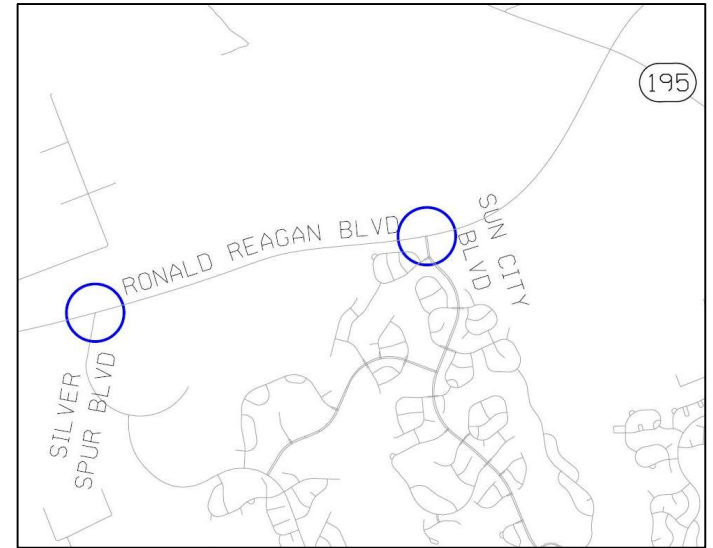

Original Contract Price = \$875,350.00

Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$875,350.00

Expenditures to Date = \$182,188.03 (21%)

Ronald Reagan at Silver Spur Ronald Reagan at Sun City

38



Ronald Reagan at Silver Spur Ronald Reagan at Sun City

39




Ronald Reagan at Silver Spur Ronald Reagan at Sun City

40



Precinct 4

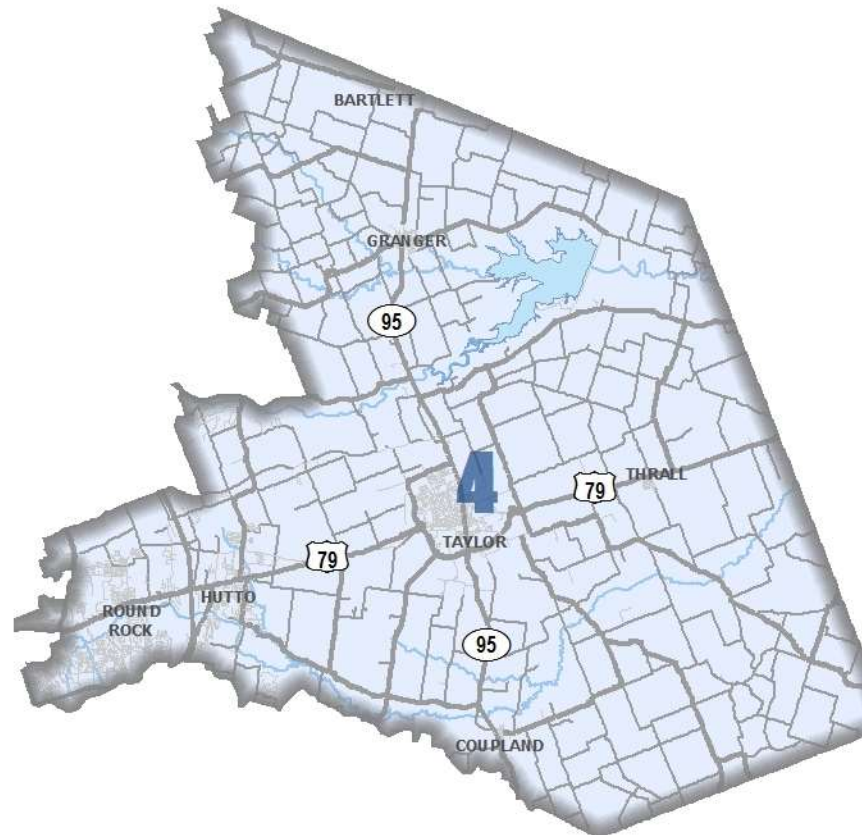



CR 101

42

(US 79 to North of Chandler Road)

Anticipated Completion
Winter 2021



Original Contract Amount = \$13,092,842.00

Total Change Orders = \$0.00

Adjusted Contract Price = \$13,092,842.00

Expenditures to Date = \$5,696,183.56 (44%)

CR 101 (US 79 to North of Chandler Road)

43



CR 101 (US 79 to North of Chandler Road)



CR 101 (US 79 to North of Chandler Road)

