



# Williamson County Commissioners Court


---

Road Bond Program

August 15, 2023



# Precinct 1

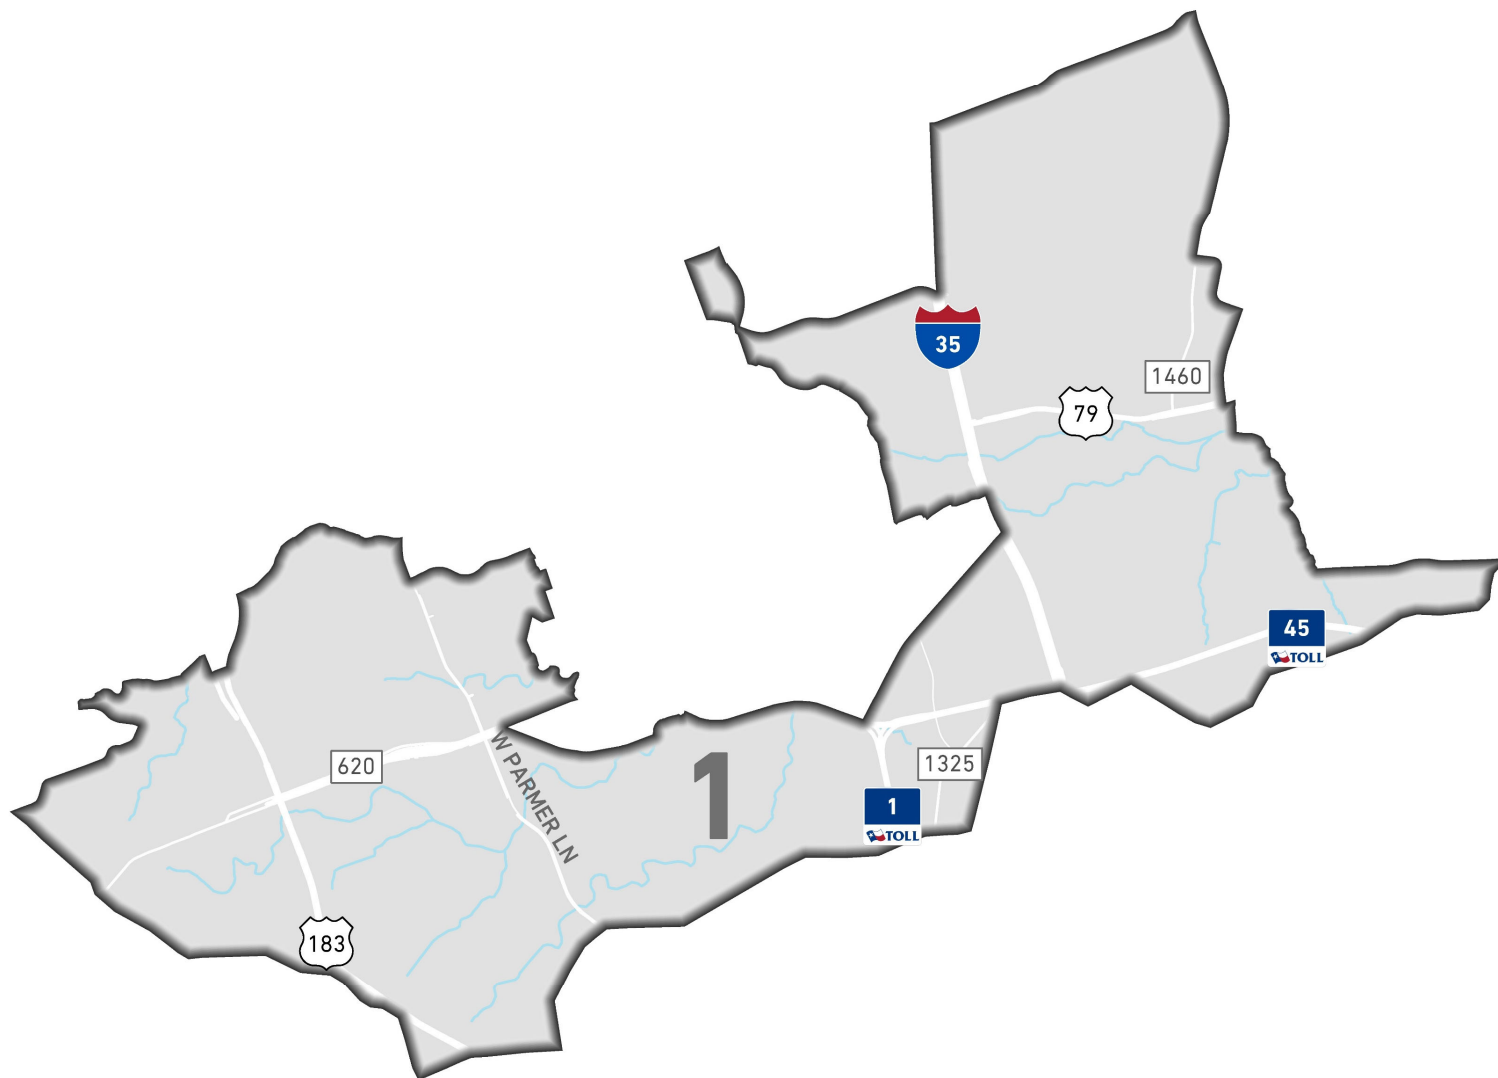



# RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)

3

Anticipated Completion  
Fall 2023



Partnership with TxDOT and the City of Round Rock  
Original Contract Amount = \$27,468,703.67  
Construction is managed by TxDOT



# RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)





# RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)






# RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)




# Precinct 2

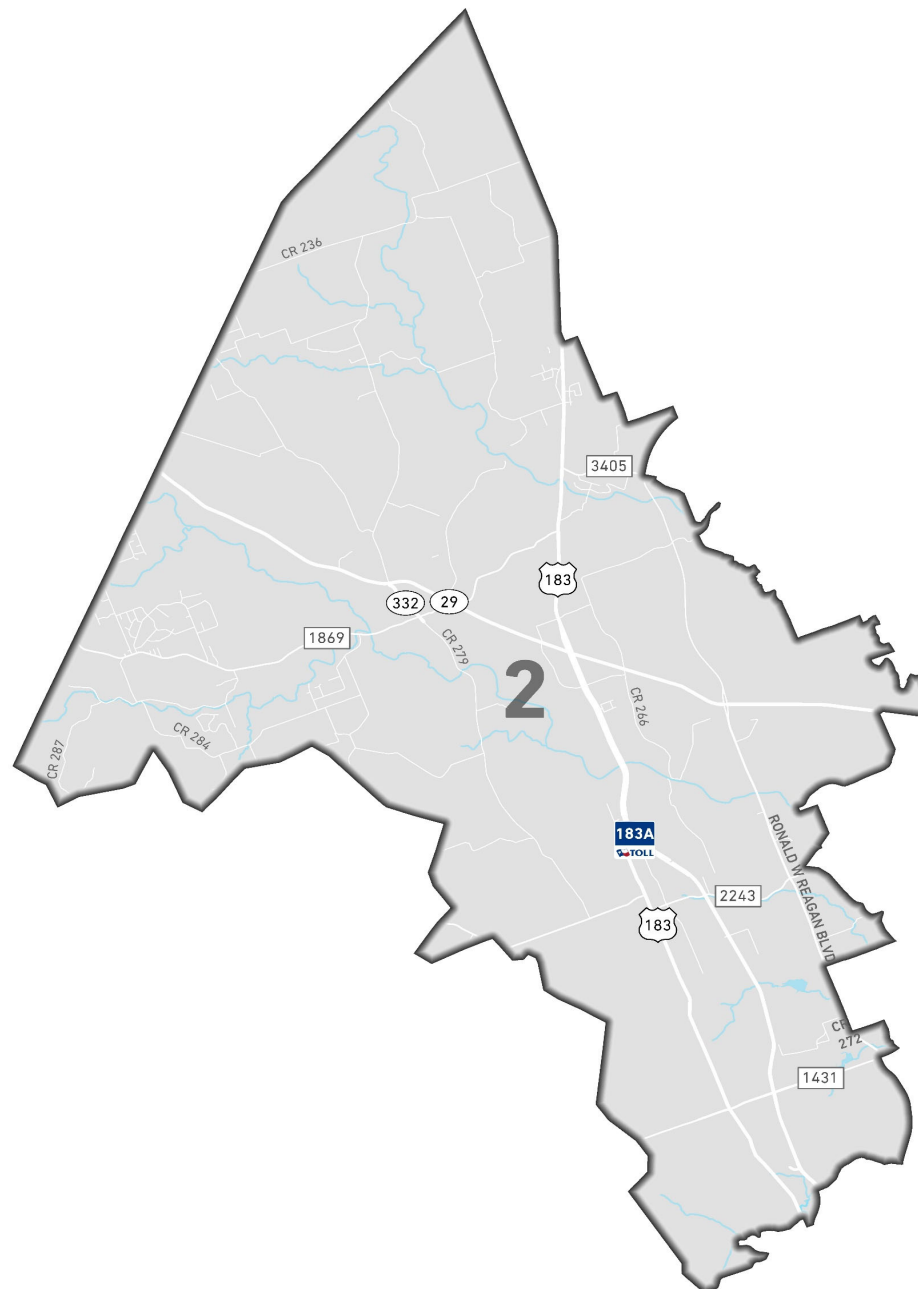



## CR 258 Extension

Anticipated Completion  
Early 2024

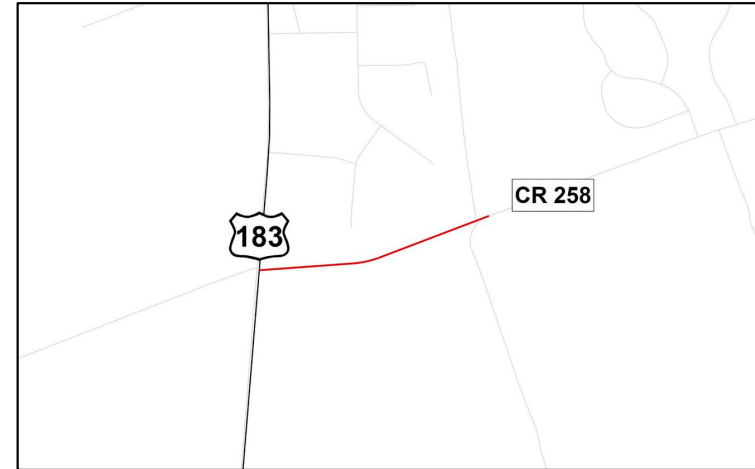

Original Contract Price = \$5,836,754.36

Total Change Orders to Date = \$291,537.19

Adjusted Contract Price = \$6,128,291.55

Expenditures to Date = \$4,239,767.11 (69%)



# CR 258 Extension





# CR 258 Extension






# CR 258 Extension






# Precinct 3





# CR 111 Westinghouse Road

Anticipated Completion  
Spring 2024

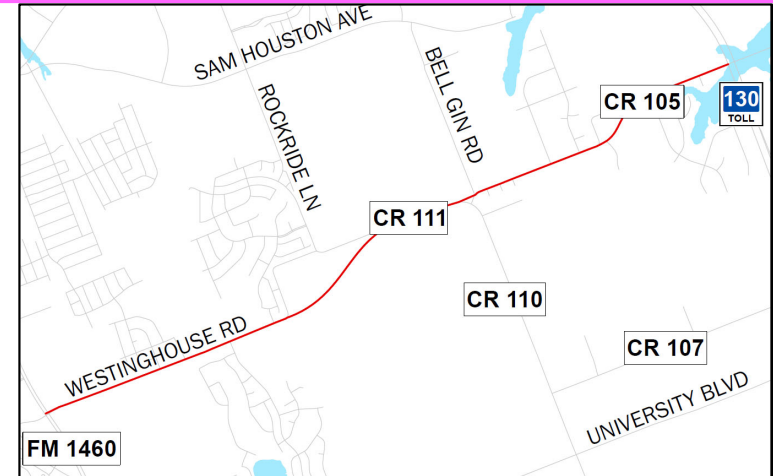

Original Contract Price = \$21,024,332.88

Total Change Orders to Date = \$1,139,215.80

Adjusted Contract Price = \$22,163,548.68

Expenditures to Date = \$15,739,435.75 (71%)

# CR 111 Westinghouse Road





# CR 111 Westinghouse Road






# CR 111 Westinghouse Road



# New Hope Drive Phase 2A

Anticipated Completion  
Spring 2024

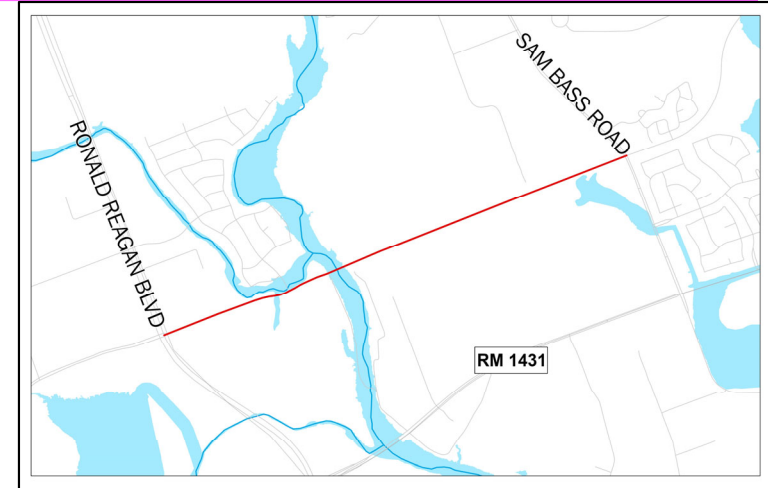

Partnership with the City of Cedar Park

Original Contract Amount = \$22,619,961.16

Construction is managed by the City of Cedar Park



# New Hope Drive Phase 2A





# New Hope Drive Phase 2A






# New Hope Drive Phase 2A





# CR 245 Reconstruction

Anticipated Completion  
Spring 2024

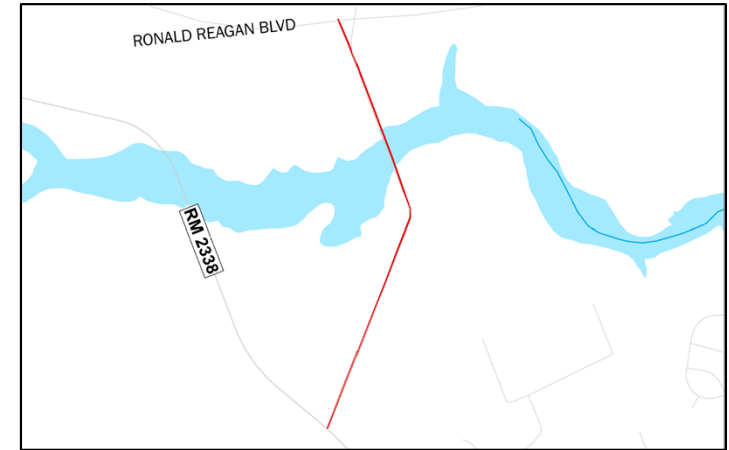

Original Contract Price = \$6,969,195.21

Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$ 6,969,195.21

Expenditures to Date = \$2,063,997.71 (30%)

# CR 245 Reconstruction





# CR 245 Reconstruction





# CR 245 Reconstruction






# Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)

---

Anticipated Completion  
Fall 2025

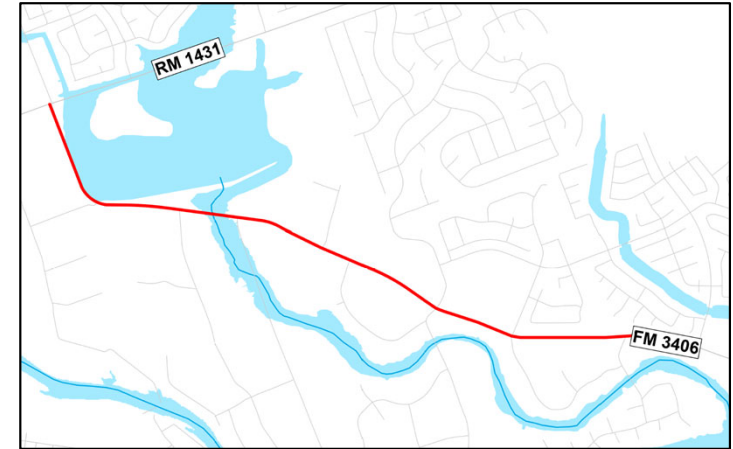

Original Contract Price = \$36,145,959.00

Total Change Orders to Date = -\$2,394,078.12

Adjusted Contract Price = \$33,751,880.88

Expenditures to Date = \$1,895,086.83 (6%)



# Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)





# Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)






# Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)






# Precinct 4

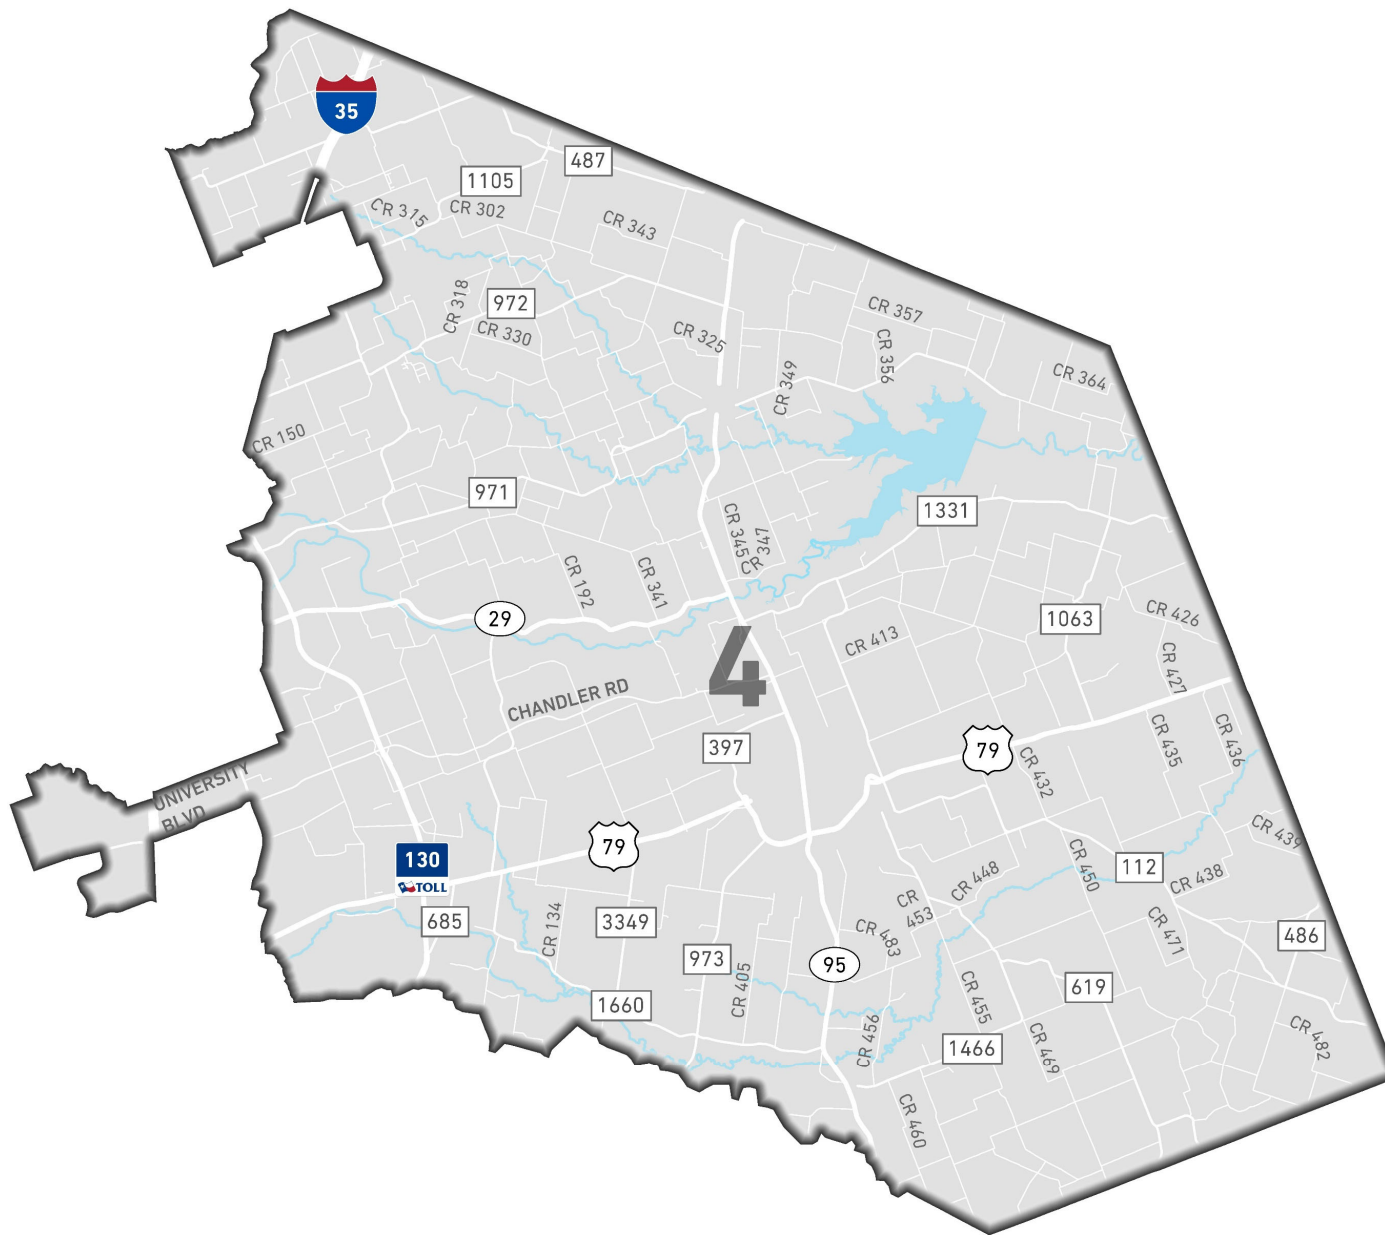

# East Wilco Highway (Southeast Loop Segment 1) (Corridor E1) (CR 138 to CR 137)

Anticipated Completion  
Summer 2023

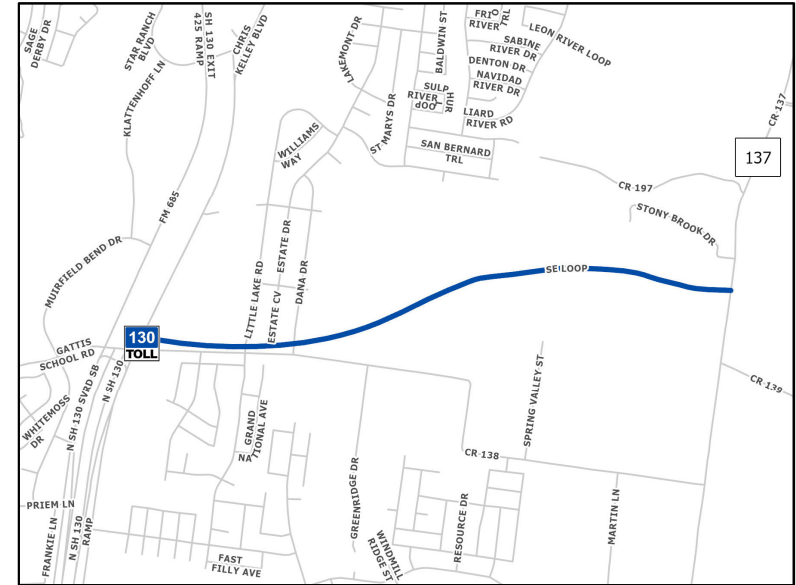

Original Contract Amount = \$11,526,789.09

Total Change Orders = \$1,649,338.56

Adjusted Contract Price = \$13,176,127.65

Expenditures to Date = \$11,145,192.29 (85%)



# East Wilco Highway (Southeast Loop Segment 1) (Corridor E1) (CR 138 to CR 137)





# East Wilco Highway (Southeast Loop Segment 1) (Corridor E1) (CR 138 to CR 137)






# East Wilco Highway (Southeast Loop Segment 1) (Corridor E1) (CR 138 to CR 137)





# CR 401 Reconstruction

Anticipated Completion  
Summer 2023

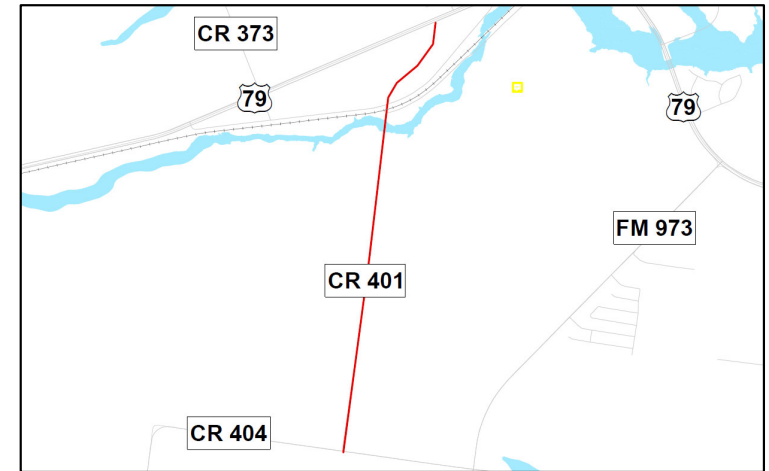

Original Contract Amount = \$12,673,200.94

Total Change Orders = \$830,893.84

Adjusted Contract Price = \$ 13,504,094.78

Expenditures to Date = \$11,597,552.94 (86%)



# CR 401 Reconstruction





# CR 401 Reconstruction






# Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)

---

Anticipated Completion  
Late 2023

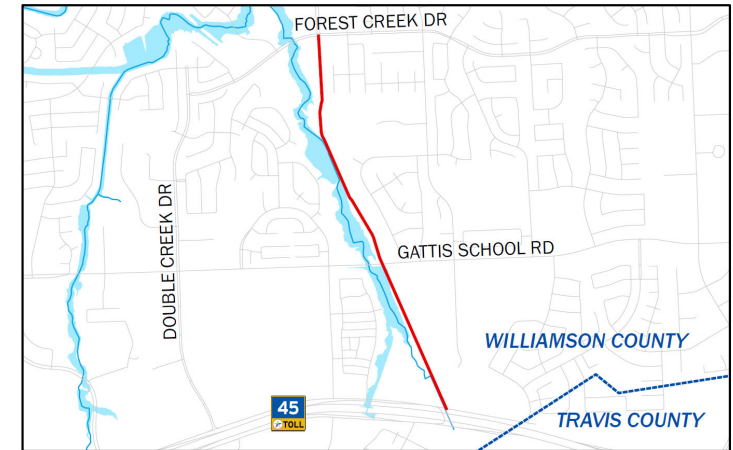

Partnership with the City of Round Rock

Original Contract Amount = \$23,409,120.97

Construction is managed by the City of Round Rock



# Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)





# Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)





# Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)






# Samsung Highway (Future County Road) <sup>41</sup> (CR 404 to FM 973)

---

Anticipated Completion  
Fall 2023

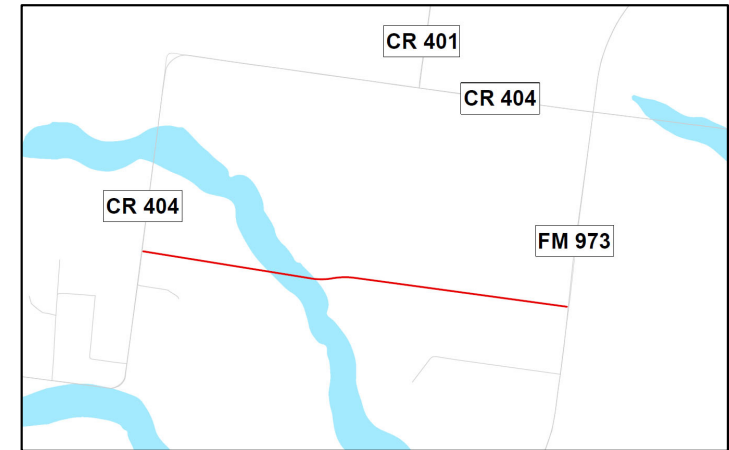

Original Contract Amount = \$11,289,929.00

Total Change Orders = \$41,260.00

Adjusted Contract Price = \$11,331,189.00

Expenditures to Date = \$10,679,501.35 (94%)





# Samsung Highway (Future County Road) (CR 404 to FM 973)








# Samsung Highway (Future County Road) (CR 404 to FM 973)





# East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)

Anticipated Completion  
Summer 2025 (Roadwork)

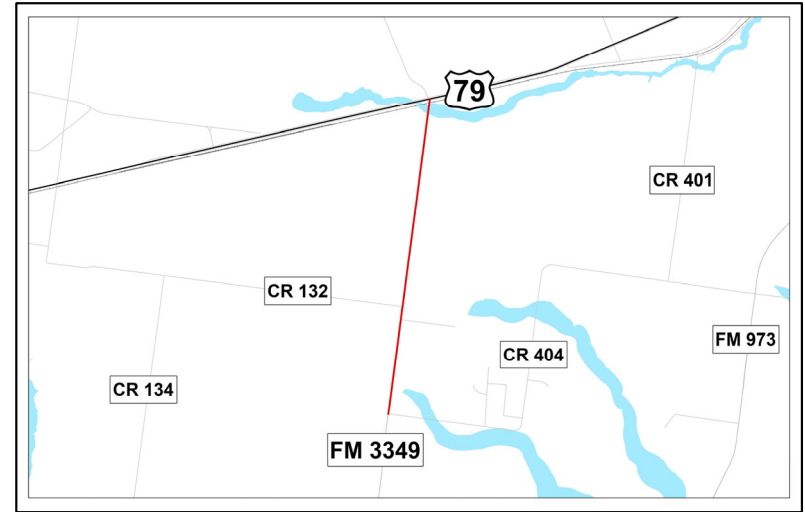

Original Contract Amount = \$81,941,038.13

Total Change Orders = \$1,202,657.22

Adjusted Contract Price = \$ 83,143,695.35

Expenditures to Date = \$17,842,375.82 (21%)



# East Wilco Highway (FM 3349 / US 79) Interchange (US 79 to CR 404)





# East Wilco Highway (FM 3349 / US 79) Interchange (US 79 to CR 404)





# East Wilco Highway (FM 3349 / US 79) Interchange (US 79 to CR 404)






# CR 366 Reconstruction (Chandler Road to Carlos G. Parker Blvd.)

---

Anticipated Completion  
Summer 2024

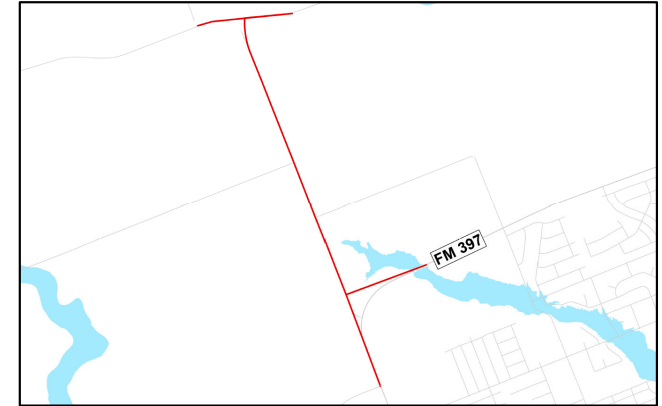

Original Contract Amount = \$17,694,262.46

Total Change Orders = \$11,562.50

Adjusted Contract Price = \$17,705,824.96

Expenditures to Date = \$4,161,766.30 (24%)



# CR 366 Reconstruction (Chandler Road to Carlos G. Parker Blvd.)







# CR 366 Reconstruction (Chandler Road to Carlos G. Parker Blvd.)





# CR 366 Reconstruction (Chandler Road to Carlos G. Parker Blvd.)





# CR 404 and FM 973 Improvements

---

Anticipated Completion  
Summer 2023



Original Contract Amount = \$4,622,143.93

Total Change Orders = \$0.00

Adjusted Contract Price = \$ 4,622,143.93

Expenditures to Date = \$4,291,953.91 (93%)



# CR 404 and FM 973 Improvements






# CR 404 and FM 973 Improvements





# Bud Stockton Extension (CR 305 to FM 487)

Anticipated Completion  
Fall 2023

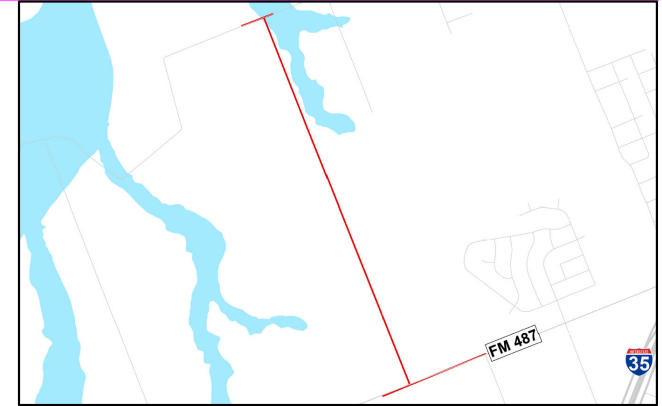

Original Contract Amount = \$5,917,275.00

Total Change Orders = \$35,830.59

Adjusted Contract Price = \$ 5,953,105.59

Expenditures to Date = \$3,010,052.50 (51%)



# Bud Stockton Extension (CR 305 to FM 487)





# Bud Stockton Extension (CR 305 to FM 487)






# Bud Stockton Extension (CR 305 to FM 487)





# Samsung Highway (CR 404 Realignment) <sup>59</sup> (FM 3349 to CR 404)

Anticipated Completion  
Summer 2024

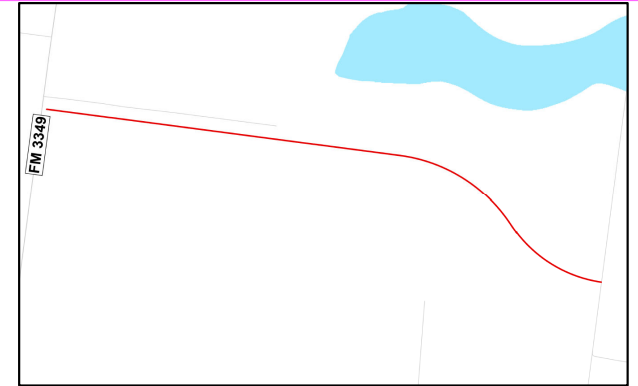

Original Contract Amount = \$5,139,487.45

Total Change Orders = \$0.00

Adjusted Contract Price = \$5,139,487.45

Expenditures to Date = \$1,054,105.16 (21%)



# Samsung Highway (CR 404 Realignment) (FM 3349 to CR 404)





# Samsung Highway (CR 404 Realignment) (FM 3349 to CR 404)





# Samsung Highway (CR 404 Realignment) (FM 3349 to CR 404)






# CR 307 Reconstruction (CR 307 North of CR 305)

---

Anticipated Completion  
Fall 2023

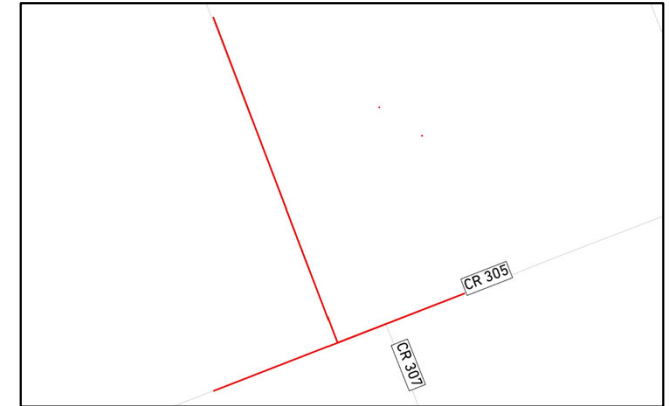

Original Contract Amount = \$2,796,832.80

Total Change Orders = \$0.00

Adjusted Contract Price = \$2,796,832.80

Expenditures to Date = \$559,664.00 (20%)



# CR 307 Reconstruction (CR 307 North of CR 305)





# CR 307 Reconstruction (CR 307 North of CR 305)





# CR 307 Reconstruction (CR 307 North of CR 305)

