


# Williamson County Commissioners Court

---

Road Bond Program  
January 23, 2024




# Precinct 1

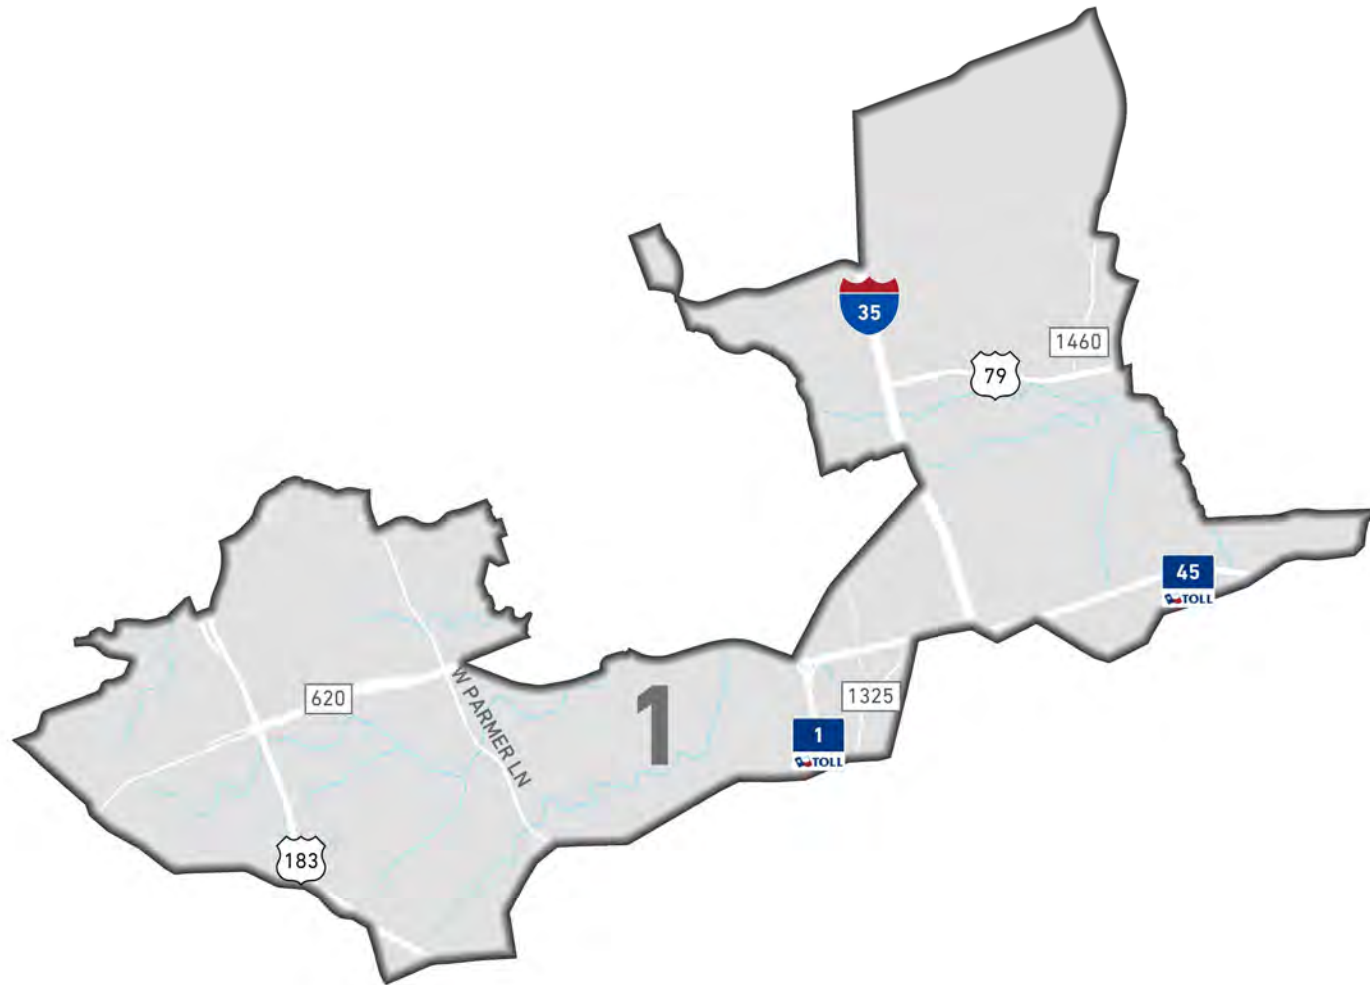

# No Active Construction Projects

# Precinct 2

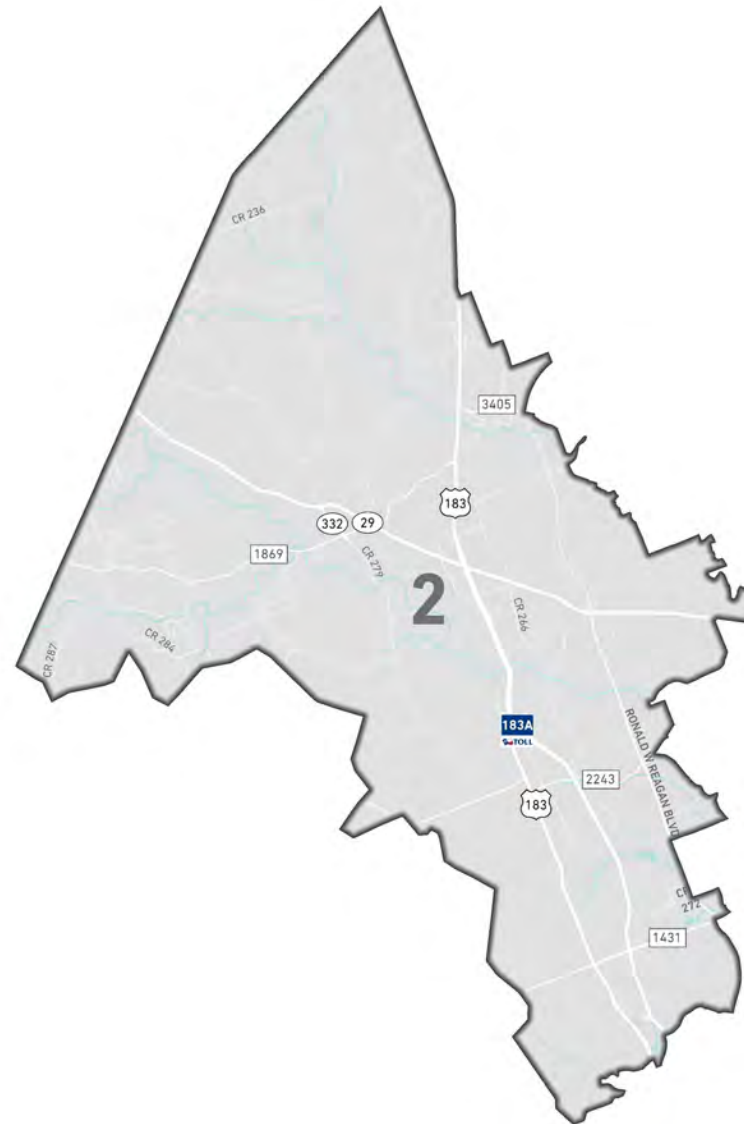

# CR 258 Extension

Substantially Complete  
December 2023



Original Contract Price = \$5,836,754.36

Total Change Orders to Date = \$831,161.15


Adjusted Contract Price = \$6,667,915.51

Expenditures to Date = \$5,702,264.83 (86%)

# CR 258 Extension




# Precinct 3

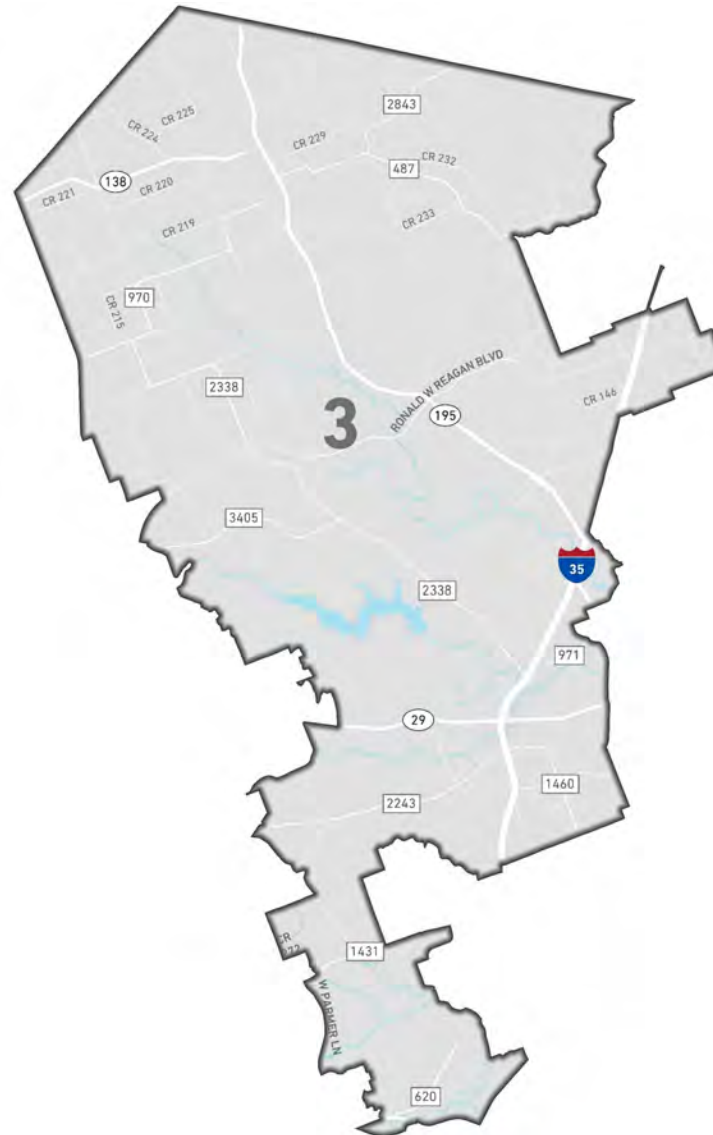

# CR 111 Westinghouse Road

Anticipated Completion  
Spring 2024

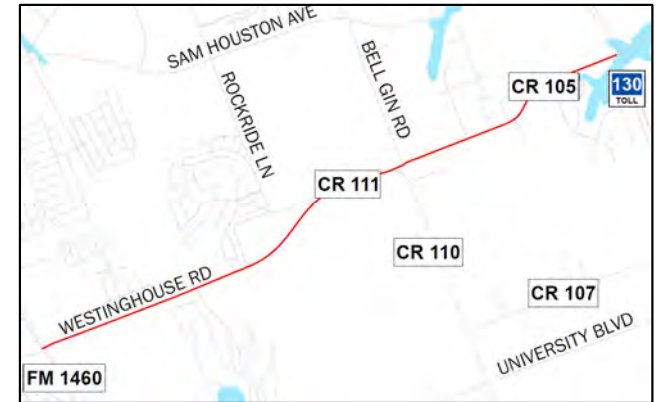

Original Contract Price = \$21,024,332.88

Total Change Orders to Date = \$1,220,648.92

Adjusted Contract Price = \$22,244,981.80

Expenditures to Date = \$17,621,967.04 (79%)



# CR 111 Westinghouse Road





# CR 111 Westinghouse Road






# CR 111 Westinghouse Road



# CR 245 Reconstruction

Substantially Complete  
December 2023

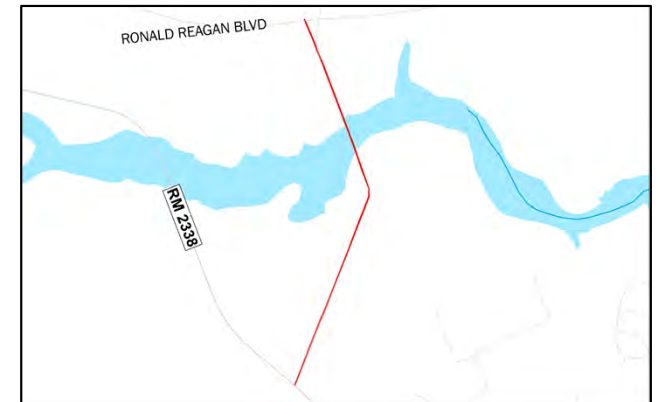

Original Contract Price = \$6,969,195.21  
Total Change Orders to Date = \$20,980.10  
Adjusted Contract Price = \$ 6,990,175.31  
Expenditures to Date = \$5,692,128.21 (81%)



# CR 245 Reconstruction





# CR 245 Reconstruction






# CR 245 Reconstruction



## Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)

Anticipated Completion  
Fall 2025

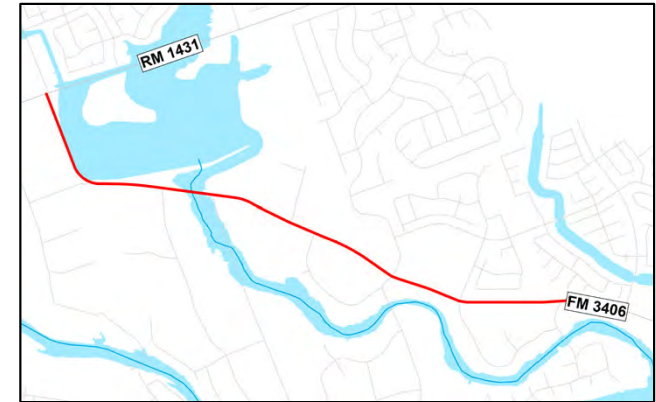

Original Contract Price = \$36,145,959.00

Total Change Orders to Date = -\$2,388,828.12

Adjusted Contract Price = \$33,757,130.88

Expenditures to Date = \$5,559,354.52 (16%)



# Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)





# Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)






# Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)




# Precinct 4

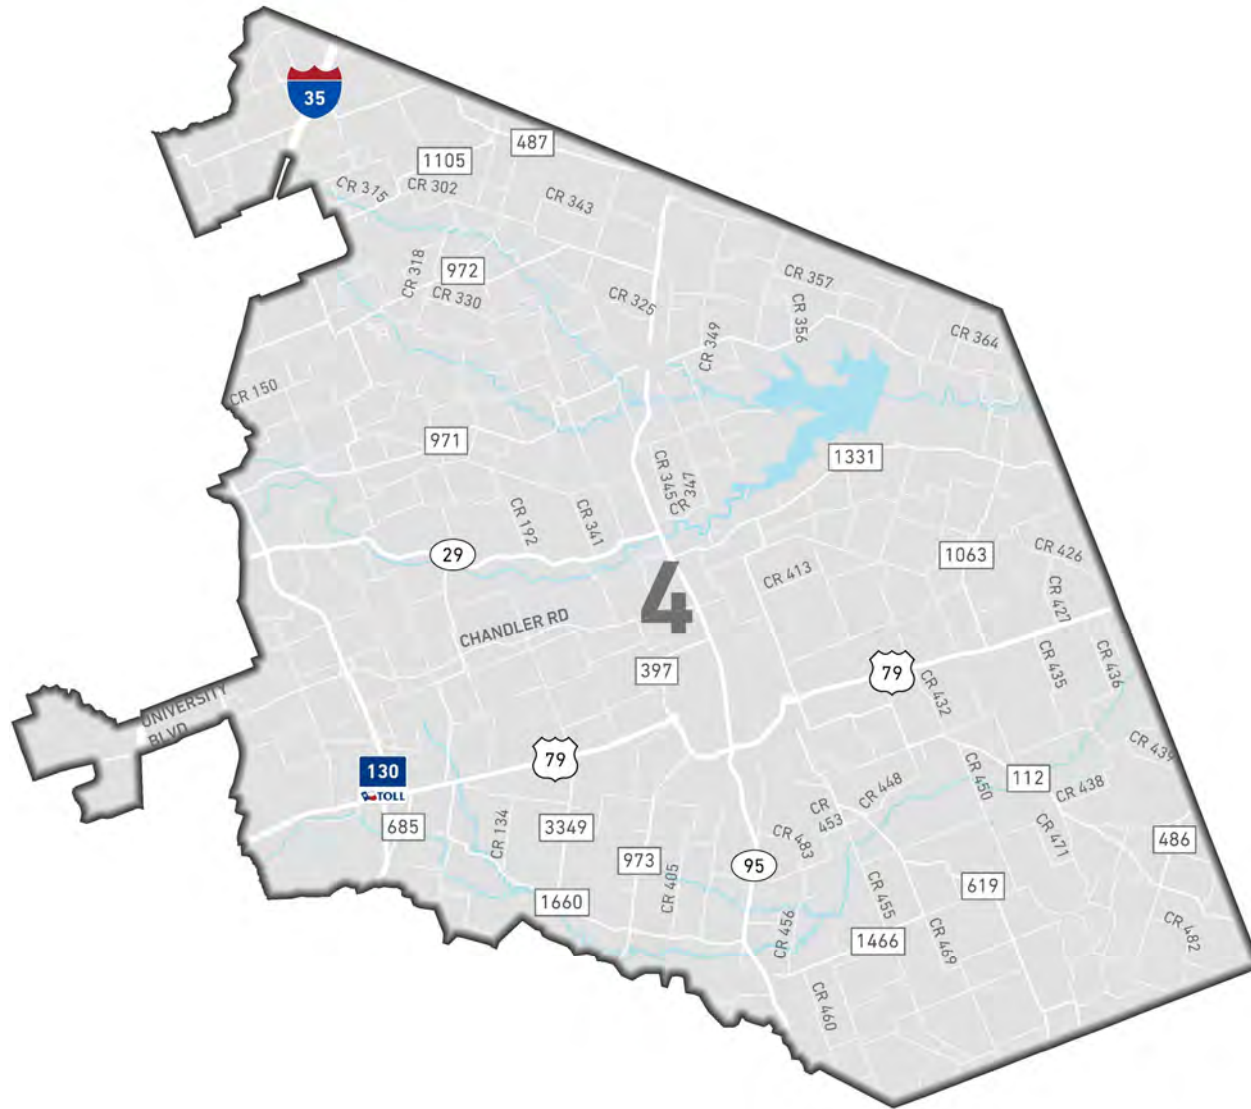



# Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)

Anticipated Completion  
Early 2024

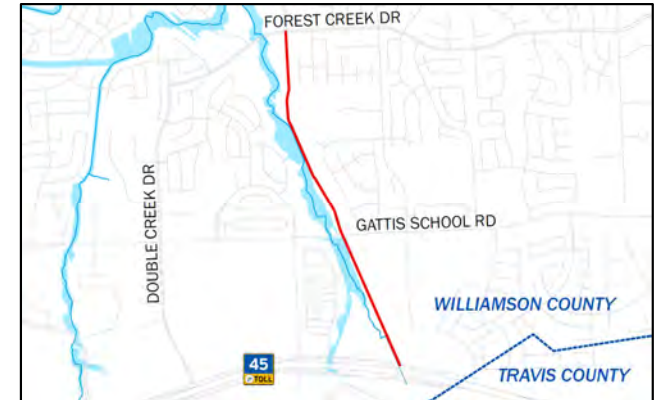

Partnership with the City of Round Rock

Original Contract Amount = \$23,409,120.97

Construction is managed by the City of Round Rock

## Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)





## Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)






## Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)





# East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)

Anticipated Completion  
Summer 2025 (Roadwork)

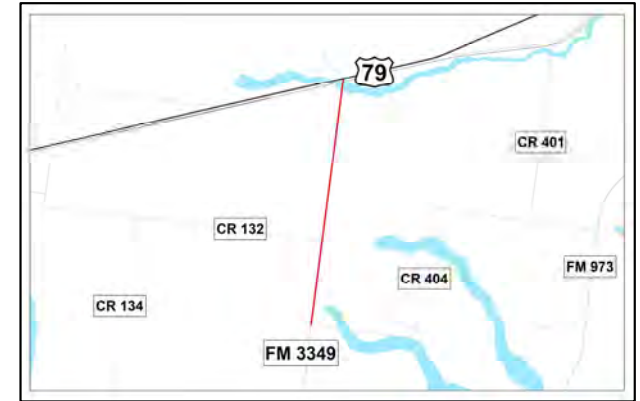

Original Contract Amount = \$81,941,038.13

Total Change Orders = \$1,843,295.83

Adjusted Contract Price = \$ 83,784,333.96

Expenditures to Date = \$32,318,295.36 (39%)

# East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)





# East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)





# East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)



# CR 366 Reconstruction (Chandler Road to Carlos G. Parker Blvd.)

Anticipated Completion  
Summer 2024



Original Contract Amount = \$17,694,262.46

Total Change Orders = \$93,578.30

Adjusted Contract Price = \$17,787,840.76

Expenditures to Date = \$9,141,597.06 (51%)



# CR 366 Reconstruction (Chandler Road to Carlos G. Parker Blvd.)





# CR 366 Reconstruction (Chandler Road to Carlos G. Parker Blvd.)





# CR 366 Reconstruction (Chandler Road to Carlos G. Parker Blvd.)





# Corridor C / SH 29 Bypass (Sam Houston Avenue at Patriot Way to SH 29)

Anticipated Completion  
Fall 2025



Original Contract Amount = \$30,540,848.03

Total Change Orders = \$0.00

Adjusted Contract Price = \$30,540,848.03

Expenditures to Date = \$5,307,536.29 (17%)

# Corridor C / SH 29 Bypass (Sam Houston Avenue at Patriot Way to SH 29)





# Corridor C / SH 29 Bypass (Sam Houston Avenue at Patriot Way to SH 29)





# Corridor C / SH 29 Bypass (Sam Houston Avenue at Patriot Way to SH 29)

