



ROAD BOND PROGRAM

Construction Summary Report


County Judge
Bill Gravell, Jr.

Commissioners
Terry Cook
Cynthia Long
Valerie Covey
Russ Boles

March 2024

WWW.WILCOTX.GOV

Volume XXVII - Issue No.3

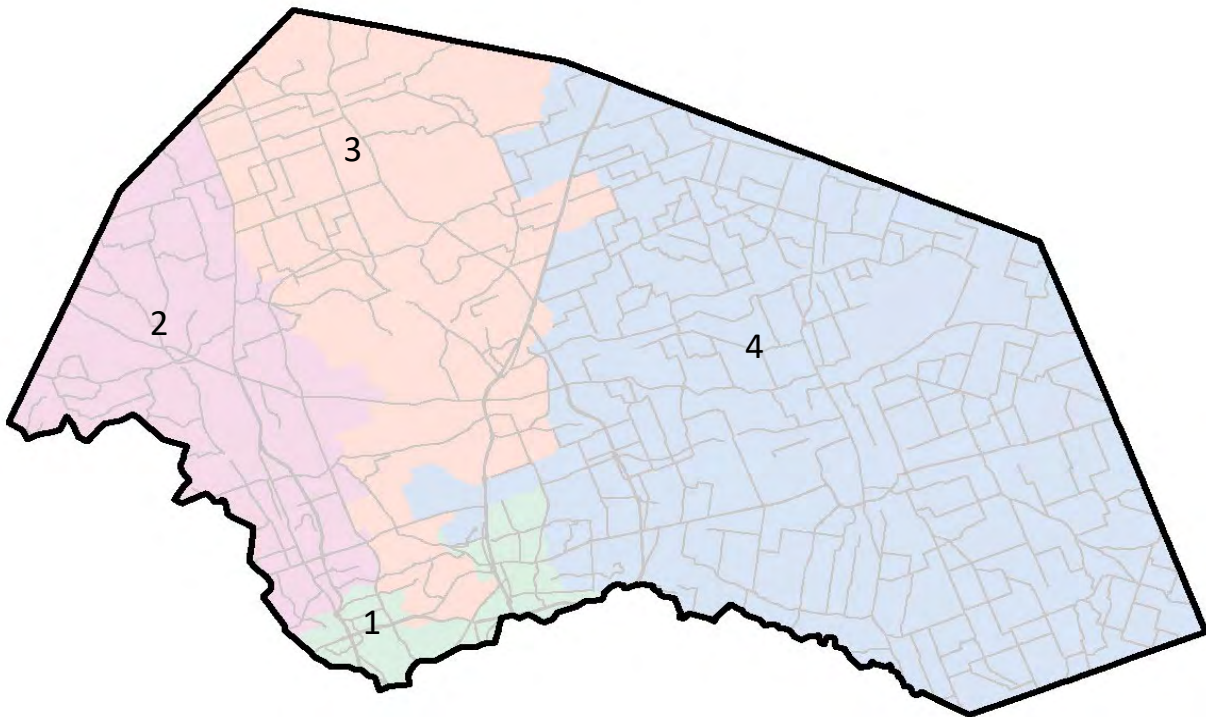

Presented By:



Table of Contents



Completed Projects	1
PRECINCT No. 1 – Commissioner Terry Cook.....	5
North Mays Street Extension Phase 1 (Paloma Drive to Oakmont Drive).....	9
PRECINCT No. 2 – Commissioner Cynthia Long	11
CR 258 Extension (US 183 to Sunset Ridge Drive).....	15
Ronald Reagan at Elizabeth Park Temporary Signals.....	16
Liberty Hill (SH 29) Bypass (RM 1869 to CR 279).....	17
PRECINCT No. 3 – Commissioner Valerie Covey	19
Great Oaks Drive Bridge at Brushy Creek	23
CR 111 Westinghouse Road.....	25
Southwest Bypass Extension	28
CR 245 Reconstruction	29
Corridor H/Sam Bass Road	30
PRECINCT No. 4 – Commissioner Russ Boles.....	32
East Wilco Highway (Southeast Loop Segment 1, Phase 1)	36
CR 401 Reconstruction.....	37
Samsung Highway (Future County Road) (CR 404 to FM 973).....	38
East Wilco Highway (FM 3349 at US 79 (FM 3349 from US to CR 404)).....	39
CR 366 (Chandler Road to Carlos G. Parker Boulevard)	42
Bud Stockton Extension (CR 305 to FM 487).....	44
CR 404 at FM 973 Improvements	45
CR 307 and CR 305 (CR 307 North of CR 305)	46
Samsung Highway (CR 404 Realignment) (FM 3349 to CR 404)	47
Corridor C / SH 29 Bypass	48
CR 332 Realignment (South of FM 487 to North of CR 313).....	50
CR 138 Right Turn Lane at SH 130.....	52
CR 129 (South of Brushy Creek to North of South County Line).....	54

WILLIAMSON COUNTY


ROAD BOND PROGRAM

COMPLETED PROJECTS

CONSTRUCTION SUBSTANTIALLY COMPLETE/OPEN TO TRAFFIC - AS OF MARCH 2024

Precinct 1

- Pond Springs Road (signal) – Apr 2002
- McNeil Road, Phase 1 – Jan 2005
- McNeil Road, Phase 2 – Feb 2007
- RM 620, Phase 1 – Jan 2009
- Pond Springs Road – Sep 2010
- County Road 174 at Brushy Creek – Jun 2011
- O'Connor Drive Extension – Apr 2012
- King of Kings Crossing – Aug 2012
- RM 620 Safety Improvements – Dec 2014
- Forest North Drainage Improvements Phase 2 – Oct 2017
- O'Connor Drive N of RM 620 – Jul 2018
- Neenah Avenue Widening – Dec 2018
- Lakeline Right Turn Lanes – Aug 2019
- Forest North Drainage Improvements – Anderson Mill – Feb 2020
- North Mays Extension- Dec 2020
- Forest North Drainage Improvements Phase 3 – Jan 2022
- RM 620 at Railroad/Chisolm Trail – Dec 2023

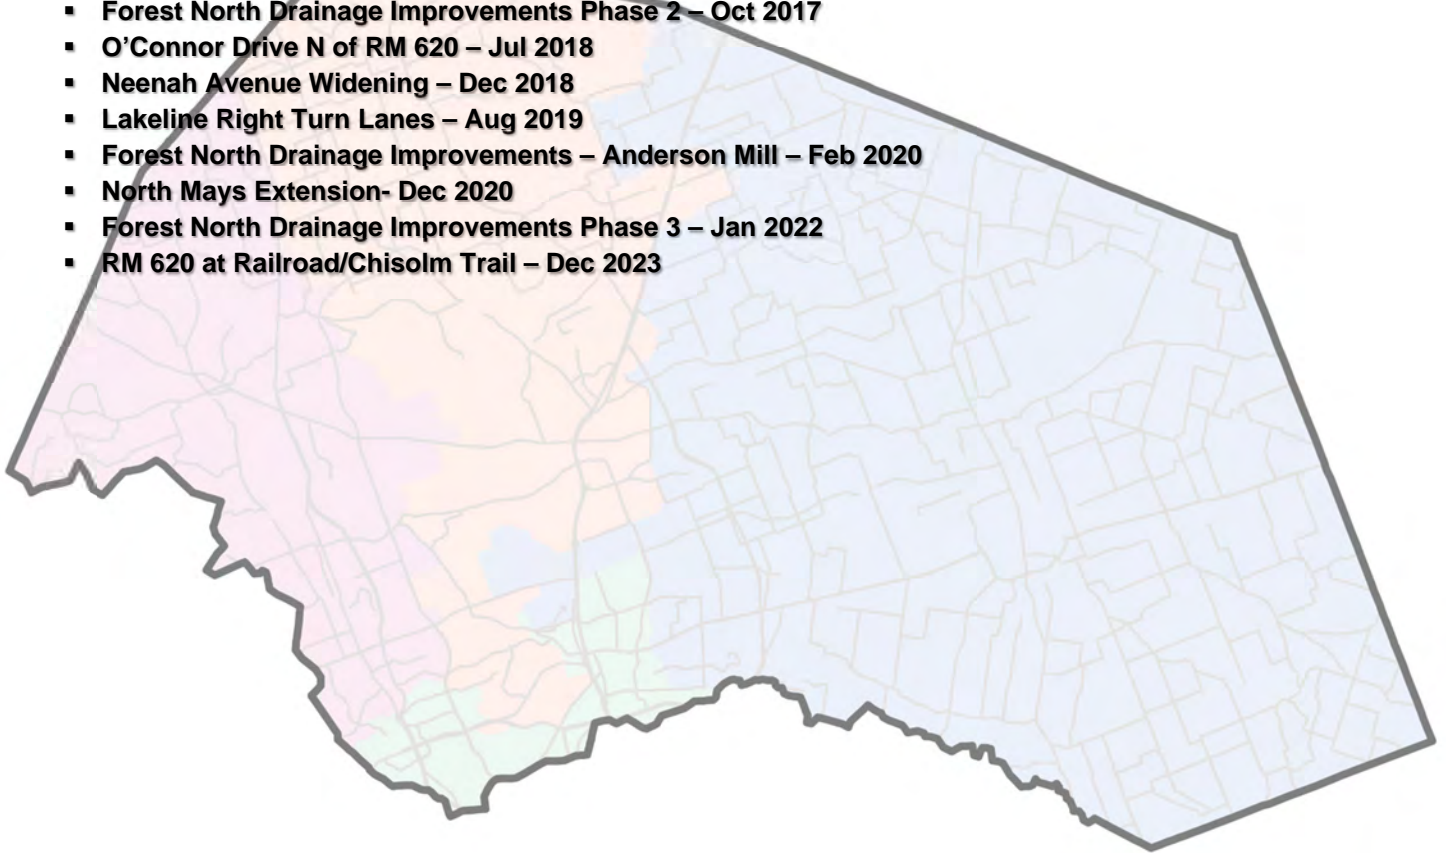

WILLIAMSON COUNTY

ROAD BOND PROGRAM

COMPLETED PROJECTS

CONSTRUCTION SUBSTANTIALLY COMPLETE/OPEN TO TRAFFIC - AS OF MARCH 2024

Precinct 2

- RM 1869 at SH 29 (signal) – Aug 2002
- River Bend Oaks – Feb 2003
- County Road 175 – Jun 2003
- County Road 200 – Sep 2003
- Ronald Reagan Blvd, South Ph. 1 – Dec 2004
- County Road 214 – Feb 2005
- County Road 258 – Sep 2006
- San Gabriel Pkwy, Ph. 1 – Feb 2007
- Ronald Reagan Blvd North Ph. 1 – Mar 2007
- Lakeline Blvd – Jul 2007
- Ronald Reagan Blvd South Ph. 2 – Feb 2008
- US 183 at CR 274 – Feb 2008
- County Road 175 Phase 2A – Jan 2010
- US 183 at FM 3405 Traffic Signal – Mar 2010
- US 183 at FM 3405 Left Turn Lanes – May 2010
- County Road 214 Phase 2A – Jan 2011
- San Gabriel Parkway Ph. 2 – Oct 2011
- US 183 (PTF) – Apr 2012
- SH 29 TWLTL Liberty Hill – Dec 2012
- Hero Way – Feb 2013
- County Roads 260/266 – Apr 2013
- County Road 277 – Jul 2014
- Lakeline Blvd at US 183 – Nov 2014
- Lakeline Blvd Ph. 2 – Apr 2015
- County Road 258 – Jul 2017
- County Road 200 at Bold Sundown – Oct 2018
- Ronald Reagan at Santa Rita Ranch – Feb 2019
- CR 200 at SH 29 / Loop 332 – Jul 2019
- Bagdad Road (CR 279) at CR 278 (River Ranch County Park Road) – Feb 2020
- San Gabriel Ranch Road Bridge – Mar 2020
- Corridor F / US 183 Planning - Jan 2021
- Seward Junction Improvements – Mar 2021
- Ronald Reagan Blvd Widening (Temporary Signals) at Santa Rita Blvd – Feb 2022
- CR 200 (CMTA Railroad to CR 201) – Oct 2022
- Ronald Reagan Safety Improvements – July 2023
- CR 258 Extension – Dec 2023


WILLIAMSON COUNTY

ROAD BOND PROGRAM

COMPLETED PROJECTS

CONSTRUCTION SUBSTANTIALLY COMPLETE/OPEN TO TRAFFIC - AS OF MARCH 2024

Precinct 3

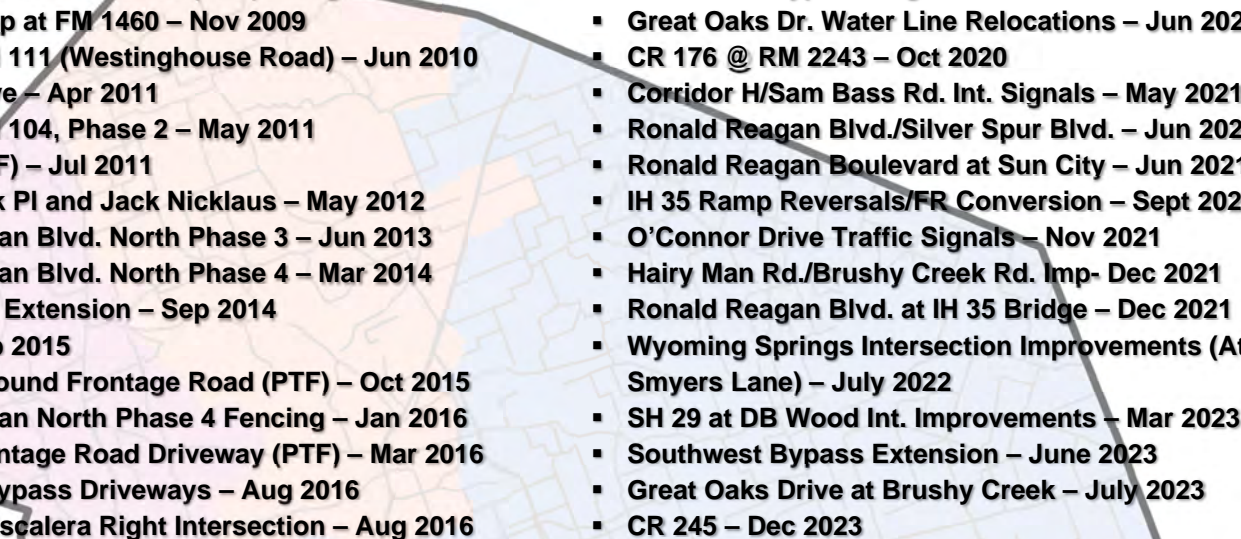- 
- A map of Williamson County, Texas, with Precinct 3 highlighted in a light blue color. The map shows the county's irregular shape and the network of roads within it. Precinct 3 is located in the western part of the county, roughly between the IH 35 corridor and the western border.
- Cedar Hollow at SH 29 (signal) – Aug 2002
 - Georgetown Inner Loop Project 2 – Aug 2003
 - Georgetown Inner Loop Project 1 – Jun 2004
 - Georgetown Inner Loop East Extension – Sep 2004
 - County Road 152 Bridge Replacement – Sep 2004
 - Inner Loop East (CR 151 to Bus 35) – Oct 2005
 - Ronald Reagan Blvd North, Ph. 2 – May 2008
 - 12" Water Main Relo. for SH 29 Widening – Jun 2008
 - SH 29 / CR 104, Ph. 1 – Jul 2008
 - IH 35 at SH 29 Turnarounds (PTF) – Aug 2008
 - SE Inner Loop at FM 1460 – Nov 2009
 - County Road 111 (Westinghouse Road) – Jun 2010
 - Williams Drive – Apr 2011
 - County Road 104, Phase 2 – May 2011
 - RM 2338 (PTF) – Jul 2011
 - SH 29 at Park Pl and Jack Nicklaus – May 2012
 - Ronald Reagan Blvd. North Phase 3 – Jun 2013
 - Ronald Reagan Blvd. North Phase 4 – Mar 2014
 - Madrid Drive Extension – Sep 2014
 - CR 245 – Sep 2015
 - IH 35 Northbound Frontage Road (PTF) – Oct 2015
 - Ronald Reagan North Phase 4 Fencing – Jan 2016
 - IH 35 NB Frontage Road Driveway (PTF) – Mar 2016
 - Southwest Bypass Driveways – Aug 2016
 - RM 2243 at Escalera Right Intersection – Aug 2016
 - SH 29 at Cedar Hollow Right Int. Imp. – Aug 2016
 - Southwest Bypass Access Route – Jul 2017
 - Pearson Ranch Road – Oct 2017
 - Arterial H Extension Phase I – Feb 2018
 - Relo. of Williamson County Regional WL – Apr 2018
 - RM 620 Phase 2 – Jul 2018
 - Southwest Bypass Segment 1 – Sept 2018
 - Inner Loop Improvements – Dec 2018
 - Neenah Ave./Pearson Ranch Rd. Signal – Jan 2019
 - Southwest Bypass Segment 2 – Jan 2020
 - Great Oaks Dr. Water Line Relocations – Jun 2020
 - CR 176 @ RM 2243 – Oct 2020
 - Corridor H/Sam Bass Rd. Int. Signals – May 2021
 - Ronald Reagan Blvd./Silver Spur Blvd. – Jun 2021
 - Ronald Reagan Boulevard at Sun City – Jun 2021
 - IH 35 Ramp Reversals/FR Conversion – Sept 2021
 - O'Connor Drive Traffic Signals – Nov 2021
 - Hairy Man Rd./Brushy Creek Rd. Imp- Dec 2021
 - Ronald Reagan Blvd. at IH 35 Bridge – Dec 2021
 - Wyoming Springs Intersection Improvements (At Smyers Lane) – July 2022
 - SH 29 at DB Wood Int. Improvements – Mar 2023
 - Southwest Bypass Extension – June 2023
 - Great Oaks Drive at Brushy Creek – July 2023
 - CR 245 – Dec 2023


WILLIAMSON COUNTY

ROAD BOND PROGRAM


COMPLETED PROJECTS

CONSTRUCTION SUBSTANTIALLY COMPLETE/OPEN TO TRAFFIC - AS OF MARCH 2024

Precinct 4

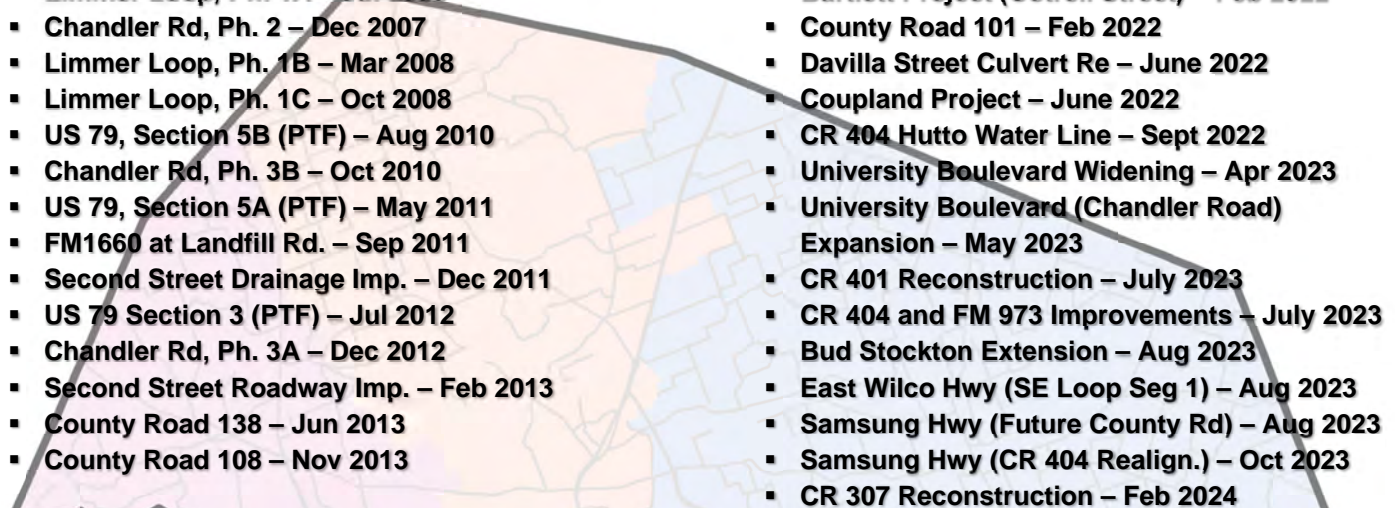- 
- A map of Williamson County, Texas, with Precinct 4 highlighted in orange. The map shows the county's irregular shape and internal road network. Precinct 4 is located in the central-northern part of the county. Other precincts are shown in various shades of blue, green, and pink.
- Bridge RPLs (CR 390, 406 & 427) – Nov 2002
 - County Road 368 and 369 – Nov 2002
 - County Road 412 – Aug 2003
 - County Road 300 and 301 – Dec 2003
 - County Road 424 Bridge RPL – Jan 2004
 - Chandler Rd. Extension, Ph. 1 – Mar 2005
 - County Road 112, Ph. 1 – Aug 2005
 - County Road 137 – Oct 2005
 - Limmer Loop, Ph. 1A – Jul 2006
 - Chandler Rd, Ph. 2 – Dec 2007
 - Limmer Loop, Ph. 1B – Mar 2008
 - Limmer Loop, Ph. 1C – Oct 2008
 - US 79, Section 5B (PTF) – Aug 2010
 - Chandler Rd, Ph. 3B – Oct 2010
 - US 79, Section 5A (PTF) – May 2011
 - FM1660 at Landfill Rd. – Sep 2011
 - Second Street Drainage Imp. – Dec 2011
 - US 79 Section 3 (PTF) – Jul 2012
 - Chandler Rd, Ph. 3A – Dec 2012
 - Second Street Roadway Imp. – Feb 2013
 - County Road 138 – Jun 2013
 - County Road 108 – Nov 2013
 - County Road 170 – Feb 2015
 - Multi-Site Traffic Signals – Jun 2016
 - Bill Pickett Trail– Nov 2016
 - County Road 110 South – May 2018
 - County Road 119 – Mar 2019
 - County Road 110 Middle – Oct 2020
 - CR Paving (401, 402 & 404) – Nov 2021
 - Thrall Project (S. Bounds Street) – Jan 2022
 - Bartlett Project (Cotrell Street) – Feb 2022
 - County Road 101 – Feb 2022
 - Davilla Street Culvert Re – June 2022
 - Coupland Project – June 2022
 - CR 404 Hutto Water Line – Sept 2022
 - University Boulevard Widening – Apr 2023
 - University Boulevard (Chandler Road) Expansion – May 2023
 - CR 401 Reconstruction – July 2023
 - CR 404 and FM 973 Improvements – July 2023
 - Bud Stockton Extension – Aug 2023
 - East Wilco Hwy (SE Loop Seg 1) – Aug 2023
 - Samsung Hwy (Future County Rd) – Aug 2023
 - Samsung Hwy (CR 404 Realign.) – Oct 2023
 - CR 307 Reconstruction – Feb 2024

2000/2006 Road Bond Program Projects Precinct 1 - Commissioner Cook

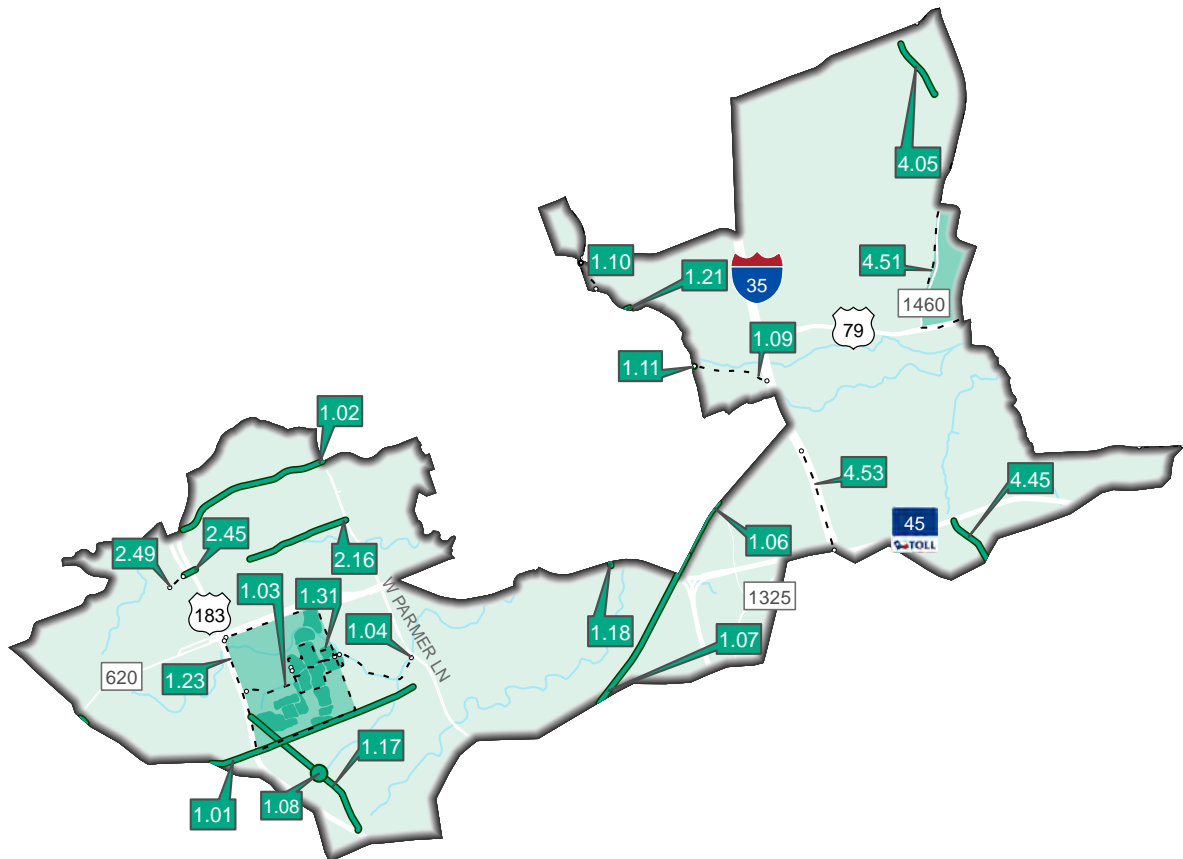

Completed/Open to Traffic

- 1.01 Anderson Mill Rd.
- 1.02 Avery Ranch Blvd. (183 to Parmer Lane)
- 1.03 Lake Creek Drainage - Phase 1 ----
- 1.04 Lake Creek Drainage - Phase 2 ----
- 1.06 McNeil Road - Phase 1
- 1.07 McNeil Road - Phase 2
- 1.08 Pond Springs at Turtle Rock Signal
- 1.09 RM 620 Feasibility ----
- 1.10 Wyoming Springs North ----
- 1.11 RM 620 Interim Improvements - Phase 1
- 1.17 Pond Springs Road
- 1.18 O'Connor Overpass at SH 45


- 1.21 CR 174 (Hairy Man Rd.) Bridge Rail Rehab
- 1.23 Forest North Drainage Improvements - Phase 1 [---]
- 1.31 Forest North Drainage Improvements - Phase 2 [---]
- 1.31 Forest North Drainage Improvements - Phase 3 [---]
- 2.16 Lakeline Blvd. (Lyndhurst to Parmer Lane)
- 2.45 Lakeline Blvd. at US 183
- 2.49 Lakeline Blvd. Right Turn Lanes ----
- 4.05 CR 112 - Phase 1
- 4.45 CR 170
- 4.53 IH 35 Operational Analysis ----

[---] Study

2013 ROAD BOND PROGRAM PROJECTS

Precinct 1 - Commissioner Cook

--- Study

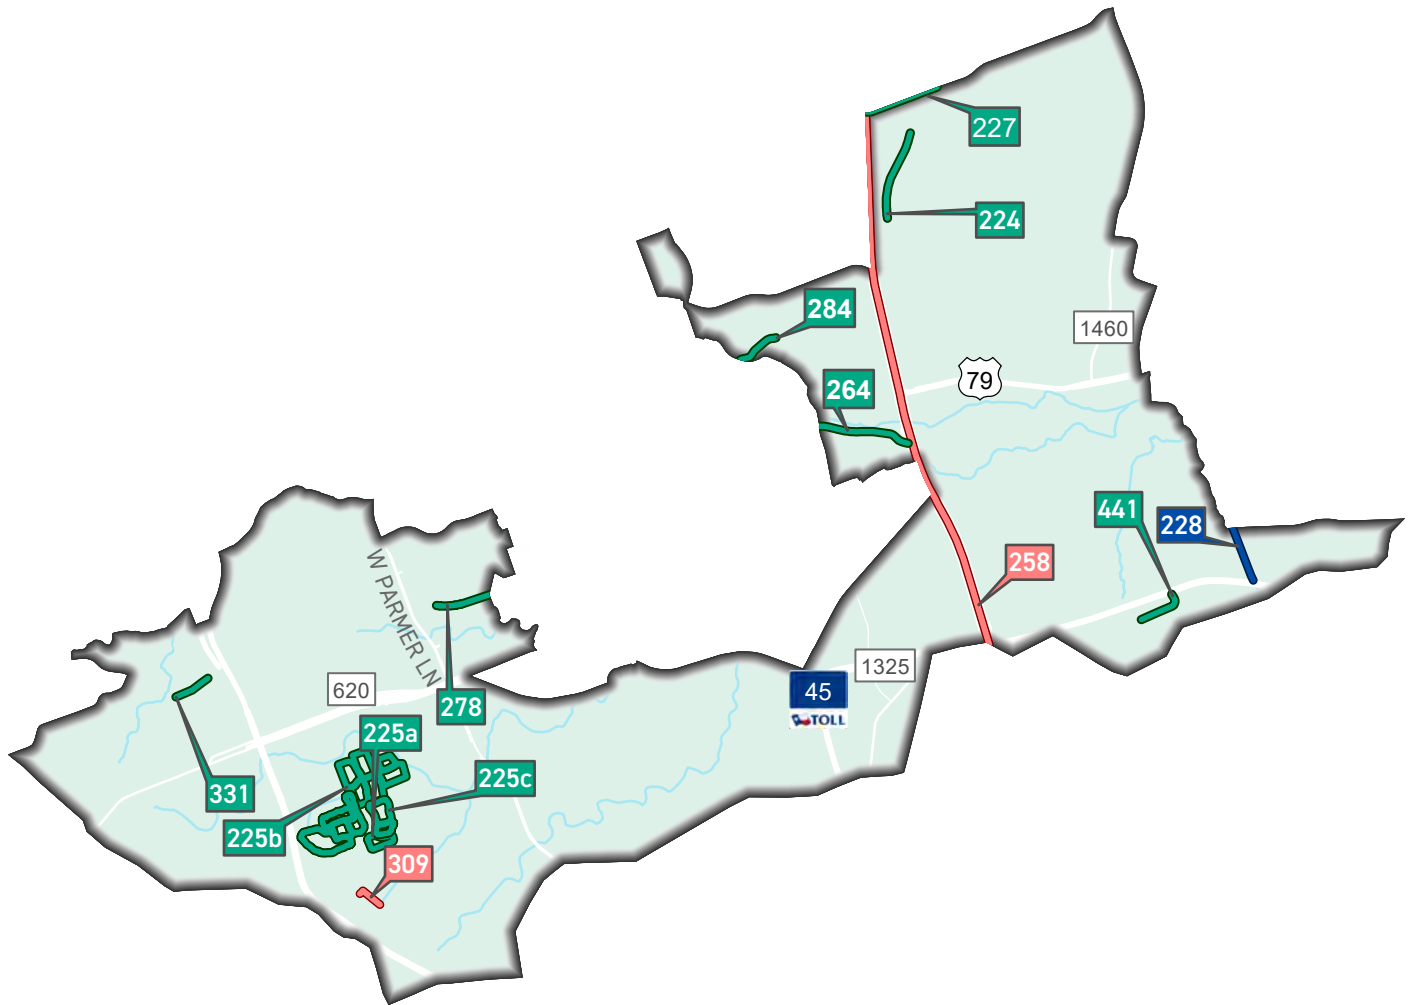

In Design

- 258 IH 35 Corridor Operational Analysis (SH 45 to RM 1431)
- 309 Pond Springs Road Area Drainage Improvements

Under Construction/Bidding

- 228 Kenney Fort Blvd Segments 2 and 3 (Forest Creek Boulevard to SH 45)


Completed/Open to Traffic

- 224 North Mays Street Extension (Paloma Drive to Oakmont Drive)
- 225a Forest North Drainage Improvements Anderson Mill Zone
- 225b Forest North Drainage Improvements Phase 2
- 225c Forest North Drainage Improvements Phase 3 (Design)
- 227 University Boulevard Widening (IH 35 to Sunrise Road)
- 264 RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)
- 278 Neenah Avenue Widening (Olive Hill Drive to 0.5 miles east of Olive Hill Drive)
- 284 Hairy Man Road/Brushy Creek Road Safety Improvements (Brushy Bend to Sam Bass Road)
- 331 Lakeline Boulevard Right Turn Lanes
- 441 Roundville Lane (A.W. Grimes Boulevard to EBFR of SH 45)

2019 ROAD BOND PROGRAM PROJECTS

Precinct 1 - Commissioner Cook

Study

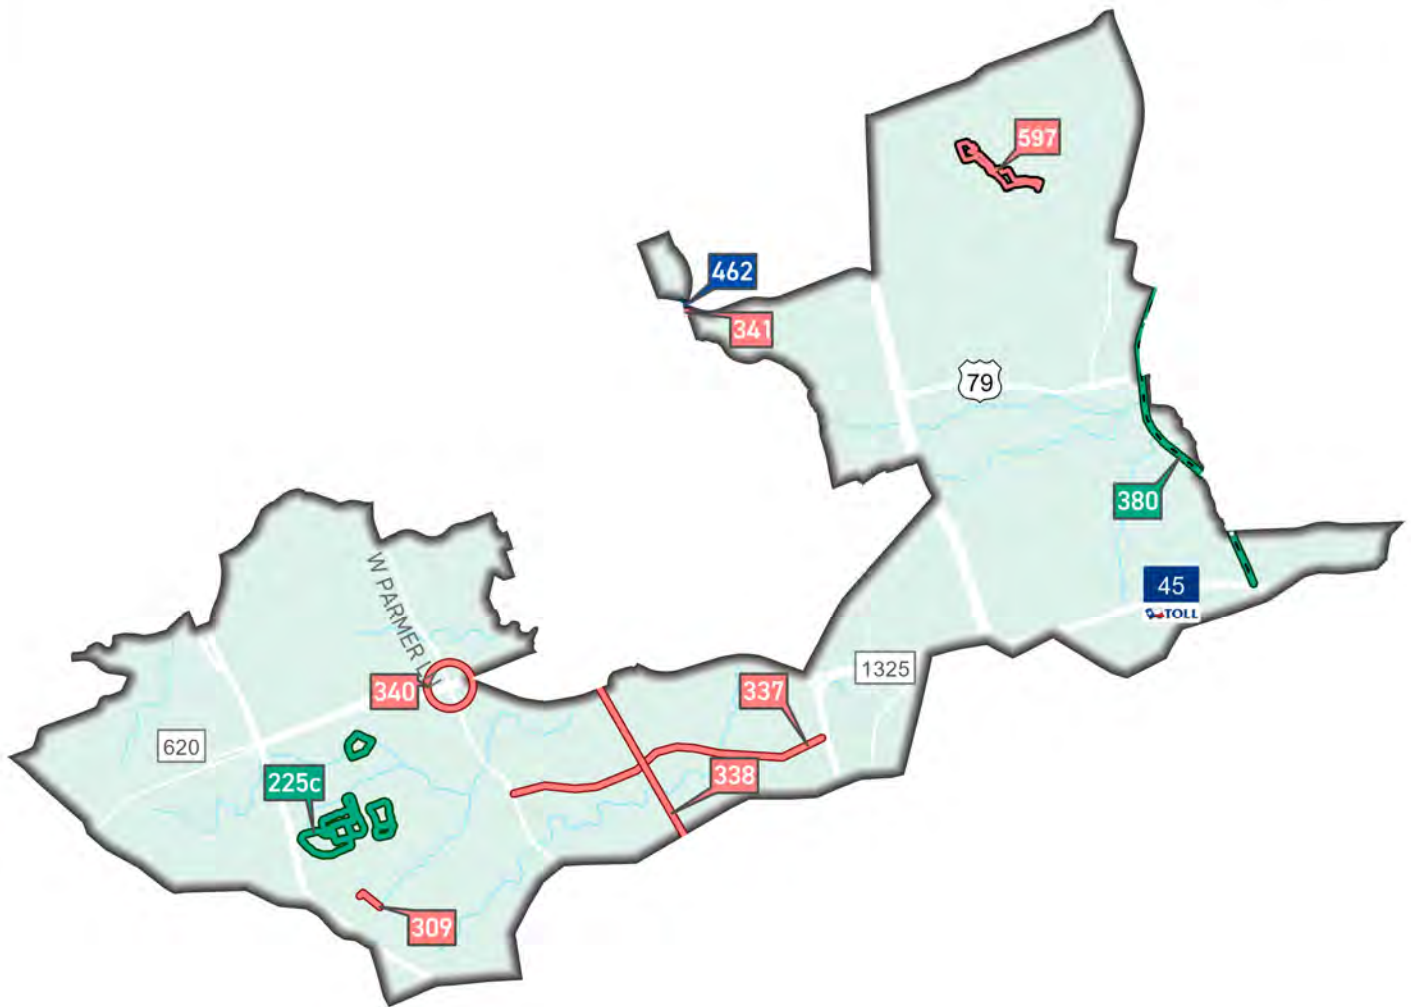

In Design

- 309 Pond Springs Road Area Drainage Improvements
- 337 Anderson Mill Road (FM734 - Loop 1)
- 338 RM 620/SH 45 Intersection to McNeil Road
- 340 Parmer Lane at SH 45 Interchange
- 341 Wyoming Springs Extension (Brightwater Boulevard/Creek Bend to Sam Bass Road)
- 597 Chandler Branch Tributary 3 - Channel Improvements Project

Under Construction/Bidding

- 462 Corridor H/Sam Bass Road (RM 1431 to Wyoming Springs Drive)


Completed/Open to Traffic

- 225c Forest North Drainage Improvements Phase 3
- 380 MoKan (University Boulevard to SH 45)

2023 ROAD BOND PROGRAM PROJECTS

Precinct 1 - Commissioner Cook

Study

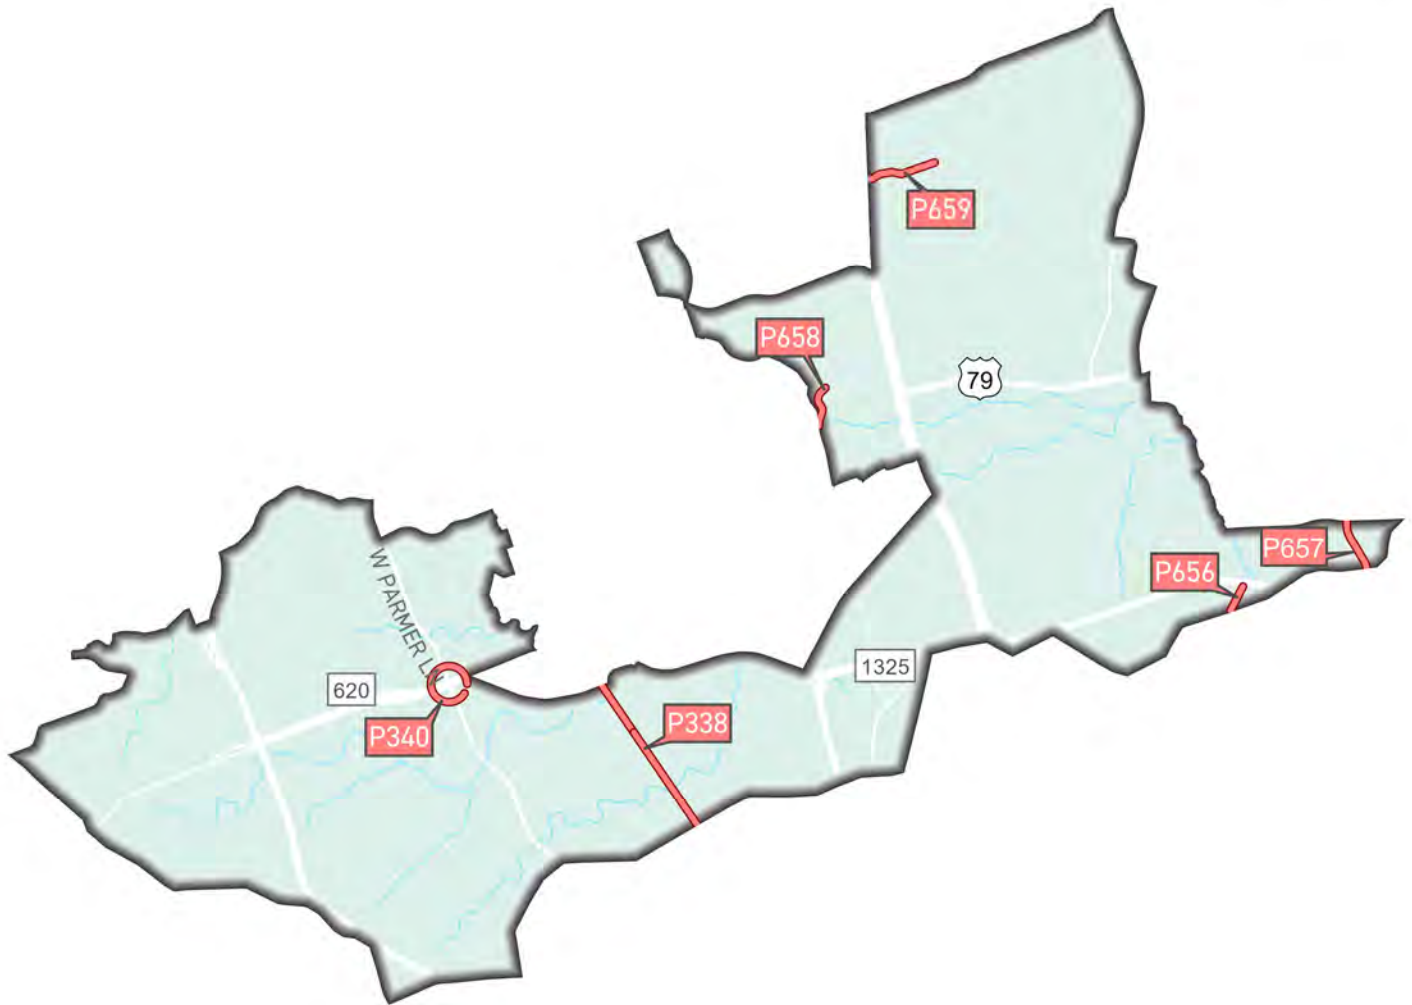

In Design

- P338 Robinson Ranch Road (SH 45 / RM 620 to McNeil Road)
- P340 Parmer Lane at SH 45 (Parmer Lane / SH 45)
- P656 Schultz Lane (Louis Henna Blvd to New Meister Lane)
- P657 Red Bud Lane Widening (Gattis School Road to Heatherwilde Blvd)
- P658 Deepwood Drive (Deepwood Dr to Sam Bass Rd)
- P659 Eagles Nest Extension (Cypress Blvd to west of Chisholm Trail Road)

Project Name: North Mays Street Extension Phase 1 (Paloma Drive to Oakmont Drive)
Project No. 1810-265

Original Contract Price = \$10,775,835.75

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>	
11/14/2018	12/4/2018	1/18/2019	1/28/2019	12/16/2020		410	279	689	
<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$) Used</u>	<u>% Time Used</u>
1	1/28/2019	1/31/2019	4	\$523,139.40	\$523,139.40	\$58,126.60	\$58,126.60	5	1
2	2/1/2019	2/28/2019	28	\$2,584.80	\$525,724.20	\$287.20	\$58,413.80	5	5
3	3/1/2019	4/30/2019	61	\$102,281.40	\$628,005.60	\$11,364.60	\$69,778.40	6	13
4	5/1/2019	5/31/2019	31	\$593,318.74	\$1,221,324.34	\$65,924.30	\$135,702.70	12	18
5	6/1/2019	6/30/2019	30	\$188,661.93	\$1,409,986.27	\$20,962.44	\$156,665.14	13	22
6	7/1/2019	7/31/2019	31	\$590,007.31	\$1,999,993.58	\$65,556.37	\$222,221.51	19	27
7	8/1/2019	8/31/2019	31	\$628,396.35	\$2,628,389.93	\$69,821.82	\$292,043.33	25	31
8	9/1/2019	9/30/2019	30	\$2,393,911.61	\$5,022,301.54	\$265,990.17	\$558,033.50	47	36
9	10/1/2019	10/31/2019	31	\$724,961.48	\$5,747,263.02	\$80,551.28	\$638,584.78	54	40
10	11/1/2019	11/30/2019	30	\$378,890.89	\$6,126,153.91	\$42,098.99	\$680,683.77	58	45
11	12/1/2019	12/31/2019	31	\$341,316.16	\$6,467,470.07	\$37,924.02	\$718,607.79	61	49
12	1/1/2020	1/31/2020	31	\$258,548.22	\$6,726,018.29	\$28,727.58	\$747,335.37	63	54
13	2/1/2020	2/29/2020	29	\$191,886.33	\$6,917,904.62	\$21,320.70	\$768,656.07	65	58
14	3/1/2020	3/31/2020	31	\$176,371.44	\$7,094,276.06	\$19,596.83	\$788,252.90	67	62
15	4/1/2020	4/30/2020	30	\$395,476.16	\$7,489,752.22	\$43,941.79	\$832,194.69	71	67
16	5/1/2020	5/31/2020	31	\$277,797.27	\$7,767,549.49	\$30,866.36	\$863,061.05	73	71
17	6/1/2020	6/30/2020	30	\$385,340.38	\$8,152,889.87	\$42,815.60	\$905,876.65	77	75
18	7/1/2020	7/31/2020	31	\$418,604.43	\$8,571,494.30	\$46,511.61	\$952,388.26	81	80
19	8/1/2020	8/31/2020	31	\$202,731.51	\$8,774,225.81	\$22,525.72	\$974,913.98	83	84
20	9/1/2020	9/30/2020	30	\$117,670.32	\$8,891,896.13	\$13,074.48	\$987,988.46	84	89
21	10/1/2020	10/31/2020	31	\$305,827.52	\$9,197,723.65	\$33,980.83	\$1,021,969.29	87	93
22	11/1/2020	11/30/2020	30	\$190,635.28	\$9,388,358.93	\$21,181.70	\$1,043,150.99	89	98
23	12/1/2020	12/31/2020	16	\$338,985.41	\$9,727,344.34	\$37,665.05	\$1,080,816.04	92	100
24	1/1/2021	2/28/2021	0	\$165,603.43	\$9,892,947.77	\$18,400.38	\$1,099,216.42	93	100
25	3/1/2021	5/31/2021	0	\$1,535,933.64	\$11,428,881.41	-\$1,099,216.42	\$0.00	97	100
26	6/1/2021	12/31/2021	0	\$18,800.00	\$11,447,681.41	\$0.00	\$0.00	97	100
27	1/1/2022	5/31/2022	0	\$264,978.20	\$11,712,659.61	\$0.00	\$0.00	99.48	100
28	6/1/2022	12/31/2022	0	\$37,397.98	\$11,750,057.59	\$0.00	\$0.00	99.80	100
29	1/1/2023	3/22/2024	0	\$24,022.80	\$11,774,080.39	\$0.00	\$0.00	100.00	100

3/31/2024 Comments - Project close out is on going. Coordinating final acceptance and transfer of maintenance with the City of Round Rock.

Change Order Number	Approved	Cost This CO	Total COs
01	5/5/2020	\$0.00	\$0.00

4B: Third Party Accommodation. Third party requested work. This Change Order modifies the contract to require that Chandler Creek, LP, a Delaware limited partnership (collectively referred to as "Seller") be an additional insured to Capital Excavation's (Contractor) commercial general liability (CGL) insurance policy and to their commercial auto liability (Auto Liability) insurance policy. Adding the Seller to the Contractor's insurance was in the terms and conditions of the Real Estate Contract between the Chandler Creek, LP and Williamson County. The Real Estate Contract was finalized after the plans were completed.

Change Order Number	Approved	Cost This CO	Total COs
02	5/5/2020	\$24,898.11	\$ 24,898.11

3F: County Convenience. Additional work desired by the County. This Change Order compensates the Contractor for modifications to Driveway #1 that include raising the elevation of the driveway to match the current driveway, improving the driveway by adding 6" of flex base to the pavement section, and using higher strength concrete. The driveway elevation was maintained to minimize the impact of flooding on the driveway access. The improvements were necessary due to the high volume of heavy truck and trailer traffic that uses the driveway.

Change Order Number	Approved	Cost This CO	Total COs
03	10/6/2020	\$67,872.45	\$ 92,770.56

3F: County Convenience. Additional work desired by the County. This Change Order compensates the Contractor for adding electronic portable changeable message boards to provide advance notification of the closure of North Mays, from Jeffery Way to Paloma Drive. The Change Order also adds compensation for the removal of the City of Round Rock Public Safety Training Center sign. Electrical ground boxes and installation of illumination on the Chandler Branch bridge will be added at the request of Oncor.

Change Order Number	Approved	Cost This CO	Total COs
04	10/6/2020	\$21,002.40	\$ 113,772.96

1A: Design Error or Omission. Incorrect PS&E. This Change Order adds a 24" encasement to the relocation of the new City of Round Rock 12" Water Line A that crosses the roadway at the north end of the project. The installation of the water line was included in the plans, but the encasement was not. The encasement is required to protect the water line under the roadway.

Change Order Number	Approved	Cost This CO	Total COs
05	2/23/2021	\$194,528.81	\$ 308,301.77

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
6	3/23/2021	\$364,733.96	\$ 673,035.73

6C: Untimely ROW/Utilities. Utilities not clear. This Change Order adds a pay item to compensate the Contractor for extended project overhead costs caused by delays to the utility relocation.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
7	4/12/2022	\$302,109.20	\$ 975,144.93


2E: Differing Site Conditions (unforeseeable). Miscellaneous difference in site conditions (unforeseeable). This Change Order provides the interim final balancing for the overrun/underrun of Contract quantities on the project as a result of addressing field conditions not accounted for in the original plans. This Change Order adds items to compensate the contractor for various work including installation of soil stabilization measures under the bridge. 4B: Third Party Accommodation. Third party requested work. This Change Order also adds a Force Account item to pay for the installation of Oncor illumination poles, wire and conduit south of the bridge.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
8	3/5/2024	\$23,099.72	\$ 998,244.65

2E: Differing Site Conditions (unforeseeable). This Change Order provides the final balancing for the overrun/underrun of Contract quantities on the project as a result of addressing field conditions not accounted for in the original plans. This Change Order also adds an item for miscellaneous riprap work that was completed as a request from the City of Round Rock.

Adjusted Price = \$11,774,080.40


2000/2006 Road Bond Program Projects Precinct 2 - Commissioner Long

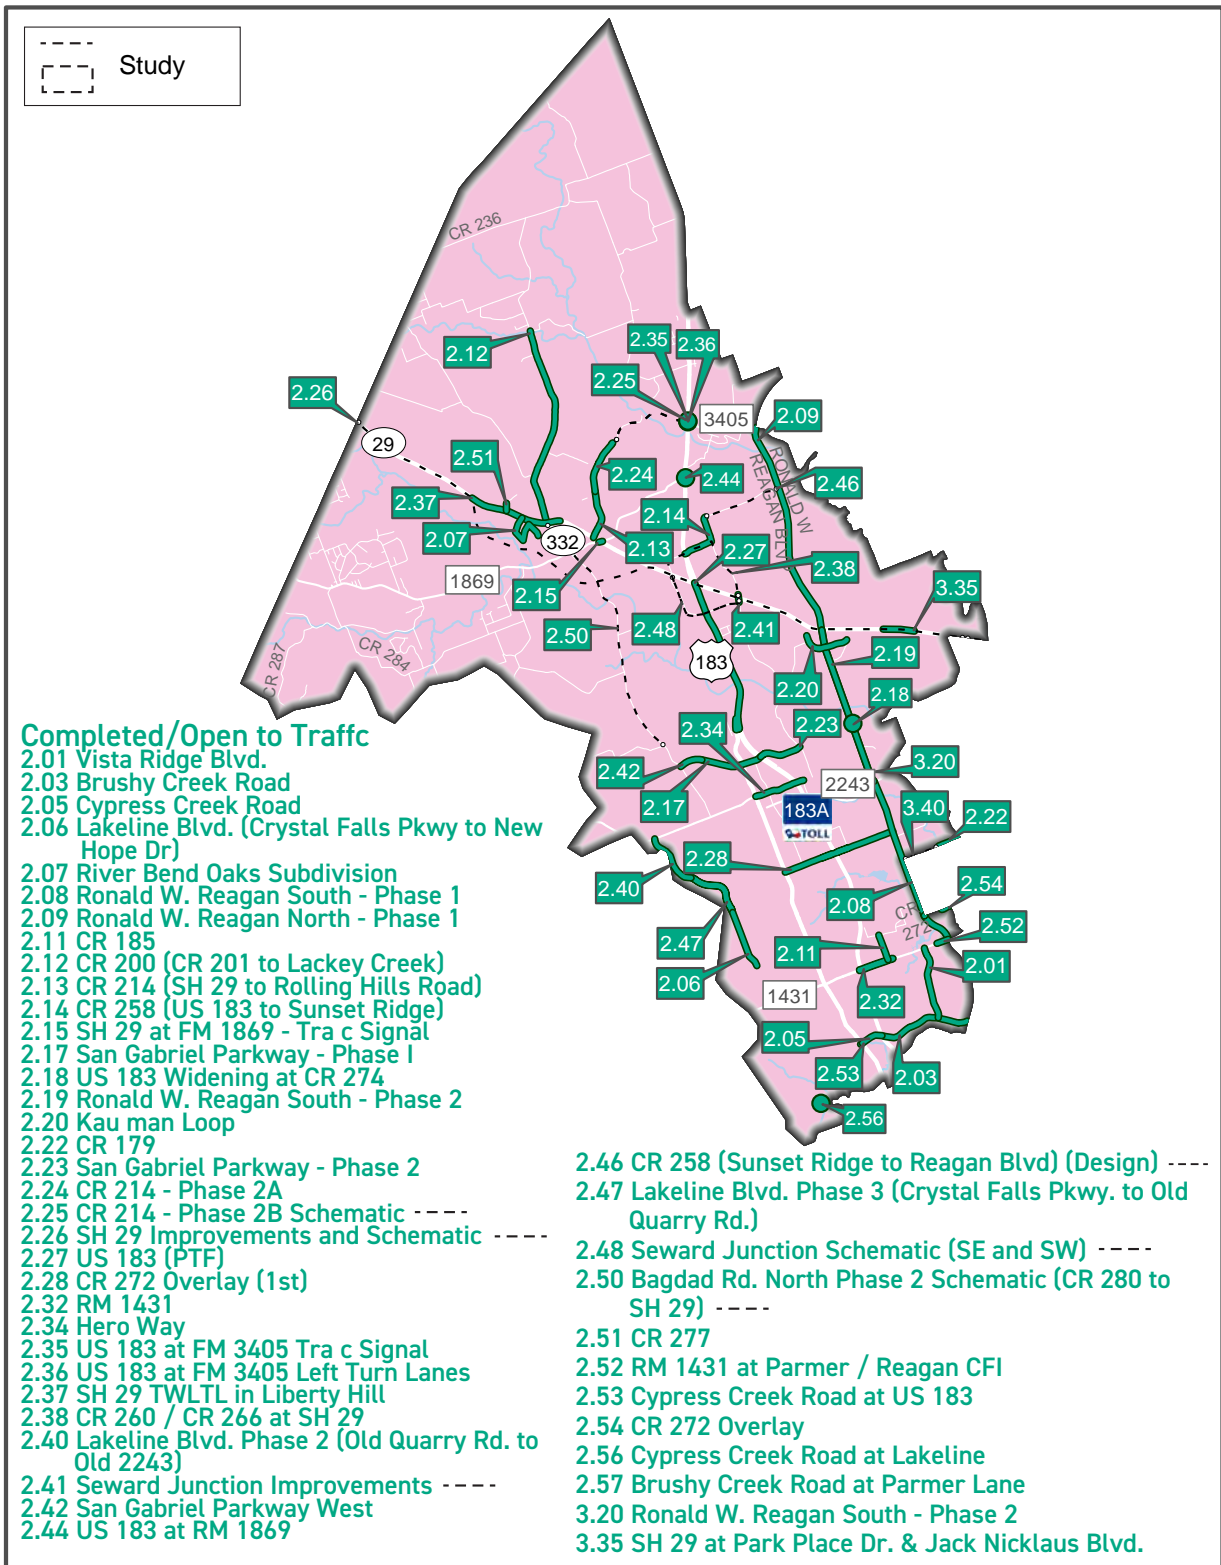

2013 ROAD BOND PROGRAM PROJECTS

Precinct 2 - Commissioner Long

--- Study

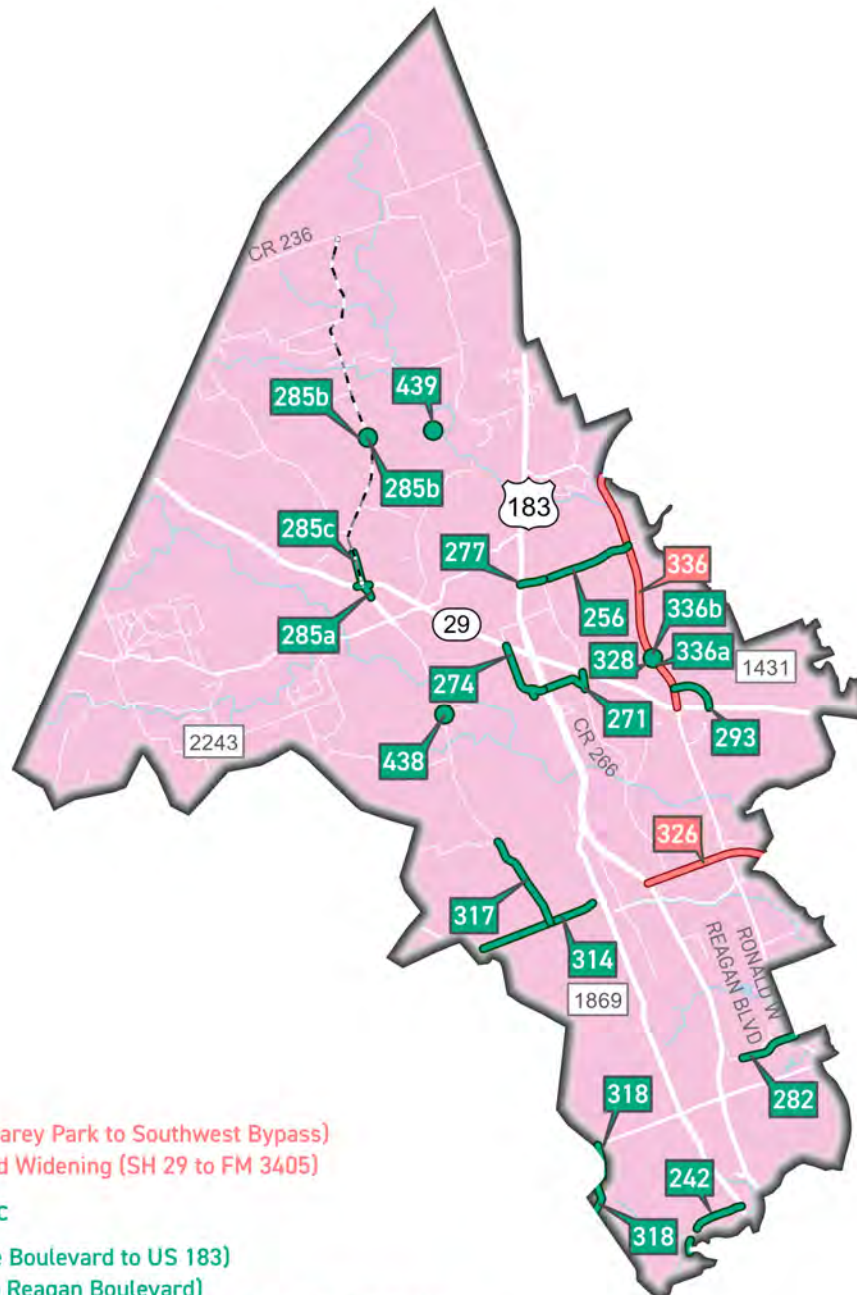

In Design

- 326 RM 2243 Realignment (Garey Park to Southwest Bypass)
- 336 Ronald Reagan Boulevard Widening (SH 29 to FM 3405)


Completed/Open to Traffic

- 242 Little Elm Trail (Lakeline Boulevard to US 183)
- 256 CR 258 (Sunset Ridge to Reagan Boulevard)
- 271 Seward Junction Southeast (US 183 at CR 259 to SH 29 at CR 266)
- 274 Seward Junction Southwest (SH 29 at CR 213 to US 183 at CR 259)
- 277 CR 258 Extension (US 183 to Sunset Ridge Drive)
- 282 New Hope Drive Phase 1 (Cottonwood Creek Trail to Ronald Reagan Boulevard)
- 285 CR 200 Study and Schematic (SH 29 to CR 236)
- 285a State Highway 29 Intersection at CR 200/Loop 332
- 285b CR 200 at Bold Sundown Left Turn Lane
- 285c CR 200 (CMTA Railroad to CR 201)
- 293 Kauffman Loop Phase 1 - Two Lanes (northeast quadrant of Reagan at SH 29)
- 314 Old 2243/Hero Way West (Lakeline Boulevard to west of US 183)
- 317 Bagdad Road North (Collaborative Way to RM 2243)
- 318 Anderson Mill Road (Gaspar Bend to RM 1431)
- 328 Ronald Reagan at Santa Rita
- 336a Ronald Reagan Boulevard Widening & Temp Signals at Santa Rita Boulevard
- 336b Ronald Reagan Safety Improvements
- 438 Bagdad Road (CR 279) at CR 278 (River Ranch County Park Road)
- 439 San Gabriel Ranch Road Bridge at Lackey Creek

2019 ROAD BOND PROGRAM PROJECTS

Precinct 2 - Commissioner Long

Study

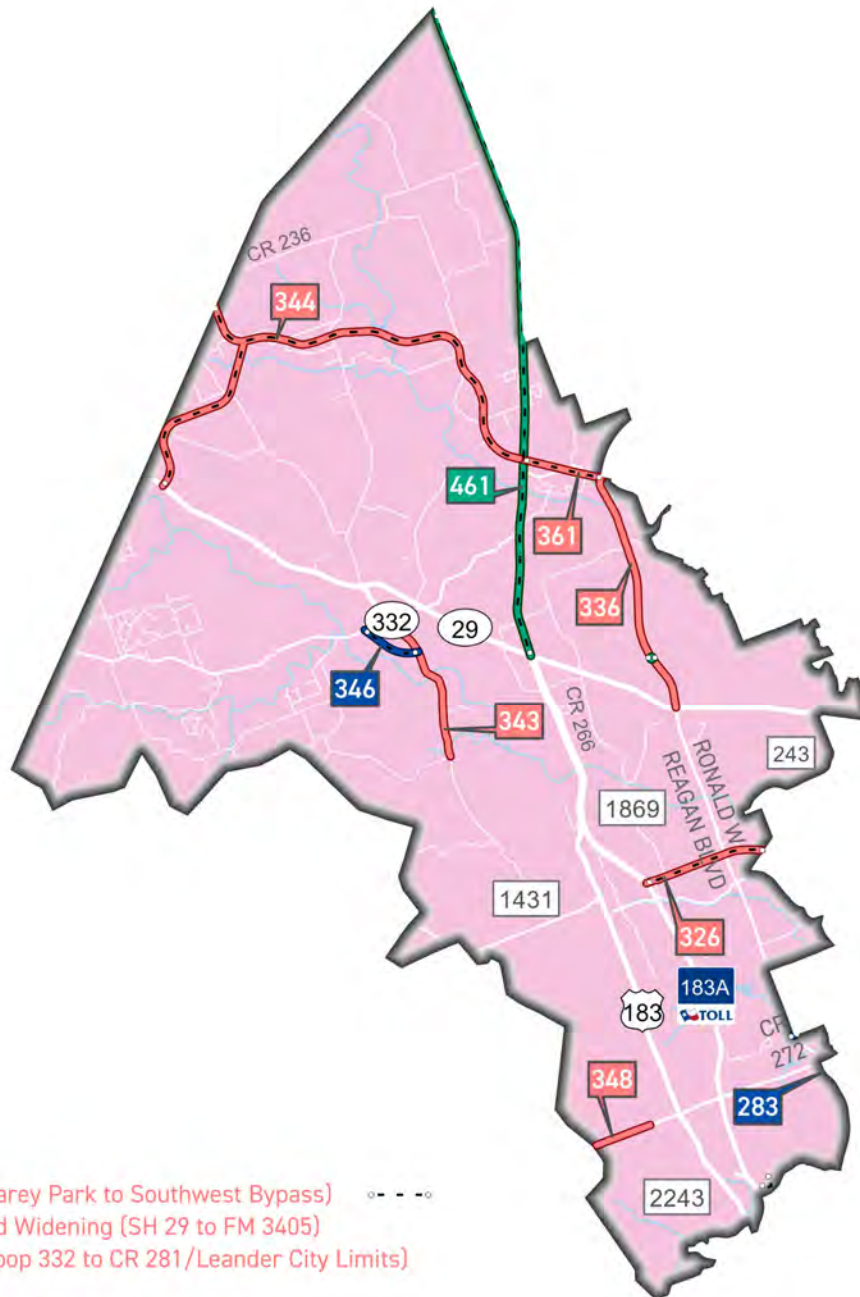

In Design

- 326 RM 2243 Realignment (Garey Park to Southwest Bypass) - - - -
- 336 Ronald Reagan Boulevard Widening (SH 29 to FM 3405)
- 343 Bagdad Road /CR 279 (Loop 332 to CR 281/Leander City Limits) to Sam Bass Road)
- 344 Corridor I2 (Burnet County Line to US 183) - - - -
- 348 Whitestone Boulevard Widening (Bagdad Road to Anderson Mill Road)
- 361 Corridor I1 (FM 3405) (Ronald Reagan Boulevard to US 183) - - - -

Under Construction/Bidding

- 283 New Hope Drive Extension Phase 2A (Ronald Reagan Boulevard to Sam Bass Road)
- 346 Liberty Hill (SH 29) Bypass (RM 1869 to CR 279)


Completed/Open to Traffic

- 461 Corridor F/US 183 (Williamson/Burnet County Line to SH 29) - - - -

2023 ROAD BOND PROGRAM PROJECTS

Precinct 2 - Commissioner Long

--- Study

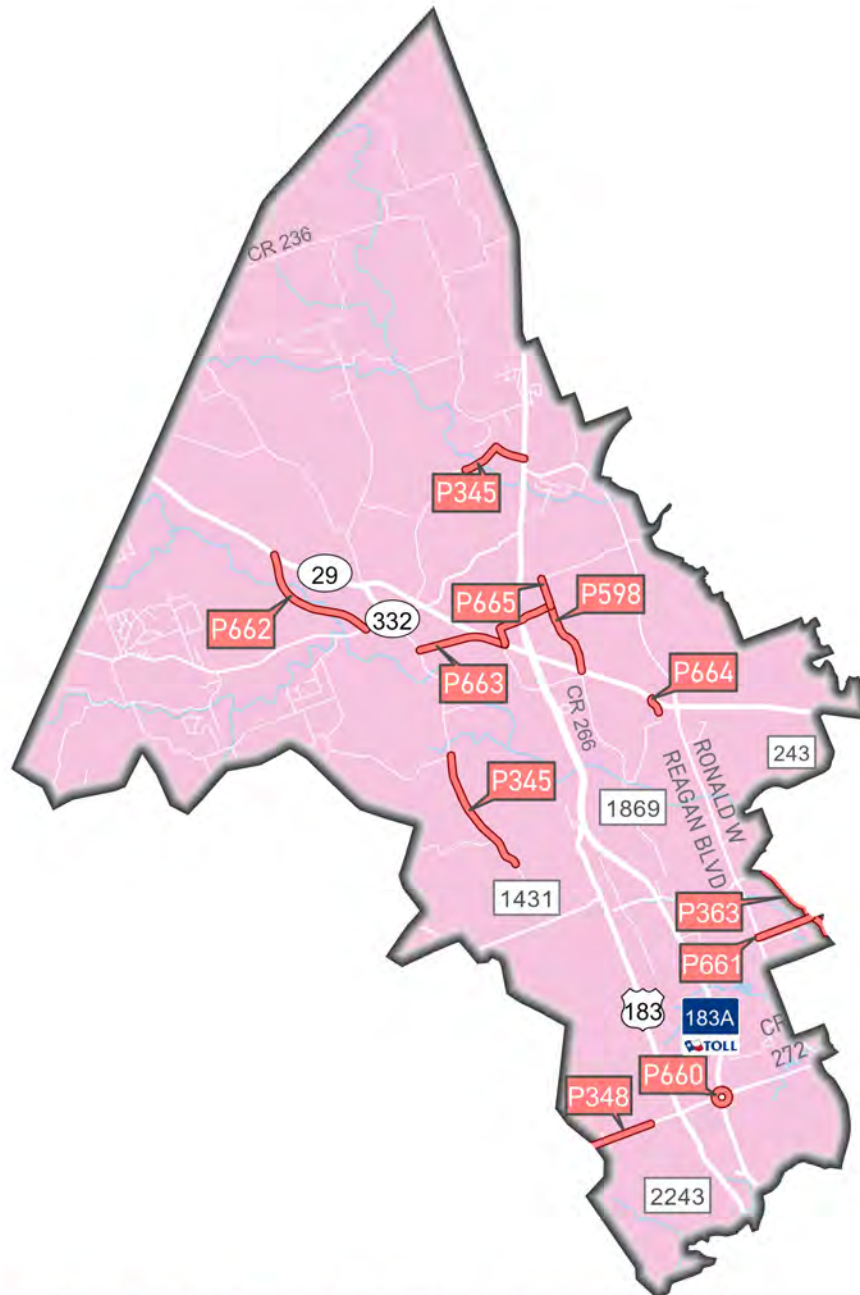

In Design

- P342 Bagdad Road (North of San Gabriel Parkway to CR 281 / Leander City Limits)
- P345 CR 214 (End of CR 214 to US 183)
- P348 Whitestone Boulevard Widening (west of Anderson Mill to Bagdad Road)
- P363 CR 175 (South of Creek Meadow Cove to RM 2243)
- P598 Seward Junction Loop (SH 29/CR 260 to SH 29/CR 213)
- P660 RM 1431 at 183A Intersection
- P661 Crystal Falls Parkway (Ronald Reagan Blvd to CR 175)
- P662 Liberty Hill Bypass West (SH 29 (west of Liberty Hill High School) to RM 1869)
- P663 Liberty Hill Bypass East (Bagdad Road/CR 279 to SH 29)
- P664 Kauffman Loop (SH 29 to north terminus of Kauffman Loop)
- P665 CR 258 (Seward Junction Loop to CR 258 Extension)

Project Name: CR 258 Extension
Project No. 22IFB141

Original Contract Price = \$5,836,754.36

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>	
9/14/2022	9/27/2022	11/28/2022	12/8/2022			395	-29	366	
<u>Invoice</u>	<u>Beginning</u>	<u>Ending</u>	<u>Days</u>	<u>Current</u>	<u>Invoiced</u>	<u>Current</u>	<u>Total</u>	<u>% (\$)</u>	<u>% Time</u>
<u>Number</u>	<u>Date</u>	<u>Date</u>	<u>Charged</u>	<u>Invoice</u>	<u>Total</u>	<u>Retainage</u>	<u>Retainage</u>	<u>Used</u>	<u>Used</u>
1	11/1/2022	11/30/2022	0	\$47,590.20	\$47,590.20	\$5,287.80	\$5,287.80	1	0
2	12/1/2022	1/31/2023	55	\$536,565.20	\$584,155.40	\$59,618.36	\$64,906.16	10	15
3	2/1/2023	2/28/2023	28	\$463,314.38	\$1,047,469.78	\$51,479.37	\$116,385.53	17	23
4	3/1/2023	3/31/2023	31	\$354,614.85	\$1,402,084.63	\$39,401.65	\$155,787.18	23	31
5	4/1/2023	4/30/2023	30	\$455,839.20	\$1,857,923.83	\$50,648.80	\$206,435.98	31	39
6	5/1/2023	5/31/2023	31	\$1,166,374.04	\$3,024,297.87	\$129,597.12	\$336,033.10	50	48
7	6/1/2023	6/30/2023	30	\$1,003,480.88	\$4,027,778.75	-\$124,044.74	\$211,988.36	64	56
8	7/1/2023	7/31/2023	31	\$614,801.35	\$4,642,580.10	\$32,357.96	\$244,346.32	73	64
9	8/1/2023	8/31/2023	31	\$170,332.60	\$4,812,912.70	\$8,964.87	\$253,311.19	76	73
10	9/1/2023	9/30/2023	30	\$192,986.82	\$5,005,899.52	\$10,157.21	\$263,468.40	79	81
11	10/1/2023	10/31/2023	31	\$175,527.78	\$5,181,427.30	\$9,238.30	\$272,706.70	82	90
12	11/1/2023	11/30/2023	30	\$235,724.29	\$5,417,151.59	\$12,406.54	\$285,113.24	86	98
13	12/1/2023	12/31/2023	14	\$252,218.57	\$5,669,370.16	\$13,274.66	\$298,387.90	89	102
14	1/1/2024	1/31/2024	0	\$268,770.72	\$5,938,140.88	-\$177,201.35	\$121,186.55	91	102

3/31/2024 Comments- The contractor continued working on punch list items and waiting on vegetation establishment.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
01	11/11/2022	\$ -	\$ -

4B: Third Party Accommodation. Third party requested work. This Change Order modifies the Contract to require that City of Georgetown, (collectively referred to as the "City") be an additional insured to Joe Bland Construction's, L.P. (Contractor) commercial general liability (CGL) insurance policy and to their commercial auto liability (Auto Liability) insurance policy. Adding the City to the Contractor's insurance was in the terms and conditions of the Interlocal Agreement between the City and Williamson County.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
02	11/22/2022	\$ 422,565.69	\$ 422,565.69

3. County Convenience 3F: Additional Work Desired By The County: This Change Order adds items to the Contract for safety improvements needed at Ronald Reagan and Elizabeth Parkway. Ronald Reagan will be widened along the west side of the roadway to allow for a left turn lane into Elizabeth Parkway.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
03	6/6/2023	22,263.50	444,829.19

4D. Third Party Accommodation. Other. This Change Order compensates the Contractor for additional work to install sleeves for future utilities across CR 258 and Questa Trail. The payment will be split between the Developer and Williamson County. This method of payment was agreed on between the Developer and Williamson County.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
04	8/1/2023	-153,292.00	291,537.19

5A. Contractor exercises option to change the traffic control plan. This Change Order removes the unnecessary traffic control and construction items from the Contract, per the agreement to completely close existing CR 258 for the duration of Summer. This Change Order also revises the Disincentive dollar amount in the Project Construction Manual to \$1,250/day. 1B. Design Error or Omission. This Change Order also revises the Unit of Measure for the asphalt items that were added in Change Order #2.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
05	9/14/2023	539,623.96	831,161.15

4B. Third Party Accommodation. Third party requested work. This Change Order provides payment to the contractor for widening the eastbound pavement, adding a right turn lane/driveway into Liberty Hill's proposed High School, and relocating an existing water line out from under the new Liberty Hill High School driveway. LHISD will reimburse the County 100%.

Adjusted Price = \$6,667,915.51

Project Name: Ronald Reagan at Elizabeth Park Temporary Signals
Project No. 23IFB21

Original Contract Price = \$216,902.22

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>		<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
2/7/2023	2/28/2023	4/7/2023	4/17/2023	7/6/2023			135		135
<u>Invoice</u>	<u>Beginning</u>	<u>Ending</u>	<u>Days</u>	<u>Current</u>	<u>Invoiced</u>	<u>Current</u>	<u>Total</u>	<u>% (\$)</u>	<u>% Time</u>
<u>Number</u>	<u>Date</u>	<u>Date</u>	<u>Charged</u>	<u>Invoice</u>	<u>Total</u>	<u>Retainage</u>	<u>Retainage</u>	<u>Used</u>	<u>Used</u>
1	4/1/2023	4/30/2023	14	\$30,069.40	\$30,069.40	\$3,341.04	\$3,341.04	15	10
2	5/1/2023	5/31/2023	31	\$64,940.18	\$95,009.58	\$7,215.58	\$10,556.62	48	33
3	6/1/2023	6/30/2023	30	\$86,210.24	\$181,219.82	-\$1,018.73	\$9,537.89	88	56
4	7/1/2023	7/31/2023	6	\$12,277.51	\$193,497.33	-\$5,588.96	\$3,948.93	91	60
5	8/1/2023	12/21/2023	0	\$17,195.08	\$210,692.41	\$350.92	\$4,299.85	99	60

3/31/2024 Comments - Project close out continues.


<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
01	5/24/2023	\$28,245.75	\$ 28,245.75

2. Unadjusted utility (unforeseeable). 2G. Other: This Change Order will add and remove items from the project due to unforeseen changes in field conditions. The project conditions have been altered since the initial design and this Change Order will correct these issues. This Change order will also compensate the contractor for installing a temporary controller so that the signal can be activated immediately rather than waiting on the permanent controller which has a long lead-time for delivery.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
02	1/30/2024	\$ (27,480.00)	\$ 765.75

2E. Miscellaneous difference in site conditions (unforeseeable)(Item 9). This Change Order provides the final balancing for the overruns/underruns of Contract quantities on the project that are a result of addressing field conditions not accounted for in the original plans.

Adjusted Price = \$217,667.97

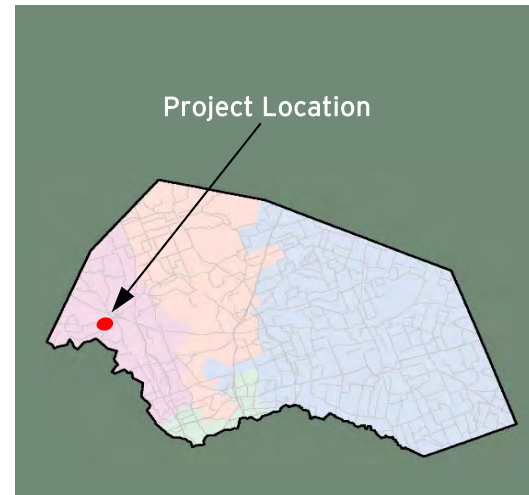

Liberty Hill Bypass Improvements (RM 1869 to CR 279)

Project Length: 2.316 Miles
Roadway Classification: Bagdad Road (Arterial);
Liberty Hill Bypass (Minor Arterial)

Project Schedule: February 2024 - Late 2025
Estimated Construction Cost: \$14.1 Million



MARCH 2024 IN REVIEW

3/1/24: Chasco Constructors continued to excavate the detention ponds at each end of the bypass. The contractor began installing various box culverts throughout the project and began building coffer dams in the existing pond for access to bridge bents.

3/8/24: The subcontractor continued stripping topsoil and roadway excavation and began roadway embankment in various locations.

3/15/24: Contractor continued roadway excavation and embankment in various locations. Chasco formed and poured concrete for Abutment 1 footing of the Tributary 2 Bridge.

3/22/24: Chasco formed and poured Abutment 6 backwall, and concrete riprap in front of Abutment 1 backwall for the Tributary 1 Bridge.

3/29/24: Chasco continued roadway excavation and embankment throughout the project and began processing flexible base at the east end of the bypass.



Design Engineer: LJA
Contractor: Chasco Constructors
Construction Observation:
Bruce Thurin, HNTB


Williamson County
Road Bond Program

Liberty Hill Bypass (SH 29) Bypass
Project No. 24IFB15


Original Contract Price = \$14,149,449.00

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>	
12/5/2023	12/12/2023	2/5/2024	2/15/2024			652		652	
<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u> <u>Used</u>	<u>% Time</u> <u>Used</u>
1	2/5/2024	2/29/2024	15	\$1,167,168.15	\$1,167,168.15	\$129,685.35	\$129,685.35	9	2
3/31/2024	Comments - Chasco Constructors continued roadway and bridge work throughout the project and began processing flexible base at the east end of the bypass.								
						Adjusted Price = \$14,149,449.00			

2000/2006 Road Bond Program Projects Precinct 3 - Commissioner Covey

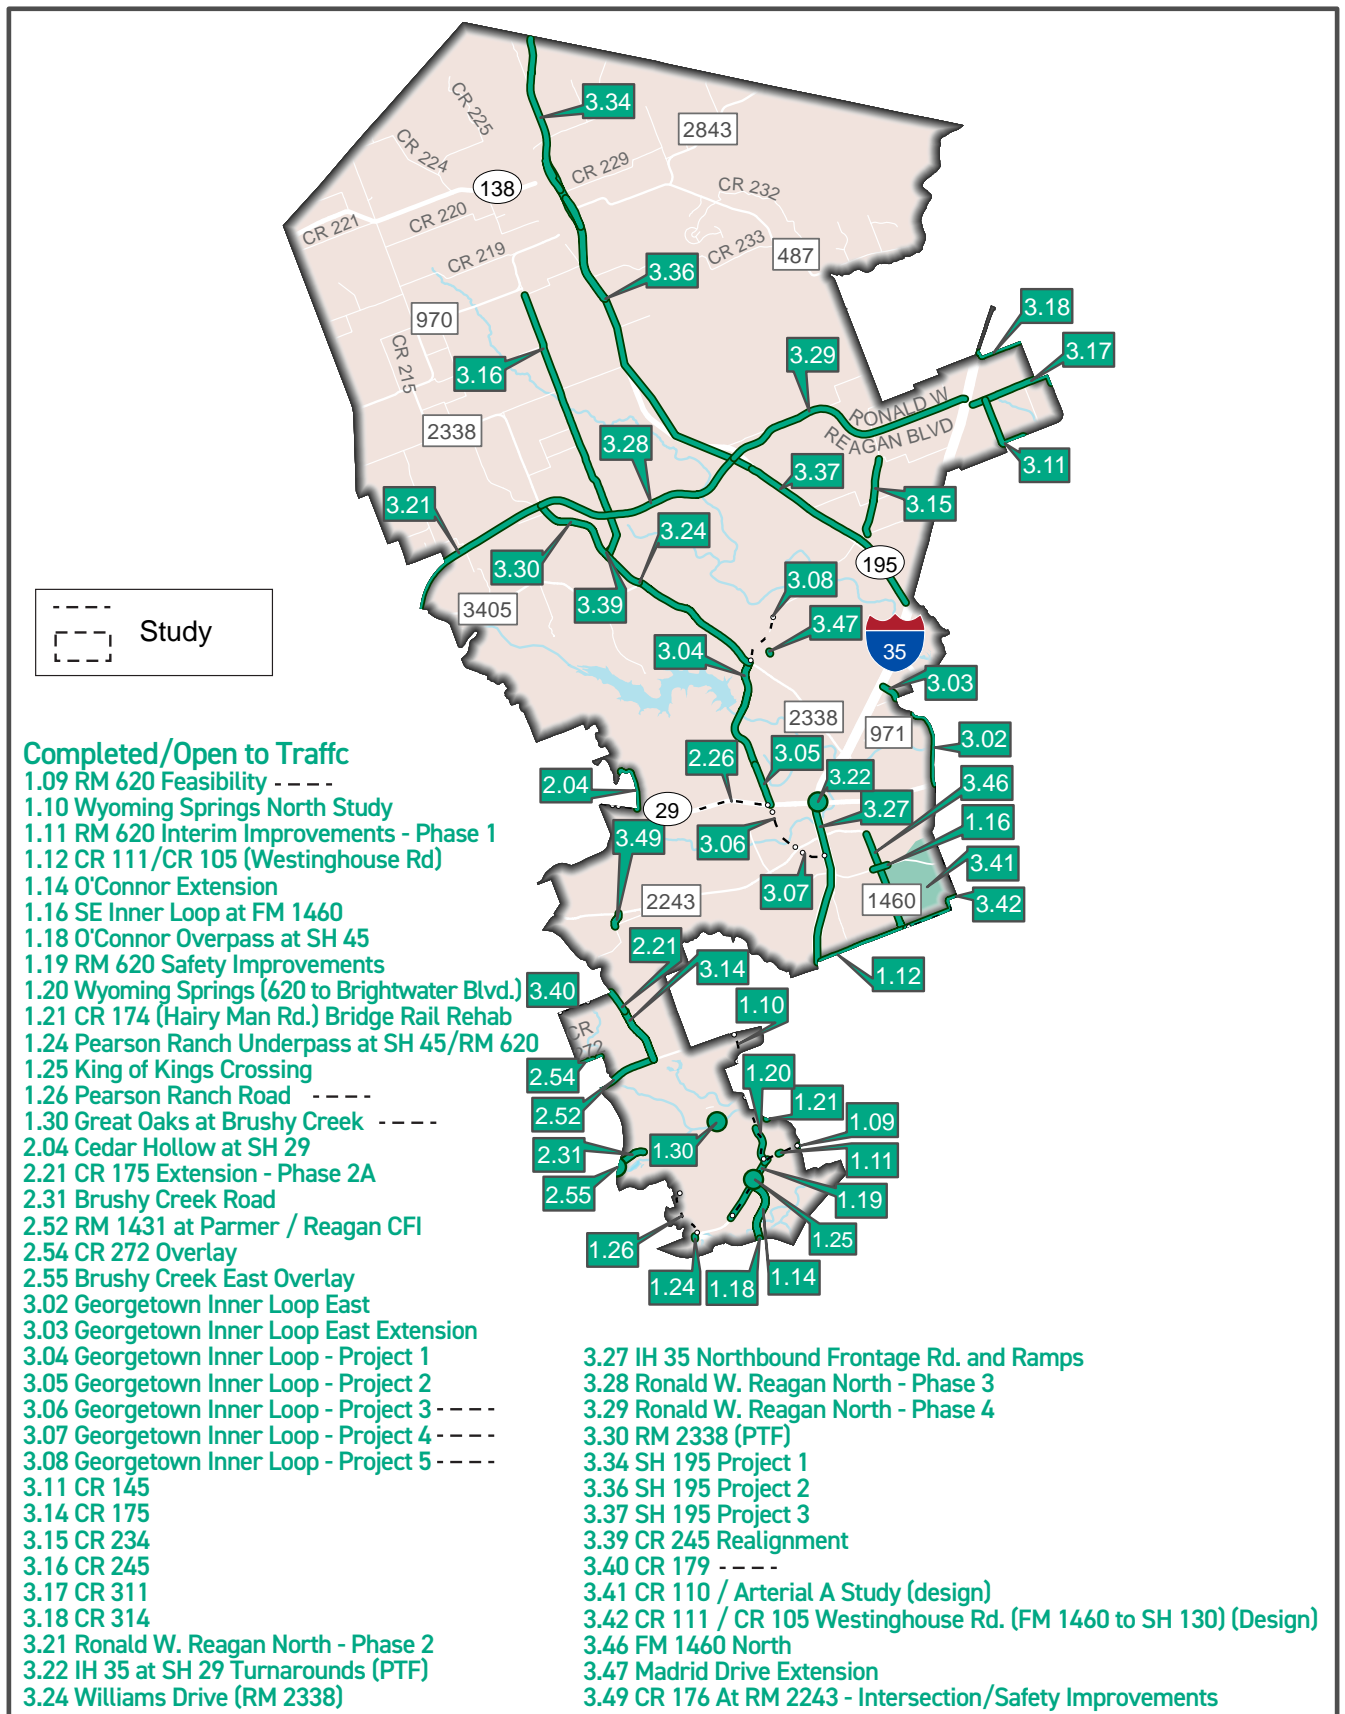

Precinct 3 - Commissioner Covey

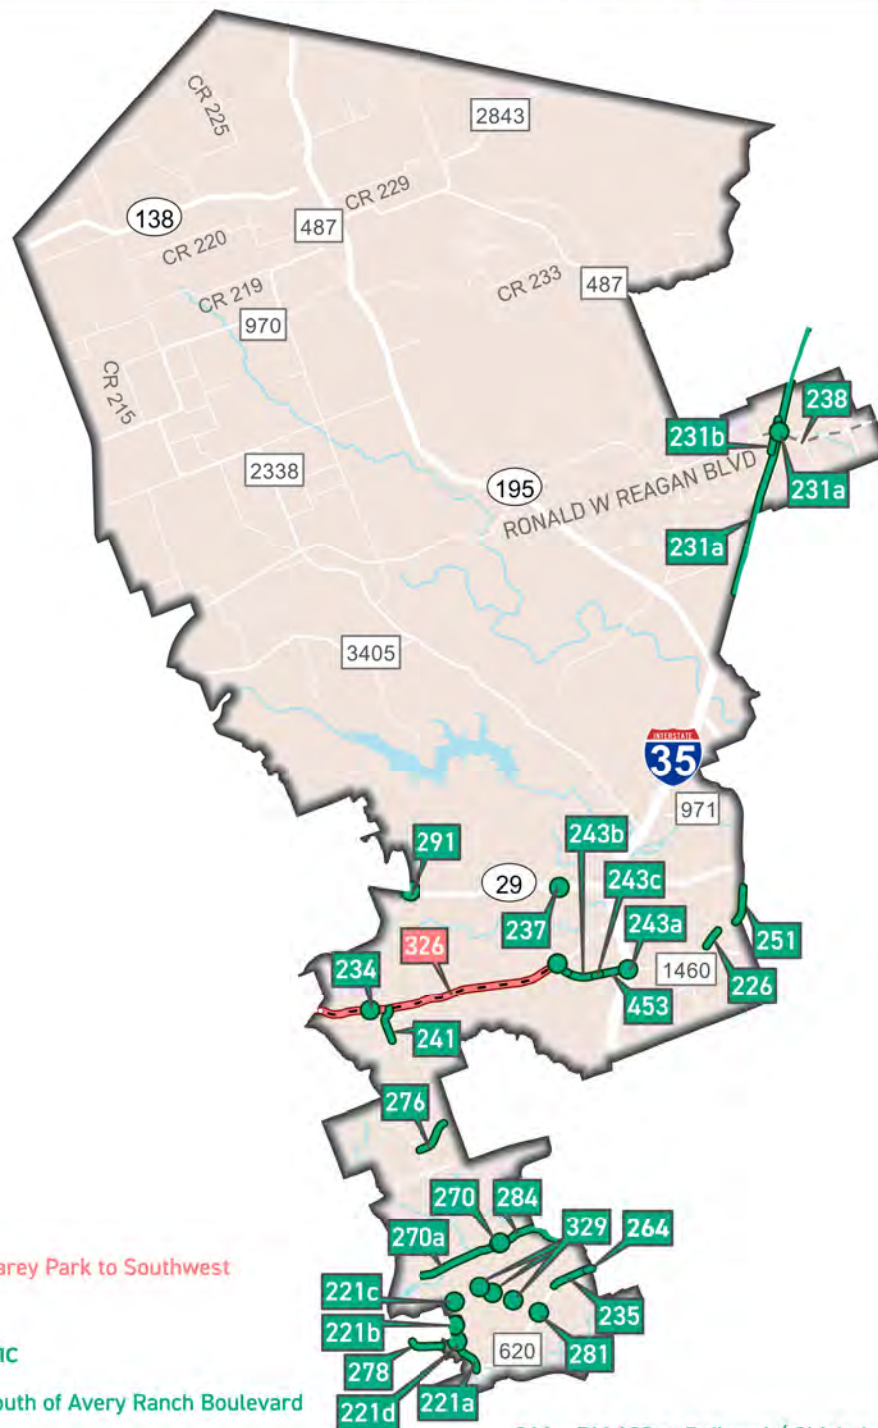

In Design

326 RM 2243 Realignment (Garey Park to Southwest Bypass)

Completed/Open to Traffic

221a Pearson Ranch Road (South of Avery Ranch Boulevard to SH 45 ROW)

221b Pearson Ranch Road and Iveans Way Pedestrian Crossing

221c Pearson Ranch Road at Avery Ranch Boulevard Traffic Signal

221d Neenah Avenue and Pearson Ranch Road Traffic Signal

226 Inner Loop Safety Improvements (LTL at Wilco Way)

231a IH 35 Ramp Reversal and Frontage Road Conversion (FM 972 to CR 312)

231b Relocation of 48" Williamson County Regional Raw Waterline - Line B

231c Ronald Reagan Boulevard at IH 35 Bridge Replacement

234 RM 2243 at Escalera Parkway (Intersection Improvements)

235 RM 620 Phase 2 (Wyoming Springs to Deep Woods)

237 SH 29 at DB Wood (Intersection Improvements)

238 Ronald Reagan Boulevard Extension Planning (IH 35 to

241 CR 176 at RM 2243 Intersecti

243a Southwest Bypass Driveways

243b Southwest Bypass Access Route

243c Southwest Bypass Segment 2 (Southbound IH 35 to RM 2243) 20

264 RM 620 at Railroad / Chisholm Trail (IH 35 Frontage
Road to Deep Wood Drive)

270 Great Oaks Drive Bridge at Brushy Creek

270a Great Oaks Drive Waterline Relocations

276 Arterial H Extension Phase 1 (CR 175 to Massey Way)

278 Neenah Avenue Widening (Olive Hill Drive to 0.5 miles east of Olive Hill Drive)

281 O'Connor Drive North of RM 620 Traffic Study and Safety Improvements

284 Hairy Man Road/Brushy Creek Road Safety Improvements
(Brushy Bend to Sam Bass Road)



291 SH 29 at Cedar Hollow (Intersection Improvements)
292 Westinghouse Road/CR 111/CR 105 (FM 1460 to SH 130)

329 O'Connor Drive Traffic Signals (Morgan Hill, Great Oaks and Liberty Walk Intersections)

453 Southwest Bypass Segment 1 (Southbound IH 35 to 0.5 miles west)

2019 ROAD BOND PROGRAM PROJECTS

Precinct 3 - Commissioner Covey

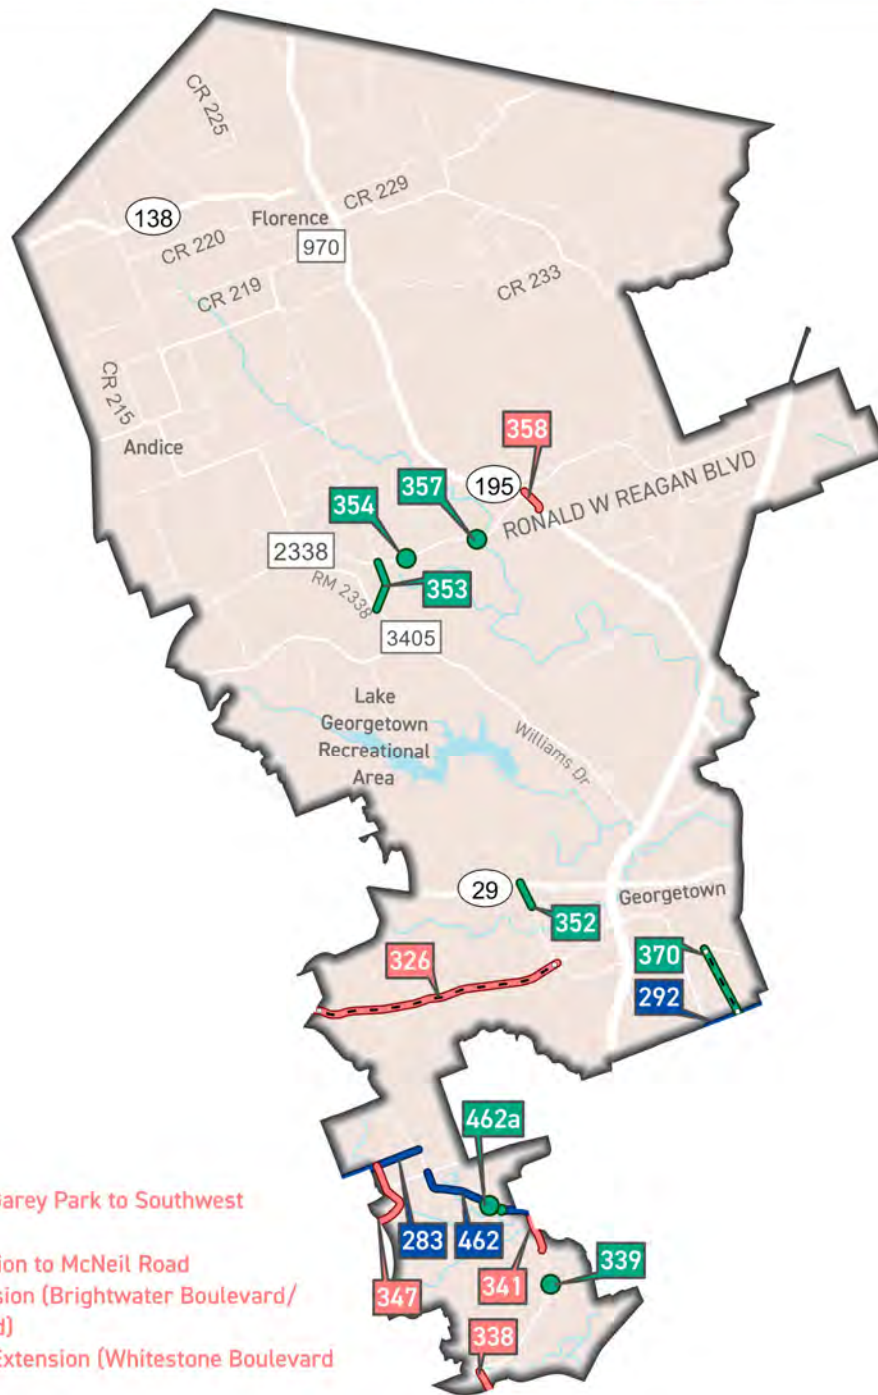

In Design

- 326 RM 2243 Realignment (Garey Park to Southwest Bypass)
- 338 RM 620/SH 45 Intersection to McNeil Road
- 341 Wyoming Springs Extension (Brightwater Boulevard/ Creek Bend to Sam Bass Road)
- 347 Toro Grande Boulevard Extension (Whitestone Boulevard to Parmer Lane)
- 358 SH 195 at Ronald Reagan Boulevard


Under Construction/Bidding

- 283 New Hope Drive Extension Phase 2A (Ronald Reagan Boulevard to Sam Bass Road)
- 292 CR 111/CR 105 Westinghouse (FM 1460 to SH 130)
- 462 Corridor H/Sam Bass Road (RM 1431 to Wyoming Springs Drive)

Completed/Open to Traffic

- 339 Wyoming Springs Intersection Improvements (At Smyers Lane)
- 352 Southwest Bypass Extension (SH 29 to Wolf Ranch Parkway)
- 353 CR 245 (North of RM 2338 to Ronald Reagan Boulevard)
- 354 Ronald Reagan at Silver Spur Boulevard
- 357 Ronald Reagan at Sun City Boulevard
- 370 MoKan (Georgetown Inner Loop to University Boulevard)
- 462a Corridor H/Sam Bass Road Interim Traffic Signals (Walsh Ranch and Great Oaks Drive Intersections)

Precinct 3 - Commissioner Covey

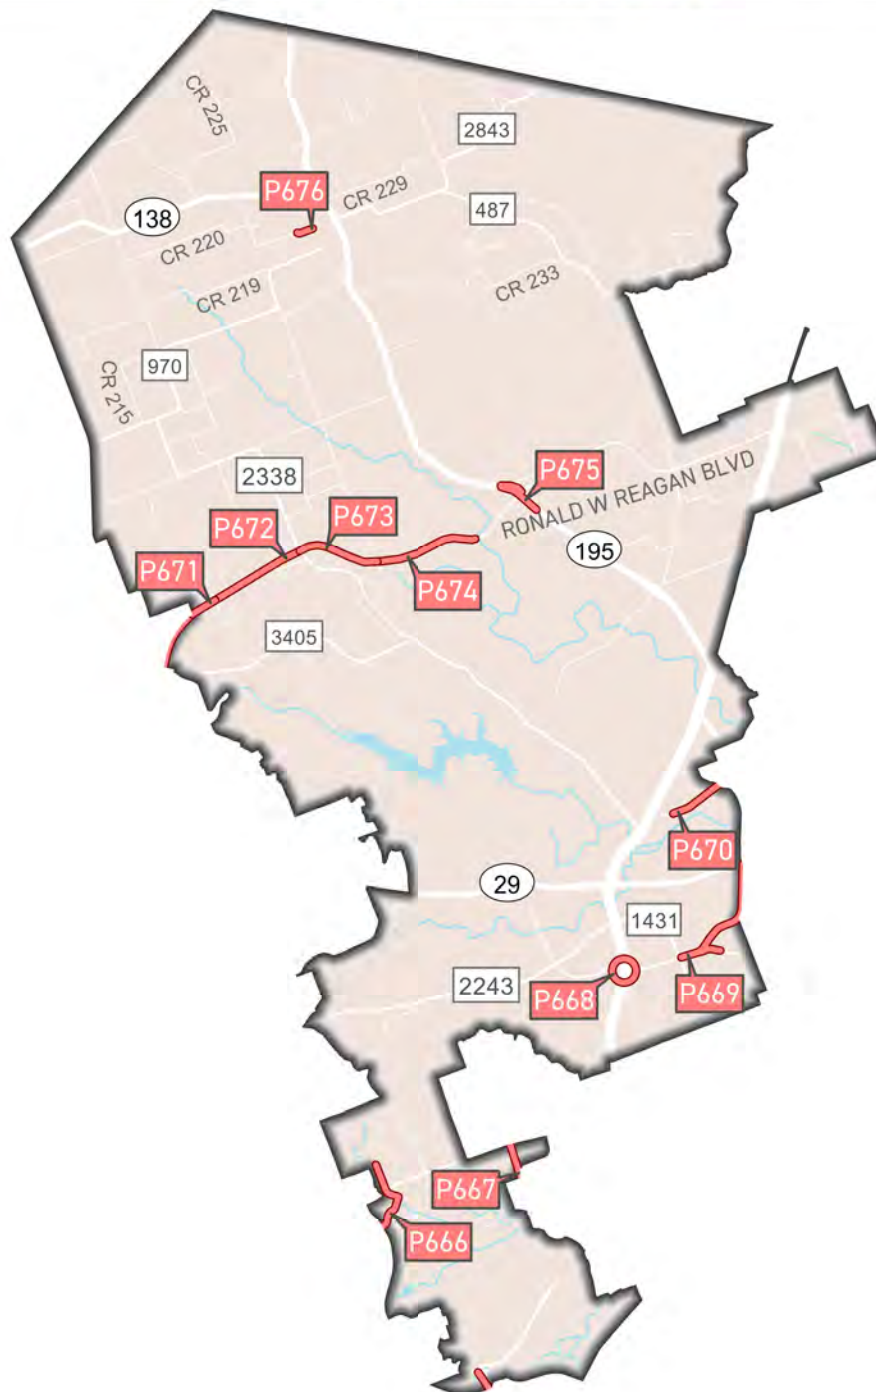

In Design

- P666 Toro Grande Boulevard Extension (Parmer Lane to New Hope)
P667 Wyoming Springs Drive (End of Wyoming Springs Drive / Behrens Ranch to RM 1431)
P668 I-35 at Inner Loop Interchange (SE Inner Loop / SW Bypass)
P669 SE Inner Loop (FM 1460 to SH 29)
P671 Ronald Reagan Boulevard Widening - Segment C1 (FM 3405 to CR 289)
P672 Ronald Reagan Boulevard Widening - Segment C2 (CR 289 to west of RM 2338)
P673 Ronald Reagan Boulevard Widening - Segment D1 (RM 2338 to CR 245)
P674 Ronald Reagan Boulevard Widening - Segment D2 (CR 245 to Sun City Blvd.)
P670 FM 971 (Gann St to SH 130)
P675 SH 195 at Ronald Reagan Boulevard - Remaining 3 Ramps
P676 West Main Street (S.Patterson Ave to CR 226)

Project Name: Great Oaks Drive Improvements at Brushy Creek
Project No. T4327

Original Contract Price = \$10,580,634.11

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>	
6/30/2021	8/3/2021	9/3/2021	9/13/2021	7/12/2023		585		585	
<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u> <u>Used</u>	<u>% Time</u> <u>Used</u>
1	9/13/2021	9/30/2021	18	\$299,881.08	\$299,881.08	\$33,320.12	\$33,320.12	3	3
2	10/1/2021	10/31/2021	31	\$305,937.90	\$605,818.98	\$33,993.10	\$67,313.22	6	8
3	11/1/2021	11/30/2021	30	\$353,916.66	\$959,735.64	\$39,324.07	\$106,637.29	10	14
4	12/1/2021	12/31/2021	31	\$323,378.73	\$1,283,114.37	\$35,930.97	\$142,568.26	13	19
5	1/1/2022	1/31/2022	31	\$388,799.66	\$1,671,914.03	\$43,199.97	\$185,768.23	18	24
6	2/1/2022	2/28/2022	28	\$496,378.98	\$2,168,293.01	\$55,153.22	\$240,921.45	23	29
7	3/1/2022	3/31/2022	31	\$243,581.01	\$2,411,874.02	\$27,064.55	\$267,986.00	25	34
8	4/1/2022	4/30/2022	30	\$232,084.08	\$2,643,958.10	\$25,787.13	\$293,773.13	28	39
9	5/1/2022	5/31/2022	31	\$754,642.60	\$3,398,600.70	\$83,849.18	\$377,622.31	36	45
10	6/1/2022	6/30/2022	30	\$340,143.43	\$3,738,744.13	\$37,793.71	\$415,416.02	39	50
11	7/1/2022	7/31/2022	31	\$475,914.67	\$4,214,658.80	\$52,879.41	\$468,295.43	44	55
12	8/1/2022	8/31/2022	31	\$373,966.90	\$4,588,625.70	\$41,551.87	\$509,847.30	48	60
13	9/1/2022	9/30/2022	30	\$334,474.19	\$4,923,099.89	\$37,163.80	\$547,011.10	52	65
14	10/1/2022	10/31/2022	31	\$596,227.60	\$5,519,327.49	\$66,247.51	\$613,258.61	58	71
15	11/1/2022	11/30/2022	30	\$150,522.30	\$5,669,849.79	\$16,724.70	\$629,983.31	59	76
16	12/1/2022	12/31/2022	31	\$210,284.10	\$5,880,133.89	\$23,364.90	\$653,348.21	62	81
17	1/1/2023	1/31/2023	31	\$487,668.38	\$6,367,802.27	\$54,185.38	\$707,533.59	67	86
18	2/1/2023	2/28/2023	28	\$319,021.56	\$6,686,823.83	\$35,446.84	\$742,980.43	70	91
19	3/1/2023	3/31/2023	31	\$481,061.68	\$7,167,885.51	\$53,451.29	\$796,431.72	75	97
20	4/1/2023	4/30/2023	30	\$1,102,824.63	\$8,270,710.14	-\$361,131.19	\$435,300.53	82	102
21	5/1/2023	5/31/2023	31	\$398,266.76	\$8,668,976.90	\$20,961.41	\$456,261.94	86	107
22	6/1/2023	6/30/2023	30	\$713,888.01	\$9,382,864.91	\$37,573.06	\$493,835.00	93	112
23	7/1/2023	7/31/2023	31	\$518,248.40	\$9,901,113.31	\$27,276.23	\$521,111.23	98	117
24	8/1/2023	8/31/2023	0	\$85,268.20	\$9,986,381.51	\$4,487.80	\$525,599.03	99	117
25	9/1/2023	9/30/2023	0	\$351,666.54	\$10,338,048.05	-\$314,618.46	\$210,980.57	100	117
26	10/1/2023	3/1/2024	0	\$28,909.60	\$10,366,957.65	\$589.99	\$211,570.56	100	100

3/31/2024 Comments - Project close out on going.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
01	3/29/2022	\$ 29,487.96	\$ 29,487.96

4B: Third Party Accommodation. Third Party Requested Work, 2E: Differing Site Condition. Miscellaneous difference in site conditions (unforeseeable), 6C: Untimely ROW/Utilities. Utilities not clear. This Change Order adds items to pay the Contractor to pour a concrete cap over an existing City of Round Rock (CORR) wastewater manhole at Bent, excavate to find an existing CORR wastewater line trench, and for standby costs due to a conflict with existing ATT line at Culvert C.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
02	9/14/2022	\$ 100,234.16	\$ 129,722.12

6C. Untimely ROW/Utilities. Utilities not clear. This Change Order adds an item to pay the Contractor for emergency repairs to the existing City of Round Rock wastewater line that was damaged while drilling for a drill shaft for the Hairy Man bridge abutment. Cost sharing (one third) was agreed to by the County with the contractor, DeNucci Constructors.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
03	3/2/2023	27,926.96	157,649.08

1A: Incorrect PS&E. This Change Order adds items to pay for traffic rail Junction Boxes, a 36' tall traffic signal pole, an Electric Service TY A, a Guardrail End Treatment, and Removable Work Zone Pavement Markings. These items of work were not properly addressed in the project plan set.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
04	3/2/2023	11,820.42	169,469.50

3L. County Convenience. Revising safety work/measures desired by the County. This Change Order adds a pay item for additional pavement widening to improve the turning radius at the south end of the existing Great Oaks bridge over Brushy Creek.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
05	3/22/2023	2,831.80	172,301.30

2. Differing Site Conditions. 2E. Miscellaneous difference in site conditions (unforeseeable)(Item 9). This Change Order adds an item to pay for additional signs needed at the Oak Ridge Drive and Great Oaks Drive intersection during Phase 3 construction. This Change Order also adds an item to pay for water valves to be adjusted on the southwest corner of the existing Great Oaks Drive and Brushy Creek Road intersection.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
06	7/11/2023	65,607.52	237,908.82

2G. Miscellaneous difference in site conditions. Unadjusted utility (unforeseeable). This Change Order adds an item to pay for the redesigned Panel 7 at Wall 1A due to BCMUD water line elevations differing from that shown in the plans. This Change Order also adds an item to pay for the reinforcing steel previously ordered and delivered to the project for the original design of Panel 7 at Wall 1A. In addition, this Change Order reduces the original item 423-6005 RETAINING WALL (SPREAD FOOTING) due to this change.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
07	7/11/2023	9,735.71	247,644.53

1A. Design Error or Omission. Incorrect PS&E: This Change Order adds a new pay item to reimburse the contractor for replacing a mis-sized traffic signal pole (Pole #7), due to incorrect height in the plans. The contractor ordered and received the traffic signal pole prior to the error being found. The contractor has delivered the mis-sized pole to the Williamson County Maintenance yard.


<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
08	9/14/2023	30,531.08	278,175.61

1A. Design Error or Omission. Incorrect PS&E: This Change Order adds new pay items to reimburse the contractor for street signs and pavement markings that were not shown in the plans. This Change Order also adds an item for a clearance sign that was shown in the plans but had no pay item to pay for the work. In addition, this Change Order adds a pay item to reimburse the contractor for ground boxes not installed.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
09	2/28/2024	-268,281.51	9,894.10

1A. Differing Site Conditions. 2E. Miscellaneous difference in site conditions (unforeseeable). This Change Order provides the final balancing for the overrun/underrun of contract quantities on the project as a result of addressing field conditions not accounted for in the original plans and adds an item for irrigation repairs at Shirley McDonald Park previously paid for under a Force Account Item. This Change Order also adds 83 days to the contract due to Utility issues and change order work.

Adjusted Price = \$10,590,528.21



**CR 111 Westinghouse Road
(FM 1460 to SH 130 and CR 110 North to CR 111)**

**Project Length: 4.633 Miles
Roadway Classification: Rural Collector**

**Project Schedule: January 2022 - Spring 2024
Estimated Construction Cost: \$22.5 Million**



MARCH 2024 IN REVIEW

3/1/2024: Capital Excavation continued to place textured colored concrete at the center median of FM 1460. The Contractor placed topsoil at the right-of-way on the north side of the roadway east of FM 1460.

3/8/2024: Contractor formed and poured curb and gutter and continued placing colored textured concrete at the center median at FM 1460.

3/15/2024: Capital Excavation formed and poured the mow strip for the metal beam guard fence east of FM 1460. Capital continued grading and placing topsoil along roadway edge throughout the project.

3/22/2024: Subcontractor placed stone matrix at the culvert by Maple Street. The Contractor performed general clean up and performed punch list items. Subcontractor ESSI seeded the road edge and placed soil retention blankets throughout project.

3/29/24: Capital Excavation worked on punch list items. Subcontractor Flasher placed pavement markings around the FM 1460 intersection.



**Design Engineer: Steger Bizzell
Contractor: Capital Excavation
Construction Observation:
Chuck Evans, HNTB**

**Williamson County
Road Bond Program**

Project Name: CR 111 Westinghouse Road
Project No. 22IFB39

Original Contract Price = \$21,024,332.88

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>	
12/15/2021	1/11/2022	1/20/2022	1/30/2022			700		700	
<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u> <u>Used</u>	<u>% Time</u> <u>Used</u>
1	2/1/2022	2/28/2022	28	\$142,149.86	\$142,149.86	\$15,794.43	\$15,794.43	1	4
2	3/1/2022	3/31/2022	31	\$1,624,724.26	\$1,766,874.12	\$180,524.92	\$196,319.35	9	8
3	4/1/2022	4/30/2022	30	\$1,286,121.32	\$3,052,995.44	\$142,902.37	\$339,221.72	15	13
4	5/1/2022	5/31/2022	31	\$1,110,146.62	\$4,163,142.06	\$123,349.64	\$462,571.36	21	17
5	6/1/2022	6/30/2022	30	\$482,208.08	\$4,645,350.14	\$53,578.66	\$516,150.02	23	21
6	7/1/2022	7/31/2022	31	\$787,719.86	\$5,433,070.00	\$87,524.44	\$603,674.46	27	26
7	8/1/2022	8/31/2022	31	\$822,906.88	\$6,255,976.88	\$91,434.10	\$695,108.56	31	30
8	9/1/2022	9/30/2022	30	\$1,707,686.45	\$7,963,663.33	\$189,742.92	\$884,851.48	39	35
9	10/1/2022	10/31/2022	31	\$1,107,286.40	\$9,070,949.73	\$123,031.82	\$1,007,883.30	45	39
10	11/1/2022	11/30/2022	30	\$518,917.48	\$9,589,867.21	\$57,657.50	\$1,065,540.80	47	43
11	12/1/2022	12/31/2022	31	\$1,285,779.15	\$10,875,646.36	-\$493,138.36	\$572,402.44	51	48
12	1/1/2023	1/31/2023	31	\$620,120.59	\$11,495,766.95	\$32,637.93	\$605,040.37	54	52
13	2/1/2023	2/28/2023	28	\$846,149.01	\$12,341,915.96	\$44,534.15	\$649,574.52	58	56
14	3/1/2023	3/31/2023	31	\$639,962.65	\$12,981,878.61	\$33,682.25	\$683,256.77	61	61
15	4/1/2023	4/30/2023	30	\$717,084.56	\$13,698,963.17	\$37,741.29	\$720,998.06	64	65
16	5/1/2023	5/31/2023	31	\$661,601.87	\$14,360,565.04	\$34,821.15	\$755,819.21	67	69
17	6/1/2023	6/30/2023	30	\$591,898.92	\$14,952,463.96	\$31,152.58	\$786,971.79	70	74
18	7/1/2023	7/31/2023	31	\$555,320.94	\$15,507,784.90	\$29,227.41	\$816,199.20	72	78
19	8/1/2023	8/31/2023	31	\$451,231.96	\$15,959,016.86	\$23,749.06	\$839,948.26	75	82
20	9/1/2023	9/30/2023	30	\$371,656.43	\$16,330,673.29	\$19,560.86	\$859,509.12	76	87
21	10/1/2023	10/31/2023	31	\$230,597.40	\$16,561,270.69	\$12,136.71	\$871,645.83	77	91
22	11/1/2023	11/30/2023	30	\$179,598.00	\$16,740,868.69	\$9,452.52	\$881,098.35	78	95
23	12/1/2023	12/31/2023	31	\$801,573.10	\$17,542,441.79	\$42,188.06	\$923,286.41	82	100
24	1/1/2024	1/31/2024	31	\$858,054.72	\$18,400,496.51	\$45,160.77	\$968,447.18	86	104
25	2/1/2024	2/29/2024	29	\$802,470.59	\$19,202,967.10	\$42,235.30	\$1,010,682.48	90	108

3/31/2024 Comments - The Contractor finished placing the top layer of HMA and switched traffic to final configuration. The contractor started working on punch list items.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
01	5/3/2022	\$233,364.00	\$ 233,364.00

2 Differing in site conditions. (Unforeseeable) 2E. Miscellaneous difference in site conditions (unforeseeable) (item 9): This change order compensates the Contractor for over-excavating unsuitable material and importing embankment material from offsite that meets the requirements in the specifications. With the limited areas on the project to find suitable material it was agreed to import the required material. A Force Account item has been created to cover half of the cost of the imported material and half of the trucking. This amount is to cover this area and any other areas that may be encountered on site.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
02	5/3/2022	\$7,553.84	\$ 240,917.84

1B. Design Error or Omission. Other: This change order compensates the Contractor for upsize changes in 6 inlet and 1 junction box to accommodate pipe size design. The revisions affected estimate page 15, summary page 18, storm drainage pages; 149 for Inlet C-5 and C-6, page 150 for Inlets E-4 and E-5, page 151 for Inlet F-6, page 153 for Inlet I-6 and page 154 for Junction Box K.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
03	7/14/2022	\$20,307.20	\$ 261,225.04

1.Design Error or Omission. 1A: incorrect PS&E. This Change Order is in response to RFI 22 that updated the quantity for pay item 106-6002 OBLITERATING ABANDONED ROADWAY. The item has been recalculated and the difference is included in this Change Order to cover the actual quantity.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
04	7/13/2022	\$454,267.40	\$ 715,492.44

1. Design Error or omission. 1B. Other: This Change Order updates the bid item quantities that were revised in the plan set summary sheet, but not reflected in the Bid Form. The Change Order also includes pay items for 2 new items that were identified in the plans, but inadvertently left off the Bid Form.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
05	11/22/2022	\$41,134.66	\$ 756,627.10

1. Design Error or Omission. 1B. Other. The existing section of the roadway in front of Gateway School was constructed prior to the project letting. This portion of the roadway was to remain in place and the proposed roadway was to tie into it. The contractor constructed around this portion of the roadway so that the tie-ins would work with the current plan design. 1B. Other. This Change Order also adds items for flowable fill and concrete dissipaters at the culvert outfalls.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
06	11/22/2022	\$24,159.20	\$ 780,786.30

2. Differing Site Conditions: (Unforeseeable) 2J. Other: While clearing the ROW, 4 water wells were encountered. This Change Order provides payment to the Contractor for having the plugging and abandoning four (4) wells, by a licensed water well company. Upon completion of the well abandonment, plugging reports will be filed.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
07	12/14/2022	\$28,440.00	\$ 809,226.30

1B. Design Error or Omission. 1B. Other: This Change Order provides additional items to the Contract for adjusting an existing headwall, wingwalls and adding concrete rail along an existing culvert that is to remain in place. Due to the height of the existing culvert, the proposed roadway can not be built to the proposed width. Raising the headwall and constructing the rail will allow for the roadway portion to be constructed to the proposed width. This rail will mirror the existing rail along the upstream portion of the existing culvert.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
08	12/14/2022	\$276,200.00	\$ 1,085,426.30

4B. Third Party Accommodation. Third party requested work: MBC Development has requested additional sleeves to be installed across CR 111 for their future development on both sides of the roadway. The Developer Agreement has been amended to reflect the change and the Developer has funded Williamson County for this additional work.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
09	4/25/2023	\$14,282.00	\$ 1,099,708.30

1. Design Error or Omission. 1B Other: This Change Order compensates the contractor for relocating the existing service line to tie into the new meter location. The meter was relocated outside of the new ROW per the plans, but the plans did not show a service line connection for the residence back in at this location. Per the ILA, the County must, at its own expense, pay all cost related to the relocation of Jonah's water lines.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
10	6/6/2023	\$39,507.50	\$ 1,139,215.80

2E. Differing in Site Conditions. Miscellaneous difference in site conditions (unforeseeable)(Item 9). This Change Order compensates the contractor for removing and replacing the existing concrete driveway at the Valero gas station as well as removing the sidewalk that is in conflict with the proposed roadway widening.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
11	8/22/2023	\$81,433.12	\$ 1,220,648.92

6 Untimely ROW/Utilities 6C: Utilities Not Clear: This Change Order compensates the contractor for relocating the existing 12-inch City of Georgetown water line that is in conflict with the culvert a Driveway 1. The water line is being relocated between the proposed box culvert and the ROW along the north side of the project.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
12	1/9/2024	\$303,603.61	\$ 1,524,252.53

6C. Utilities not clear. This Change Order adds an item to the contract for inefficient work and delays the contractor experienced due to the utilities not being cleared throughout the project.

Adjusted Price = \$22,548,585.41

Project Name: Southwest Bypass Extension
Project No. 22IFB110

Original Contract Price = \$4,288,543.00

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>	
6/23/2022	7/12/2022	8/18/2022	8/29/2022	6/22/2023		239	59	298	
<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u> <u>Used</u>	<u>% Time</u> <u>Used</u>
1	8/29/2022	8/31/2022	3	\$77,542.20	\$77,542.20	\$8,615.80	\$8,615.80	2	1
2	9/1/2022	9/30/2022	30	\$126,769.50	\$204,311.70	\$14,085.50	\$22,701.30	6	11
3	10/1/2022	10/31/2022	31	\$460,653.35	\$664,965.05	\$51,183.71	\$73,885.01	19	21
4	11/1/2022	11/30/2022	30	\$148,852.80	\$813,817.85	\$16,539.20	\$90,424.21	23	32
5	12/1/2022	12/31/2022	31	\$180,500.40	\$994,318.25	\$20,055.60	\$110,479.81	28	42
6	1/1/2023	1/31/2023	31	\$308,200.50	\$1,302,518.75	\$34,244.50	\$144,724.31	37	52
7	2/1/2023	2/28/2023	28	\$424,385.10	\$1,726,903.85	\$47,153.90	\$191,878.21	49	62
8	3/1/2023	3/31/2023	31	\$778,428.08	\$2,505,331.93	-\$60,018.63	\$131,859.58	68	72
9	4/1/2023	4/30/2023	30	\$585,017.55	\$3,090,349.48	\$30,790.39	\$162,649.97	83	82
10	5/1/2023	5/31/2023	31	\$109,588.94	\$3,199,938.42	\$5,767.84	\$168,417.81	86	93
11	6/1/2023	6/30/2023	22	\$220,158.23	\$3,420,096.65	\$11,587.28	\$180,005.09	92	100
12	7/1/2023	7/31/2023	0	\$123,360.35	\$3,543,457.00	\$6,492.65	\$186,497.74	96	100
13	8/1/2023	8/31/2023	0	\$139,934.87	\$3,683,391.87	\$7,364.99	\$193,862.73	99	100
14	9/1/2023	9/30/2023	0	\$130,311.87	\$3,813,703.74	-\$116,032.04	\$77,830.69	100	100
15	10/1/2023	10/20/2023	0	\$7,967.34	\$3,821,671.08	\$162.60	\$77,993.29	100	100
16	10/21/2023	11/30/2023	0	\$10,139.93	\$3,831,811.01	\$206.93	\$78,200.22	100	100

3/31/2024 Comments - Project closeout continues. The punch list items are completed, waiting on vegetation establishment

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
01	7/18/2023	3,440.89	3,440.89

2C. Differing Site Conditions (unforeseeable). New development (conditions changing after PS&E completed). This Change Order covers several different changes that took place on the project, including adjusting the ditch along Wolf Ranch to avoid water line, installing cave gates instead of the fencing, revising the sidewalk under the bridge, placing concrete driveway instead of asphalt driveway into Wolf Ranch Apartments and revising the SWPPP sheets per the updated WPAP. 5D. Contractor Convenience. Additional safety work/measures desired by the contractor. Barrier was installed along the work zone for the SH 29 widening at the Southwest Bypass.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
02	9/14/2023	15,802.83	19,243.72

2. Differing Site Conditions (unforeseeable) 2I. Additional safety needs (unforeseeable): This Change Order compensates the contractor for adjusting the guardrail north of Wolf Ranch Parkway on Southwest Bypass due to site distance concerns.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
03	12/5/2023	-410,375.49	-391,131.77

2E. Miscellaneous difference in site conditions (unforeseeable)(Item 9). This Change Order provides the final balancing for the overruns/underruns of contract quantities on the project that are a result of addressing field conditions not accounted for in the original plans.

Adjusted Price = \$3,897,411.23

Project Name: CR 245 Reconstruction
Project No. 23IFB12

Original Contract Price = \$6,969,195.21


<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>	
12/6/2022	12/13/2022	2/1/2023	2/10/2023			423		423	
<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u> <u>Used</u>	<u>% Time</u> <u>Used</u>
1	2/10/2023	2/28/2023	19	\$143,464.59	\$143,464.59	\$15,940.51	\$15,940.51	2	4
2	3/1/2023	3/31/2023	31	\$355,908.11	\$499,372.70	\$39,545.35	\$55,485.86	8	12
3	4/1/2023	4/30/2023	30	\$378,182.90	\$877,555.60	\$42,020.32	\$97,506.18	14	19
4	5/1/2023	5/31/2023	31	\$541,611.28	\$1,419,166.88	\$60,179.03	\$157,685.21	23	26
5	6/1/2023	6/30/2023	30	\$438,431.06	\$1,857,597.94	\$48,714.56	\$206,399.77	30	33
6	7/1/2023	7/31/2023	31	\$1,157,295.20	\$3,014,893.14	\$128,588.36	\$334,988.13	48	41
7	8/1/2023	8/31/2023	31	\$1,149,398.96	\$4,164,292.10	-\$115,814.86	\$219,173.27	63	48
8	9/1/2023	9/30/2023	30	\$601,990.01	\$4,766,282.11	\$31,683.68	\$250,856.95	72	55
9	10/1/2023	10/31/2023	31	\$97,202.52	\$4,863,484.63	\$5,115.92	\$255,972.87	73	62
10	11/1/2023	11/30/2023	30	\$544,037.17	\$5,407,521.80	\$28,633.54	\$284,606.41	81	62
11	12/1/2023	1/31/2024	62	\$128,644.67	\$5,536,166.47	\$6,770.77	\$291,377.18	83	70
12	2/1/2024	2/29/2024	0	\$231,946.39	\$5,768,112.86	-\$173,660.59	\$117,716.59	84	73
13	3/1/2024	3/31/2024	0	\$48,401.14	\$5,816,514.00	\$987.78	\$118,704.37	85	73

3/31/2024 Comments - Awaiting vegetation establishment.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
01	8/22/2023	20,980.10	20,980.10

1. Design Error or Omission. 1B. Other: This Change Order compensates the contractor for removing a portion of a structure that encroaches the new ROW. 2. Differing in Site Conditions: (Unforeseeable) 2E: Miscellaneous difference in site conditions (unforeseeable)(Item 9). This Change Order addresses karst features that were encountered while excavating to subgrade south of Smokestack Ln. The karst features were closed per SWCA and TCEQ recommendations.

Adjusted Price = \$6,990,175.31

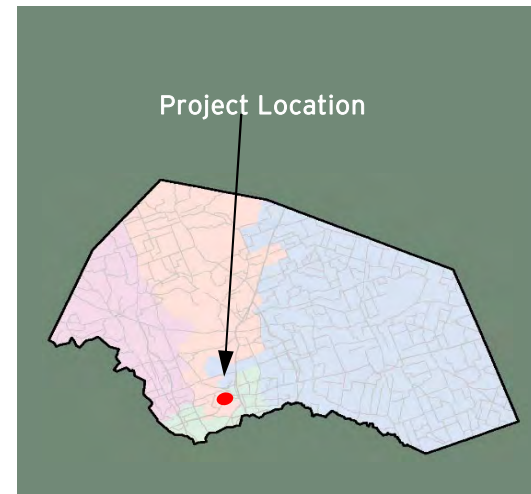

**Corridor H/Sam Bass Road
(RM 1431 to Wyoming Springs Drive)**

**Project Length: 2.578 Miles
Roadway Classification: Urban Minor Arterial**

**Project Schedule: January 2022 - Fall 2025
Estimated Construction Cost: \$33.8 Million**



MARCH 2024 IN REVIEW


3/1/2024: Cash Construction excavated the bore pit for the BCMUD water line crossing of Sam Bass Road at Tonkawa Trail. Subcontractor reworked the detour subgrade at Deer Trail Circle. AT&T Contractor is on site relocating existing AT&T lines between Deer Trail Circle and Great Oaks Drive.

3/8/2024: Subcontractor reworked a section of the detour subgrade near Deer Trail Circle. Contractor CTRB completed the BCMUD 24-inch casing bore across Sam Bass at Tonkawa Trail.

3/15/2024: Contractor placed the embankment at the bridge abutments for Dry Fork Creek. Subcontractor CTRB continued boring the Round Rock 60-inch casing at Thousand Oaks.

3/22/2024: Cash removed the thrust block concrete from the existing Round Rock water line at RM 1431. The Contractor placed the final embankment at the bridge abutments at Dry Fork Creek.

3/29/24: Cash Construction continued installing the Round Rock 42-inch water line near Thousand Oaks.

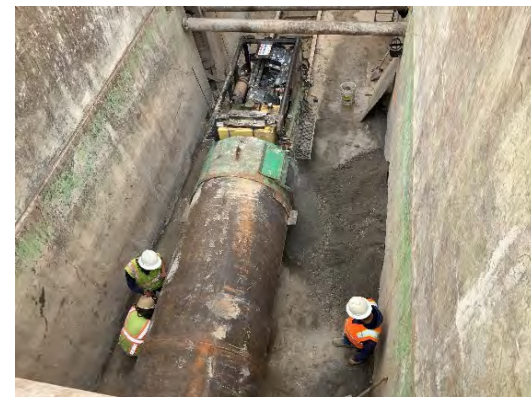

**Design Engineer: K Friese
Contractor: Cash Construction
Construction Observation:
Tracy Cooper, HNTB**

**Williamson County
Road Bond Program**

Project Name: Corridor H/Sam Bass Road
Project No. 23IFB8

Original Contract Price = \$36,145,959.00

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>	
12/20/2022	1/13/2023	3/13/2023	3/23/2023			911		911	
<u>Invoice</u>	<u>Beginning</u>	<u>Ending</u>	<u>Days</u>	<u>Current</u>	<u>Invoiced</u>	<u>Current</u>	<u>Total</u>	<u>% (\$)</u>	<u>% Time</u>
<u>Number</u>	<u>Date</u>	<u>Date</u>	<u>Charged</u>	<u>Invoice</u>	<u>Total</u>	<u>Retainage</u>	<u>Retainage</u>	<u>Used</u>	<u>Used</u>
1	4/1/2023	4/30/2023	30	\$21,095.55	\$21,095.55	\$2,343.95	\$2,343.95	0	3
2	5/1/2023	5/31/2023	31	\$511,459.79	\$532,555.34	\$56,828.87	\$59,172.82	2	7
3	6/1/2023	6/30/2023	30	\$1,024,886.41	\$1,557,441.75	\$113,876.26	\$173,049.08	5	10
4	7/1/2023	7/31/2023	31	\$148,136.40	\$1,705,578.15	\$16,459.60	\$189,508.68	6	13
5	8/1/2023	8/31/2023	31	\$915,201.56	\$2,620,779.71	\$101,689.06	\$291,197.74	9	17
6	9/1/2023	9/30/2023	30	\$510,079.42	\$3,130,859.13	\$56,675.50	\$347,873.24	10	20
7	10/1/2023	10/31/2023	31	\$900,115.81	\$4,030,974.94	\$100,012.86	\$447,886.10	13	23
8	11/1/2023	11/30/2023	30	\$731,394.97	\$4,762,369.91	\$81,266.11	\$529,152.21	16	27
9	12/1/2024	12/31/2024	31	\$241,049.16	\$5,003,419.07	\$26,783.24	\$555,935.45	16	27
10	1/1/2024	1/31/2024	31	\$412,213.73	\$5,415,632.80	\$45,801.53	\$601,736.98	18	30
11	2/1/2024	2/29/2024	29	\$986,810.97	\$986,810.97	\$109,645.66	\$711,382.64	21	37

3/31/2024 Comments - Cash Construction continued installing the Round Rock 42-inch and 12" BCMUD water lines. They completed the drilled shafts for the Dry Fork Bridge and continued roadway excavation near Thousand Oaks.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
01	6/27/2023	\$ (2,394,078.12)	\$ (2,394,078.12)


1B: Design Error or Omission. Other. This Change Order revises the earthwork quantities, BCMUD water line items and driveway quantities, per plan revisions issued after the Bid was awarded. The quantity for Item 110-6001 excavation was reduced by over 25% and the unit price is revised because it is considered a major bid item per the Contract.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
02	8/22/2023	\$ 5,250.00	\$ (2,388,828.12)

1B. Design Error or Omission. Other: This Change Order updates incorrect unit prices that were inadvertently used for two existing items in Change Order 1.

Adjusted Price = \$33,757,130.88



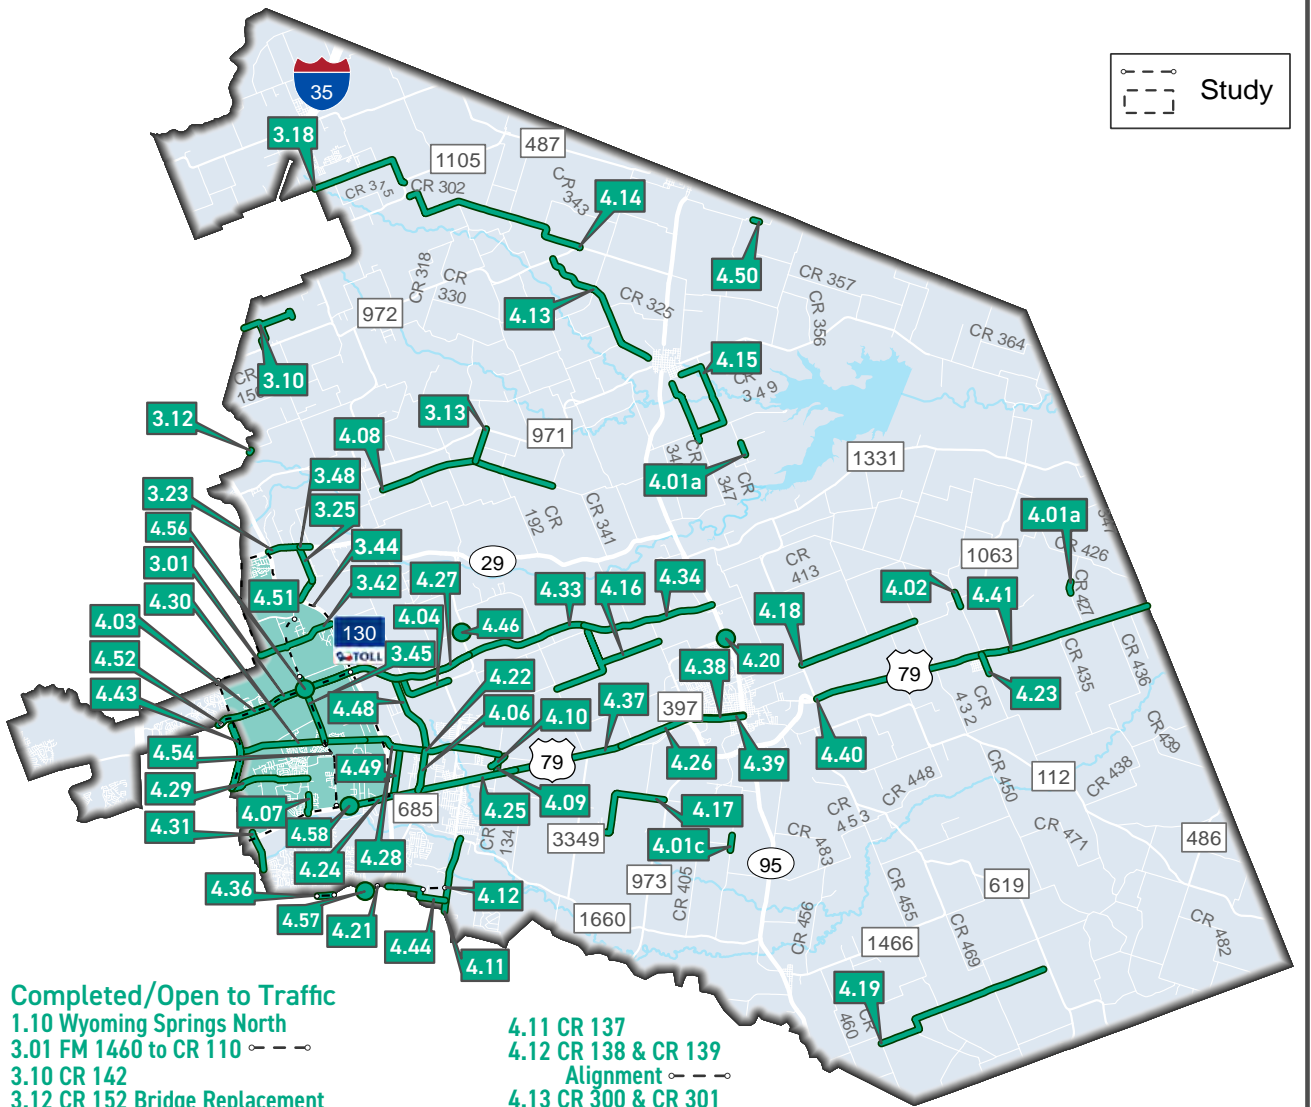

2000/2006 Road Bond Program Projects Precinct 4 - Commissioner Boles



Completed/Open to Traffic


- 1.10 Wyoming Springs North
- 3.01 FM 1460 to CR 110
- 3.10 CR 142
- 3.12 CR 152 Bridge Replacement
- 3.13 CR 157
- 3.18 CR 314
- 3.23 SH 29/CR 104 - Phase 1
- 3.25 CR 104 - Phase 2
- 3.42 CR 111 / CR 105 (Westinghouse Rd.) - FM 1460 to SH 130
- 3.44 CR 110 North (North of CR 107 to North of Sam Houston)
- 3.45 CR 110 Middle (North of Limmer Loop to CR 107)
- 3.48 SH 29 Widening - 12" Water Main Relocation
- 4.01a CR 427 Bridge Replacement
- 4.01b CR 390 Bridge Replacement
- 4.01c CR 406 Bridge Replacement
- 4.02 CR 424 Bridge Replacement
- 4.03 Chandler Road - Phase 1
- 4.04 CR 100
- 4.06 CR 119
- 4.07 CR 122 at US 79
- 4.08 CR 124
- 4.09 CR 132
- 4.10 CR 136
- 4.11 CR 137
- 4.12 CR 138 & CR 139 Alignment
- 4.13 CR 300 & CR 301
- 4.14 CR 302
- 4.15 CR 347 & CR 348
- 4.16 CR 368 & CR 369 (CR 101 to CR 366)
- 4.17 CR 404
- 4.18 CR 412
- 4.19 CR 466
- 4.20 FM 397 at SH 95 Signal
- 4.21 Gattis School Rd. ROW
- 4.22 Limmer Loop - Phase 1A
- 4.23 Thrall School Zone
- 4.24 US 79 - Section 1
- 4.25 US 79 - Section 2
- 4.26 US 79 - Section 3A
- 4.27 Chandler Rd. - Phase 2
- 4.28 Limmer Loop - Phase 1B
- 4.29 CR 113 / Old Settlers Blvd.
- 4.30 Limmer Loop - Phase 1C
- 4.31 Kenney Fort Boulevard - Phase 1
- 4.33 Chandler Rd. - Phase 3A
- 4.34 Chandler Rd. - Phase 3B
- 4.36 Gattis School Road
- 4.37 US 79 - Section 3 (PTF)
- 4.38 2nd Street Improvements
- 4.39 2nd Street Drainage Improvements
- 4.40 US 79 Section 5A (PTF)
- 4.41 US 79 Section 5B (PTF)
- 4.43 FM 1460 Section 2
- 4.44 CR 138
- 4.46 FM 1660 at Landfill Rd. (CR 128)
- 4.48 CR 119
- 4.49 CR 108
- 4.50 CR 351 at Donahoe Creek
- 4.51 CR 110 / Arterial A
- 4.52 University Blvd. (Chandler Rd.) Expansion
- 4.54 CR 110 South - (US 79 to Limmer Lp)
- 4.56 CR 110 at University Blvd. (Signal)
- 4.57 Gattis School Rd. at Winterfield Dr. (Signal)
- 4.58 Tradesman Park Crossing

Precinct 4 - Commissioner Boles

- 214 CR 119 (Limmer Loop to Chandler Road)
227 University Boulevard Widening (IH 35 to Sunrise Road)
238 Ronald Reagan Boulevard Extension Planning (IH 35 to SH 95)   
269 CR 101 (US 79 to North of Chandler Road)
261 CR 110 Middle (Limmer Loop to CR 107)
260 CR 110 South (US 79 to Limmer Loop)
296 CR 366 Widening (Chandler Road to Carlos G. Parker Boulevard)
297 East Williamson County Park Road / Bill Pickett Trail (Carlos Parker Boulevard to Chandler Road)
302a SH 130 Frontage Roads Phase 3 (Southbound Frontage Road US 79 to Limmer Loop)
302b SH 130 Traffic Study   
306a Relocation of 48" Williamson County Regional Raw Waterline - Line A
306b CR 305 at IH 35 Bridge Replacement
327 University Boulevard (Chandler Road) Expansion (FM 1460 to SH 130)
332 FM 3349/US 79 Interchange (US 79 to CR 404)   
506 Oak Bluff and Greenfield Drainage Improvements


2019 ROAD BOND PROGRAM PROJECTS

Precinct 4 - Commissioner Boles

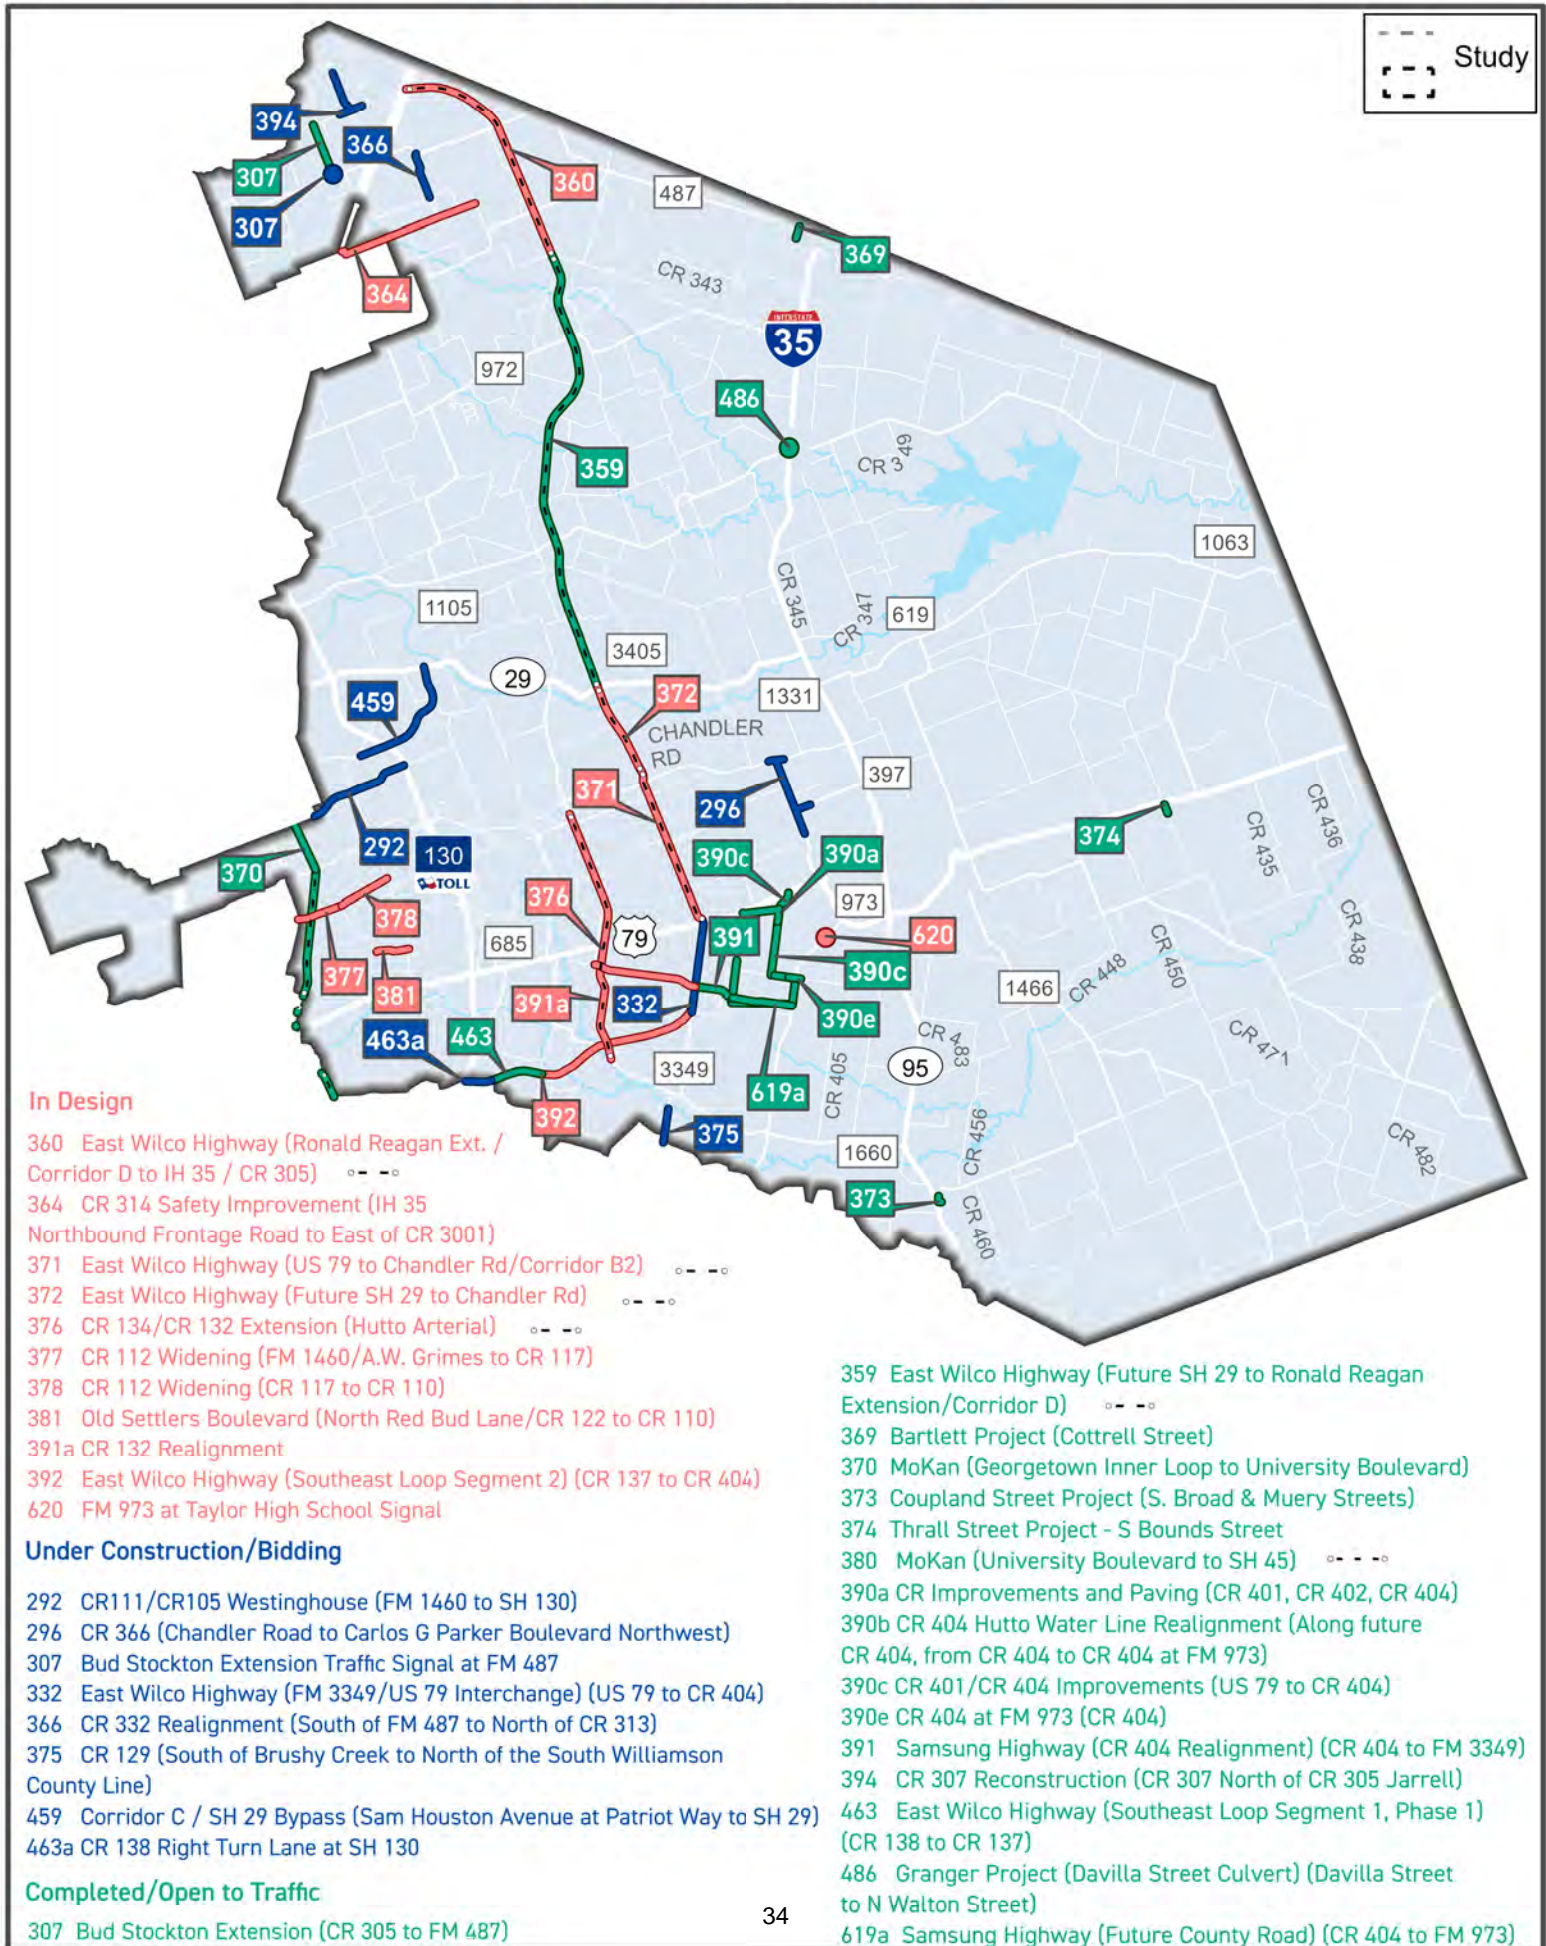

2023 ROAD BOND PROGRAM PROJECTS

Precinct 4 - Commissioner Boles

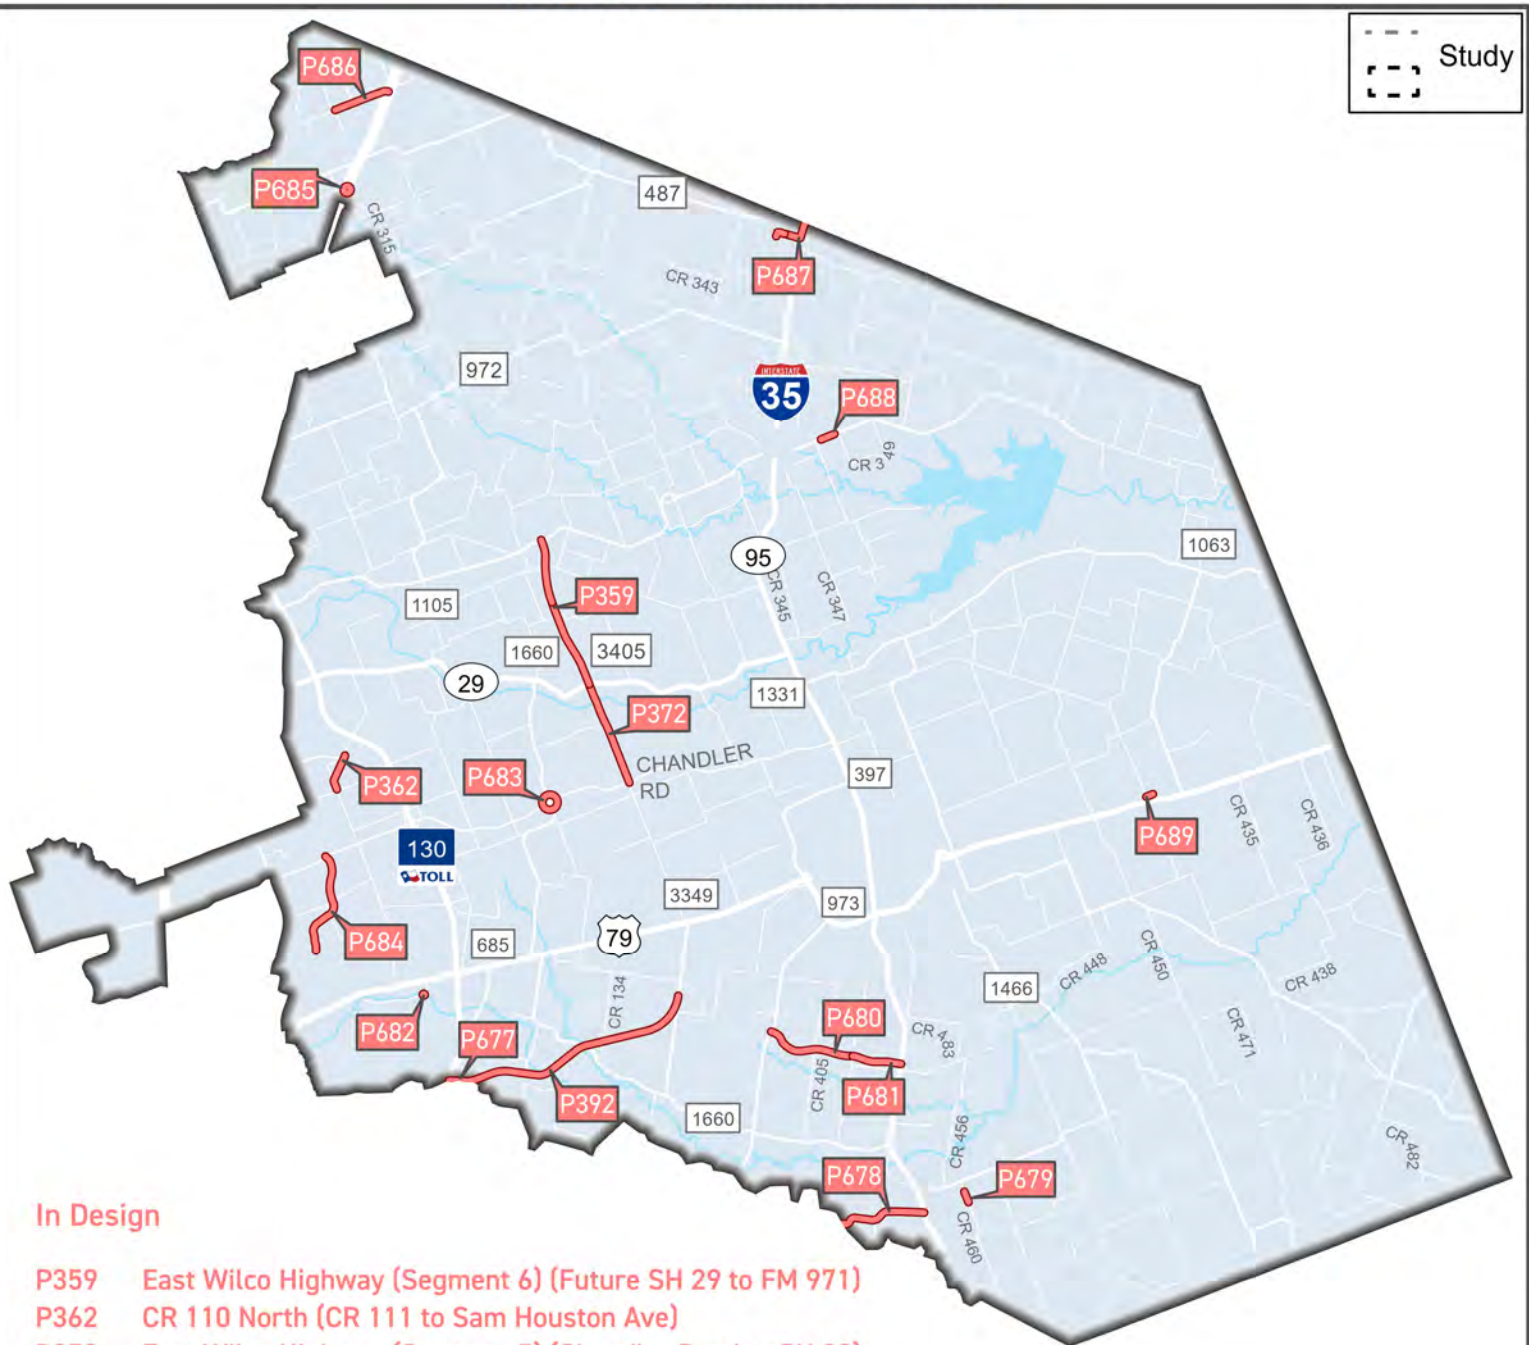

In Design

- P359 East Wilco Highway (Segment 6) (Future SH 29 to FM 971)
- P362 CR 110 North (CR 111 to Sam Houston Ave)
- P372 East Wilco Highway (Segment 5) (Chandler Road to SH 29)
- P392 East Wilco Highway (Southeast Loop - Segment 2)(Corridor E1) (Construction)(CR 137 south of Hutto and CR 404)
- P677 CR 138 (SH 130 NBFR to east of Derby Day Ave)
- P678 CR 458 (County Line to SH 95)
- P679 CR 460 (future Coupland High School Turn Lanes)
- P680 Corridor A2 (FM 973 to CR 406)
- P681 Corridor A2 (CR 406 to SH 95)
- P682 CR 123 (Brushy Creek)
- P683 Chandler Road (FM 1660 Overpass)
- P684 Kenney Fort Boulevard - Segments 5 & 6 (Old Settlers Boulevard to North of University Boulevard)
- P685 Sonterra Boulevard (IH-35 Frontage Road and Sonterra Blvd Intersection)
- P686 CR 305 (IH 35 to CR 307)
- P687 Salt Lake, Brook, Front Street (Salt Lake Street to Clark Street)
- P688 FM 971 (future Granger High School Turn Lanes)
- P689 North Barker Street (CR 424 to east end of North Barker Street)

Project Name: East Wilco Highway (Southeast Loop, Segment 1)
Project No. T3346

Original Contract Price = \$11,526,789.09

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>	
3/30/2021	4/27/2021	7/12/2021	7/19/2021	8/31/2023		534	24	558	
<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u> <u>Used</u>	<u>% Time</u> <u>Used</u>
1	7/19/2021	8/31/2021	44	\$767,411.06	\$767,411.06	\$85,267.90	\$85,267.90	7	8
2	9/1/2021	9/30/2021	30	\$328,739.28	\$1,096,150.34	\$36,526.58	\$121,794.48	10	13
3	10/1/2021	10/31/2021	31	\$221,811.16	\$1,317,961.50	\$24,645.69	\$146,440.17	12	19
4	11/1/2021	11/30/2021	30	\$278,008.69	\$1,595,970.19	\$30,889.85	\$177,330.02	15	24
5	12/1/2021	12/31/2021	31	\$331,070.23	\$1,927,040.42	\$36,785.58	\$214,115.60	18	30
6	1/1/2022	1/31/2022	31	\$624,535.89	\$2,551,576.31	\$69,392.88	\$283,508.48	23	35
7	2/1/2022	2/28/2022	28	\$352,666.85	\$2,904,243.16	\$39,185.20	\$322,693.68	27	40
8	3/1/2022	3/31/2022	31	\$815,310.79	\$3,719,553.95	\$90,590.09	\$413,283.77	34	46
9	4/1/2022	4/30/2022	30	\$741,856.71	\$4,461,410.66	\$82,428.53	\$495,712.30	41	51
10	5/1/2022	5/31/2022	31	\$625,433.98	\$5,086,844.64	\$69,492.66	\$565,204.96	46	57
11	6/1/2022	6/30/2022	30	\$498,845.27	\$5,585,689.91	\$55,427.25	\$620,632.21	51	62
12	7/1/2022	7/31/2022	31	\$521,580.90	\$6,107,270.81	\$57,953.44	\$678,585.65	56	68
13	8/1/2022	8/31/2022	31	\$672,002.44	\$6,779,273.25	\$74,666.93	\$753,252.58	62	73
14	9/1/2022	9/30/2022	30	\$936,075.41	\$7,715,348.66	\$104,008.38	\$857,260.96	70	79
15	10/1/2022	10/31/2022	31	\$851,880.44	\$8,567,229.10	-\$406,354.16	\$450,906.80	74	84
16	11/1/2022	11/30/2022	30	\$625,071.12	\$9,192,300.22	\$32,898.48	\$483,805.28	80	90
17	12/1/2022	12/31/2022	31	\$290,510.48	\$9,482,810.70	\$15,290.02	\$499,095.30	82	95
18	1/1/2023	1/31/2023	31	\$55,998.20	\$9,538,808.90	\$2,947.27	\$502,042.57	83	101
19	2/1/2023	2/28/2023	28	\$161,924.00	\$9,700,732.90	\$8,522.32	\$510,564.89	84	106
20	3/1/2023	3/31/2023	31	\$291,588.78	\$9,992,321.68	\$15,346.78	\$525,911.67	86	111
21	4/1/2023	4/30/2023	30	\$160,641.77	\$10,152,963.45	\$8,454.83	\$534,366.50	88	117
22	5/1/2023	5/31/2023	31	\$79,909.01	\$10,232,872.46	\$4,205.73	\$538,572.23	98	122
23	6/1/2023	6/30/2023	30	\$355,060.22	\$10,587,932.68	\$18,687.38	\$557,259.61	92	128
24	7/1/2023	7/31/2023	31	\$61,540.97	\$10,649,473.65	\$3,239.00	\$560,498.61	92	133
25	8/1/2023	8/31/2023	31	\$316,670.90	\$10,966,144.55	\$16,666.89	\$577,165.50	95	139
26	9/1/2023	9/30/2023	0	\$84,593.72	\$11,050,738.27	\$4,452.30	\$581,617.80	96	139
27	10/1/2023	10/31/2023	0	\$8,808.52	\$11,059,546.79	\$463.61	\$582,081.41	96	139

3/31/2024 Comments - Project closeout continues.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
01	8/3/2021	\$ 148,710.35	\$ 148,710.35

6B. This Change Order adds the installation of barbed wire fence and gates along the north and south sides of the right of way on the Wolfe property. The Contractor will not be able to start work until the fence is installed. Twenty four (24) days are being added to the contract to compensate the contractor for this impact.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
02	10/4/2022	\$73,007.39	\$221,717.74

2C. Differing site conditions (Unforeseeable). New development (conditions changing after PS&E completed): This Change Order documents various changes to the contract related to new developer and Church driveways on the west end of the project. 3F. County Convenience. Additional work desired by the County: In addition to the driveways, the bridge rail was changed along the bridge to a more appealing look. 1B. Design Error or Omission. Other: Additional excavation was needed in Pond 21 to create more volume and line EA had to be adjusted for optimum flow along Wall 4.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
03	2/28/2023	\$177,807.62	\$399,525.36

1A. Incorrect PS&E. This Change Order replaces the SGT and MBGF with Crash Cushion Attenuators on the proposed eastbound lane at both bridges due to them not being able to be installed per plan because of the post locations being in the MSE rock backfill. 2E. Miscellaneous difference in site conditions (unforeseeable)(Item 9). This Change Order also compensates the contractor for replacing a portion of an existing concrete driveway that needed to be removed to install the 48in RCP on Line B35.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
04	3/28/2023	\$156,231.96	\$555,757.32

2. Differing Site Conditions (Unforeseeable) 2E: Miscellaneous difference in site conditions (unforeseeable)(Item 9): This Change Order is adding items to the Contract that have been previously paid for under the existing Force Account line item.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
05	7/20/2023	\$1,093,581.24	\$1,649,338.56

1. Design Error or Omission. 1A: Incorrect PS&E. This Change Order addresses quantity revisions with the earthwork, roadway and various other bid items. The original quantities were incorrect in the Bid documents. The Engineer of Record re-calculated the quantities and provided revised numbers.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
06	9/27/2023	-\$1,015,961.92	\$633,376.64

3M. County Convenience. Other. Due to the existing utility conflicts impeding the remaining construction, this Change Order will remove all remaining work from Phases 2-4 from the project.

Adjusted Price = \$12,160,165.73

Project Name: CR 401 Reconstruction Project
Project No. 22IFB57

Original Contract Price = \$12,673,200.94

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>	
3/11/2022	3/22/2022	4/21/2022	5/2/2022	7/7/2023		505	-70	435	
<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u> <u>Used</u>	<u>% Time</u> <u>Used</u>
1	4/14/2022	4/21/2022	0	\$541,350.00	\$541,350.00	\$60,150.00	\$60,150.00	5	0
2	4/22/2022	5/31/2022	30	\$213,264.25	\$754,614.25	\$23,696.03	\$83,846.03	6	7
3	6/1/2022	7/1/2022	31	\$1,394,793.70	\$2,149,407.95	\$154,977.08	\$238,823.11	17	14
4	7/2/2022	7/31/2022	30	\$690,418.59	\$2,839,826.54	\$76,713.17	\$315,536.28	22	21
5	8/1/2022	8/31/2022	31	\$276,688.62	\$3,116,515.16	\$30,743.18	\$346,279.46	25	28
6	9/1/2022	9/30/2022	30	\$784,682.38	\$3,901,197.54	\$87,186.93	\$433,466.39	31	35
7	10/1/2022	10/31/2022	31	\$776,738.57	\$4,677,936.11	\$86,304.29	\$519,770.68	37	42
8	11/1/2022	11/30/2022	30	\$875,684.24	\$5,553,620.35	\$97,298.25	\$617,068.93	44	49
9	12/1/2022	12/31/2022	31	\$422,000.74	\$5,975,621.09	\$46,888.97	\$663,957.90	47	56
10	1/1/2023	1/31/2023	31	\$616,120.11	\$6,591,741.20	\$68,457.79	\$732,415.69	52	63
11	2/1/2023	2/28/2023	28	\$598,319.58	\$7,190,060.78	\$66,479.95	\$798,895.64	57	70
12	3/1/2023	3/31/2023	31	\$603,951.86	\$7,794,012.64	\$67,105.76	\$866,001.40	62	77
13	4/1/2023	4/30/2023	30	\$945,657.20	\$8,739,669.84	-\$406,018.78	\$459,982.62	66	84
14	5/1/2023	5/31/2023	31	\$1,082,327.54	\$9,821,997.38	\$56,964.61	\$516,947.23	74	91
15	6/1/2023	6/30/2023	30	\$1,195,677.91	\$11,017,675.29	\$62,930.42	\$579,877.65	83	98
16	7/1/2023	7/31/2023	7	\$760,493.51	\$11,778,168.80	\$40,025.97	\$619,903.62	88	99
17	8/1/2023	8/31/2023	0	\$16,945.32	\$11,795,114.12	\$891.86	\$620,795.48	88	99
18	9/1/2023	9/30/2023	0	\$543,436.59	\$12,338,550.71	-\$368,988.32	\$251,807.16	90	99
19	10/1/2023	10/31/2023	0	\$156,673.75	\$12,495,224.46	\$3,197.42	\$255,004.58	91	99
20	11/1/2023	11/30/2023	0	\$335,156.29	\$12,830,380.75	\$6,839.93	\$261,844.51	93	99
21	12/1/2023	12/31/2023	0	\$309,329.80	\$13,139,710.55	\$6,312.85	\$268,157.36	95	99
22	1/1/2024	1/31/2024	0	\$53,097.83	\$13,192,808.38	\$1,083.63	\$269,240.99	96	99
23	2/1/2024	2/29/2024	0	\$38,782.60	\$13,231,590.98	\$791.48	\$270,032.47	96	99

3/31/2024 Comments - Project close out in progress.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
01	9/15/2022	\$ 13,315.52	\$ 13,315.52

3G. County Convenience. Compliance requirements of new laws and/or policies. Revised the pavement section within the US 79 TxDOT ROW to meet their requirements and revised some signal phasing/timing at the proposed intersection of US 79 and CR 401.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
02	9/20/2022	\$ 414,400.00	\$ 427,715.52

4B. Third Party Accommodation. Third party requested work. This Change Order reduces the Contract Time by 70 days, from 505 Calendar days to 435 Calendar Days with a maximum incentive cap. This acceleration in the Contract Time is necessary, in order to meet the County's project delivery deadline of 7/31/2023.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
03	10/5/2022	\$ 214,351.37	\$ 642,066.89

3F. County Convenience. Additional work desired by the County. This Change Order changes the City of Taylor water line pipe material from ductile iron to PVC. This is necessary, due to the availability of materials.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
04	2/28/2023	\$ 188,826.95	\$ 830,893.84

2G. Differing in site conditions. Unadjusted Utility (Unforeseeable) This Change Order adds new items to the Contract to adjust the existing 16in City of Taylor water line on the north side of US 79 which is in conflict with the proposed pavement and ditch cuts. 4B. Third Party Requested Work. An additional 6in line and fire hydrant assembly are being added at the request of the City of Taylor.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
05	8/22/2023	\$ -	\$ 830,893.84

2. Differing Site Conditions. 2E. Miscellaneous difference in site conditions (unforeseeable)(Item 9) This Change Order compensates the Contractor for additional work to the Jonah water line that had to be rerouted due to a conflict with the bore pit for the City of Taylor water line. A Force Account line item has been created to cover the cost of the repair to the Jonah water line.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
06	12/19/2023	\$399,968.56	\$ 1,230,862.40

2E. Miscellaneous difference in site conditions (unforeseeable). Due to changing conditions in the field, certain items required quantity adjustments. 2I. Additional safety needs (unforeseeable). Additional small signs were added for safety concerns near the railroad crossing. This Change Order also adds items for crash cushion repairs needed due to the damage that occurred during construction.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
07	1/30/2024	\$137,831.49	\$ 1,368,693.89

2E. Miscellaneous difference in site conditions (unforeseeable)(Item 9). This Change Order adjusts quantities in the Contract due to unforeseen conditions that were identified in the field. This Change Order also adds additional items to the Contract for work being performed in and around the UPRR ROW per requirements.

Adjusted Price = \$14,041,894.83

Project Name: Samsung Highway (Future County Road) (CR 404 to FM 973)

Project No. 22IFB126

Original Contract Price = \$11,289,929.00

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>		<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
7/12/2022	7/19/2022	8/5/2022	8/15/2022	9/5/2023			413		413
<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u> <u>Used</u>	<u>% Time</u> <u>Used</u>
1	8/15/2022	9/27/2022	44	\$415,099.80	\$415,099.80	\$46,122.20	\$46,122.20	4	11
2	9/28/2022	10/31/2022	34	\$1,256,916.42	\$1,672,016.22	\$139,657.38	\$185,779.58	16	19
3	11/1/2022	11/30/2022	30	\$529,743.42	\$2,201,759.64	\$58,860.38	\$244,639.96	21	26
4	12/1/2022	12/31/2022	31	\$196,710.30	\$2,398,469.94	\$21,856.70	\$266,496.66	23	34
5	1/1/2023	1/31/2023	31	\$942,884.78	\$3,341,354.72	\$104,764.98	\$371,261.64	33	41
6	2/1/2023	2/28/2023	28	\$895,707.90	\$4,237,062.62	\$99,523.10	\$470,784.74	41	48
7	3/1/2023	3/31/2023	31	\$2,066,773.05	\$6,303,835.67	\$229,641.45	\$700,426.19	61	55
8	4/1/2023	4/30/2023	30	\$1,637,718.64	\$7,941,554.31	-\$282,449.65	\$417,976.54	73	63
9	5/1/2023	5/31/2023	31	\$1,177,188.70	\$9,118,743.01	\$61,957.30	\$479,933.84	84	70
10	6/1/2023	7/31/2023	61	\$1,026,783.27	\$10,145,526.28	\$54,041.23	\$533,975.07	94	85
11	8/1/2023	8/31/2023	31	\$78,532.37	\$10,224,058.65	\$4,133.28	\$538,108.35	94	92
12	9/1/2023	9/30/2023	5	\$339,420.15	\$10,563,478.80	-\$322,527.15	\$215,581.20	94	94

3/31/2024 Comments - Project closeout continues.


<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
01	1/24/2023	41,260.00	\$ 41,260.00

1B. Design Error or Omission. Other: This Change Order adds two items to the Contract for installing a 4' x 2' box culvert (EE) and related wingwalls/headwalls. The work was shown in the plans but not included in the bid tab. This Change Order also removes SET (TY 1) (S=5ft)(HW=3FT) (6:1) (C) item. The work was removed from the plans but the item was left in the bid tab. These plan revisions were made prior to bidding due to outstanding items on the TxDOT permit for the work at the FM 973 tie-in.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
02	7/18/2023	83,559.50	\$ 124,819.50

2E. Miscellaneous difference in site conditions (unforeseeable)(Item 9). This Change Order adds quantities to existing items due to unexpected changes in field conditions, causing overruns on the project. The excavation and embankment quantities had to be adjusted, due to the existing elevations at the west tie-in. The 18-inch and 36-inch drill shafts needed to be extended to ensure the shafts had proper embedment into stable material.


Adjusted Price = \$11,414,748.50



**East Wilco Highway (FM 3349 at US 79)
(FM 3349 from US 79 to CR 404 and new interchange on US 79 at FM 3349 and CR 101)**

**Project Length: 4.108 Miles
Roadway Classification: Rural Major Collector**

**Project Schedule: October 2022 - Summer 2025 (Roadwork)
Estimated Construction Cost: \$83.8 Million**

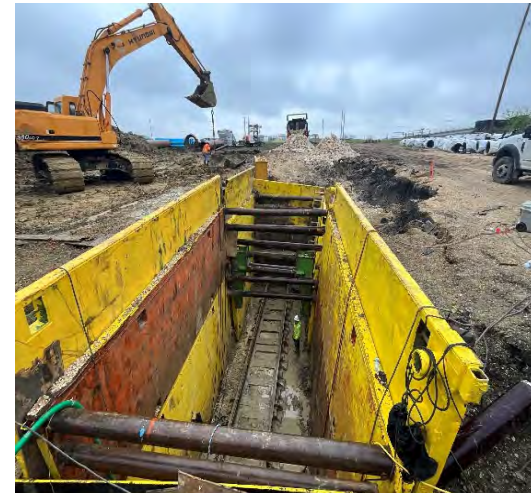

MARCH 2024 IN REVIEW

3/1/2024: James Construction Group (JCG) continued to excavate along the southbound frontage road, north and south of US 79.

3/8/2024: JCG continued prep work for beam installation on the southbound frontage road bridge and continued building up the MSE walls for the southbound frontage road and the northbound frontage road bridges.

3/15/2024: JCG continued swale excavation along the southbound frontage road, north and south of US 79. JCG continued the 6-inch rock riprap installation at both north and southbound frontage road bridges.

3/22/2024: JCG completed beam installation and began beam surveys and foam fills on the southbound frontage road bridge.

3/29/24: JCG continued building up the MSE walls and continued excavation and installation of 6-inch rock riprap at both the northbound frontage road and southbound frontage road bridges. Subcontractor began pushing 24-inch water line pipe through bore under US 79.



**Design Engineer: HDR
Contractor: James Construction
Construction Observation:
Asif Mirzazada, HNTB**

**Williamson County
Road Bond Program**

Project Name: East Wilco Highway (FM 3349 at US 79)
Project No. 22IFB139

Original Contract Price = \$81,941,038.13

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>	
8/24/2022	9/26/2022	10/6/2022	10/17/2022			1394		1394	
<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time Used</u>
1	10/18/2022	11/25/2022	39	\$755,690.77	\$755,690.77	\$0.00	\$0.00	1	2
2	11/26/2022	12/25/2022	30	\$5,128,955.59	\$5,884,646.36	\$0.00	\$0.00	7	0
3	12/26/2022	1/25/2023	31	\$1,448,580.10	\$7,333,226.46	\$0.00	\$0.00	9	7
4	1/26/2023	2/25/2023	31	\$1,272,882.90	\$8,606,109.36	\$0.00	\$0.00	10	9
5	2/26/2023	3/25/2023	28	\$2,922,159.15	\$11,528,268.51	\$0.00	\$0.00	14	11
6	3/26/2023	4/25/2023	31	\$1,453,458.85	\$12,981,727.36	\$0.00	\$0.00	15	14
7	4/26/2023	5/25/2023	30	\$1,672,497.88	\$14,654,225.24	\$0.00	\$0.00	17	16
8	5/26/2023	6/25/2023	31	\$3,188,150.58	\$17,842,375.82	\$0.00	\$0.00	21	18
9	6/26/2023	7/25/2023	30	\$2,251,767.13	\$20,094,142.95	\$0.00	\$0.00	24	20
10	7/26/2023	8/25/2023	31	\$2,453,925.93	\$22,548,068.88	\$0.00	\$0.00	27	22
11	8/26/2023	9/30/2023	36	\$4,580,138.95	\$27,128,207.83	\$0.00	\$0.00	32	25
12	10/1/2023	10/25/2023	25	\$3,017,528.73	\$30,145,736.56	\$0.00	\$0.00	36	27
13	10/26/2023	11/25/2023	31	\$2,172,558.80	\$32,318,295.36	\$0.00	\$0.00	39	29
14	11/26/2023	12/25/2023	30	\$1,638,115.30	\$33,956,410.66	\$0.00	\$0.00	41	31
15	12/26/2023	1/25/2024	31	\$4,633,009.82	\$38,589,420.48	\$0.00	\$0.00	46	33
16	1/26/2024	2/25/2024	31	\$4,487,381.38	\$43,076,801.86	\$0.00	\$0.00	51	36
17	2/26/2024	3/25/2024	29	\$3,973,465.64	\$47,050,267.50	\$0.00	\$0.00	56	38

3/31/2024 Comments - JCG completed beam setting on northbound frontage road and southbound frontage road bridges north of US 79 and started installing pre-cast deck panels on the southbound frontage road bridge. They continued roadway excavation and lime treatment for southbound frontage road south of US 79 and placing concrete for Box Culvert wingwall at several locations. Subcontractor Patin continued installing the Jonah water line and sleeves for future water and wastewater services.

Change Order Number 01 Approved 4/25/2023 Cost This CO 925,354.41 Total COs 925,354.41
3. County Convenience. 3L Revising safety work/measures desired by the County: This Change Order provides funds to compensate the contractor for installing safety improvements on US 79 until the permanent overpasses are built. By installing these traffic control measures the drivers traveling north bound on FM 3349 can no longer proceed straight or make a left turn at the US 79 intersection. The same will apply for traffic traveling south on CR 101. Drivers will need to make a right turn on US 79

Change Order Number 02 Approved 4/25/2023 Cost This CO 82,000.00 Total COs 1,007,354.41
3. County Convenience. 3L Revising safety work/measures desired by the County: The original bid item 36-inch Ductile Iron Pipe has long lead time of material procurement and is not readily available. Contractor proposed two options with shorter lead time to the City of Hutto as alternatives. City of Hutto has approved option 2, which is 36-inch PVC DR 18 pipe as an alternative with \$82,000 increase in cost to the current item and allows contractor to procure material quicker. The cost of this material change is 100% reimbursable by the City of Hutto.

Change Order Number 03 Approved 7/20/2023 Cost This CO 195,302.81 Total COs 1,202,657.22
3. County Convenience. 3F Additional work desired by the County: This Change Order compensates the contractor for installing one steel utility sleeve casing 24 inches in diameter on FM 3349 at station 421+00.

Change Order Number 04 Approved 8/8/2023 Cost This CO -472,492.20 Total COs 730,165.02
3. County Convenience. 4D Other "Deletion of work requested by the City of Hutto": This Change Order eliminates City of Hutto 16-inch water main line relocations project and 50 LF of 16-inch water line relocation under City of Hutto water line casing project from the original scope of work. The omission of work was requested by the City of Hutto. The cost for restocking of the ordered material and any other related fee is 100% reimbursable by the City of Hutto.

Change Order Number 05 Approved 0/14/23 Cost This CO -5,274.97 Total COs 724,890.05
5. Contractor Convenience. 5E Other: This Change Order is to revise the Stone Riprap material cost due to a material substitution request from the contractor. James Construction proposed material that has a specific gravity below the Contract requirements but has been accepted by TxDOT in other projects. The EOR approved the use of this material and recommended a reduction in price. This Change Order will result in a cost savings for the proposed material. This Change Order also adds new items to the Contract to pay the Contractor for additional work that was originally paid under the Force Account Line item.

Change Order Number 06 Approved 10/20/2023 Cost This CO 130,053.00 Total COs 854,943.05
3. County Convenience. 3F Additional work desired by the County: This Change Order compensates the contractor for upsizing 562 LF of 12-inch PVC pipe and fittings to 16-inch PVC pipe for the Jonah waterline project due to increased demand. The decision to upsize the pipe was at Jonah's request and will be 100% funded by the Jonah Water Special Utility District.

Change Order Number 07 Approved 10/20/2023 Cost This CO 661,031.30 Total COs 1,515,974.35

3F. Additional work desired by the County : This Change Order compensates the contractor for installing southbound frontage road right turn lane at FM 3349 for City of Hutto Mega Site. This work was requested by the City of Hutto and is 100% reimbursable by the City of Hutto.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
08	10/20/2023	327,321.48	1,843,295.83

1. Design Error or Omission. 1B. Other: This Change Order compensates the contractor for installation of 280 linear feet of 36-inch Ductile Iron (DI) pipe for City of Hutto water line project, instead of the previously specified 36-inch PVC pipe. This adjustment is required for the 48-inch bored steel casing under FM 3349 and the transition to a 56-inch casing for the open cut section. This modification was requested by and is 100% reimbursable by the City of Hutto.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
09	1/30/2024	-368,749.53	1,474,546.30

5. Contractor Convenience. 5A Contractor exercises option to change the traffic control plan: This Change Order revises the as-bid Traffic Control Plan (TCP) and construction phasing of the FM 3349 project. The modified TCP allows the Contractor to work on both, the North Bound and South Bound Frontage Roads simultaneously. The changes to the TCP and construction phasing do not impact the project's completion date and results in savings on several contract items.


<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
10	1/30/2024	67,965.30	1,542,511.60

4. Third Party Accommodation. 4B. Third party requested work: This Change Order compensates the Contractor for installing 390 LF of 4-inch steel casing with 1.5" HDPE water service line and fittings for the Jonah waterline project on FM 3349 at station 475+50. This work was requested by the Jonah Water Special Utility District and is 100% reimbursed by the Jonah Water Special Utility District.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
11	2/1/2024	271,902.72	1,814,414.32

3. County Convenience. 3F. Additional work desired by the County: This Change Order provides compensation to the Contractor for the installation of a 24-inch Steel Encasement Sleeve spanning 470 linear feet in the Jonah water line project on FM 3349 at station 426+51. The sleeve is part of the Williamson County real estate agreement excuted during the ROW acquisition.

Adjusted Price = \$83,755,452.45



CR 366 Reconstruction (Chandler Road to Carlos G. Parker Boulevard)

Project Length: 2.751 Miles
Roadway Classification: Rural Arterial

Project Schedule: January 2023 - Summer 2024
Estimated Construction Cost: \$17.7 Million



MARCH 2024 IN REVIEW

3/1/2024: James Construction Group continued processing flexible base along FM 397 and Chandler Road. JCG poured the deck for Bull Branch Bridge and removed Oncor poles and filled the holes with flow fill.

3/8/2024: JCG continued processing embankment along FM 397. JCG continued curing operations of the deck at Bull Branch Tributary Bridge.

3/15/2024: JCG finished curing operations of the deck at Bull Branch Tributary Bridge. Subcontractor Texas Materials applied prime coat, seal coat and paved asphalt along CR 366.

3/22/2024: JCG continued processing flexible base along CR 366 and continued processing embankment along FM 397. Subcontractor Patin began concrete paving.

3/29/24: Subcontractor formed and poured various driveways along CR 366. Subcontractor Texas Materials applied seal coat along CR 366 and continued paving along Chandler Road.



Design Engineer: Garver
Contractor: James Construction
Construction Observation:
Cristian Vasquez, HNTB

Williamson County
Road Bond Program

Project Name: CR 366 Reconstruction (Chandler Road to Carlos G. Parker Boulevard)

Project No. 22IFB138

Original Contract Price = \$17,694,262.46

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>	
8/31/2022	9/28/2022	12/27/2022	1/6/2023			515		515	
<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time</u>
1	1/6/2023	2/28/2023	54	\$1,184,919.53	\$1,184,919.53	\$131,657.73	\$131,657.73	7	10
2	3/1/2023	3/31/2023	31	\$220,649.15	\$1,405,568.68	\$24,516.57	\$156,174.30	9	17
3	4/1/2023	4/30/2023	30	\$195,624.79	\$1,601,193.47	\$21,736.09	\$177,910.39	10	22
4	5/1/2023	5/31/2023	31	\$540,591.96	\$2,141,785.43	\$60,065.77	\$237,976.16	13	28
5	6/1/2023	6/30/2023	30	\$1,603,804.24	\$3,745,589.67	\$178,200.47	\$416,176.63	23	34
6	7/1/2023	7/31/2023	31	\$781,944.84	\$4,527,534.51	\$86,882.76	\$503,059.39	28	40
7	8/1/2023	8/31/2023	31	\$1,589,668.07	\$6,117,202.58	\$176,629.79	\$679,689.18	38	46
8	9/1/2023	9/30/2023	30	\$933,910.69	\$7,051,113.27	\$103,767.85	\$783,457.03	44	52
9	10/1/2023	10/31/2023	31	\$448,939.28	\$7,500,052.55	\$49,882.14	\$833,339.17	47	58
10	11/1/2023	11/30/2023	30	\$314,298.57	\$7,814,351.12	\$34,922.07	\$868,261.24	49	64
11	12/1/2023	12/31/2023	31	\$413,086.23	\$8,227,437.35	\$45,898.47	\$914,159.71	45	64
12	1/1/2024	1/31/2024	31	\$452,008.26	\$8,679,445.61	\$50,223.14	\$964,382.85	54	76
13	2/1/2024	2/29/2024	29	\$653,498.36	\$9,332,943.97	\$72,610.92	\$1,036,993.77	75	76

3/31/2024 Comments - JCG continued placing flex base and HMA at Chandler Rd widening and Carlos G Parker Blvd widening. Subcontractor Patin started placing continuously reinforced concrete pavement at the intersection of CR 366 and FM 397. JCG continued doing bridge work and placing top soil and soil blankets at various locations.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
01	6/6/2023	\$ 11,562.50	\$ 11,562.50

1A. Design Error or Omission. Incorrect PS&E. : This change order adds the installation of the construction exits along CR 366 and FM 397 Carlos G Parker to access to the project site. The construction entrances or exits are to provide a stable pathway to keep the mud sediment off the public roads and improve safety.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
02	12/12/2023	\$ 82,015.80	\$ 93,578.30

2I: Additional safety needs (unforeseeable): This Change Orders provides funds to compensates the Contractor to implement a full closure of CR 366 until the completion of the project. The full closure is needed due to the severe rutting and pavement failures the road experienced after construction started. Williamson County and the City of Taylor agreed to close the road to through traffic and implement a detour route to improve the safety of the traveling public and facilitate the construction of the new road. 2E: Miscellaneous difference in site conditions (unforeseeable)(Item 9): This Change Order also creates new contract items for mowing and potholing to locate unmarked utilities within the project limits.

Adjusted Price = \$17,787,840.76

Project Name: Bud Stockton Extension (CR 305 to FM 487)

Project No. 23IFB13

Original Contract Price = \$5,917,275.00

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>	
12/12/2022	12/20/2022	1/3/2023	2/9/2023	8/14/2023		177	6	183	
<u>Invoice</u>	<u>Beginning</u>	<u>Ending</u>	<u>Days</u>	<u>Current</u>	<u>Invoiced</u>	<u>Current</u>	<u>Total</u>	<u>% (\$)</u>	<u>% Time</u>
<u>Number</u>	<u>Date</u>	<u>Date</u>	<u>Charged</u>	<u>Invoice</u>	<u>Total</u>	<u>Retainage</u>	<u>Retainage</u>	<u>Used</u>	<u>Used</u>
1	2/1/2023	2/28/2023	16	\$173,685.65	\$173,685.65	\$19,298.41	\$19,298.41	3	9
2	3/1/2023	3/31/2023	31	\$509,598.69	\$683,284.34	\$56,622.07	\$75,920.48	13	26
3	4/1/2023	4/30/2023	30	\$596,757.76	\$1,280,042.10	\$66,306.42	\$142,226.90	25	42
4	5/1/2023	5/31/2023	31	\$935,377.65	\$2,215,419.75	\$103,930.85	\$246,157.75	43	59
5	6/1/2023	6/30/2023	30	\$493,627.50	\$2,709,047.25	\$54,847.50	\$301,005.25	52	75
6	7/1/2023	7/31/2023	31	\$1,774,451.07	\$4,483,498.32	\$197,161.23	\$498,166.48	87	92
7	8/1/2023	8/31/2023	14	\$822,967.99	\$5,306,466.31	-\$218,878.78	\$279,287.70	92	100
8	9/1/2023	9/30/2023	0	\$220,970.36	\$5,527,436.67	-\$166,482.87	\$112,804.83	98	100
9	10/1/2023	10/31/2023	0	\$27,078.46	\$5,554,515.13	\$552.62	\$113,357.45	98	100
10	11/1/2023	3/1/2024	0	\$15,204.70	\$5,569,719.83	\$310.30	\$113,667.75	99	100

3/31/2024 Comments - Awaiting vegetation establishment.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
01	3/7/2023	\$ 35,830.59	\$ 35,830.59

6D. Untimely ROW/Utilities. Other.: As part of the ROW Agreement, Williamson County is responsible for installing the new fence along the ROW. The Agreement was finalized after the design, so the items were not included in the bid documents. Also, temporary fence must be installed around the existing pond while the pond is being backfilled.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
02	8/23/2023	\$ 97,110.00	\$ 132,940.59

2. Differing Site Conditions (unforeseeable) 2E: Miscellaneous difference in site conditions (unforeseeable)(Item 9). This Change Order compensates the Contractor for performing full-depth repairs to the existing Bud Stockton Loop pavement prior to the 1-inch overlay of hot mix asphalt.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
03	2/14/2024	-292,169.97	-159,229.38

2E. Miscellaneous difference in site conditions (unforeseeable) (Item 9). This Change Order provides the final balancing for the overruns/underruns of Contract quantities on the project that are a result of addressing field conditions not accounted for in the original plans. 2I. Additional safety needs (unforeseeable). Due to the new stop condion on FM 487, TxDot requested LED stop signs and rumble strips be installed to make a safer condition at the new all-way stop. 2J. Other: Installing a 6in sleeve for Jarrell ISD High School under their new driveway off of Bud Stockton.

Adjusted Price = \$5,758,045.62

Project Name: CR 404 at FM 973

Project No. 23IFB6

Original Contract Price = \$4,622,143.93

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>	
11/22/2022	12/6/2022	2/1/2023	2/10/2023	7/7/2023		150		150	
<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time Used</u>
1	2/10/2023	2/28/2023	19	\$358,668.36	\$358,668.36	\$39,852.04	\$39,852.04	8	13
2	3/1/123	3/31/2023	31	\$668,379.48	\$1,027,047.84	\$74,264.32	\$114,116.36	24	33
3	4/1/2023	4/30/2023	30	\$601,756.01	\$1,628,803.85	\$66,861.78	\$180,978.14	38	53
4	5/1/2023	5/31/2023	31	\$555,140.47	\$2,183,944.32	\$61,682.27	\$242,660.41	50	74
5	6/1/2023	6/30/2023	30	\$1,893,411.89	\$4,077,356.21	-\$28,062.78	\$214,597.63	89	94
6	7/1/2023	7/31/2023	7	\$383,976.61	\$4,461,332.82	\$20,209.29	\$234,806.92	98	99
7	8/1/2023	8/31/2023	0	\$48,047.09	\$4,509,379.91	\$2,528.79	\$237,335.71	99	99
8	9/1/2023	9/30/2023	0	\$150,388.70	\$4,659,768.61	-\$142,238.46	\$95,097.25	99	99
9	10/1/2023	10/31/2023	0	\$26,065.94	\$4,685,834.55	\$531.96	\$95,629.21	99	99
10	11/1/2023	2/23/2024	0	\$31,961.25	\$4,717,795.80	\$652.27	\$96,281.48	100	99

3/31/2024 Comments - The contractor is waiting for vegetation establishment.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
01	9/14/2023	294,199.97	294,199.97

2E. Miscellaneous difference in site conditions (unforeseeable)(Item 9). This Change Order compensates the contractor for multiple different adjustments made throughout the project. There were revisions made due to the Samsung site, signals, drainage, and some additional safety measures requested by Williamson County. 1B. Design Error or Omission. Other. This Change Order also corrects the incorrect asphalt quantities provided in the bid tabs.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
02	2/14/2024	-102,266.57	191,933.40

2E. Miscellaneous difference in site conditions (unforeseeable)(Item9). This Change Order provides the balancing for the overruns/underruns of Contract quantities on the project that are a result of addressing field conditions not accounted for in the original plans. 2I. Additional safety needs (unforeseeable). This change order also adds advanced flashing beacons and signs for additional safety measures.

Adjusted Price = \$4,814,077.33

Project Name: CR 307 and CR 305
Project No. 23IFB34

Original Contract Price = \$2,796,832.80

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
2/22/2023	3/7/2023	4/7/2023	4/17/2023			120	169	289

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time</u>
1	4/1/2023	4/30/2023	13	\$105,372.90	\$105,372.90	\$11,708.10	\$11,708.10	4	4
2	5/1/2023	5/31/2023	31	\$78,480.00	\$183,852.90	\$8,720.00	\$20,428.10	7	15
3	6/1/2023	6/30/2023	30	\$319,844.70	\$503,697.60	\$35,538.30	\$55,966.40	20	26
4	7/1/2023	7/31/2023	31	\$298,387.80	\$802,085.40	\$33,154.20	\$89,120.60	31	36
5	8/1/2023	8/31/2023	31	\$262,632.60	\$1,064,718.00	\$29,181.40	\$118,302.00	42	47
6	9/1/2023	9/30/2023	30	\$9,900.00	\$1,074,618.00	\$1,100.00	\$119,402.00	42	57
7	10/1/2023	10/31/2023	31	\$128,916.90	\$1,203,534.90	\$14,324.10	\$133,726.10	47	68
8	11/1/2023	11/30/2023	30	\$554,425.38	\$1,757,960.28	-\$41,201.87	\$92,524.23	65	79
9	12/1/2023	12/31/2023	31	\$6,650.00	\$1,764,610.28	\$350.00	\$92,874.23	65	79
10	1/1/2024	1/31/2024	31	\$585,425.81	\$2,350,036.09	\$30,811.88	\$123,686.11	87	89
11	2/1/2024	2/29/2024	12	\$158,831.53	\$2,508,867.62	-\$72,484.73	\$51,201.38	90	100
12	3/1/2024	3/31/2024	0	\$31,267.10	\$2,540,134.72	\$638.10	\$51,839.48	91	100

3/31/2024 Comments - Awaiting vegetation establishment.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
01	11/2/2023	\$ 10,447.50	\$ 10,447.50

2. Differing Site Conditions (unforeseeable) 2I. Additional safety needs (unforeseeable): This Change Order adds work zone pavement markings to the CR307 portion of the project. With the added amount of traffic on CR 307 due to the new school opening, the temporary pavement markings were added as an additional safety measure for the traveling public.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
02	2/14/2024	\$ 35,000.00	\$ 45,447.50

6C. Utilities not clear. This Change Order adds days to the contract time and increases the Barricades, signs, and traffic handling item due to the utility conflicts not being cleared by the dates stated in the Project Construction Manual.

Adjusted Price = \$2,842,280.30


Project Name: Samsung Highway (CR 404 Realignment) (FM 3349 to CR 404)
Project No. 23IFB33

Original Contract Price = \$5,139,487.45

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>		<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
2/15/2023	2/28/2023	4/12/2023	4/24/2023	10/2/2023			312		312
<u>Invoice</u>	<u>Beginning</u>	<u>Ending</u>	<u>Days</u>	<u>Current</u>	<u>Invoiced</u>	<u>Current</u>	<u>Total</u>	<u>% (\$)</u>	<u>% Time</u>
<u>Number</u>	<u>Date</u>	<u>Date</u>	<u>Charged</u>	<u>Invoice</u>	<u>Total</u>	<u>Retainage</u>	<u>Retainage</u>	<u>Used</u>	<u>Used</u>
1	4/24/2023	5/31/2023	38	\$427,494.19	\$427,494.19	\$47,499.35	\$47,499.35	9	12
2	6/1/2023	6/30/2023	30	\$521,200.45	\$948,694.64	\$57,911.17	\$105,410.52	21	22
3	7/1/2023	7/31/2023	31	\$1,021,845.73	\$1,970,540.37	\$113,538.41	\$218,948.93	43	32
4	8/1/2023	8/31/2023	31	\$950,205.70	\$2,920,746.07	-\$65,225.45	\$153,723.48	60	42
5	9/1/2023	9/30/2023	30	\$1,130,322.24	\$4,051,068.31	\$59,490.64	\$213,214.12	83	51
6	10/1/2023	10/31/2023	2	\$857,687.88	\$4,908,756.19	-\$113,035.42	\$100,178.70	97	52
7	11/1/2023	11/30/2023	0	\$83,329.71	\$4,992,085.90	\$1,700.60	\$101,879.30	99	52
8	12/1/2023	12/31/2023	0	\$6,676.54	\$4,998,762.44	\$136.26	\$102,015.56	99	52

3/31/2024 Comments - Close out process under way.


Adjusted Price = \$5,139,487.45

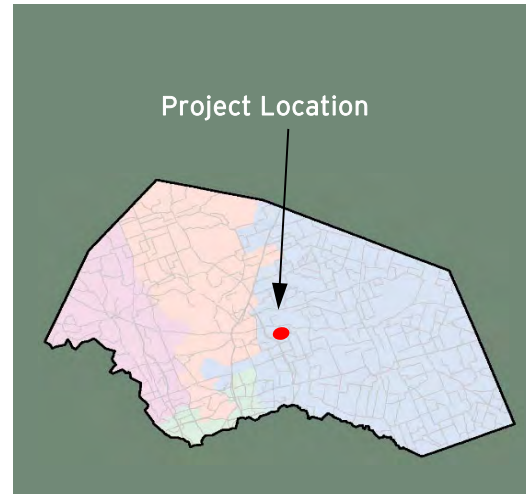

**Corridor C / SH 29 Bypass
(Sam Houston Avenue at Patriot Way to SH 29)**

**Project Length: 2.3 Miles
Roadway Classification: Suburban Arterial**

**Project Schedule: Fall 2023 - Summer 2026
Estimated Construction Cost: \$30.5 Million**

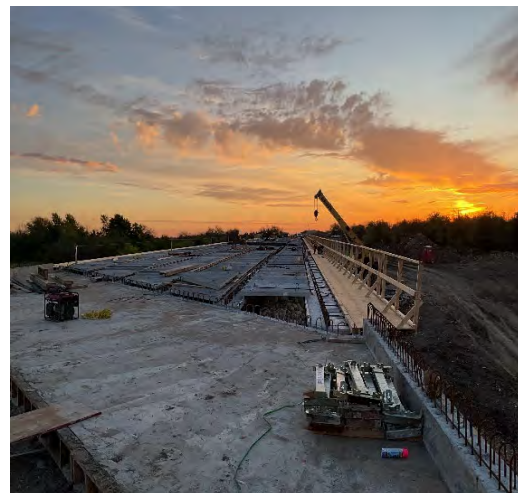

MARCH 2024 IN REVIEW

3/1/2024: Capital Excavation placed the rock riprap underneath the Mankins Branch West Bridge. Capital poured various columns and caps for the SH 130 Bridge and the Mankins Branch East Bridge.

3/8/2024: The subcontractor poured various columns and caps for the SH 130 Bridge and the Mankins Branch East Bridge. The contractor continued installing the new Jonah water line at CR 106 and SH 29.

3/15/2024: Capital Excavation placed all columns and caps at the east and west Mankins Bridges, all columns up to Bent 14 and caps up to Bent 10 of the SH 130 Bridge.

3/22/2024: The subcontractor completed placing the overhang brackets and began installing and tying deck rebar on the West Mankins Branch Bridge.

3/29/2024: Capital Excavation continued processing embankment throughout the project and lime-treated the subgrade from SH 29 to the east Mankins Bridge. Subcontractor formed and poured headwalls and wingwalls at culvert on the west end of the project.



**Design Engineer: Atkins
Contractor: Capital Excavation
Construction Observation:
Noe Cruz, HNTB**

**Williamson County
Road Bond Program**


Corridor C / SH 29 Bypass
Project No. 23IFB67

Original Contract Price = \$30,540,848.03

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>	
8/15/2023	8/22/2023	9/20/2023	9/30/2023			973		973	
<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time Used</u>
1	9/30/2023	9/30/2023	1	\$1,397,211.48	\$1,397,211.48	\$155,245.72	\$155,245.72	5	0
2	10/1/2023	10/31/2023	31	\$1,541,032.92	\$2,938,244.40	\$171,225.88	\$326,471.60	11	3
3	11/1/2023	11/30/2023	30	\$1,838,538.26	\$4,776,782.66	\$204,282.03	\$530,753.63	17	6
4	12/1/2023	12/31/2023	31	\$2,431,249.16	\$7,208,031.82	\$270,138.79	\$800,892.42	26	10
5	1/1/2024	1/31/2024	31	\$1,078,672.93	\$8,286,704.75	\$119,852.55	\$920,744.97	30	13
6	2/1/2024	2/29/2024	29	\$2,770,832.24	\$11,057,536.99	\$307,870.25	\$1,228,615.22	40	16

3/31/2024 Comments - Capital Excavation continued placing concrete at columns and bent caps for the SH 130 Bridge; they also continued installing reinforcing steel for the bridge deck at W Mankins Branch Bridge and finished setting beams at the E Mankins Branch Bridge. Capital continued roadway excavation and embankment east of SH 130 and continued installing the new Jonah water line at CR 106 and SH 29.

Adjusted Price = \$30,540,848.03

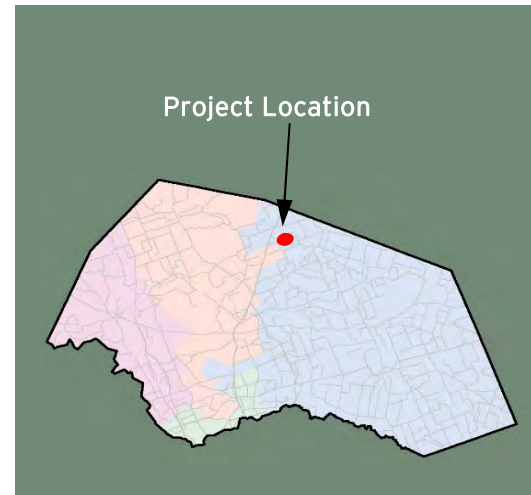

**CR 332 Realignment
(South of FM 487 to North of CR 313)**

**Project Length: 0.407 Miles
Roadway Classification: Minor Collector**

**Project Schedule: Early 2024 - Fall 2024
Estimated Construction Cost: \$2.5 Million**



MARCH 2024 IN REVIEW

3/1/24: Chasco Construction continued excavating and installing the Jarrell Schwertner water line and the Sonterra MUD water line. Chasco continued roadway and channel excavation in the proposed roadway.

3/8/24: Chasco Constructors completed installing water lines for the Lone Star Regional Water Authority, Jarrell Schwertner, and Sonterra MUD. Chasco continued to perform testing of all water lines.

3/15/24: Chasco Constructors completed the tie-in installations to existing water lines for Lone Star Regional Water Authority and Jarrell Schwertner. Chasco continued roadway excavation and embankment of the proposed roadway.

3/22/24: Chasco continued channel and roadway excavation and embankment of proposed roadway.

3/29/24: Chasco continued channel and roadway excavation and embankment of proposed roadway.




**Design Engineer: Seiler Lankes Group
Contractor: Chasco Constructors
Construction Observation:
Joseph Jones, HNTB**

**Williamson County
Road Bond Program**

**CR 332 Realignment
Project No. 24IFB14**

Original Contract Price = \$2,545,345.00

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>	
12/5/2023	12/12/2023	2/5/2024	2/15/2024			240		240	
<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u> <u>Used</u>	<u>% Time</u> <u>Used</u>
1	2/5/2024	2/29/2024	15	\$535,916.70	\$535,916.70	\$59,546.30	\$59,546.30	23	6
3/31/2024	Comments -	Chasco Constructors completed the installation of water lines for Sonterra, Jarrell-Schwertner and Lone Star RWA. They continued the channel and roadway excavation and embankment of the proposed roadway.							
							Adjusted Price =	\$2,545,345.00	



CR 138 Right Turn Lane at SH 130

Project Length: 0.640 Miles
Roadway Classification: Rural Arterial

Project Schedule: Early 2024 - Summer 2024
Estimated Construction Cost: \$1.7 Million



MARCH 2024 IN REVIEW

3/1/24: Smith Contracting completed excavating for the East Wilco Highway eastbound right turn lane and widening and began processing the select fill material in the same area. Smith began obliterating sections of CR 138.

3/8/24: Subcontractor completed placing the select fill material and began processing the first lift of flexible base for the CR 138 widening. Smith removed the old Star Driveway and completed forming the new driveway.

3/15/24: Smith Contracting continued processing flexible base along CR 138. Subcontractor poured the Star Driveway and all aprons for the drainage inlets.

3/22/24: Subcontractor continued obliterating CR 138 near the east end of the project and began excavating Pond B. Smith continued grading the right-ofway and cutting ditches throughout the project.

3/29/24: The contractor began forming the concrete ditch and sidewalk on the east end of the project.




Design Engineer: RTG
Contractor: Smith Contracting
Construction Observation:
 Garrett Sartin, HNTB

Williamson County
Road Bond Program

CR 138 Right Turn Lane at SH 130
Project No. 24IFB19

Original Contract Price = \$1,748,938.75

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>	
12/19/2023	1/9/2024	2/12/2024	2/22/2024			120		120	
<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time</u>
1	2/20/2024	2/29/2024	10	\$167,340.78	\$167,340.78	\$18,593.42	\$18,593.42	11	8
3/31/2024	Comments -	Smith Contracting placed Ty B HMA at the right turn lane widening and completed the removal and replacement of the Old Star concrete driveway. They continued excavation at the detention pond and began forming the concrete ditch and sidewalk on the east end of the project.							
						Adjusted Price =		\$1,748,938.75	



CR 129
(South of Brushy Creek to North of Williamson County Line)

Project Length: 0.468 Miles
Roadway Classification: Rural Highway

Project Schedule: Early 2024 - Fall 2024
Estimated Construction Cost: \$2.4 Million



MARCH 2024 IN REVIEW

3/1/24: Notice to proceed was given on 2/21/24 with work beginning on 3/4/24.

3/8/24: Chasco Constructors began clearing the right-of-way and removing old property line fences.

3/15/24: Chasco continued clearing the right-of-way and cutting down trees along the old property lines. Oncore began relocating their utility poles.

3/22/24: Chasco potholed utilities on the south end of the project. Subcontractor Woolery built the chain link fence on the east side of the rightof-way in the middle of the project. Oncor continued relocating their utility poles throughout the project.

3/29/24: Chasco continued potholing utilities throughout the project. Oncor continued relocating their utility poles throughout the project.



Design Engineer: Garver
Contractor: Chasco Constructors
Construction Observation:
Kyle McCoy, HNTB

Williamson County
Road Bond Program

County Road 129
Project No. 24IFB23

Original Contract Price = \$2,463,313.00

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
1/17/2024	1/30/2024	2/21/2024	3/4/2024			215		215

3/31/2024 Comments - Chasco Constructors are locating utilities throughout the project.

Adjusted Price = \$2,463,313.00
