


Williamson County Commissioners Court

Road Bond Program
October 15, 2024




Precinct 1



Projects under planning and
design, no active
construction projects.

Precinct 2

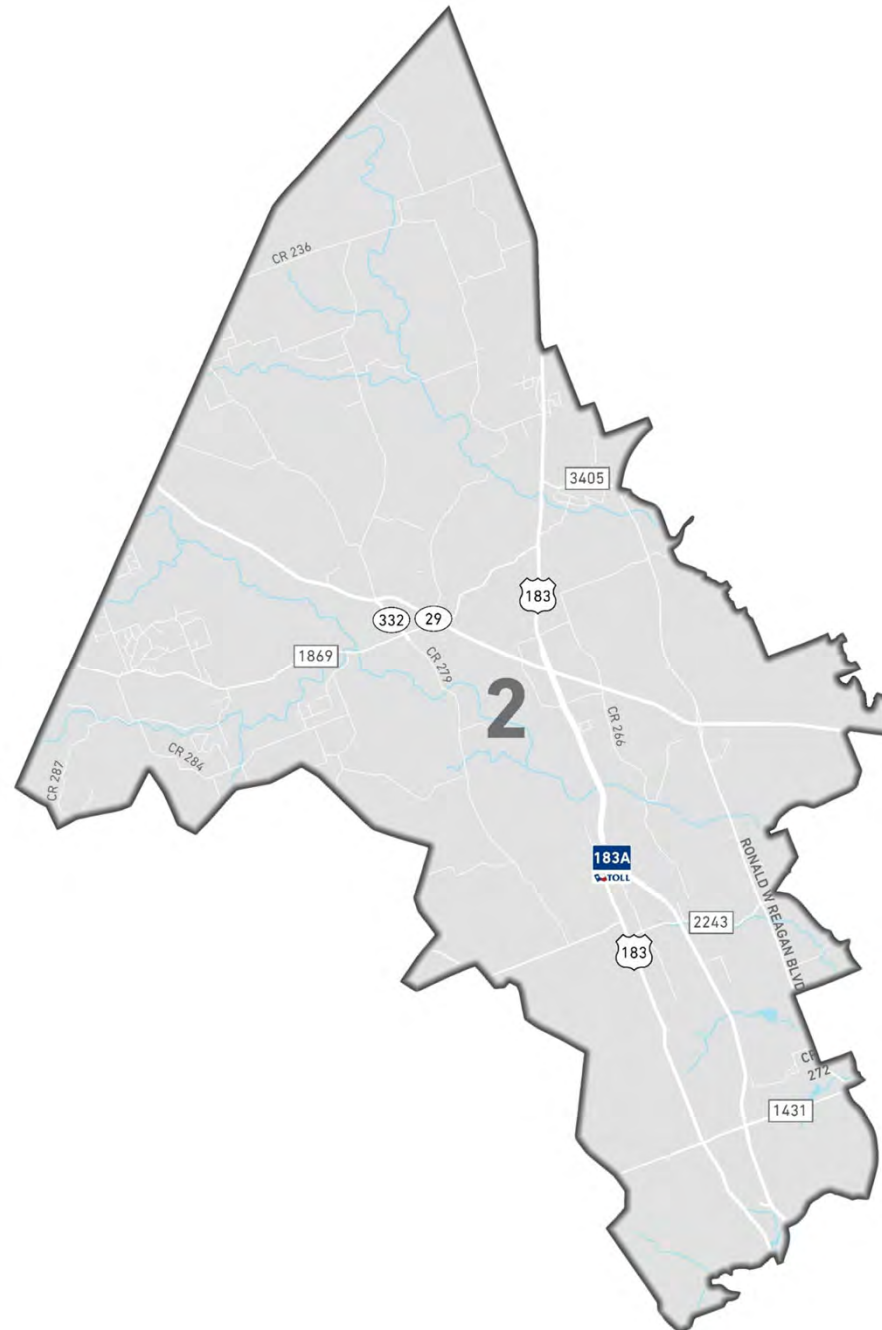

Liberty Hill (SH 29) Bypass (RM 1869 to CR 279)

Anticipated Completion
Late 2025



Original Contract Price = \$14,149,449.00

Total Change Orders to Date = \$280,462.00

Adjusted Contract Price = \$ 14,429,911.00

Expenditures to Date = \$6,672,645.75 (46%)

Liberty Hill (SH 29) Bypass (RM 1869 to CR 279)



Liberty Hill (SH 29) Bypass (RM 1869 to CR 279)




Liberty Hill (SH 29) Bypass (RM 1869 to CR 279)



Ronald Reagan Widening (SH 29 to FM 3405)

Anticipated Completion
Summer 2027

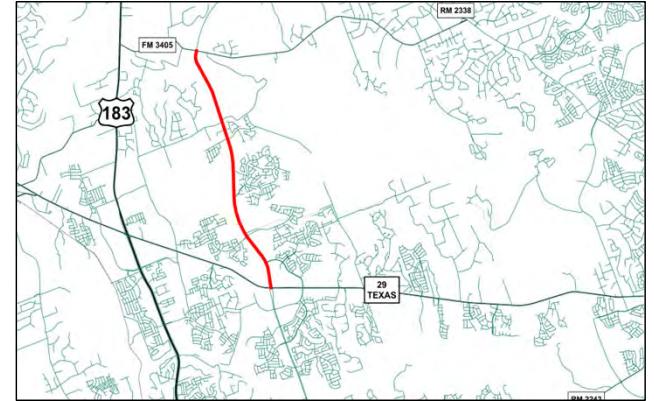

Original Contract Price = \$52,159,299.00

Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$52,159,299.00

Expenditures to Date = \$2,255,123.86 (4%)

Ronald Reagan Widening (SH 29 to FM 3405)




Ronald Reagan Widening (SH 29 to FM 3405)



Ronald Reagan Widening (SH 29 to FM 3405)




Precinct 3

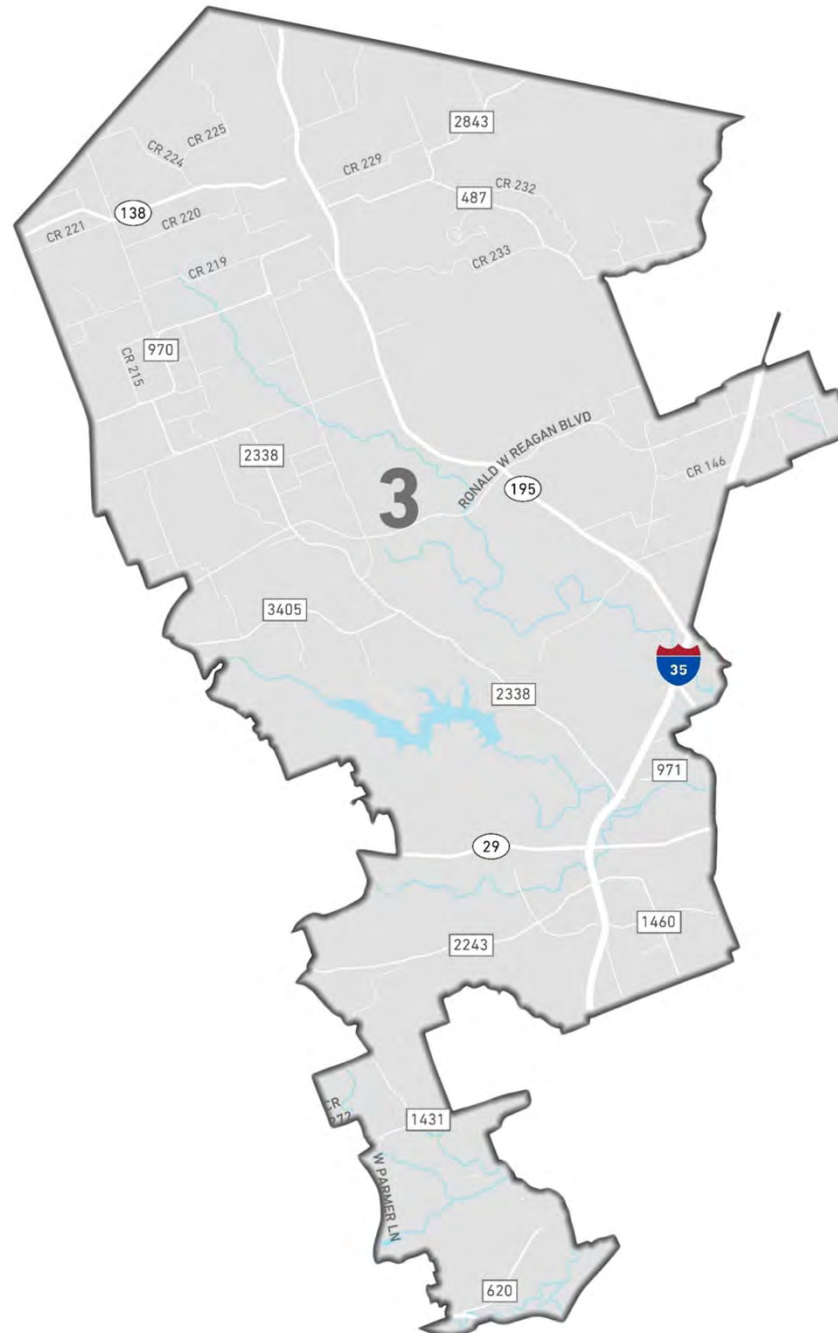

New Hope Drive Phase 2A (Ronald Reagan Boulevard to Sam Bass Road)

Anticipated Completion

Fall 2024

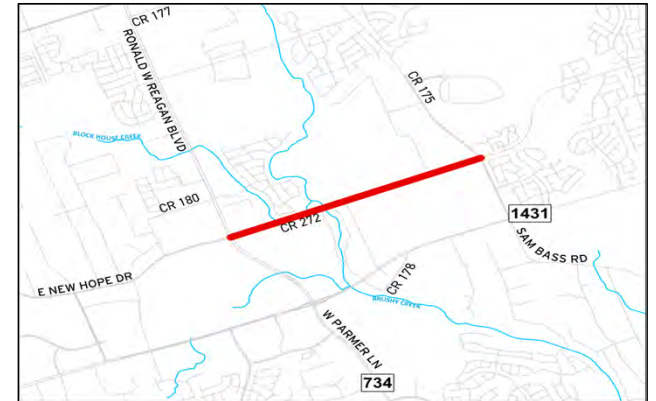

Partnership with the City of Cedar Park

Original Contract Amount = \$22,619,961.16

Construction is managed by the City of Cedar Park

New Hope Drive Phase 2A (Ronald Reagan Boulevard to Sam Bass Road)




New Hope Drive Phase 2A (Ronald Reagan Boulevard to Sam Bass Road)



Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)

Anticipated Completion
Fall 2025

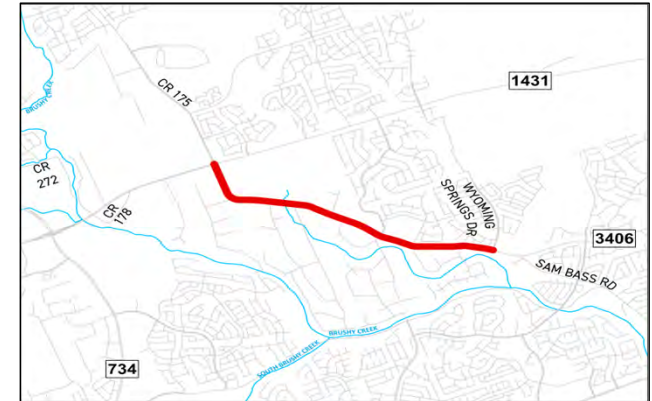

Original Contract Price = \$36,145,959.00

Total Change Orders to Date = -\$2,192,985.66

Adjusted Contract Price = \$33,952,973.34

Expenditures to Date = \$15,758,972.92 (46%)

Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)




Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)



Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)




Precinct 4

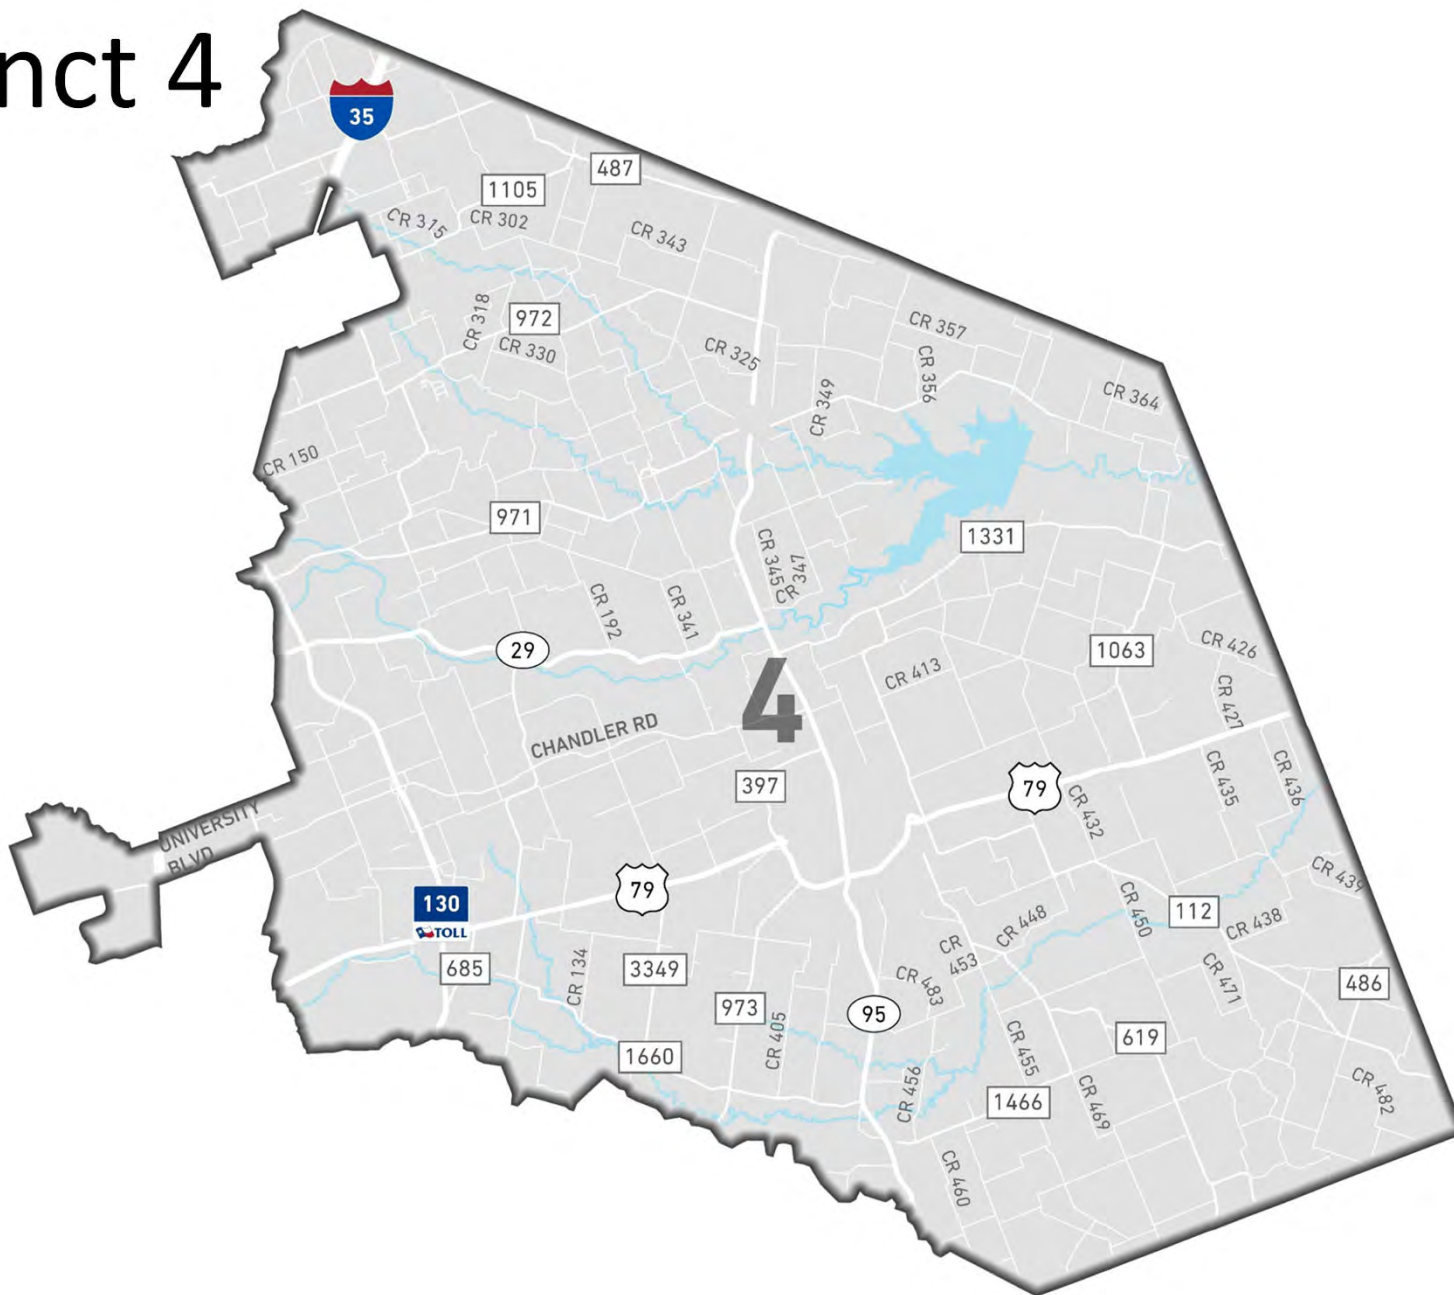

Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)

Anticipated Completion
Fall 2024

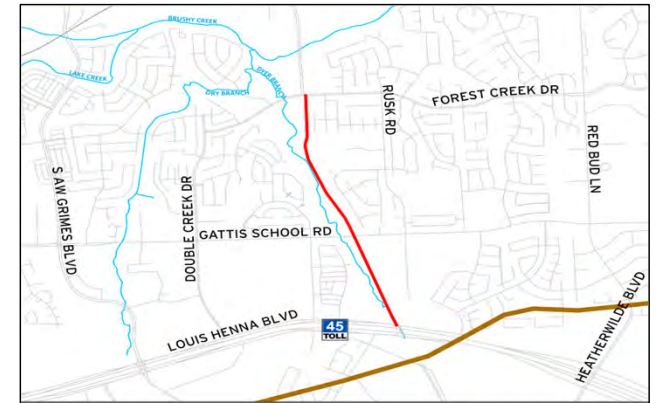

Partnership with the City of Round Rock

Original Contract Amount = \$23,409,120.97

Construction is managed by the City of Round Rock

Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)



Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)



Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)



East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)

Anticipated Completion
Summer 2025 (Roadwork)



Original Contract Amount = \$81,941,038.13

Total Change Orders = \$2,162,933.94

Adjusted Contract Price = \$84,103,972.07

Expenditures to Date = \$56,111,758.61 (67%)

East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)



East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)




East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)



East Wilco Highway - Segment 2 (CR 137 South of Hutto and CR 404)

Anticipated Completion
Summer 2028

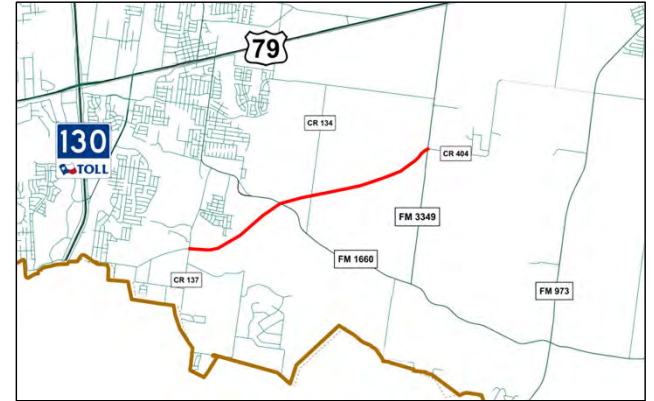

Original Contract Amount = \$64,407,606.63

Total Change Orders = \$0.00

Adjusted Contract Price = \$ 64,407,606.63

Expenditures to Date = \$0.00 (0%)

East Wilco Highway – Segment 2 (CR 137 South of Hutto and CR 404)



East Wilco Highway – Segment 2 (CR 137 South of Hutto and CR 404)



CR 366 Reconstruction (Chandler Road to Carlos G. Parker Boulevard)

Substantially Complete
August 2024



Original Contract Amount = \$17,694,262.46

Total Change Orders = \$232,406.95

Adjusted Contract Price = \$17,926,669.41

Expenditures to Date = \$17,098,518.51 (95%)

CR 366 Reconstruction (Chandler Road to Carlos G. Parker Boulevard)



CR 366 Reconstruction (Chandler Road to Carlos G. Parker Boulevard)



Corridor C / SH 29 Bypass (Sam Houston Avenue at Patriot Way to SH 29)

Anticipated Completion
Summer 2026



Original Contract Amount = \$30,540,848.03

Total Change Orders = \$15,769.50

Adjusted Contract Price = \$30,556,617.53

Expenditures to Date = \$24,471,100.18 (80%)

Corridor C / SH 29 Bypass (Sam Houston Avenue at Patriot Way to SH 29)



Corridor C / SH 29 Bypass (Sam Houston Avenue at Patriot Way to SH 29)




Corridor C / SH 29 Bypass (Sam Houston Avenue at Patriot Way to SH 29)



CR 129

(South of Brushy Creek to North of South County Line)

Substantially Complete
September 2024

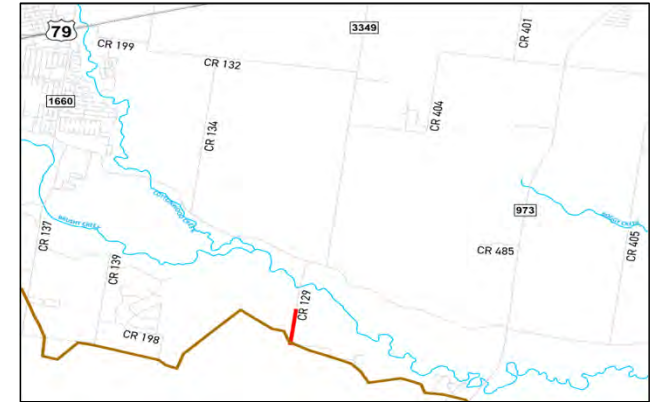

Original Contract Amount = \$2,463,313.00

Total Change Orders = \$0.00

Adjusted Contract Price = \$ 2,463,313.00

Expenditures to Date = \$1,823,400.31 (74%)

CR 129

(South of Brushy Creek to North of South County Line)



CR 129

(South of Brushy Creek to North of South County Line)



CR 129


(South of Brushy Creek to North of South County Line)



Bud Stockton Extension (Traffic Signal at FM 487)

Anticipated Completion

Fall 2024

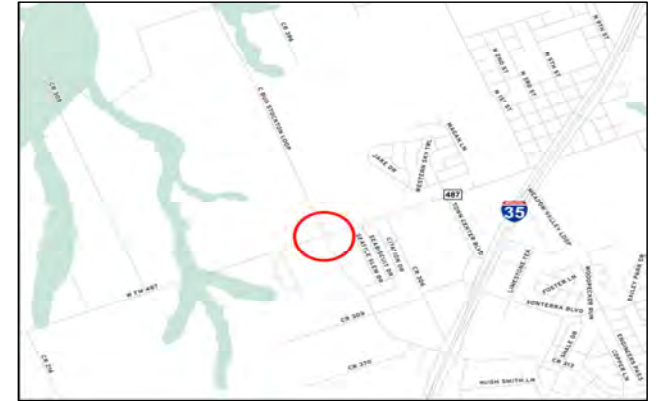

Original Contract Amount = \$553,983.00

Total Change Orders = \$0.00

Adjusted Contract Price = \$ 553,983.00

Expenditures to Date = \$114,300.00 (21%)

Bud Stockton Extension (Traffic Signal at FM 487)



Bud Stockton Extension (Traffic Signal at FM 487)

