


# Williamson County Commissioners Court

---

Road Bond Program  
November 19, 2024




# Precinct 1

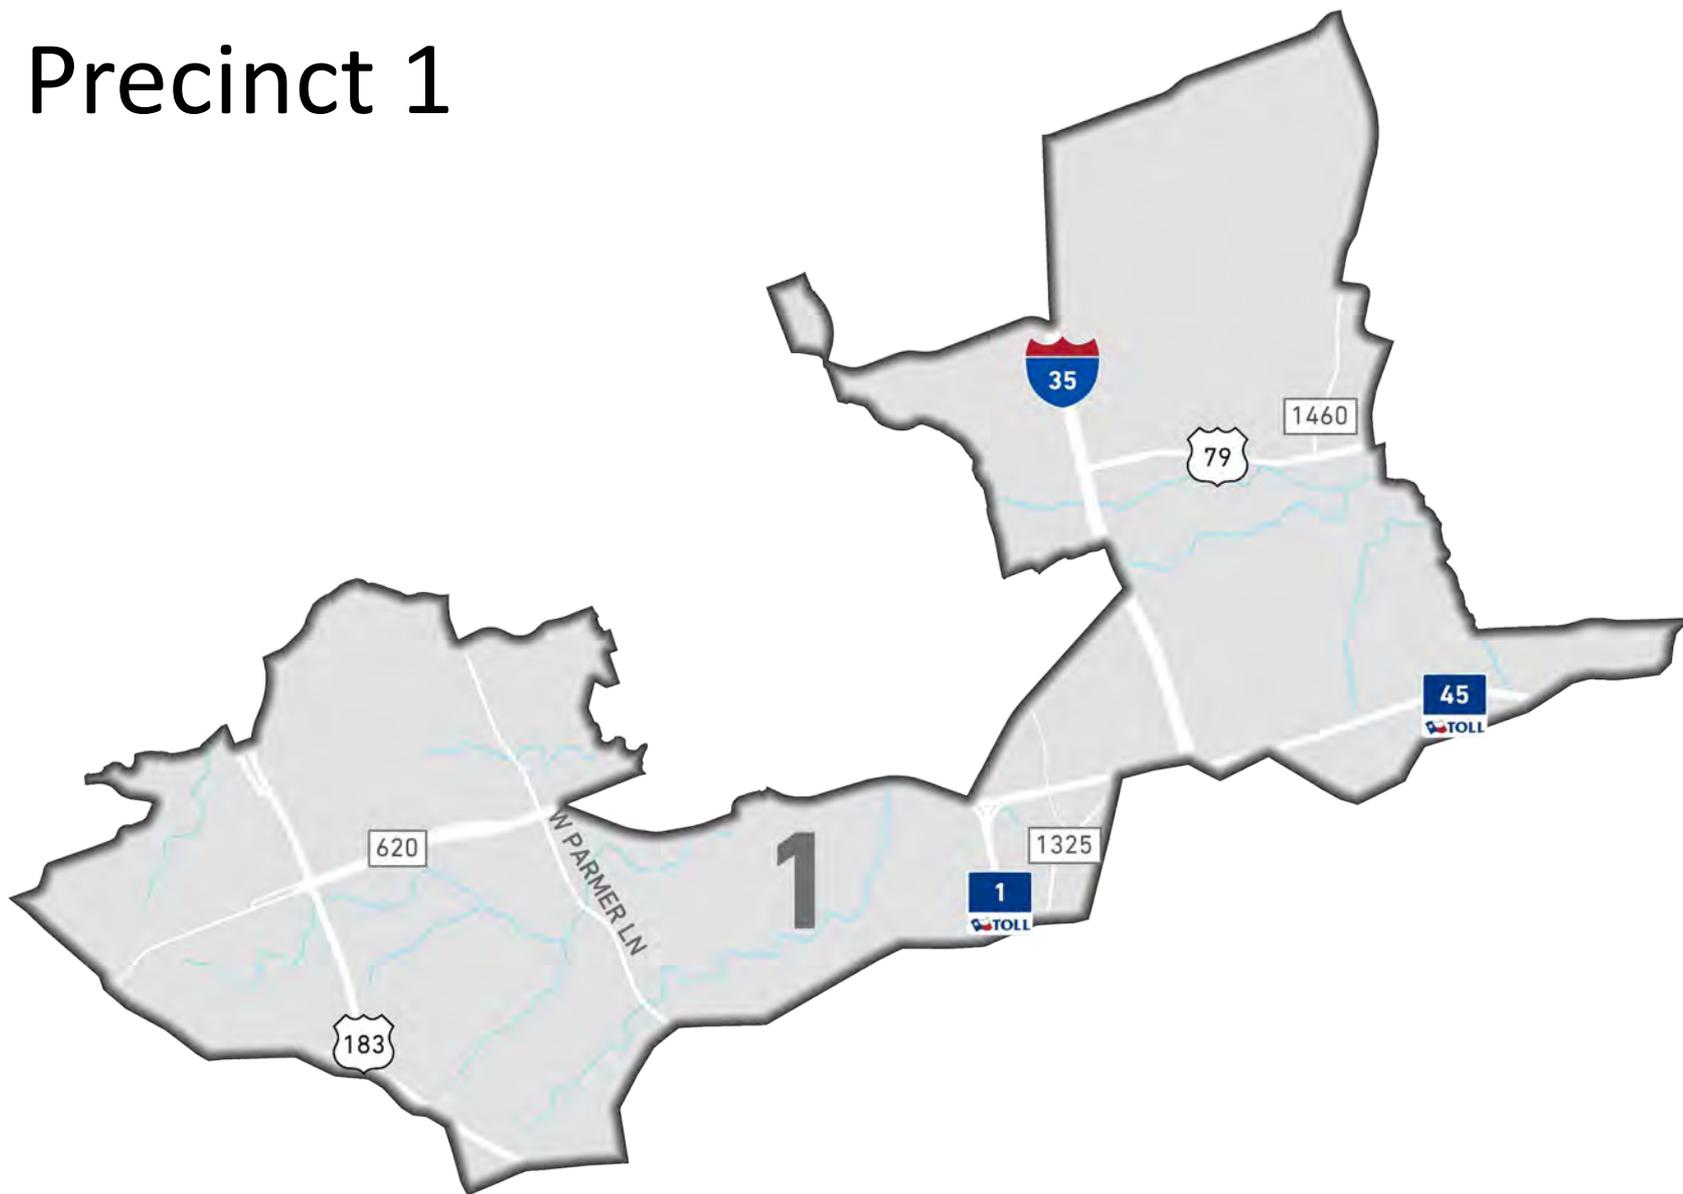

Projects under planning and design, no active construction projects.

# Precinct 2

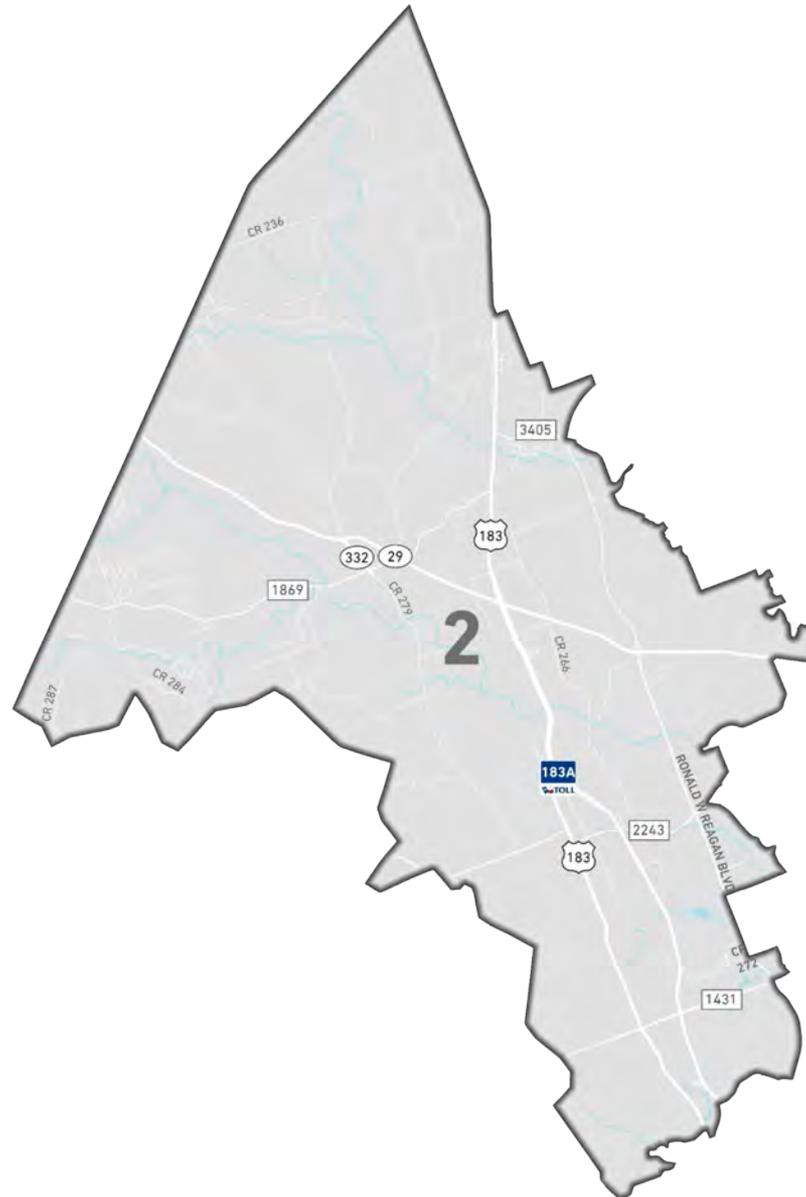

# Liberty Hill (SH 29) Bypass (RM 1869 to CR 279)

Anticipated Completion

Late 2025



Original Contract Price = \$14,149,449.00

Total Change Orders to Date = \$280,462.00

Adjusted Contract Price = \$ 14,429,911.00

Expenditures to Date = \$7,718,733.65 (54%)

# Liberty Hill (SH 29) Bypass (RM 1869 to CR 279)



# Liberty Hill (SH 29) Bypass (RM 1869 to CR 279)




# Liberty Hill (SH 29) Bypass (RM 1869 to CR 279)



# Ronald Reagan Widening (SH 29 to FM 3405)

Anticipated Completion  
Summer 2027

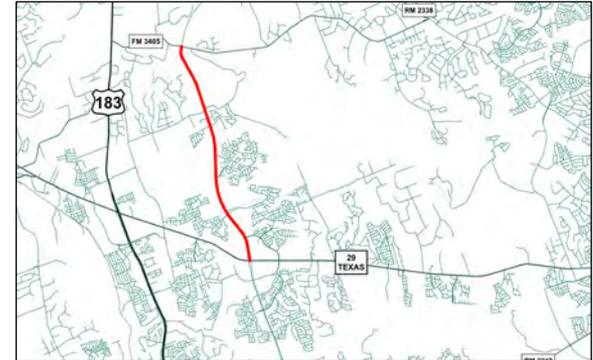


Original Contract Price = \$52,159,299.00

Total Change Orders to Date = \$145,428.00

Adjusted Contract Price = \$52,304,727.00

Expenditures to Date = \$2,255,123.86 (4%)

# Ronald Reagan Widening (SH 29 to FM 3405)

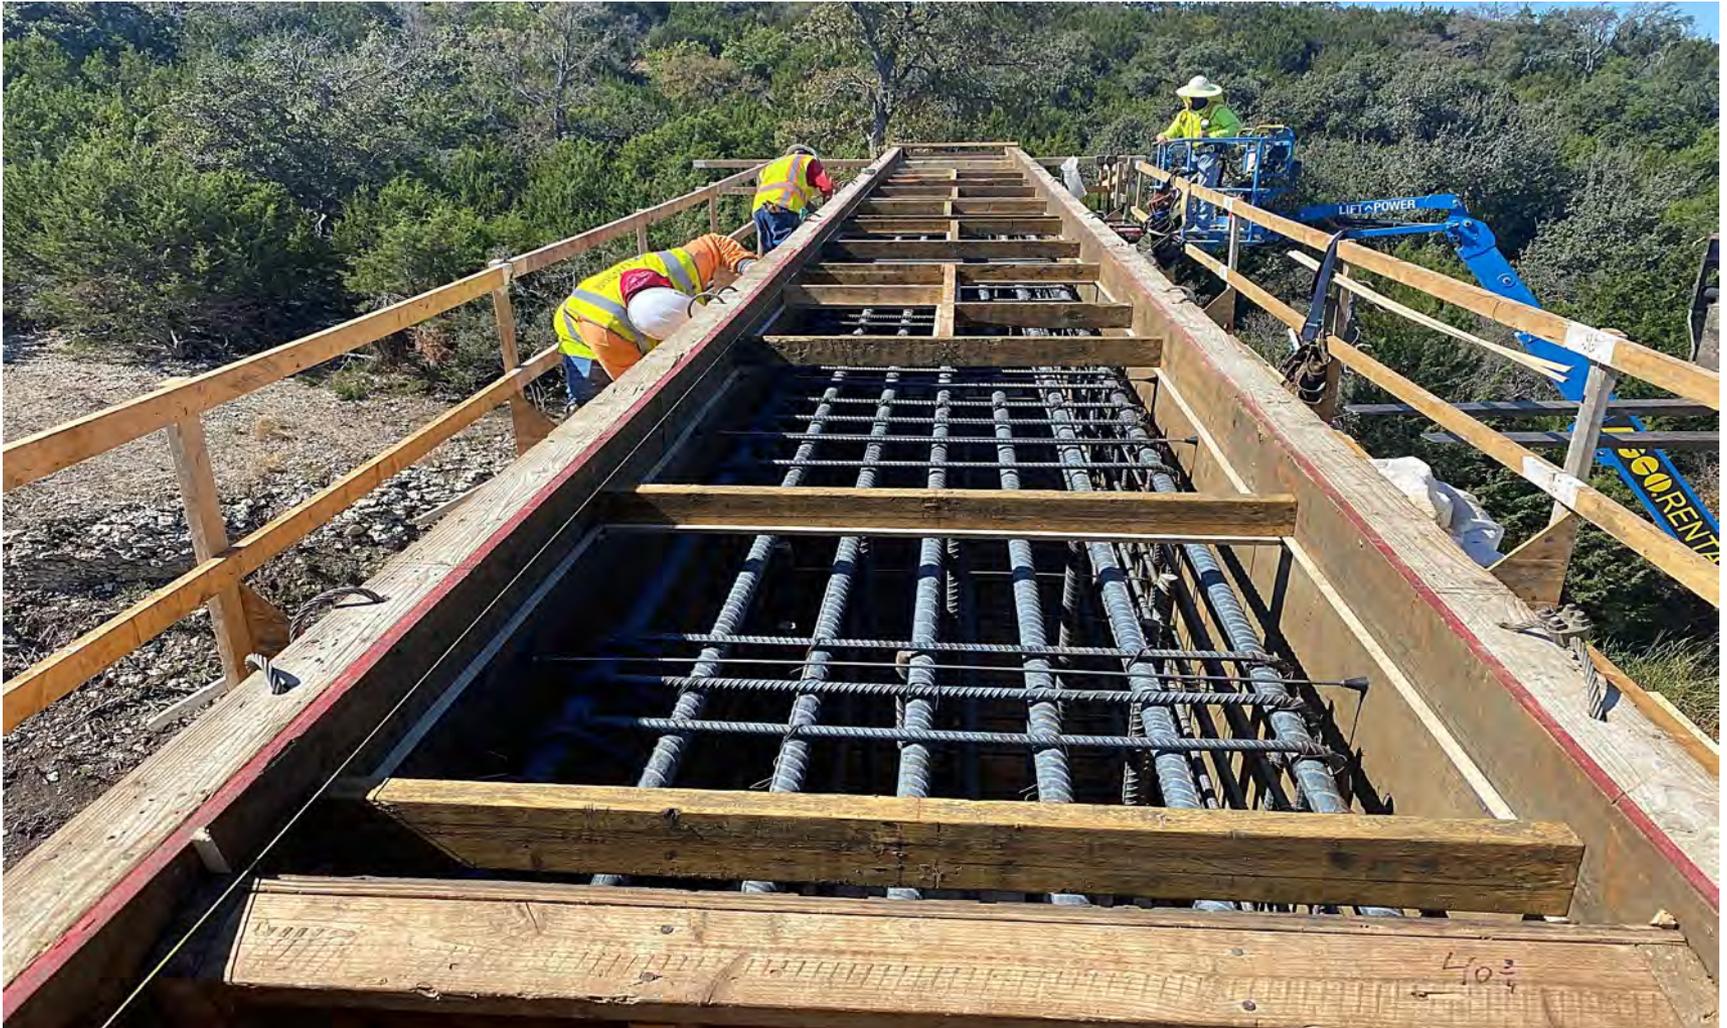


# Ronald Reagan Widening (SH 29 to FM 3405)



# Ronald Reagan Widening (SH 29 to FM 3405)




# Precinct 3

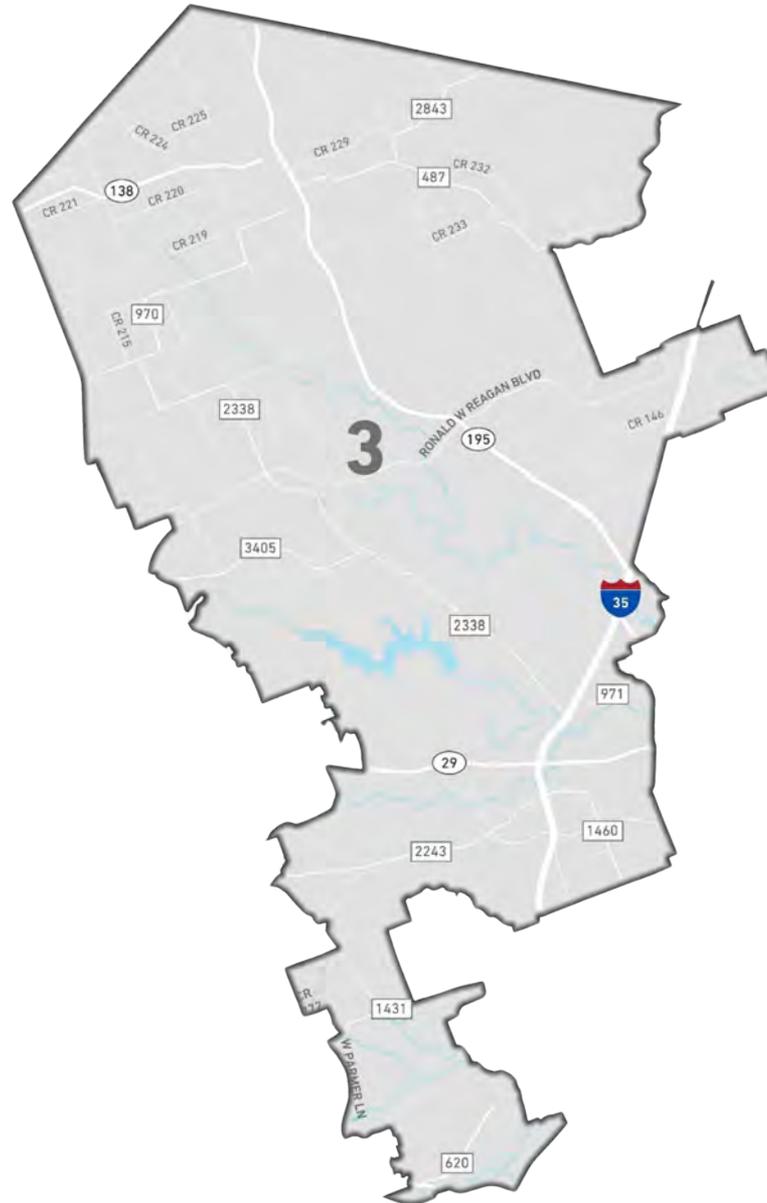

# New Hope Drive Phase 2A (Ronald Reagan Boulevard to Sam Bass Road)

Anticipated Completion

Fall 2024

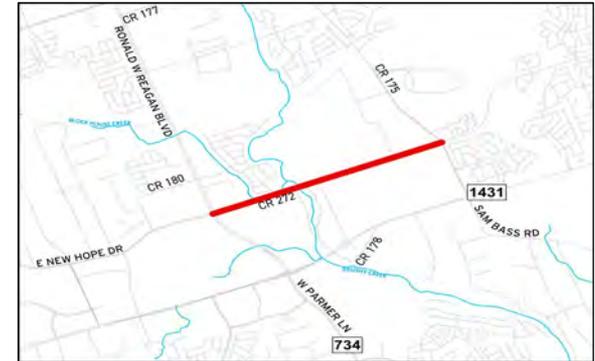

Partnership with the City of Cedar Park

Original Contract Amount = \$22,619,961.16

Construction is managed by the City of Cedar Park

# New Hope Drive Phase 2A (Ronald Reagan Boulevard to Sam Bass Road)



# New Hope Drive Phase 2A (Ronald Reagan Boulevard to Sam Bass Road)




# New Hope Drive Phase 2A (Ronald Reagan Boulevard to Sam Bass Road)



# Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)

Anticipated Completion  
Fall 2025

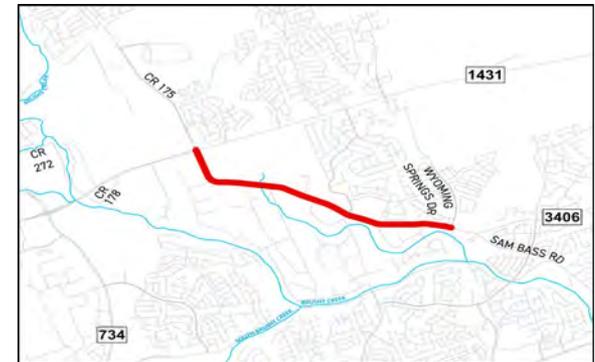

Original Contract Price = \$36,145,959.00

Total Change Orders to Date = -\$2,192,985.66

Adjusted Contract Price = \$33,952,973.34

Expenditures to Date = \$16,880,508.29 (50%)

# Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)




# Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)



# Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)



# Precinct 4

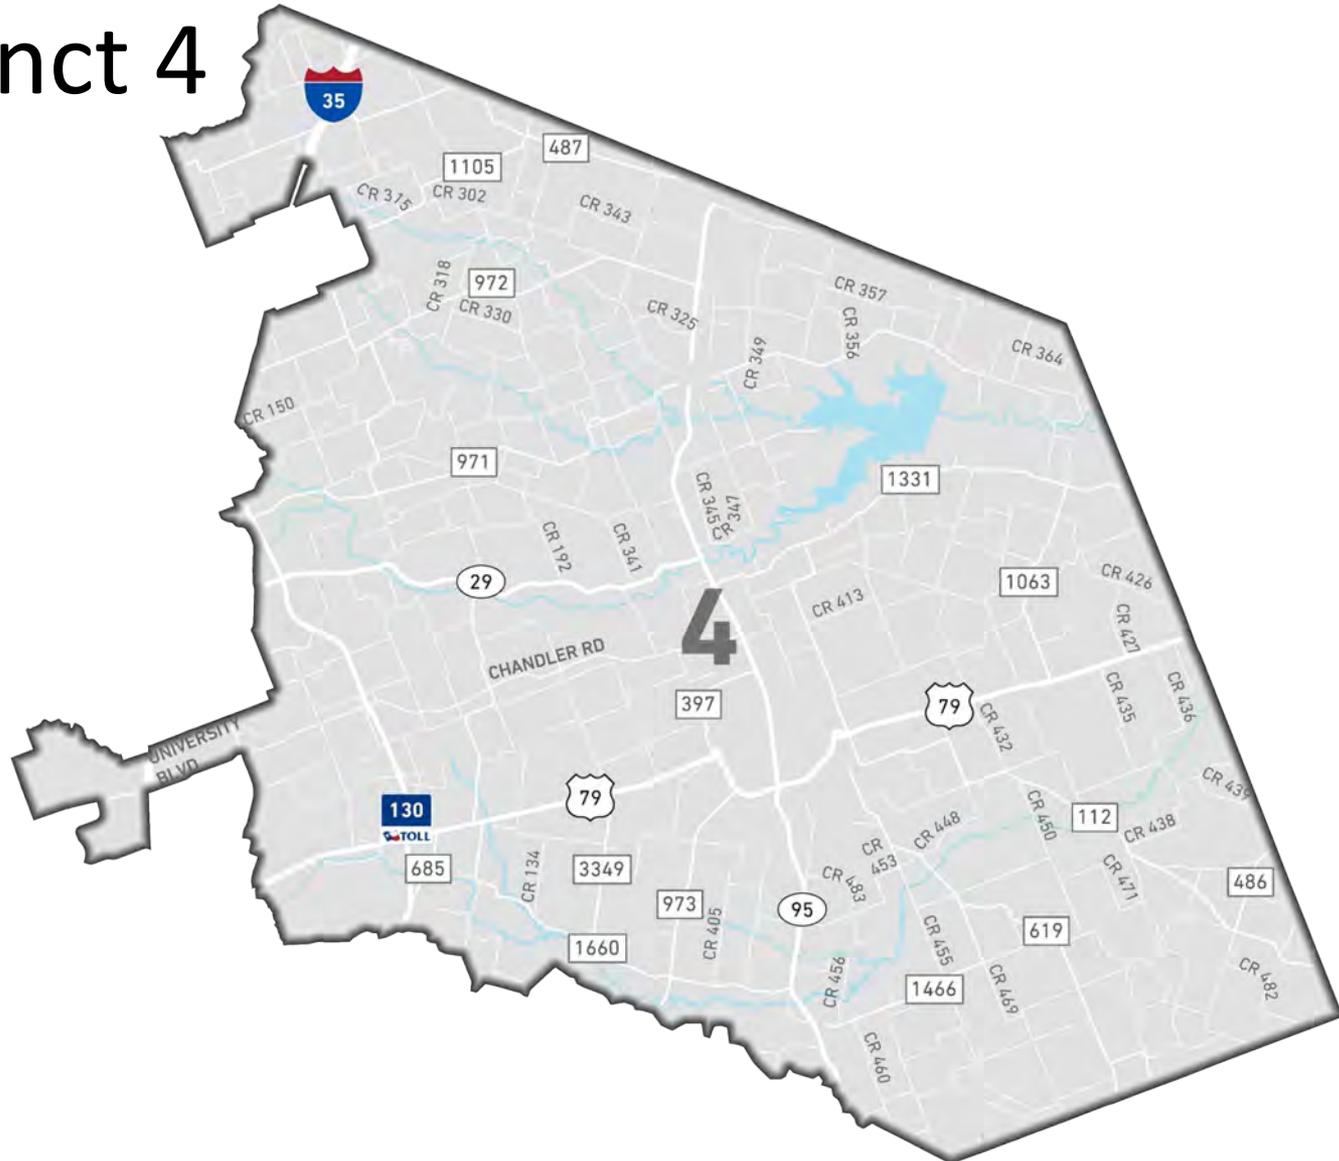

# Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)

Anticipated Completion  
Fall 2024



Partnership with the City of Round Rock

Original Contract Amount = \$23,409,120.97

Construction is managed by the City of Round Rock

# Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)



# Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)



# Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)



# East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)

Anticipated Completion  
Summer 2025 (Roadwork)



Original Contract Amount = \$81,941,038.13

Total Change Orders = \$2,162,933.94

Adjusted Contract Price = \$84,103,972.07

Expenditures to Date = \$58,817,909.02 (70%)

# East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)



# East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)




# East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)



# East Wilco Highway - Segment 2 (CR 137 South of Hutto and CR 404)

Anticipated Completion  
Summer 2028

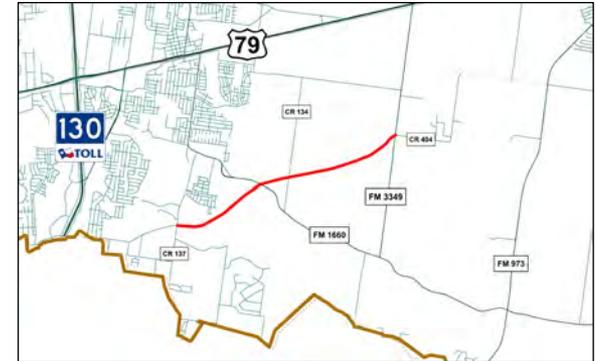

Original Contract Amount = \$64,407,606.63

Total Change Orders = \$0.00

Adjusted Contract Price = \$ 64,407,606.63

Expenditures to Date = \$0.00 (0%)

# East Wilco Highway – Segment 2 (CR 137 South of Hutto and CR 404)



# East Wilco Highway – Segment 2 (CR 137 South of Hutto and CR 404)



# East Wilco Highway – Segment 2 (CR 137 South of Hutto and CR 404)



# Corridor C / SH 29 Bypass (Sam Houston Avenue at Patriot Way to SH 29)

Anticipated Completion  
Summer 2026



Original Contract Amount = \$30,540,848.03

Total Change Orders = \$15,769.50

Adjusted Contract Price = \$30,556,617.53

Expenditures to Date = \$26,153,412.61 (86%)

# Corridor C / SH 29 Bypass (Sam Houston Avenue at Patriot Way to SH 29)



# Corridor C / SH 29 Bypass (Sam Houston Avenue at Patriot Way to SH 29)



# Corridor C / SH 29 Bypass (Sam Houston Avenue at Patriot Way to SH 29)



# Bud Stockton Extension (Traffic Signal at FM 487)

Anticipated Completion  
Late 2024



Original Contract Amount = \$553,983.00

Total Change Orders = \$0.00

Adjusted Contract Price = \$ 553,983.00

Expenditures to Date = \$112,000.00 (20%)

# Bud Stockton Extension (Traffic Signal at FM 487)



# Bud Stockton Extension (Traffic Signal at FM 487)

