


Williamson County Commissioners Court

Road Bond Program
December 17, 2024




Precinct 1

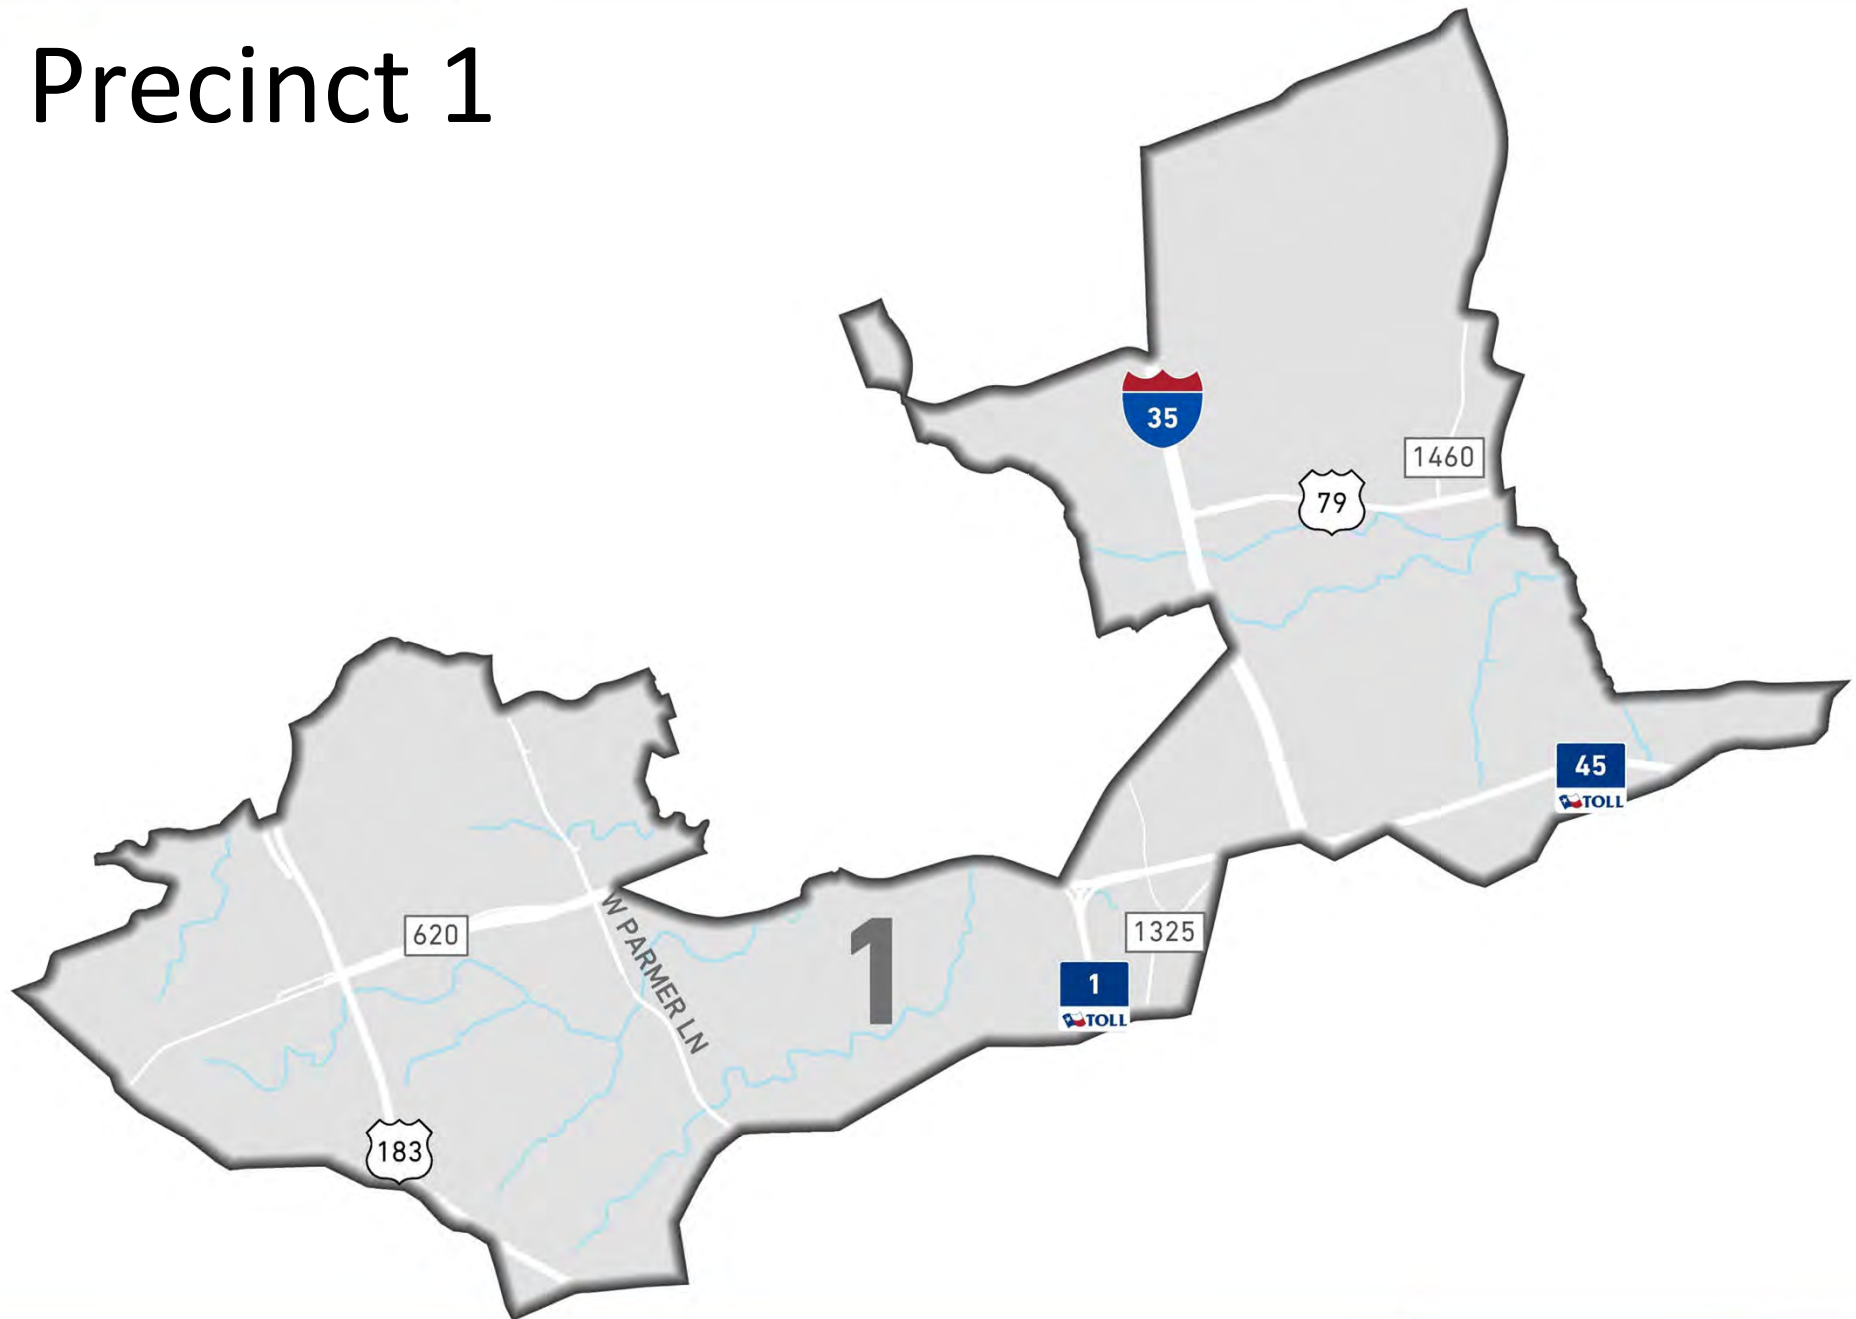

Projects under planning and
design, no active
construction projects.

Precinct 2

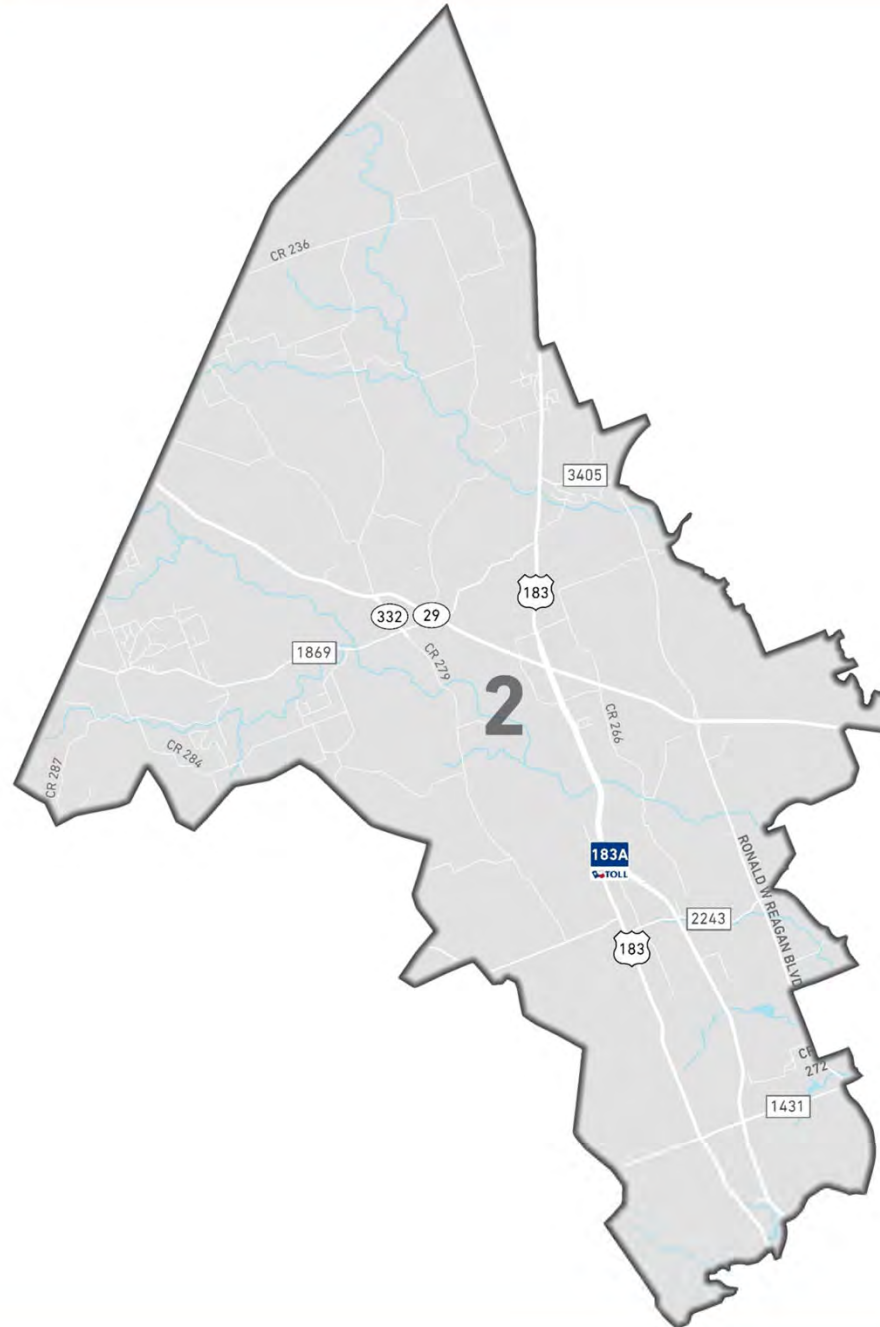

Liberty Hill (SH 29) Bypass

Anticipated Completion
Late 2025



Original Contract Price = \$14,149,449.00

Total Change Orders to Date = \$280,462.00

Adjusted Contract Price = \$ 14,429,911.00

Expenditures to Date = \$7,718,733.65 (54%)

Liberty Hill (SH 29) Bypass




Liberty Hill (SH 29) Bypass



Ronald Reagan Widening (SH 29 to FM 3405)

Anticipated Completion
Summer 2027

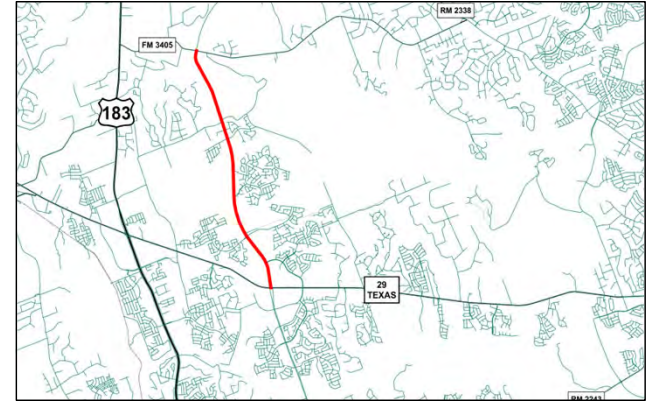

Original Contract Price = \$52,159,299.00

Total Change Orders to Date = \$174,790.00

Adjusted Contract Price = \$52,334,089.00

Expenditures to Date = \$5,194,655.36 (10%)

Ronald Reagan Widening (SH 29 to FM 3405)




Ronald Reagan Widening (SH 29 to FM 3405)



Ronald Reagan Widening (SH 29 to FM 3405)




Precinct 3

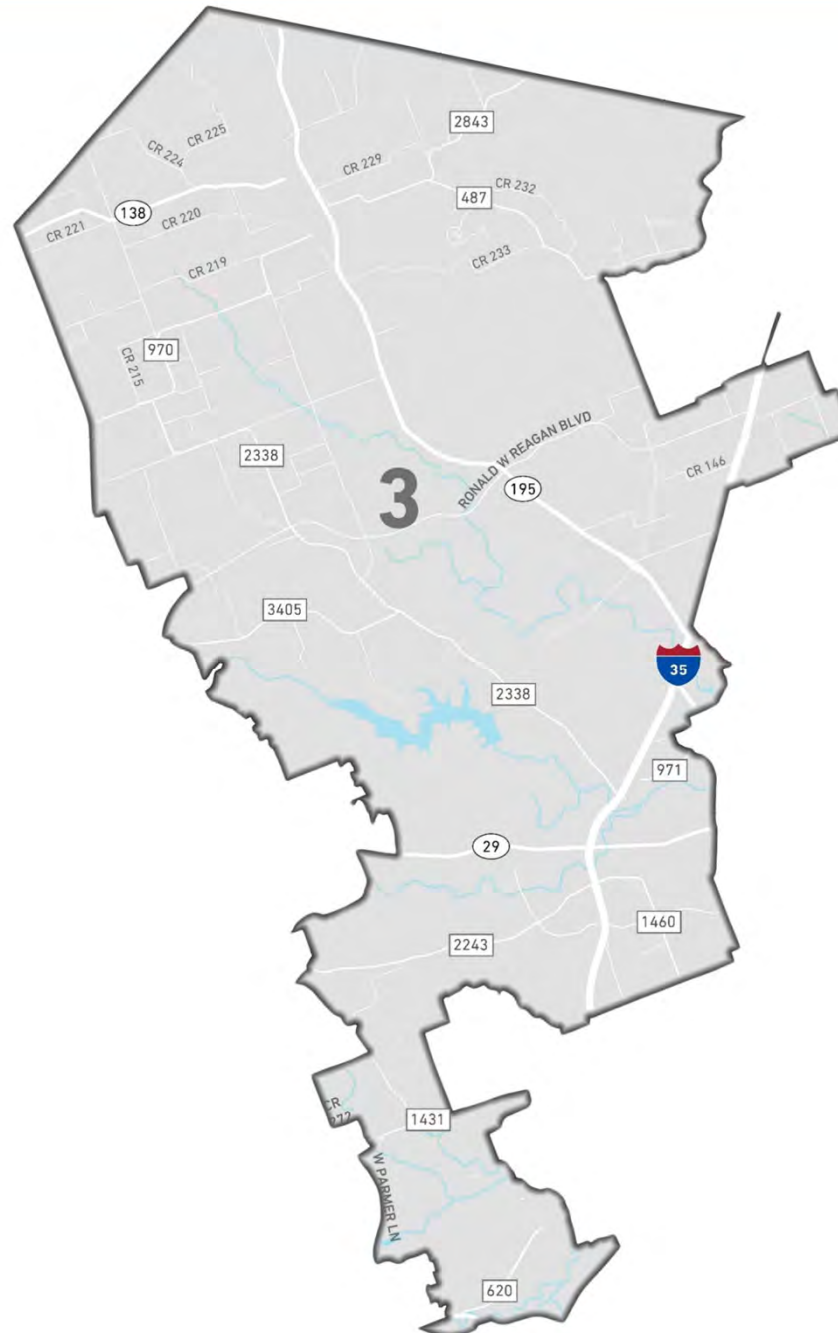

New Hope Drive Phase 2A

Substantially Complete
November 2024

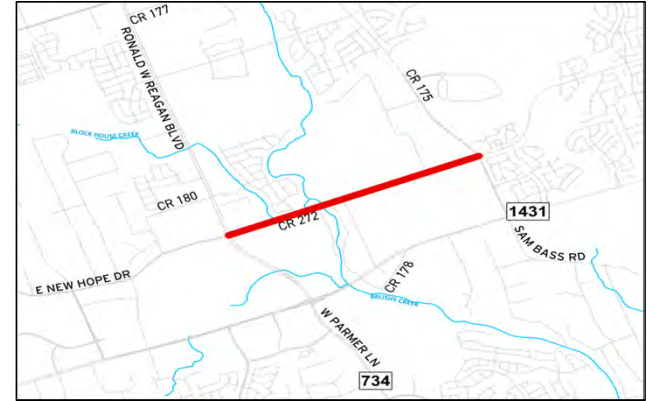

Partnership with the City of Cedar Park

Original Contract Amount = \$22,619,961.16


Construction is managed by the City of Cedar Park

New Hope Drive Phase 2A



Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)

Anticipated Completion
Fall 2025

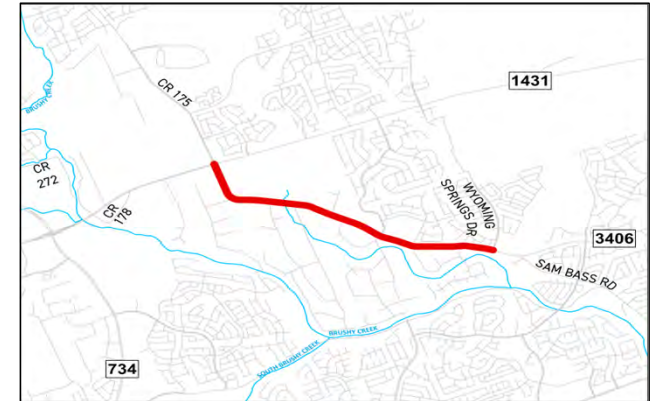

Original Contract Price = \$36,145,959.00

Total Change Orders to Date = -\$2,192,985.66

Adjusted Contract Price = \$33,952,973.34

Expenditures to Date = \$17,827,716.03 (53%)

Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)




Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)



Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)



Precinct 4

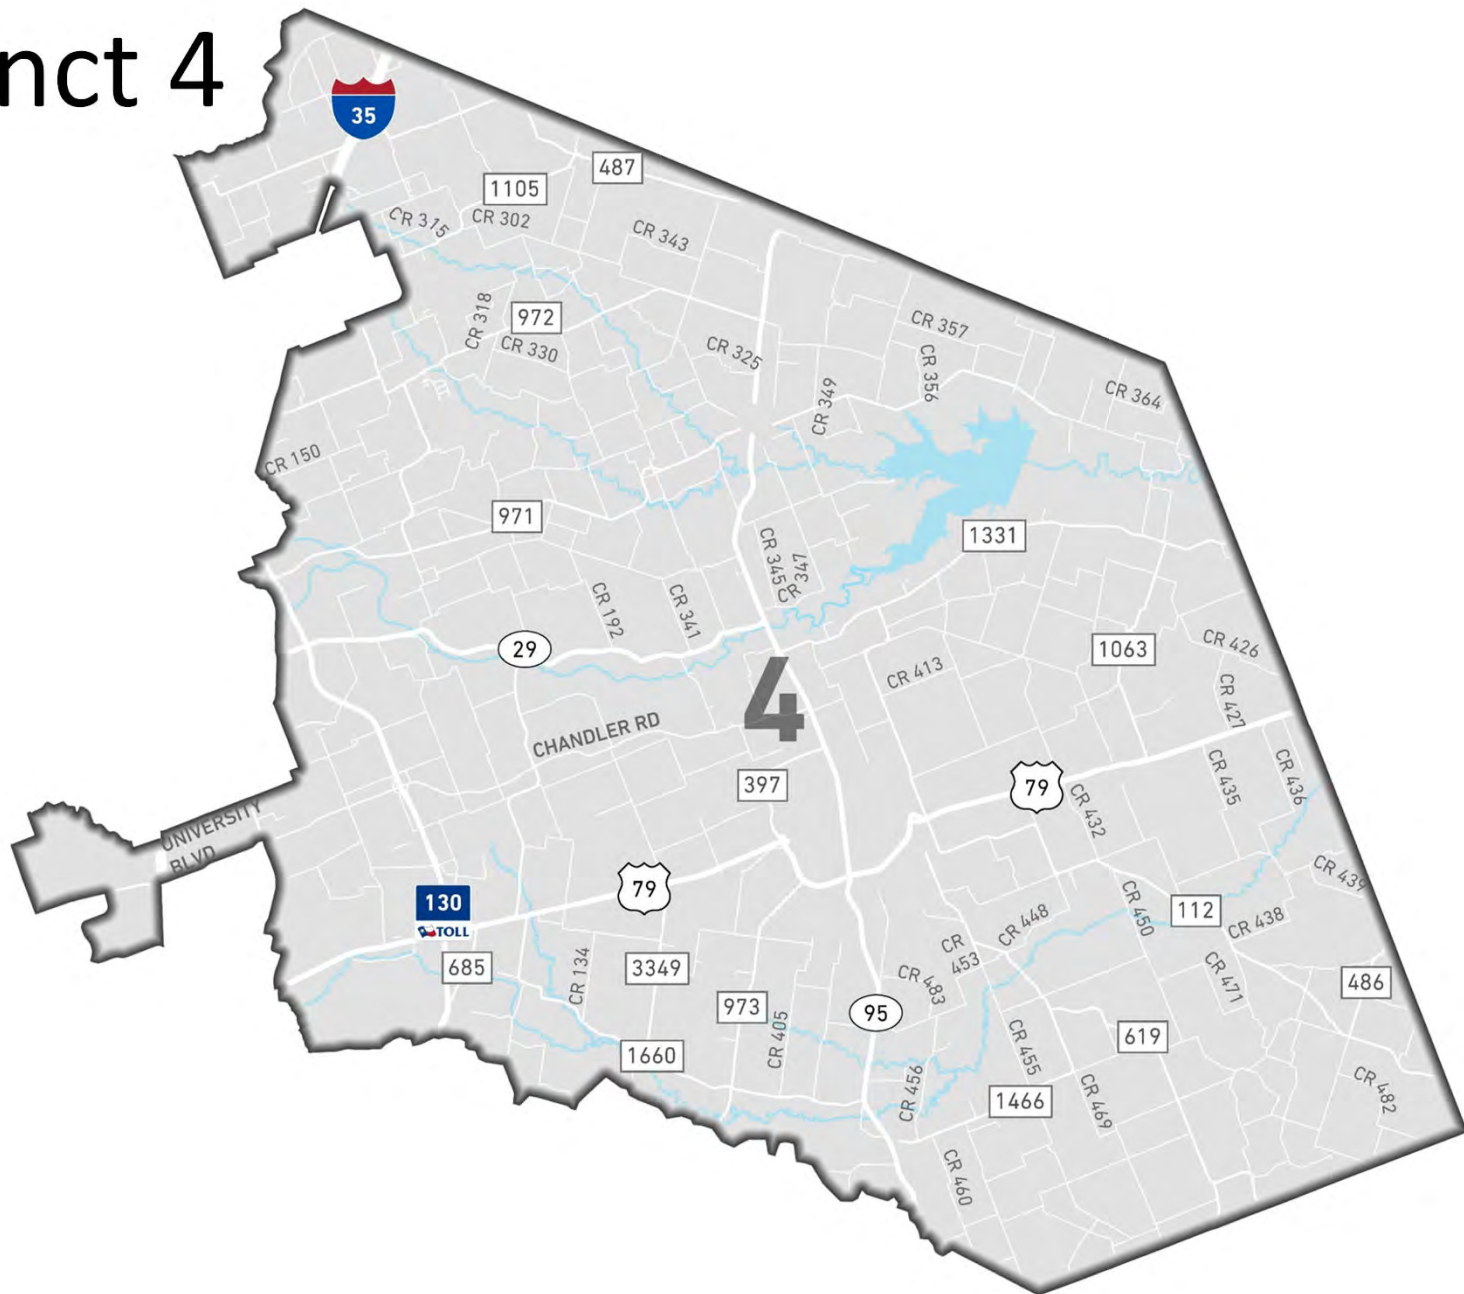

Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)

Anticipated Completion
Late 2024




Partnership with the City of Round Rock
Original Contract Amount = \$23,409,120.97
Construction is managed by the City of Round Rock

Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)



East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)

Anticipated Completion
Summer 2025 (Roadwork)

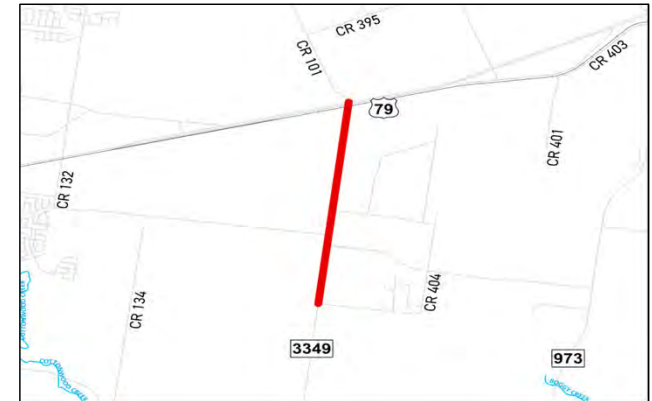

Original Contract Amount = \$81,941,038.13

Total Change Orders = \$2,330,517.59

Adjusted Contract Price = \$84,271,555.72

Expenditures to Date = \$58,817,909.02 (70%)

East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)



East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)




East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)



East Wilco Highway - Segment 2 (CR 137 South of Hutto and CR 404)

Anticipated Completion
Summer 2028

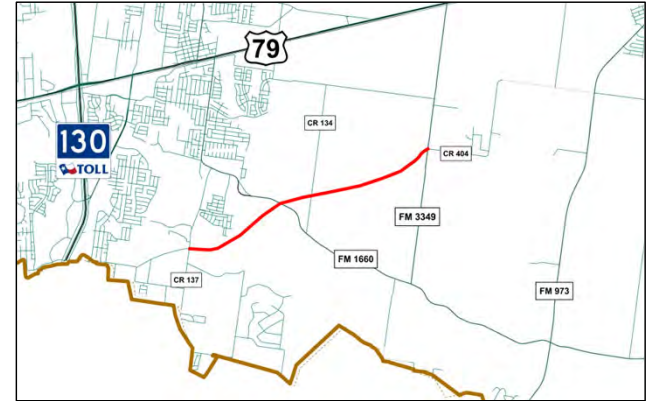

Original Contract Amount = \$64,407,606.63

Total Change Orders = \$0.00

Adjusted Contract Price = \$64,407,606.63

Expenditures to Date = \$4,494,169.84 (7%)

East Wilco Highway – Segment 2 (CR 137 South of Hutto and CR 404)



East Wilco Highway – Segment 2 (CR 137 South of Hutto and CR 404)



East Wilco Highway – Segment 2 (CR 137 South of Hutto and CR 404)



Corridor C / SH 29 Bypass (Sam Houston Avenue at Patriot Way to SH 29)

Anticipated Completion
Summer 2026



Original Contract Amount = \$30,540,848.03

Total Change Orders = \$15,769.50

Adjusted Contract Price = \$30,556,617.53

Expenditures to Date = \$27,494,645.17 (90%)

Corridor C / SH 29 Bypass (Sam Houston Avenue at Patriot Way to SH 29)



Corridor C / SH 29 Bypass (Sam Houston Avenue at Patriot Way to SH 29)




Corridor C / SH 29 Bypass (Sam Houston Avenue at Patriot Way to SH 29)



Bud Stockton Extension (Traffic Signal at FM 487)

Anticipated Completion
Late 2024

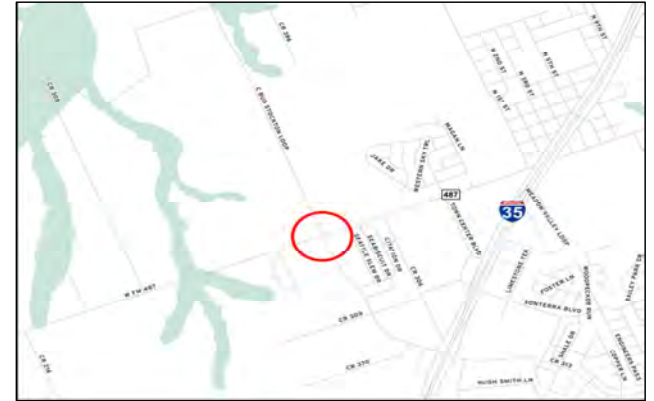

Original Contract Amount = \$553,983.00

Total Change Orders = \$0.00

Adjusted Contract Price = \$ 553,983.00

Expenditures to Date = \$112,000.00 (20%)

Bud Stockton Extension (Traffic Signal at FM 487)



Bud Stockton Extension (Traffic Signal at FM 487)

