


Williamson County Commissioners Court

Road Bond Program
January 28, 2025




Precinct 1

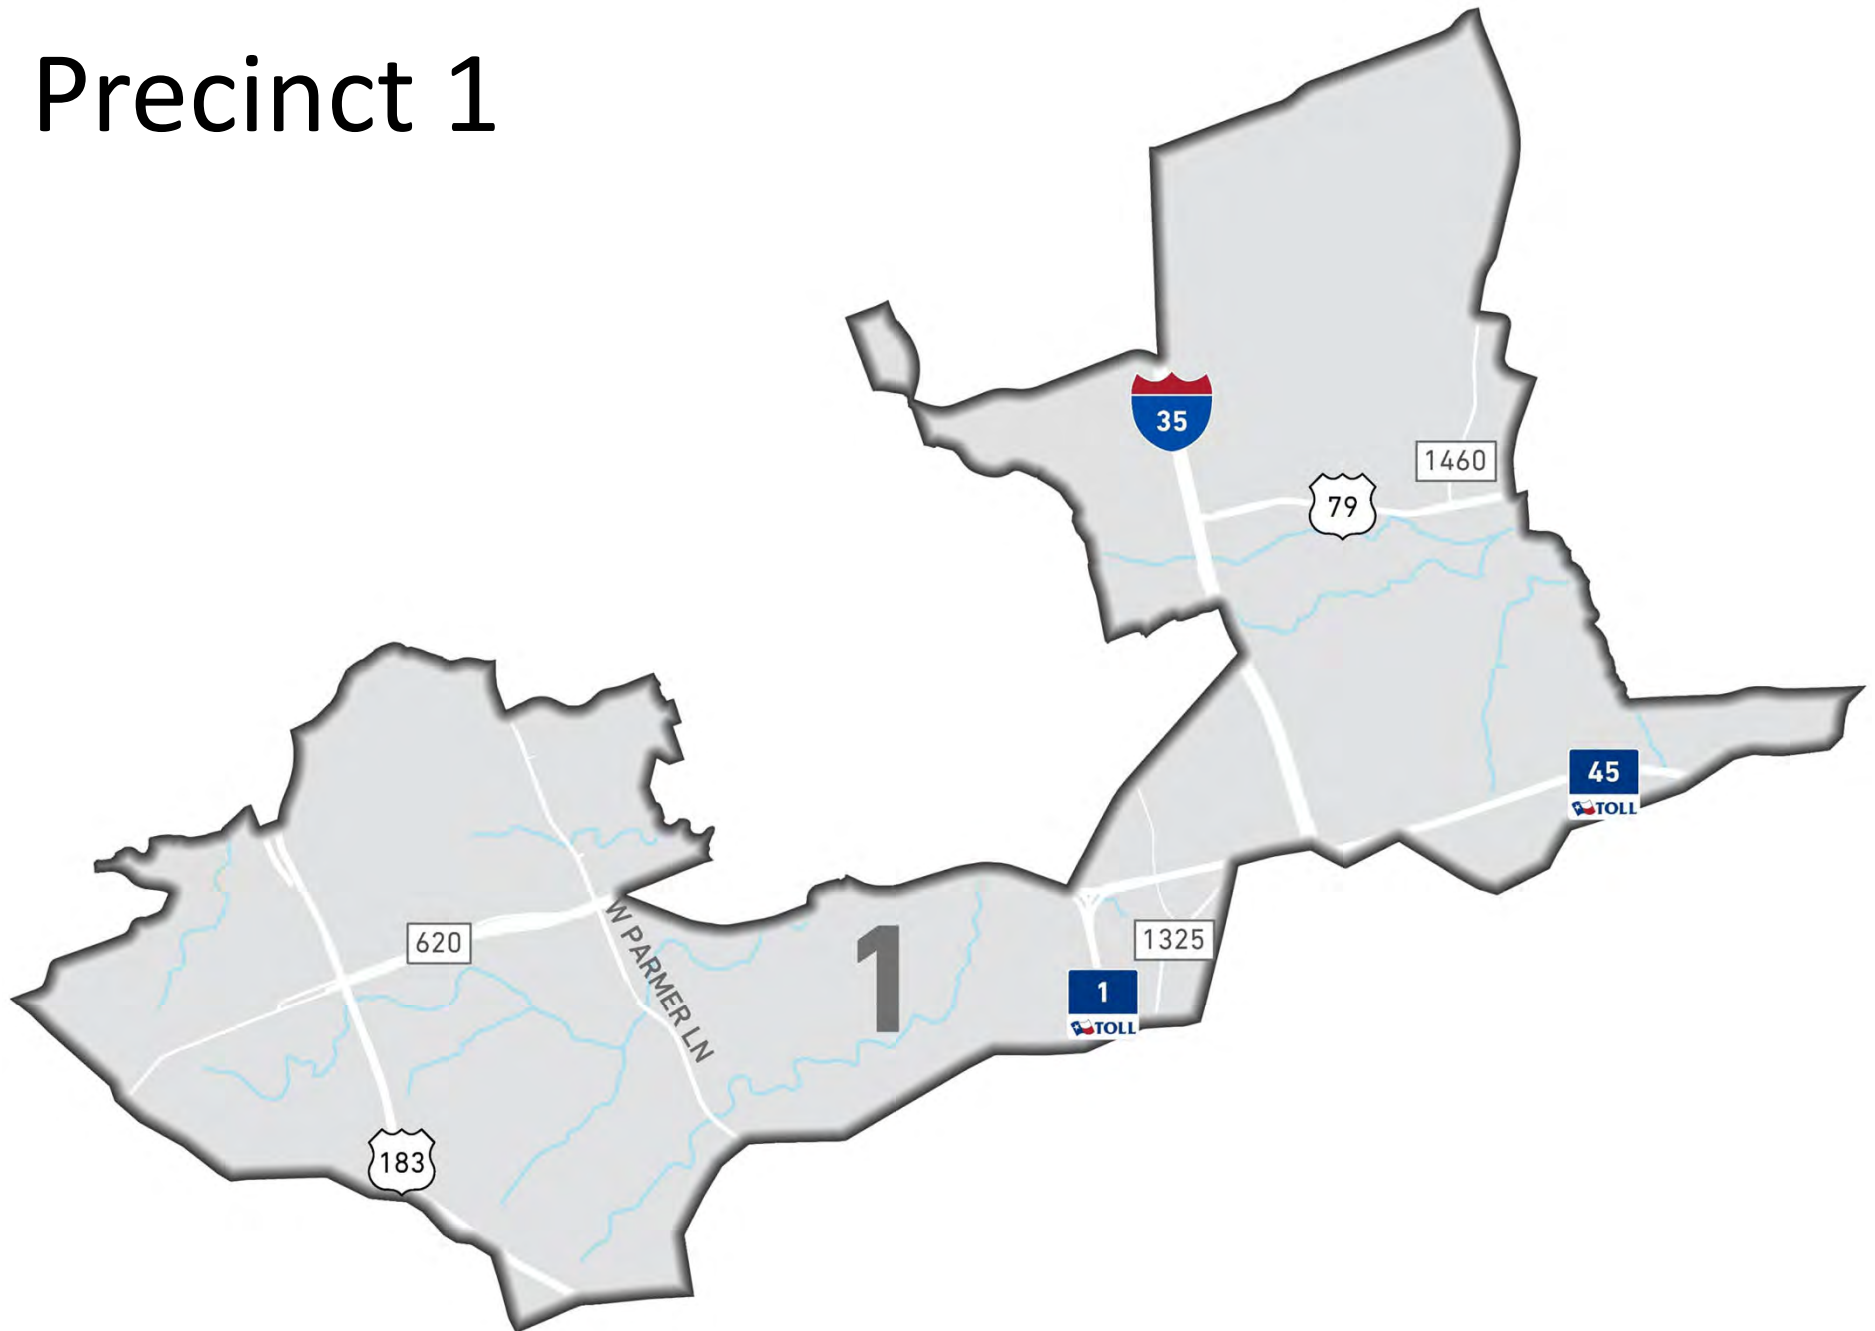

Projects under planning and
design, no active
construction projects.

Precinct 2

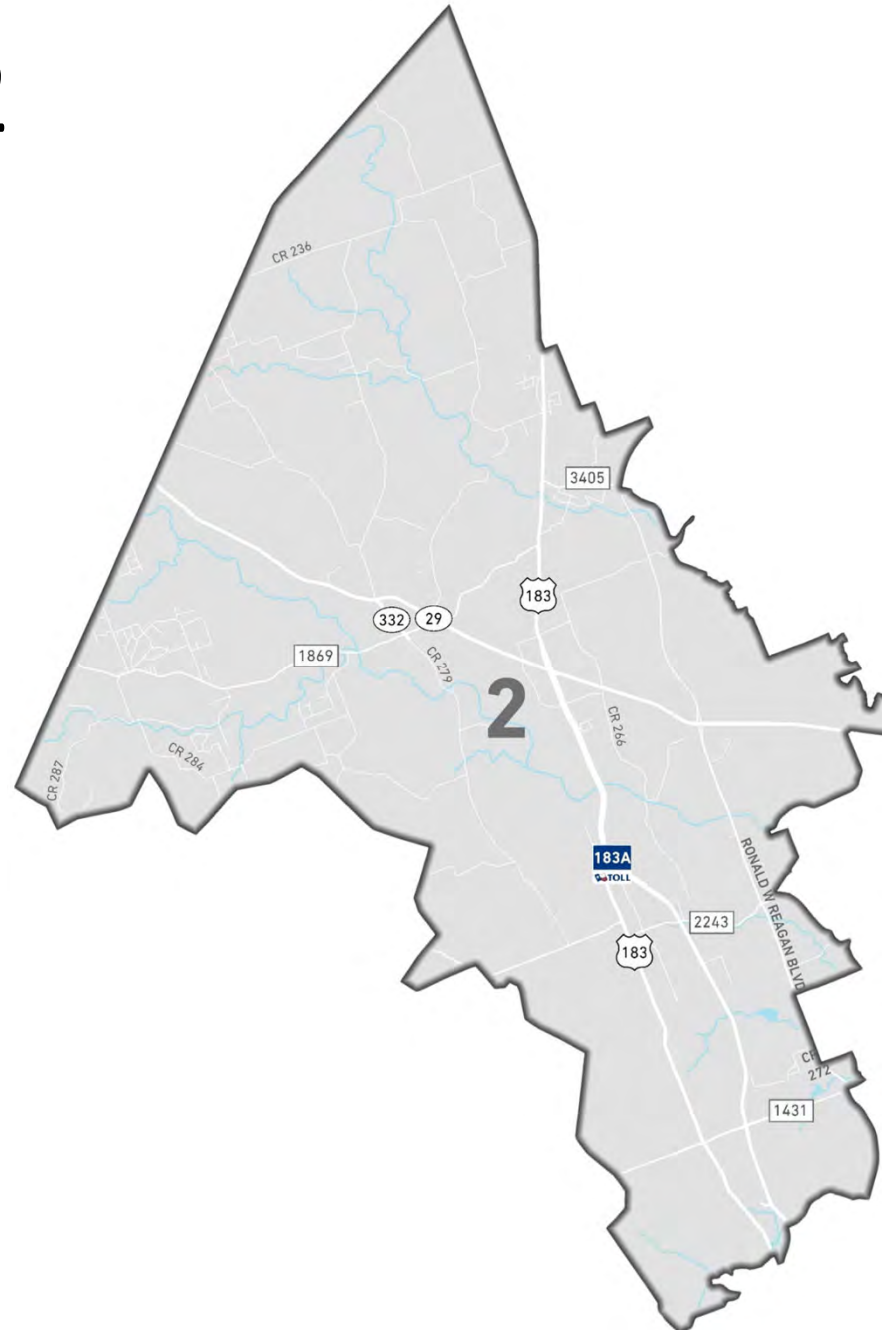

Liberty Hill (SH 29) Bypass (RM 1869 to FM 3405)

Anticipated Completion
Late 2025



Original Contract Price = \$14,149,449.00

Total Change Orders to Date = \$280,462.00

Adjusted Contract Price = \$ 14,429,911.00

Expenditures to Date = \$8,373,257.65 (58%)

Liberty Hill (SH 29) Bypass RM 1869 to CR 279



Liberty Hill (SH 29) Bypass RM 1869 to CR 279




Liberty Hill (SH 29) Bypass RM 1869 to CR 279



Ronald Reagan Widening (SH 29 to FM 3405)

Anticipated Completion
Summer 2027

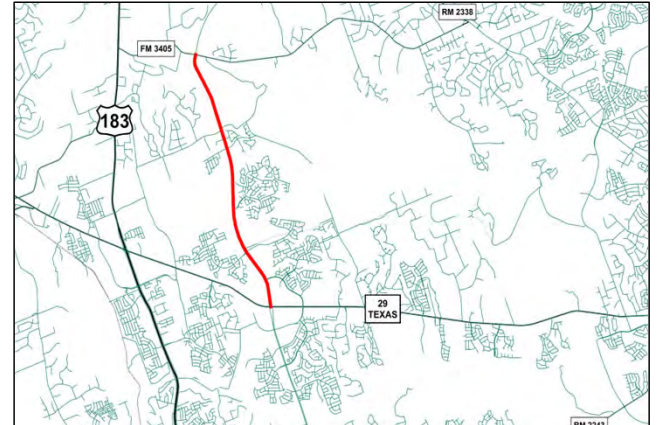

Original Contract Price = \$52,159,299.00

Total Change Orders to Date = \$203,752.50

Adjusted Contract Price = \$52,363,051.50

Expenditures to Date = \$9,831,651.49 (19%)

Ronald Reagan Widening (SH 29 to FM 3405)




Ronald Reagan Widening (SH 29 to FM 3405)



Ronald Reagan Widening (SH 29 to FM 3405)




Precinct 3

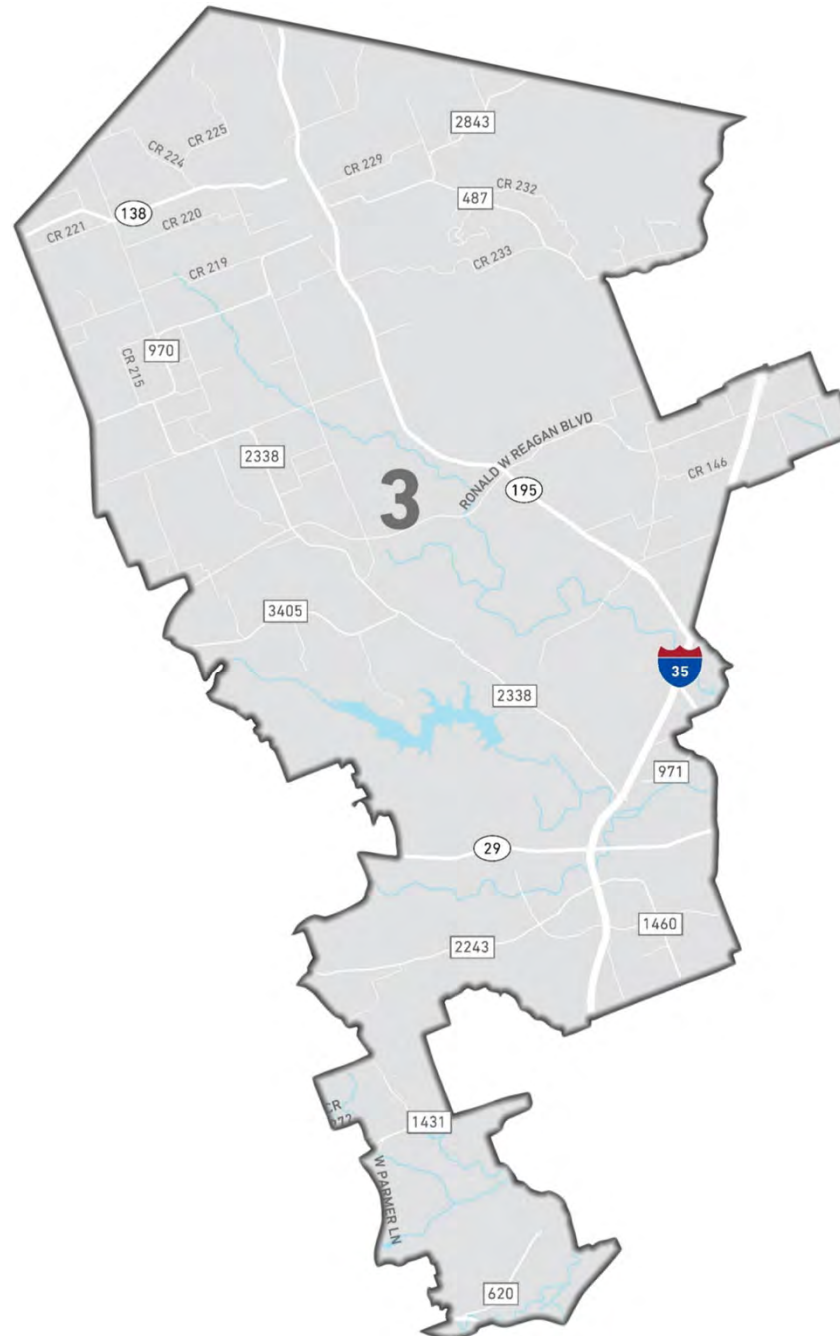

Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)

Anticipated Completion
Fall 2025

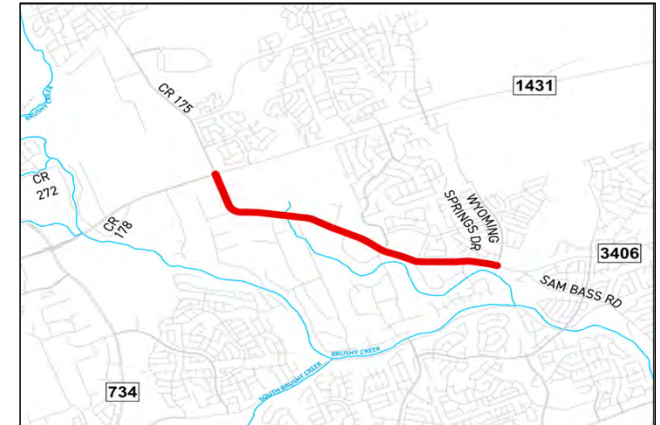

Original Contract Price = \$36,145,959.00

Total Change Orders to Date = -\$2,192,985.66

Adjusted Contract Price = \$33,952,973.34

Expenditures to Date = \$18,752,581.47 (55%)

Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)



Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)




Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)



Wyoming Springs Extension (Brightwater Boulevard/Creek Bend to Sam Bass Road)

Anticipated Completion
Late 2026

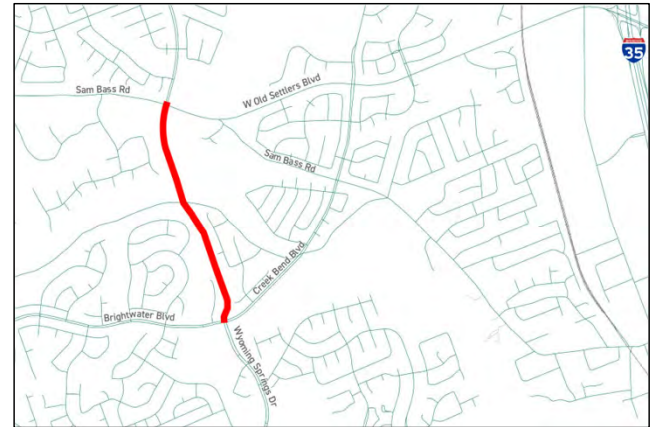

Partnership with the City of Round Rock


Original Contract Amount = \$25,917,630.47

Construction is managed by the City of Round Rock

Wyoming Springs Extension (Brightwater Boulevard/Creek Bend to Sam Bass Road)




Precinct 4

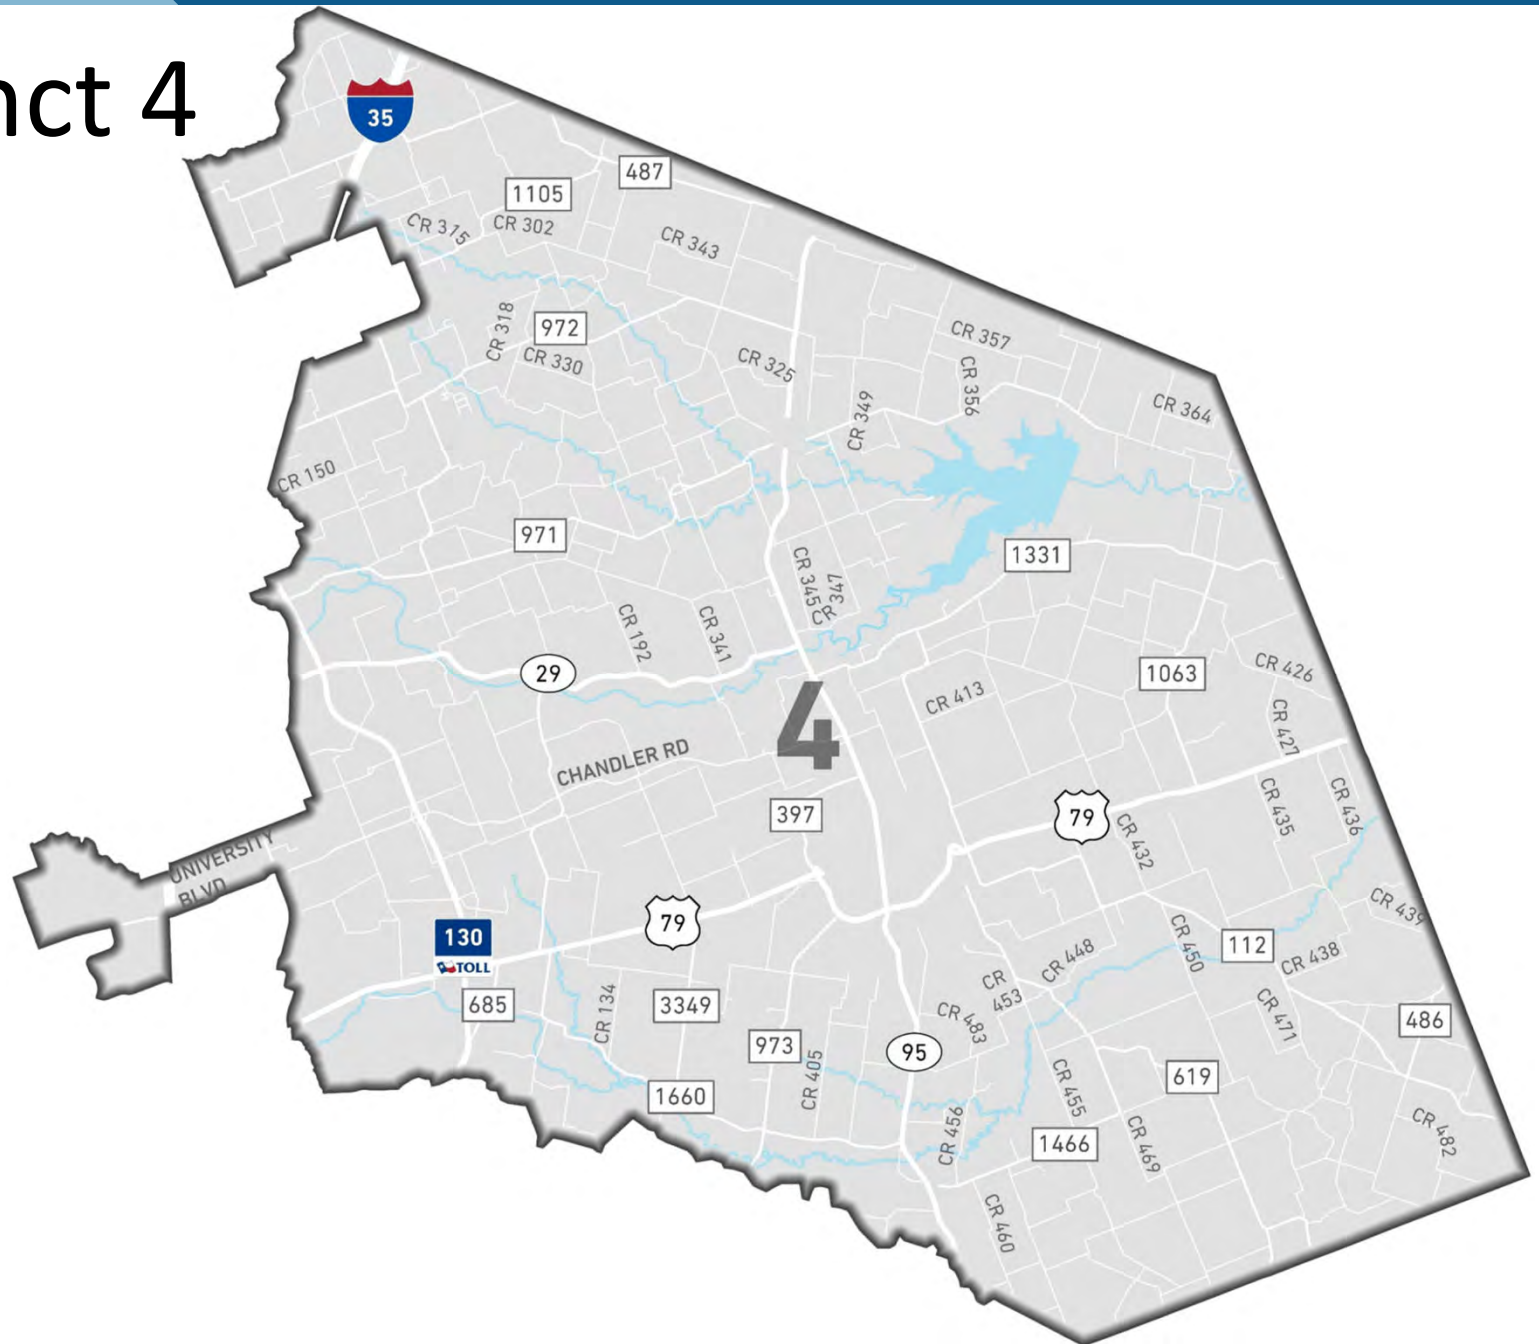

Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)

Substantially Complete
December 2024

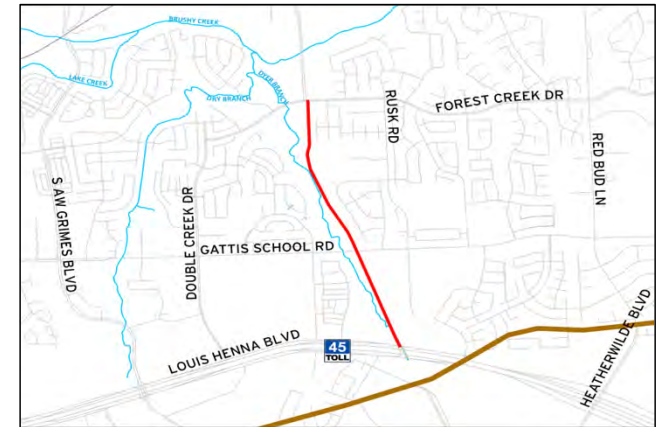

Partnership with the City of Round Rock

Original Contract Amount = \$23,409,120.97

Construction is managed by the City of Round Rock

Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)




Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)



East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)

Anticipated Completion
Summer 2025 (Roadwork)

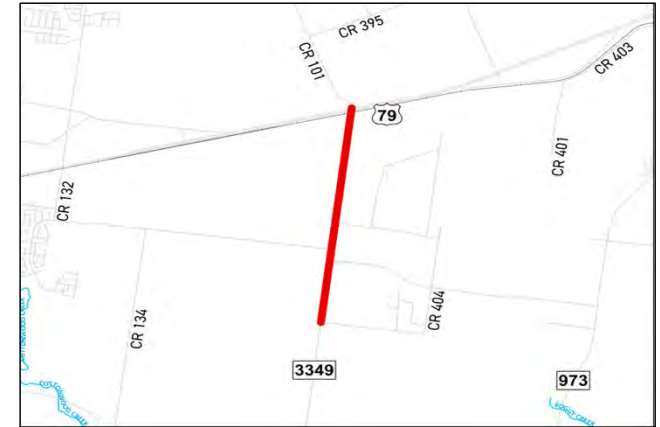

Original Contract Amount = \$81,941,038.13

Total Change Orders = \$2,335,980.09

Adjusted Contract Price = \$84,277,018.22

Expenditures to Date = \$61,915,469.59 (73%)

East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)



East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)



East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)



East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)



East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)



East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)



East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)



East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)



East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)




East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)



East Wilco Highway - Segment 2 (CR 137 South of Hutto and CR 404)

Anticipated Completion
Summer 2028

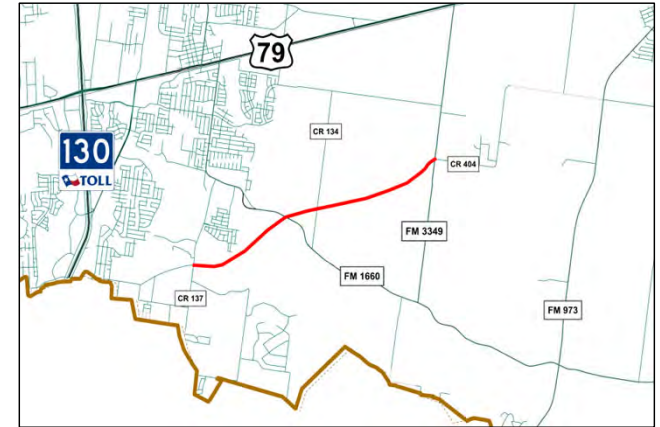

Original Contract Amount = \$64,407,606.63

Total Change Orders = \$0.00

Adjusted Contract Price = \$64,407,606.63

Expenditures to Date = \$8,226,558.76 (13%)

East Wilco Highway – Segment 2 (CR 137 South of Hutto and CR 404)



East Wilco Highway – Segment 2 (CR 137 South of Hutto and CR 404)



East Wilco Highway – Segment 2 (CR 137 South of Hutto and CR 404)



Bud Stockton Extension (Traffic Signal at FM 487)

Anticipated Completion
Early 2025



Original Contract Amount = \$553,983.00

Total Change Orders = \$0.00

Adjusted Contract Price = \$ 553,983.00


Expenditures to Date = \$169,350.00 (31%)

Bud Stockton Extension (Traffic Signal at FM 487)



Old Settlers Boulevard (North Red Bud Lane/CR 122 to CR 110)

Anticipated Completion
Fall 2025

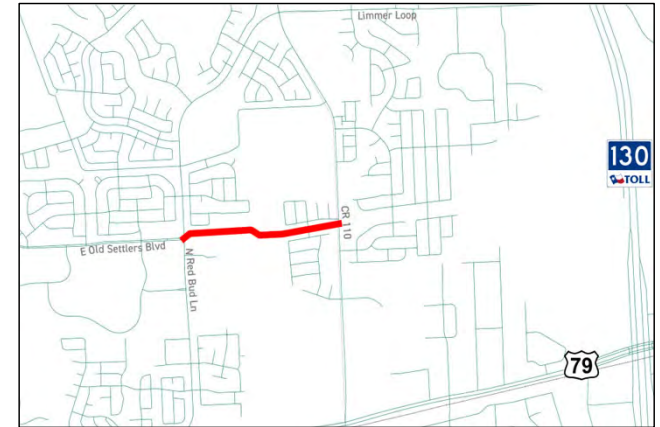

Partnership with the City of Round Rock

Original Contract Amount = \$14,920,847.10

Construction is managed by the City of Round Rock

Old Settlers Boulevard (North Red Bud Lane/CR 122 to CR 110)



Old Settlers Boulevard (North Red Bud Lane/CR 122 to CR 110)



Old Settlers Boulevard (North Red Bud Lane/CR 122 to CR 110)

