




# **WILLIAMSON COUNTY COMMISSIONERS COURT**

ROAD BOND PROGRAM  
March 25, 2025


# PRECINCT 1

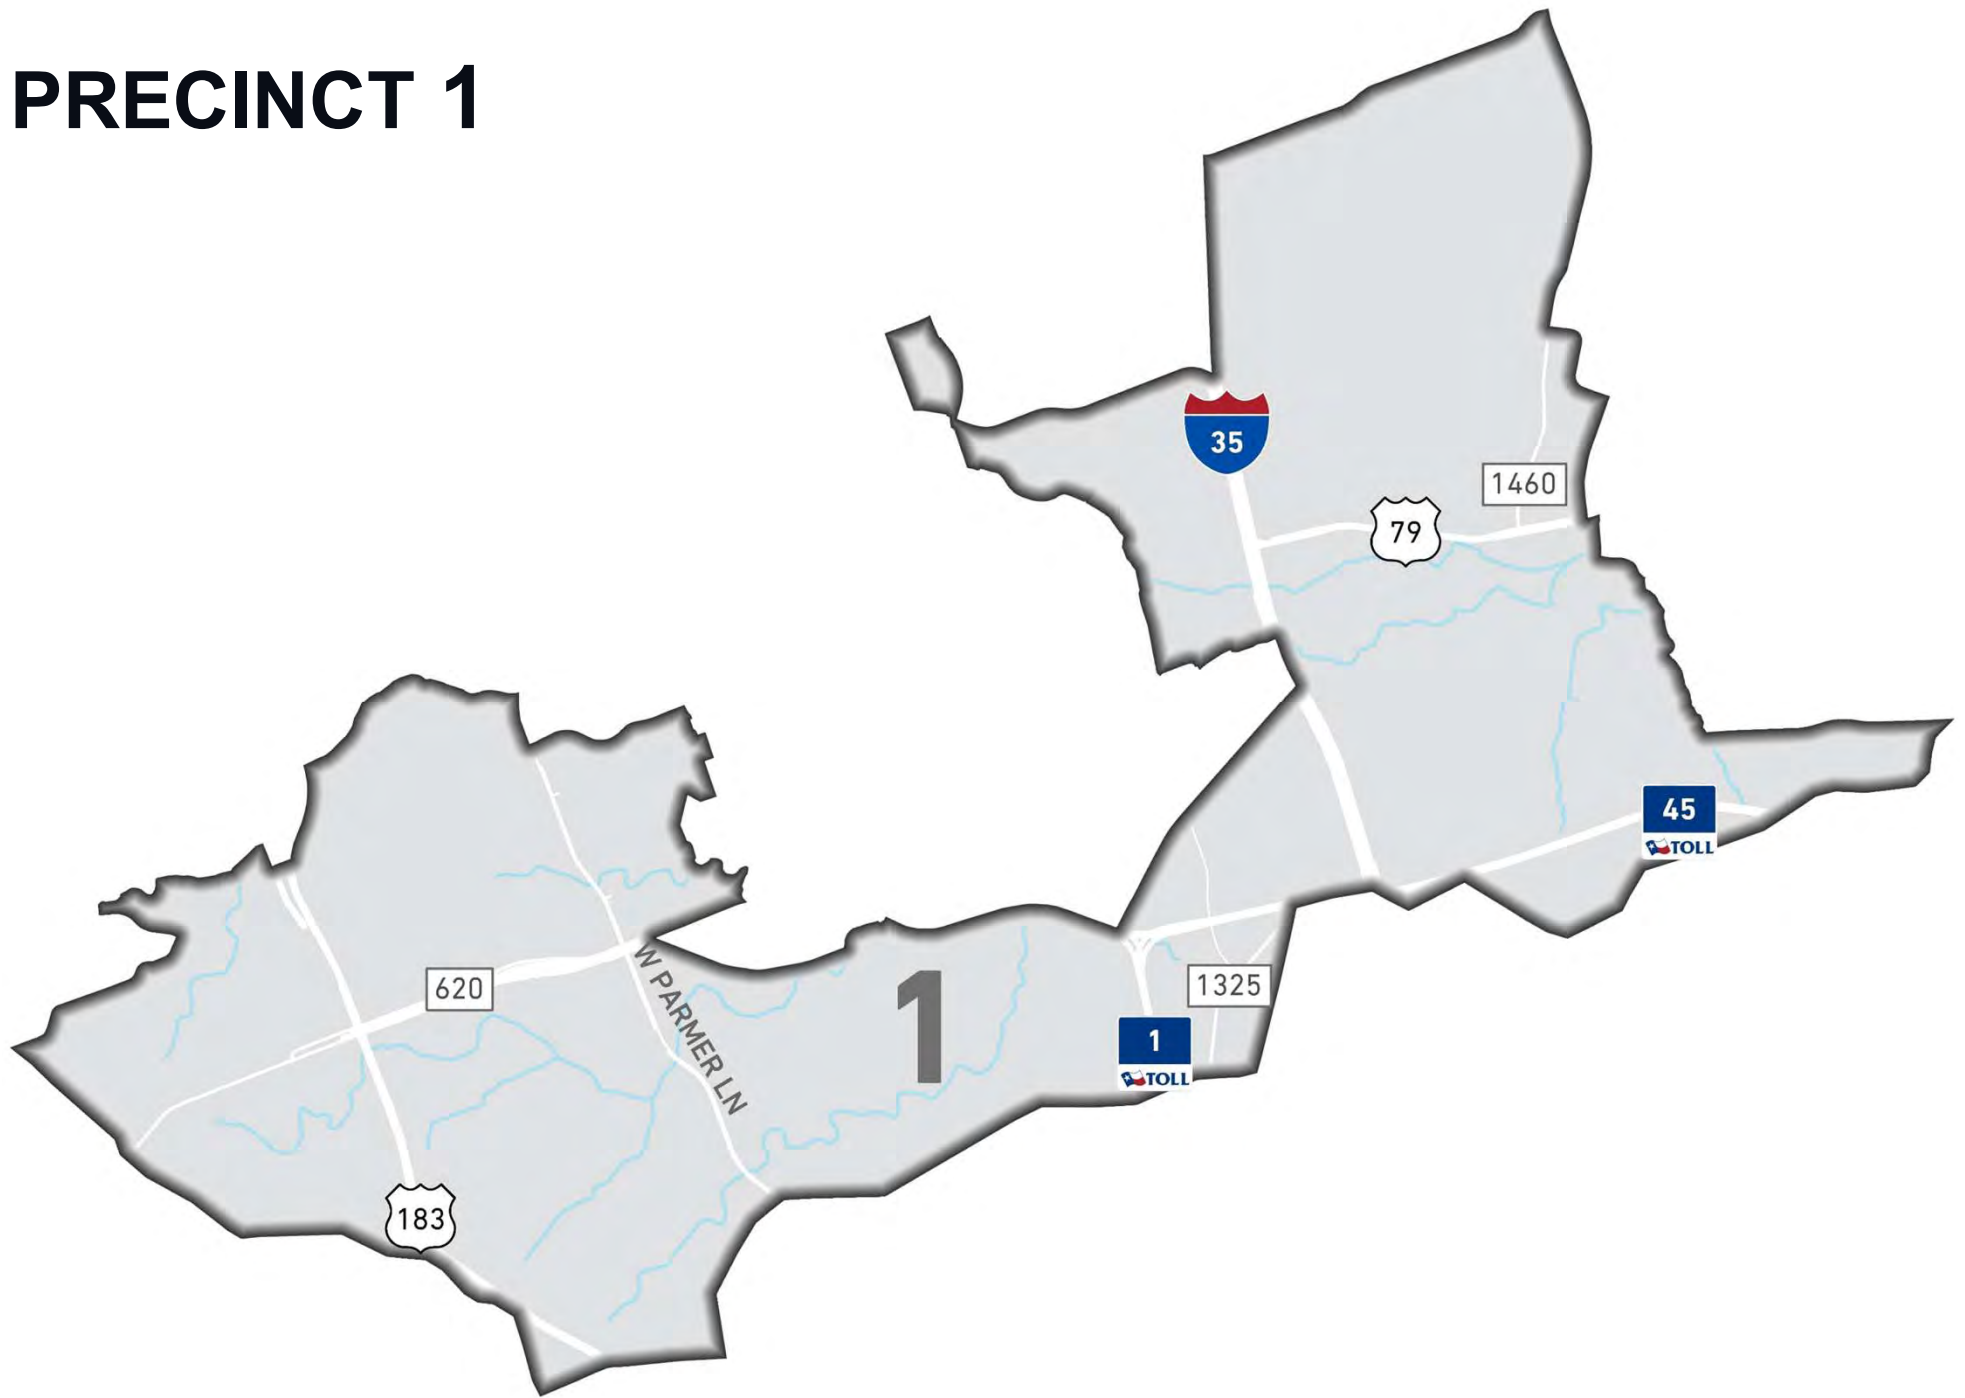

Projects under planning and  
design, no active  
construction projects.




# PRECINCT 2

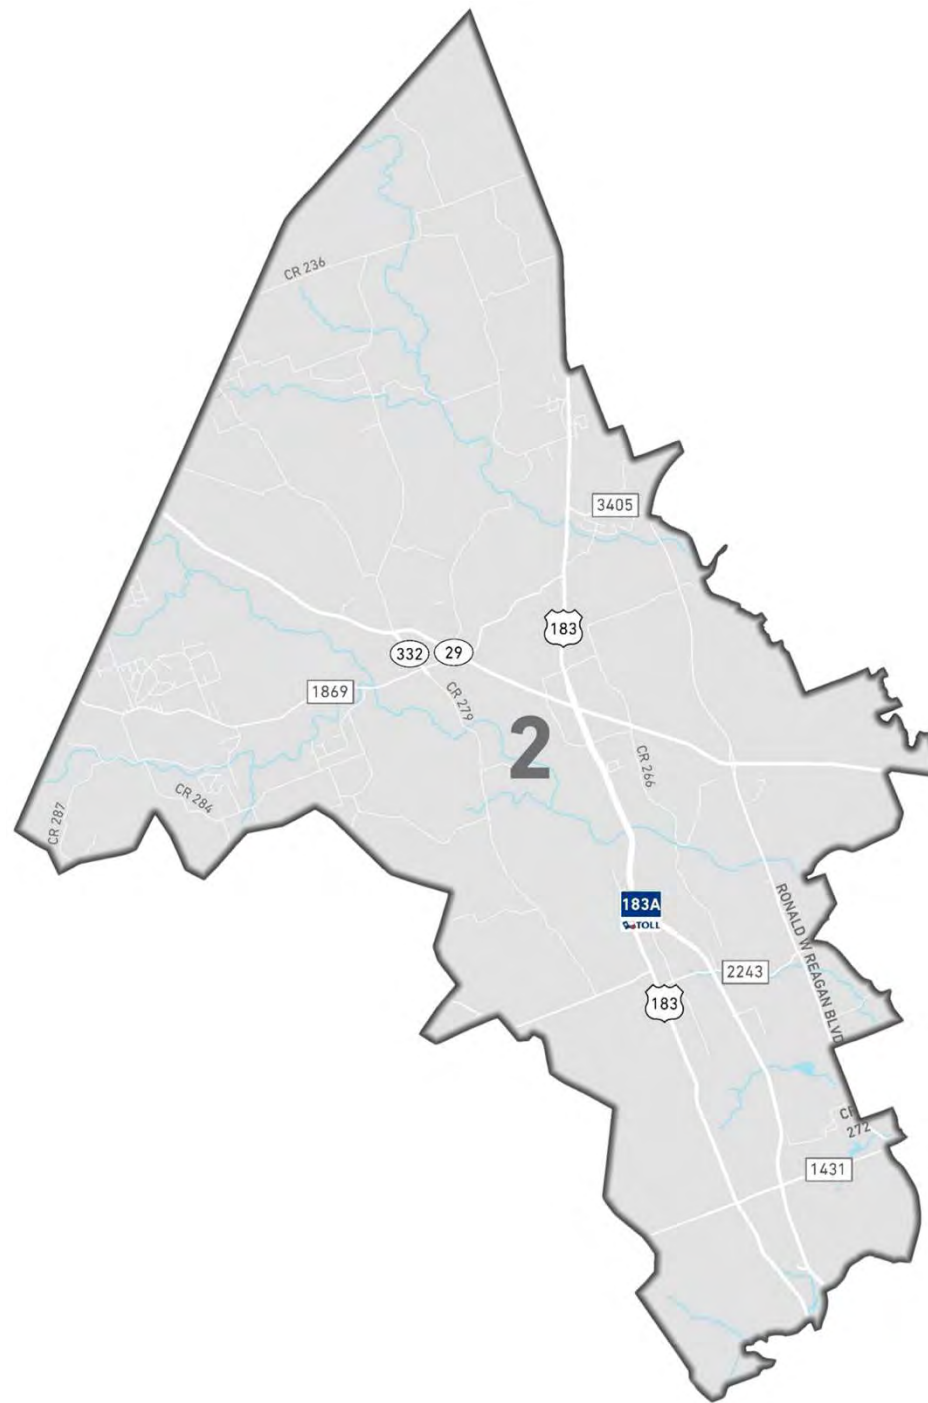



# Liberty Hill (SH 29) Bypass (RM 1869 to CR 279)

Anticipated Completion  
Late 2025

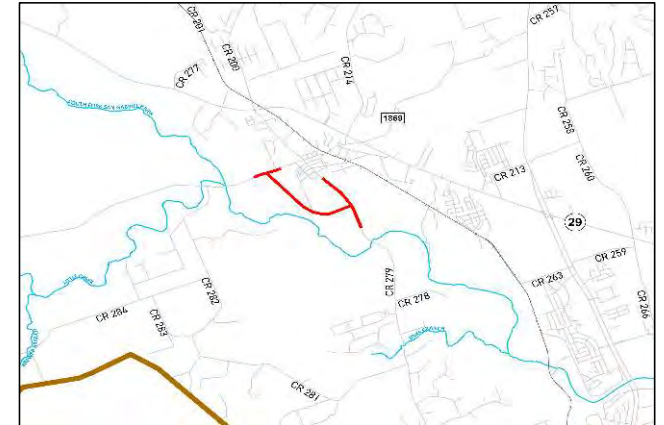

Original contract amount = \$14,149,449.00


Total change orders = \$295,362.00

Adjusted contract price = \$14,444,811.00

Expenditures to date = \$9,995,297.79 (69%)



# Liberty Hill (SH 29) Bypass (RM 1869 to CR 279)





# Liberty Hill (SH 29) Bypass (RM 1869 to CR 279)






# Liberty Hill (SH 29) Bypass (RM 1869 to CR 279)





# Ronald Reagan Widening (SH 29 to FM 3405)

Anticipated Completion  
Summer 2027

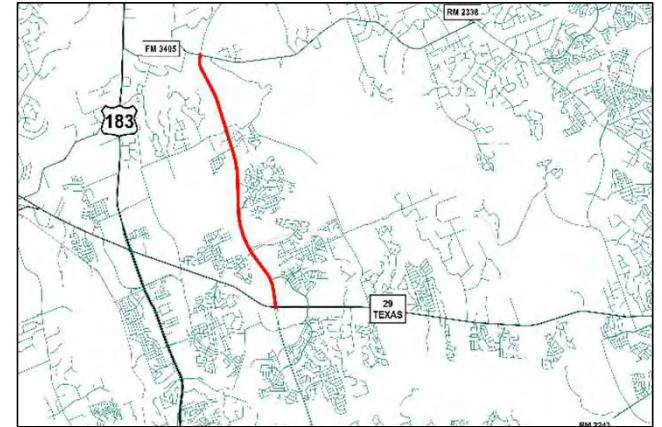

Original Contract Price = \$52,159,299.00

Total Change Orders to Date = \$294,302.50

Adjusted Contract Price = \$52,453,601.50

Expenditures to Date = \$14,438,113.56 (28%)



# Ronald Reagan Widening (SH 29 to FM 3405)





# Ronald Reagan Widening (SH 29 to FM 3405)






# Ronald Reagan Widening (SH 29 to FM 3405)






# PRECINCT 3



# Corridor H/Sam Bass Road (RM 1431 to Wyoming Springs Drive)

Anticipated Completion  
Fall 2025

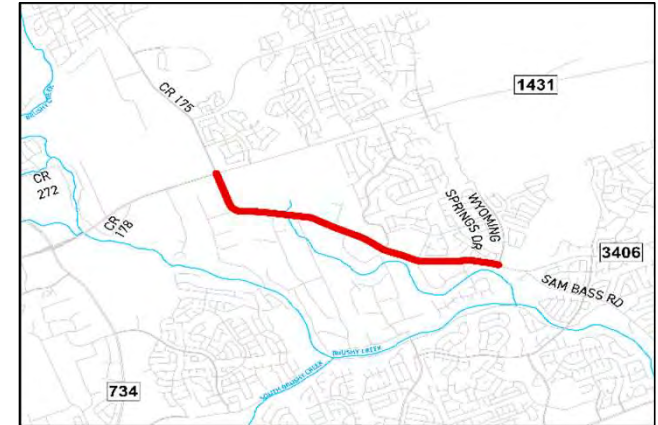

Original Contract Price = \$36,145,959.00

Total Change Orders to Date = -\$1,686,175.04


Adjusted Contract Price = \$34,459,783.96

Expenditures to Date = \$20,205,254.38 (59%)






# Corridor H/Sam Bass Road (RM 1431 to Wyoming Springs Drive)






# Corridor H/Sam Bass Road (RM 1431 to Wyoming Springs Drive)






# Corridor H/Sam Bass Road (RM 1431 to Wyoming Springs Drive)





# Wyoming Springs Extension (Brightwater Boulevard/Creek Bend to Sam Bass Road)

Anticipated Completion  
Late 2026

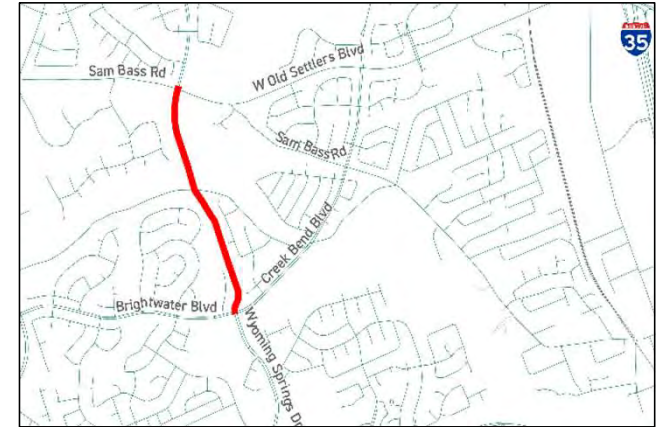


Partnership with the City of Round Rock

Original Contract Amount = \$25,917,630.47

Construction is managed by the City of Round Rock

# Wyoming Springs Extension (Brightwater Boulevard/Creek Bend to Sam Bass Road)





# Wyoming Springs Extension (Brightwater Boulevard/Creek Bend to Sam Bass Road)





# Wyoming Springs Extension (Brightwater Boulevard/Creek Bend to Sam Bass Road)





# CR 255

## (CR 254 to Ronald Reagan Boulevard)

Anticipated Completion  
Summer 2026



Original Contract Price = \$20,847,300.93

Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$20,847,300.93

Expenditures to Date = \$2,902,839.98 (14%)






# CR 255 (CR 254 to Ronald Reagan Boulevard)





# CR 255


## (CR 254 to Ronald Reagan Boulevard)






# CR 255

## (CR 254 to Ronald Reagan Boulevard)






# PRECINCT 4

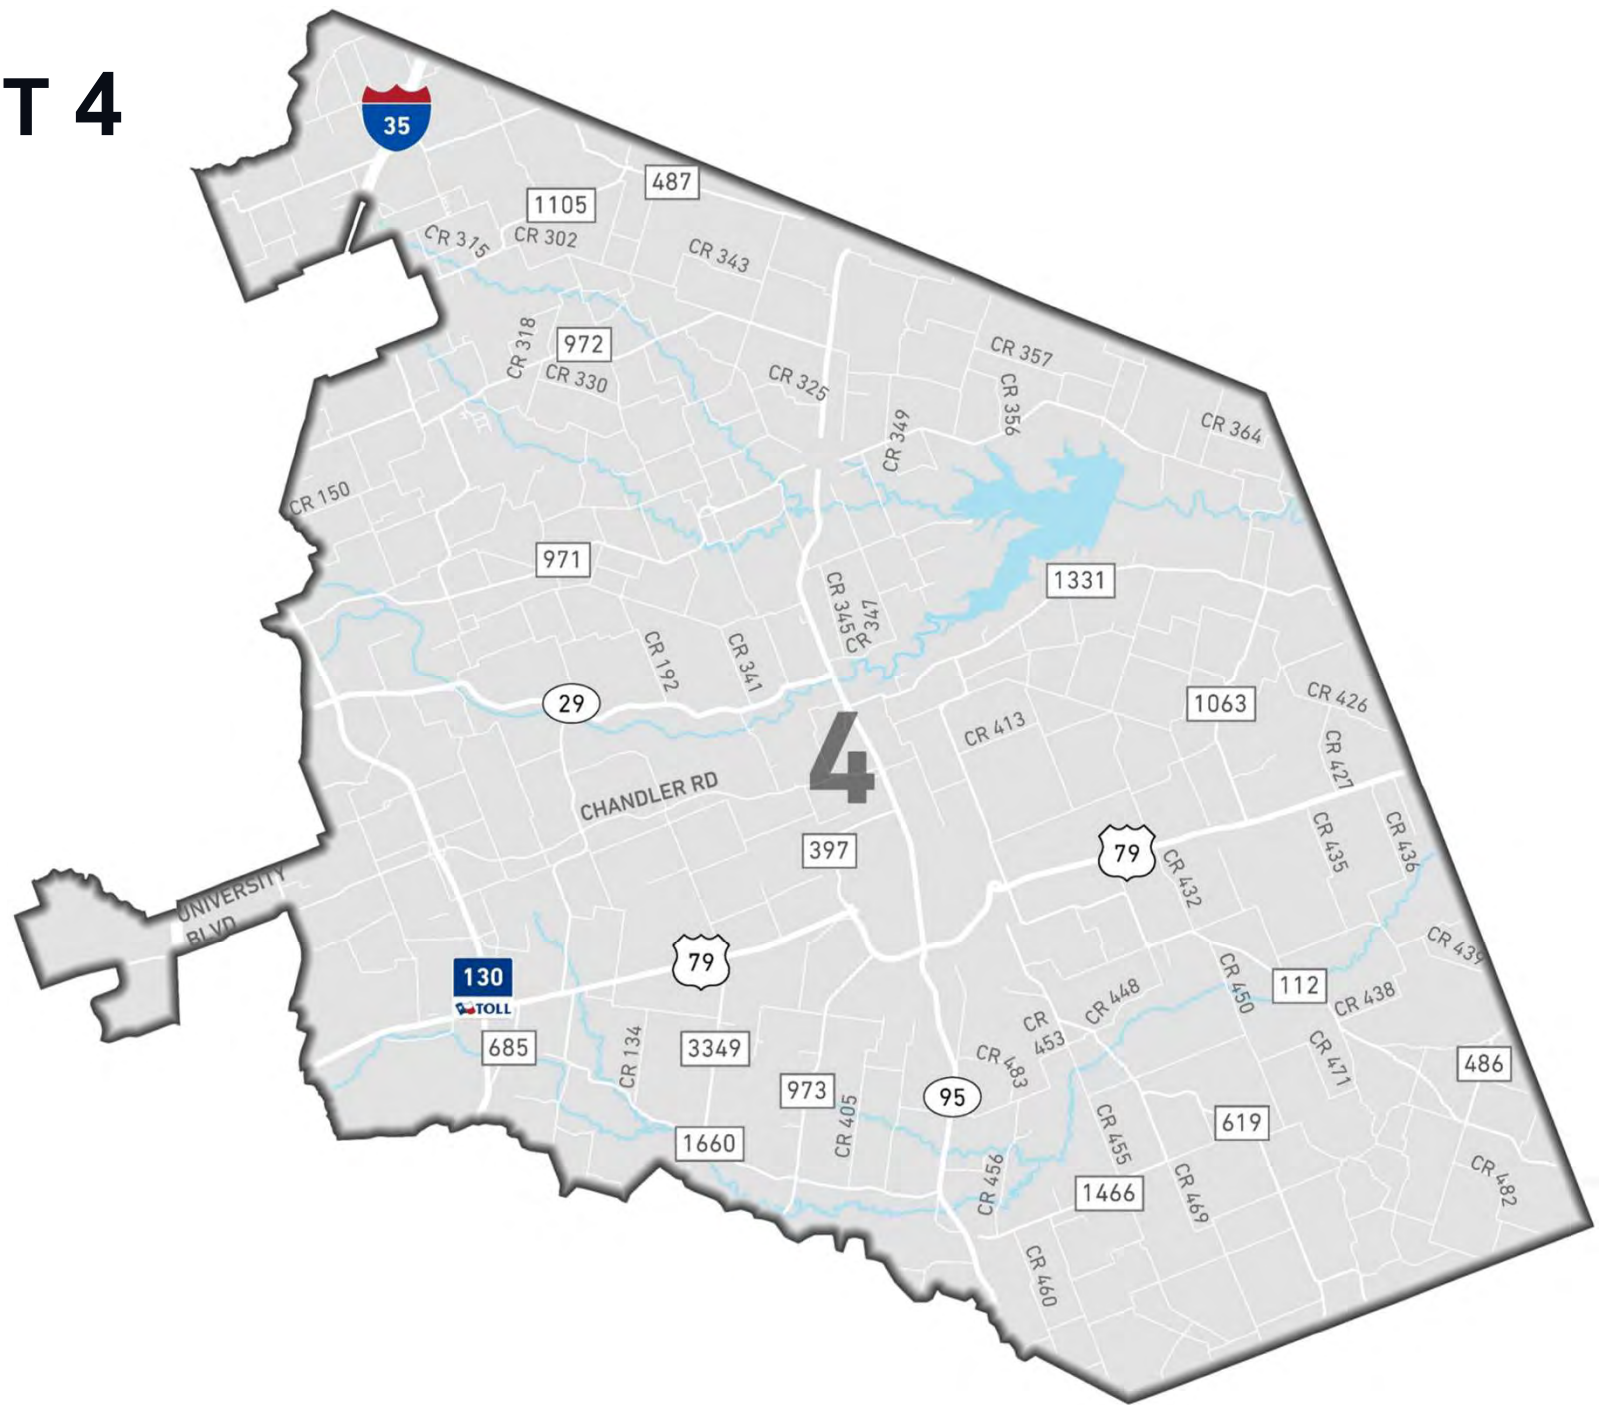



# East Wilco Highway (FM 3349/US 79 Interchange) (US 79 to CR 404)

Anticipated Completion  
Summer 2025 (Roadwork)

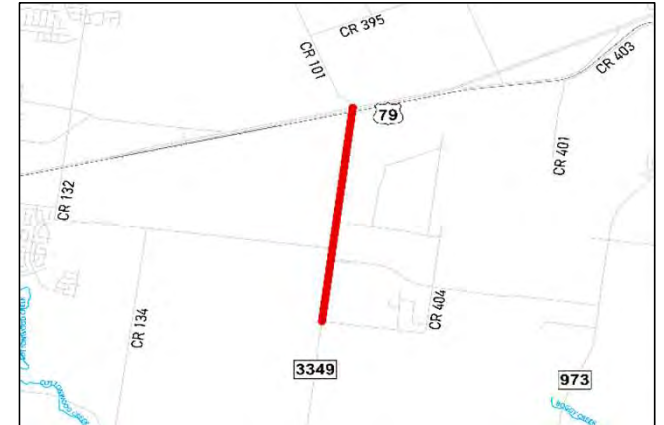

Original Contract Amount = \$81,941,038.13

Total Change Orders = \$2,335,980.09


Adjusted Contract Price = \$84,277,018.22

Expenditures to Date = \$65,825,780.86 (78%)





# East Wilco Highway (FM 3349/US 79 Interchange) (US 79 to CR 404)





# East Wilco Highway (FM 3349/US 79 Interchange) (US 79 to CR 404)






# East Wilco Highway (FM 3349/US 79 Interchange) (US 79 to CR 404)





# East Wilco Highway - Segment 2 (CR 137 South of Hutto to CR 404)

Anticipated Completion  
Summer 2028

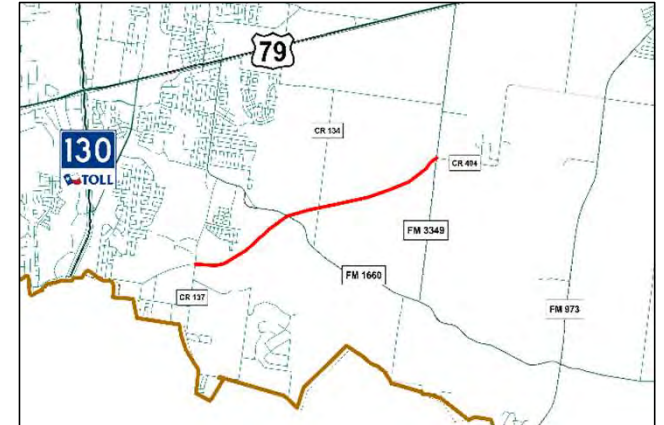

Original contract amount = \$64,407,606.63

Total change orders = \$0.00

Adjusted contract price = \$64,407,606.63

Expenditures to date = \$18,223,155.68 (28%)





# East Wilco Highway - Segment 2 (CR 137 South of Hutto and CR 404)





# East Wilco Highway - Segment 2 (CR 137 South of Hutto and CR 404)






# East Wilco Highway - Segment 2 (CR 137 South of Hutto and CR 404)





# Bud Stockton Extension (Traffic Signal at FM 487)

Substantially Complete  
March 2025

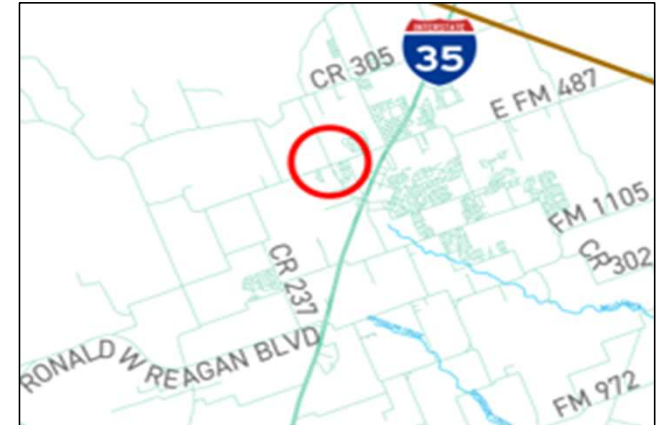

Original Contract Amount = \$553,983.00

Total Change Orders = \$0.00

Adjusted Contract Price = \$553,983.00

Expenditures to Date = \$423,854.00 (77%)





# Bud Stockton Extension (Traffic Signal at FM 487)





# Bud Stockton Extension (Traffic Signal at FM 487)






# Bud Stockton Extension (Traffic Signal at FM 487)





# Old Settlers Boulevard (North Red Bud Lane/CR 122 to CR 110)

Anticipated Completion  
Fall 2025

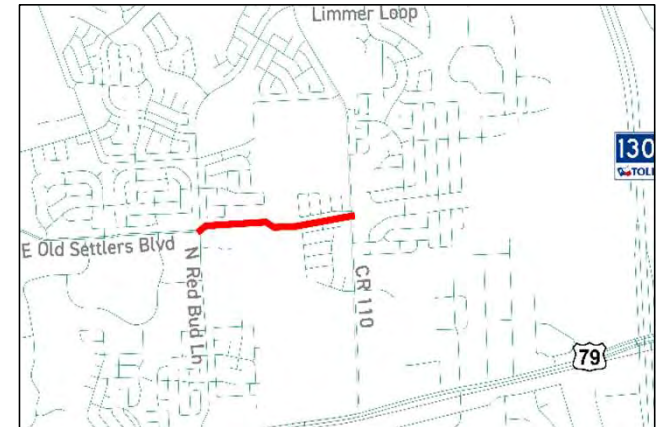

Partnership with the City of Round Rock


Original Contract Amount = \$14,920,847.10

Construction is managed by the City of Round Rock





# Old Settlers Boulevard (North Red Bud Lane/CR 122 to CR 110)






# Old Settlers Boulevard (North Red Bud Lane/CR 122 to CR 110)






# Old Settlers Boulevard (North Red Bud Lane/CR 122 to CR 110)

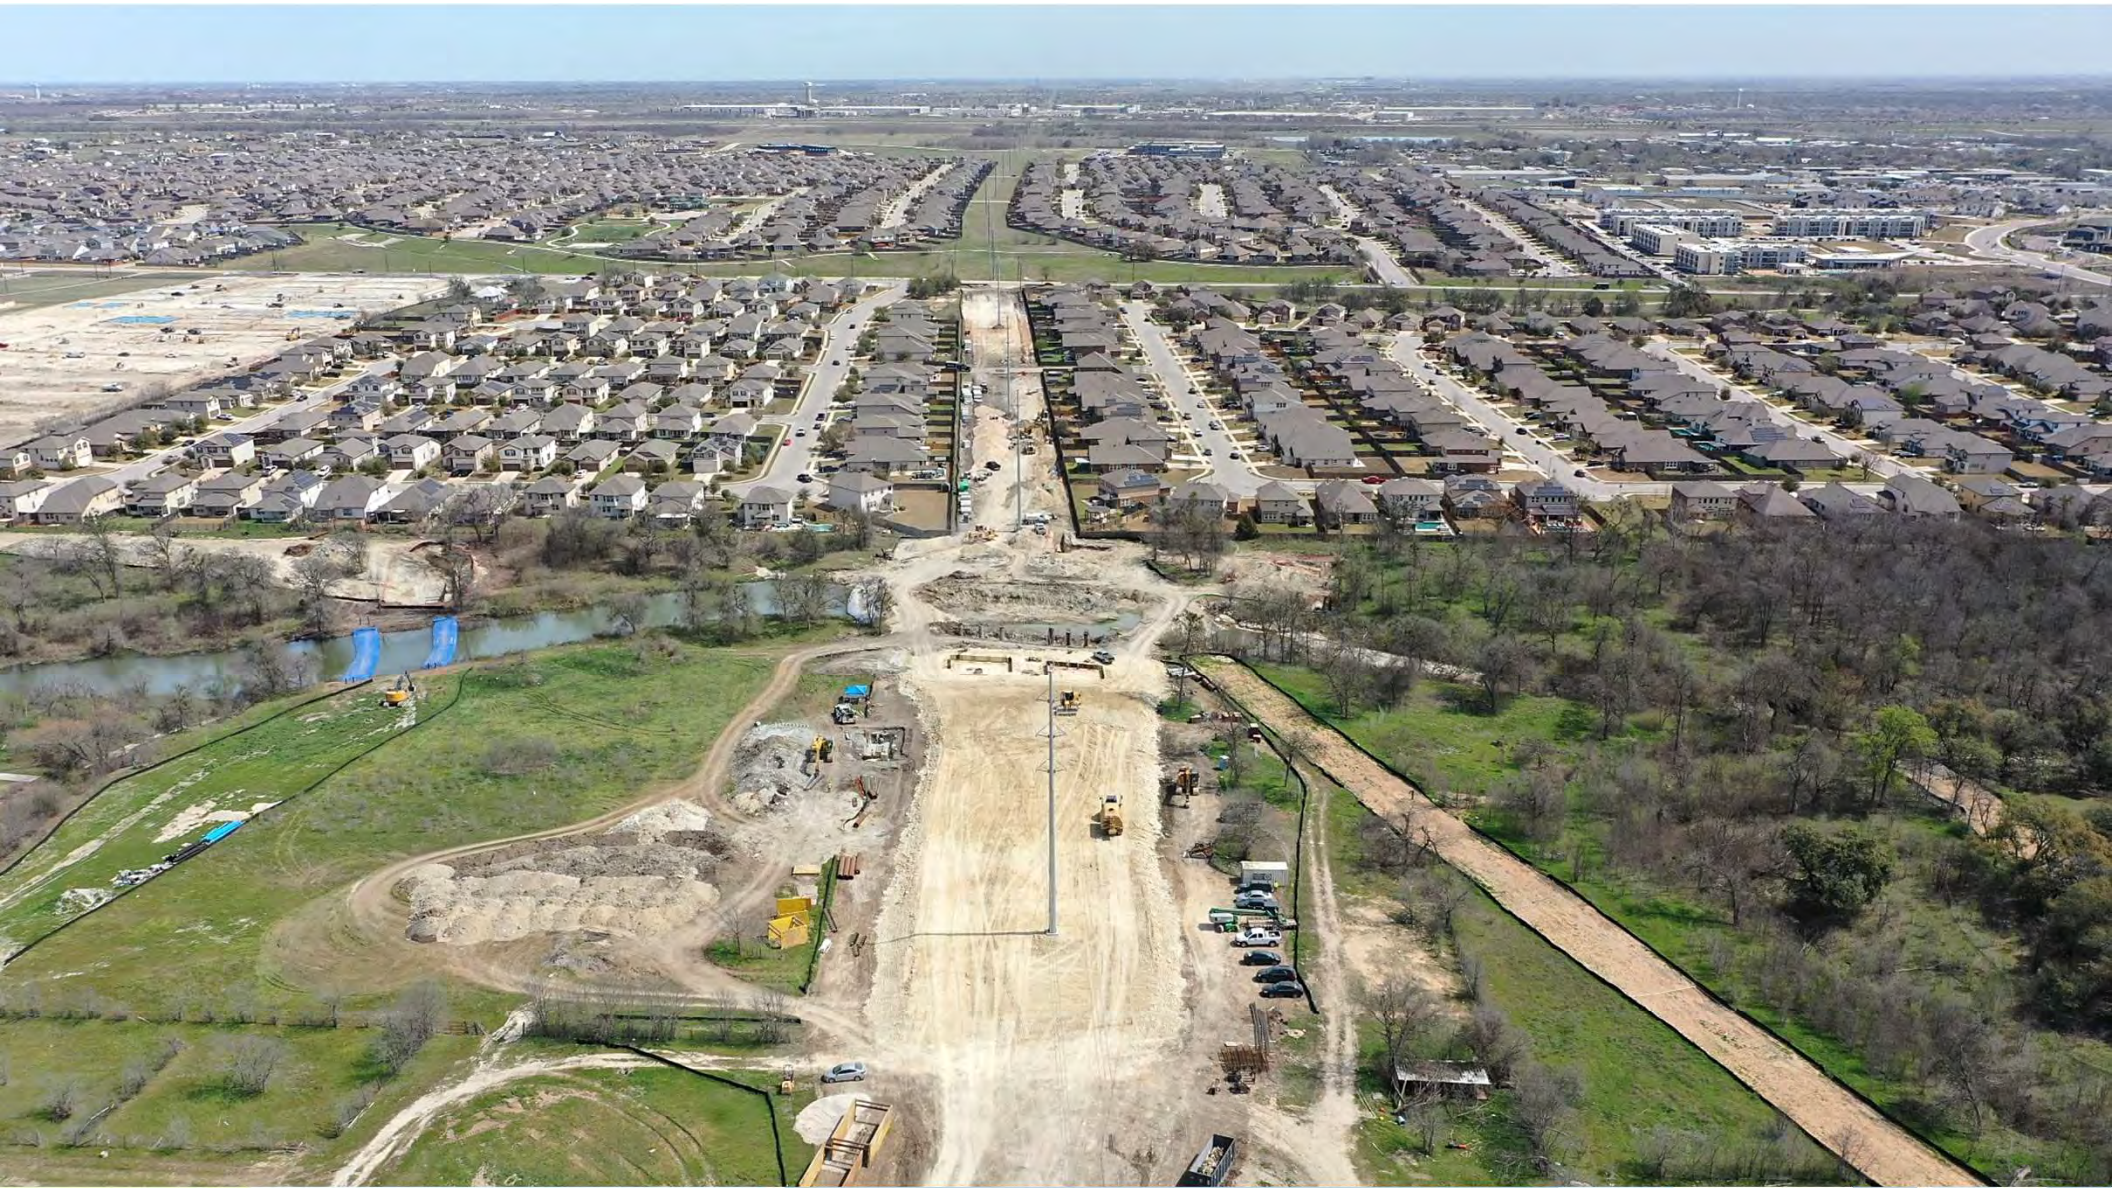



# CR 112 Widening (FM 1460/A.W. Grimes to CR 117)

Anticipated Completion  
Late 2026

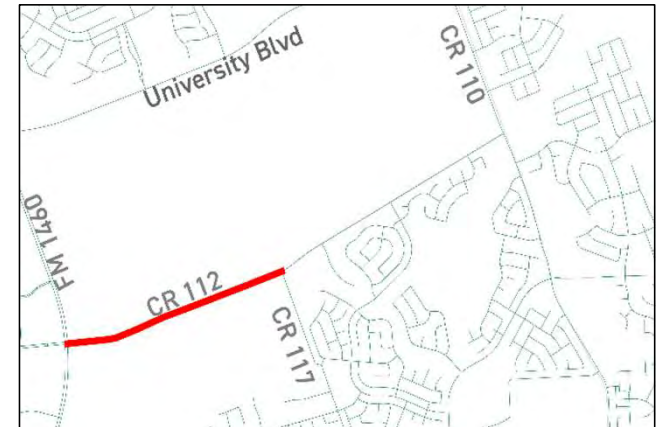

Partnership with the City of Round Rock

Original Contract Amount = \$13,119,712.35

Construction is managed by the City of Round Rock





# CR 112 Widening (FM 1460/A.W. Grimes to CR 117)





# CR 112 Widening (FM 1460/A.W. Grimes to CR 117)






# CR 112 Widening (FM 1460/A.W. Grimes to CR 117)





# CR 112 Widening (CR 117 to CR 110)

Anticipated Completion  
Late 2026

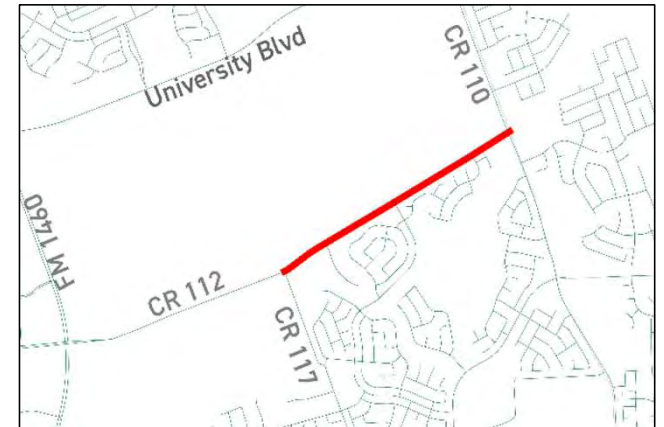

Partnership with the City of Round Rock

Original Contract Amount = \$20,434,128.40

Construction is managed by the City of Round Rock





# CR 112 Widening (CR 117 to CR 110)

