


Projects under planning and design, no active construction projects.




PRECINCT 2



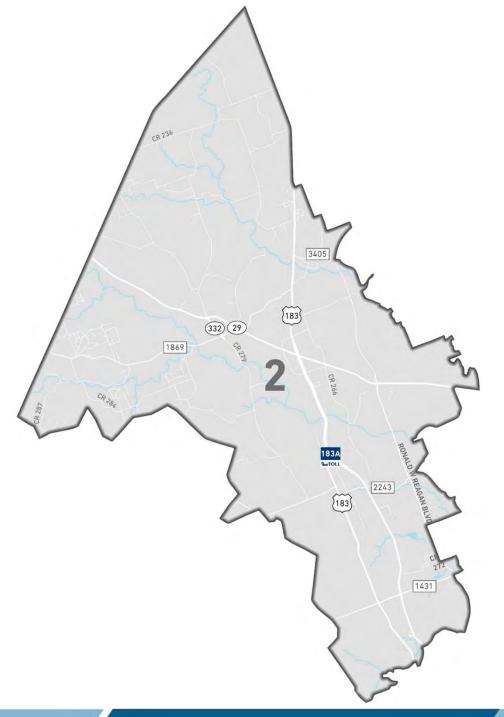

Liberty Hill (SH 29) Bypass (RM 1869 to CR 279)

Anticipated Completion Late 2025

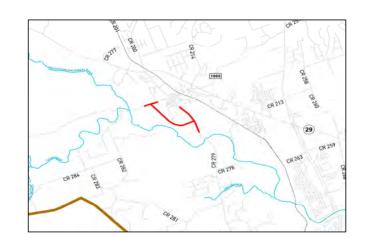

Original contract amount = \$14,149,449.00

Total change orders = \$295,362.00

Adjusted contract price = \$14,444,811.00


Expenditures to date = \$10,677,813.03 (74%)




Liberty Hill (SH 29) Bypass (RM 1869 to CR 279)



Liberty Hill (SH 29) Bypass (RM 1869 to CR 279)

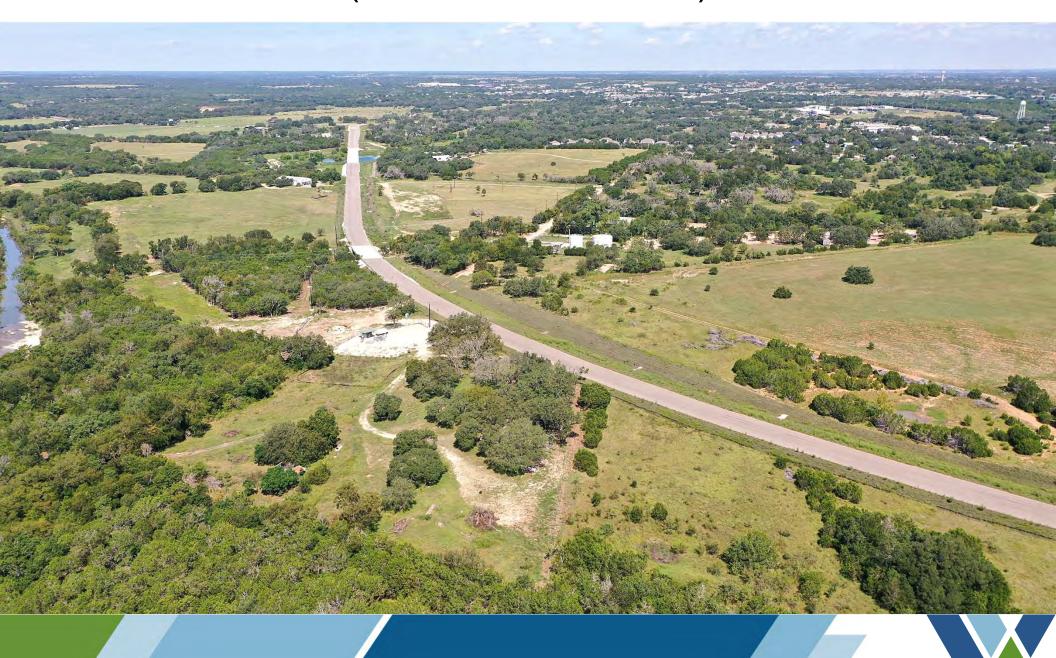

Anticipated Completion Summer 2027



Original Contract Price = \$52,159,299.00

Total Change Orders to Date = \$310,563.50

Adjusted Contract Price = \$52,469,862.50

Expenditures to Date = \$25,146,843.32 (48%)











PRECINCT 3

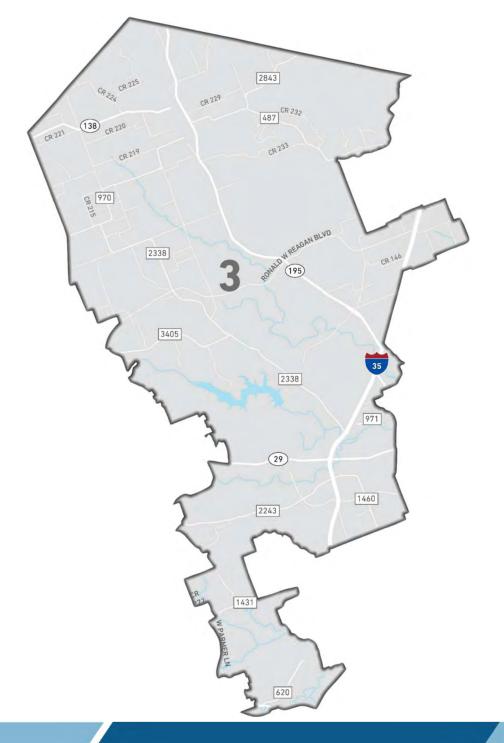



Anticipated Completion Early 2026




Original Contract Price = \$36,145,959.00

Total Change Orders to Date = -\$1,659,570.56

Adjusted Contract Price = \$34,486,388.44

Expenditures to Date = \$25,655,224.80 (74%)




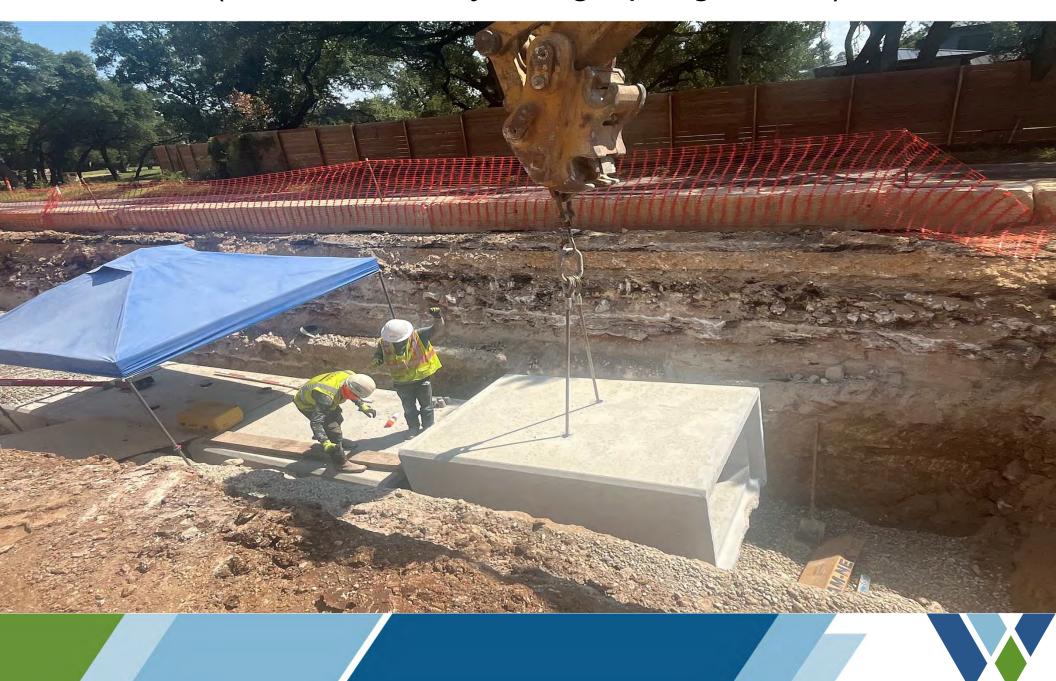





Anticipated Completion Late 2026




Partnership with the City of Round Rock

Original Contract Amount = \$25,917,630.47

Construction is managed by the City of Round Rock




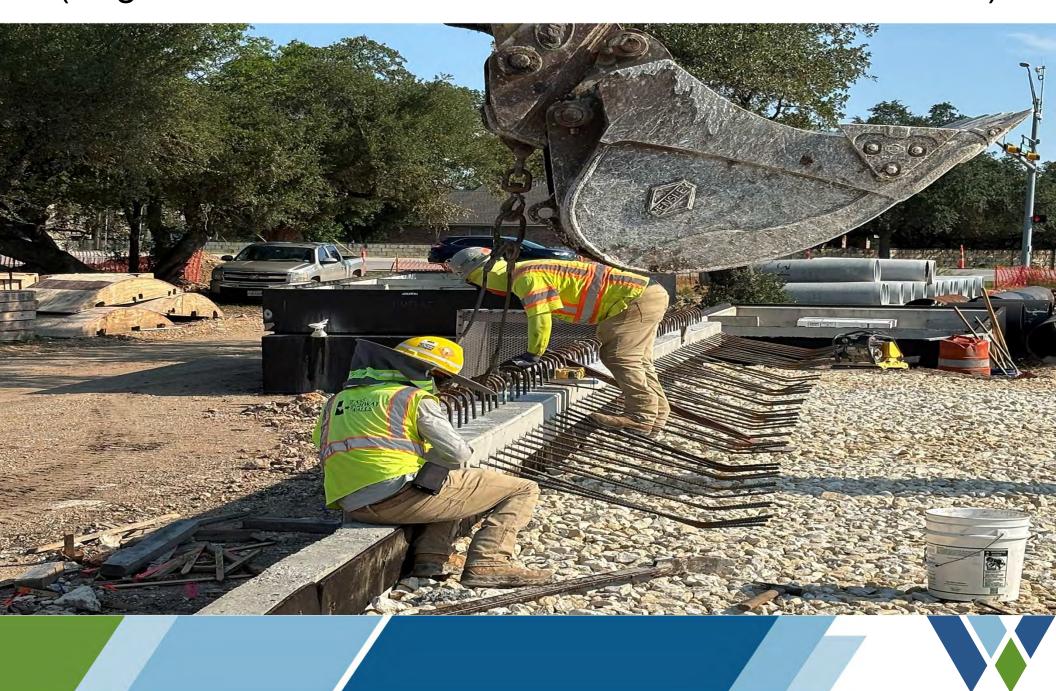





Anticipated Completion Summer 2026



Original Contract Price = \$20,847,300.93

Total Change Orders to Date = -\$13,235.52


Adjusted Contract Price = \$20,834,065.41

Expenditures to Date = \$10,152,349.86 (49%)








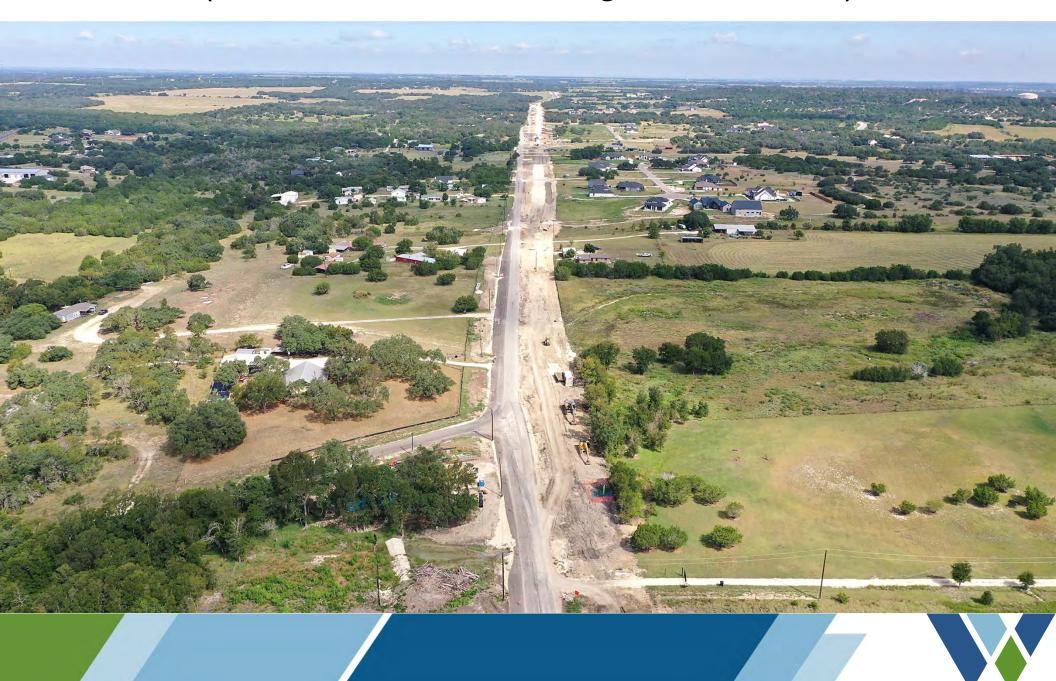

Anticipated Completion Early 2026





Original Contract Price = \$2,706,129.45


Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$2,706,129.45

Expenditures to Date = \$193,535.97 (7%)

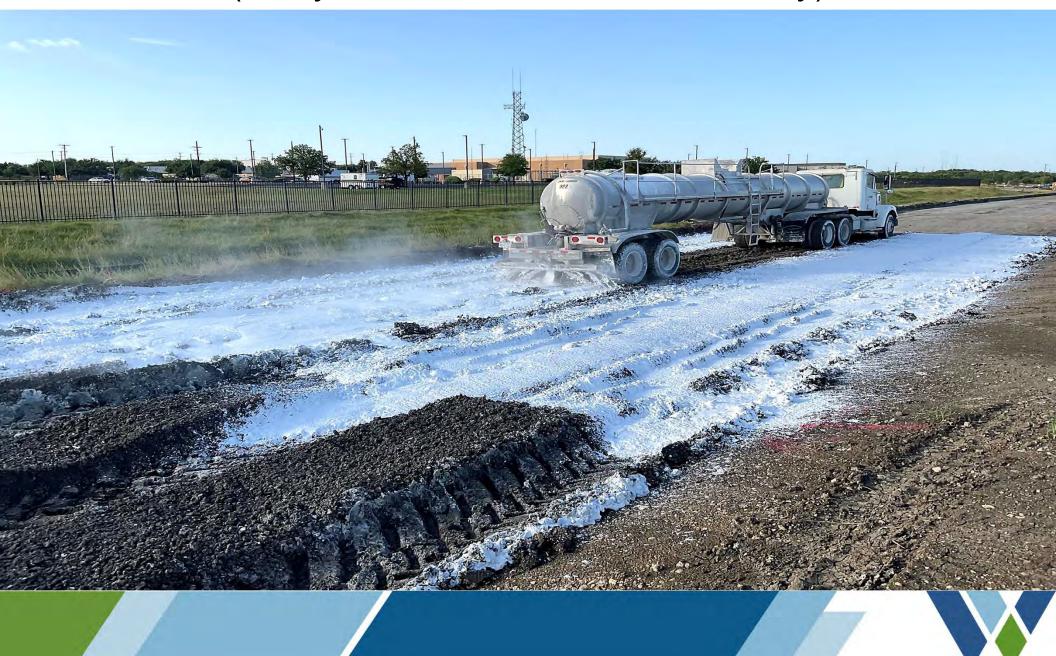


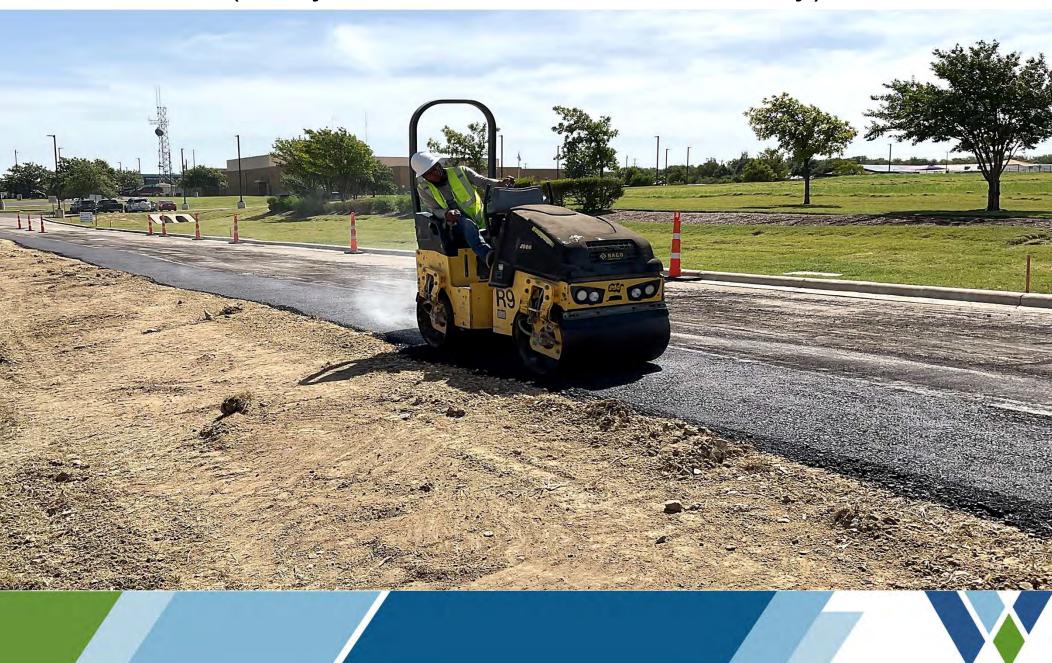

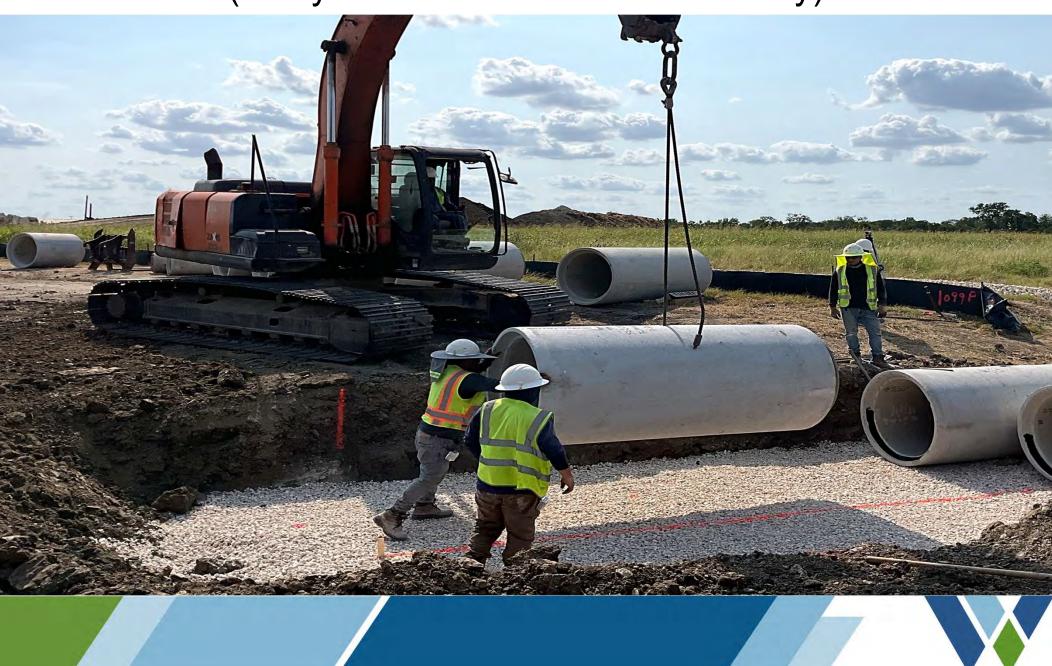

SH 195 at Ronald Reagan Boulevard (Single Ramp at Ronald Reagan Boulevard)

Anticipated Completion Summer 2026



Original Contract Price = \$3,608,141.00

Total Change Orders to Date = \$0.00


Adjusted Contract Price = \$3,608,141.00

Expenditures to Date = \$0.00 (0%)




SH 195 at Ronald Reagan Boulevard (Single Ramp at Ronald Reagan Boulevard)



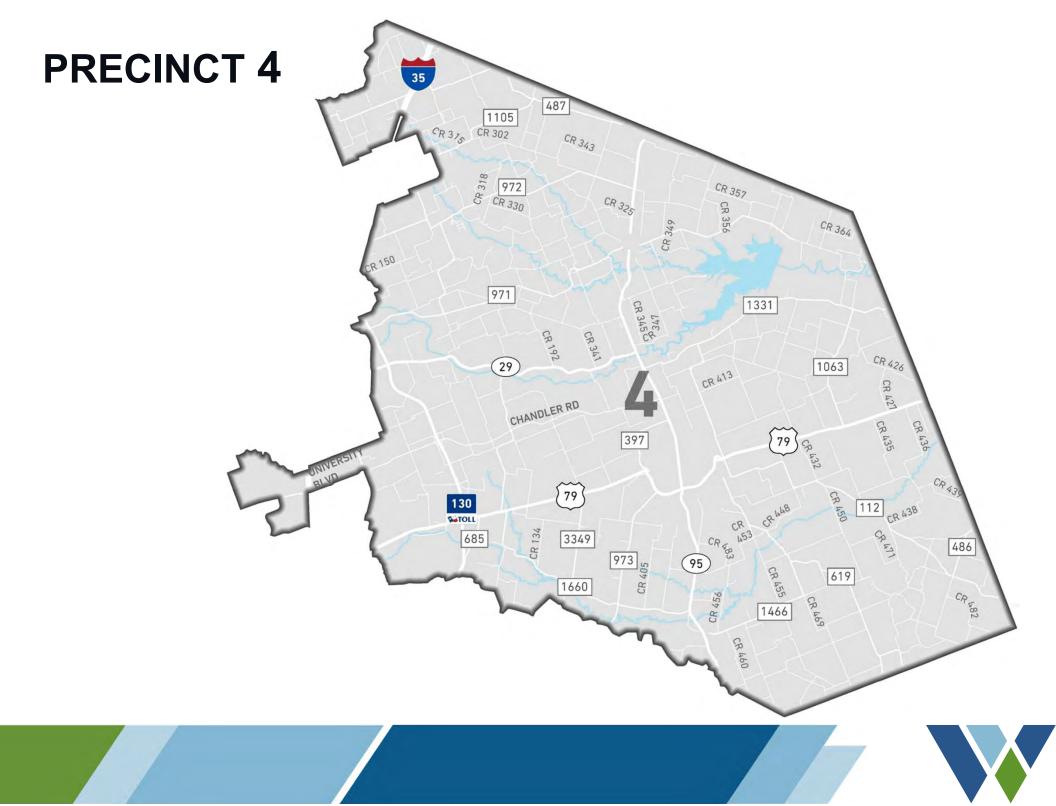

Substantially Complete June 2025 (Roadwork) Anticipated Completion Spring 2027 (Rail Relocation)



Original Contract Amount = \$81,941,038.13


Total Change Orders = \$3,631,637.67

Adjusted Contract Price = \$85,572,675.80

Expenditures to Date = \$73,312,385.47 (86%)






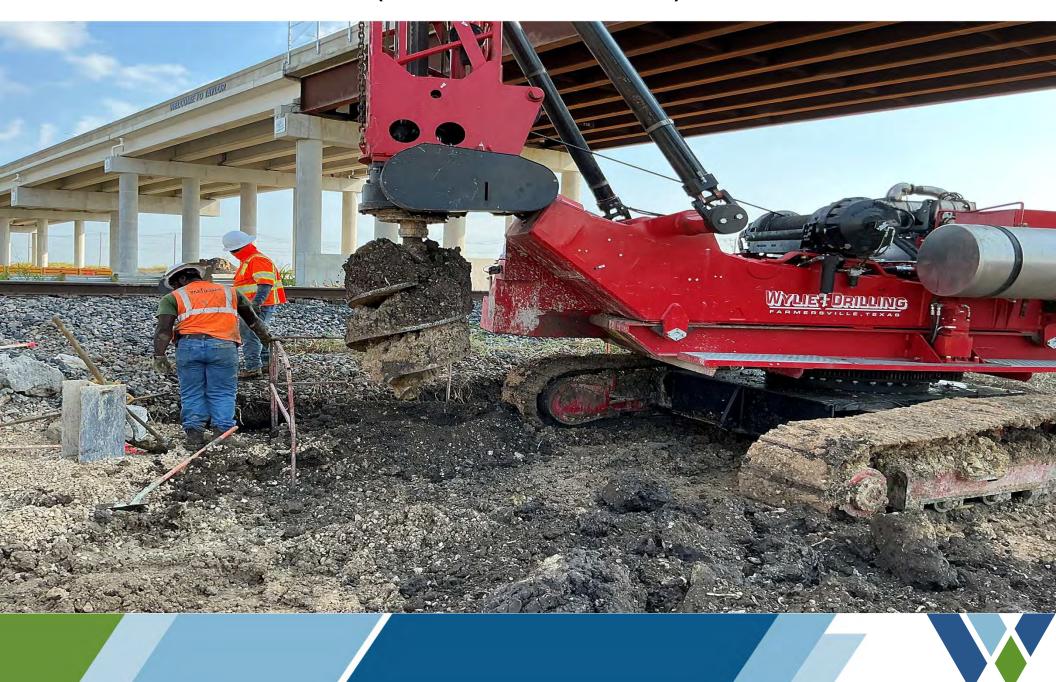



East Wilco Highway - Segment 2 (CR 137 South of Hutto to CR 404)

Anticipated Completion Summer 2028



Original contract amount = \$64,407,606.63


Total change orders = -\$1,907,404.64

Adjusted contract price = \$62,500,201.99

Expenditures to date = \$37,124,554.48 (59%)




East Wilco Highway - Segment 2 (CR 137 South of Hutto and CR 404)

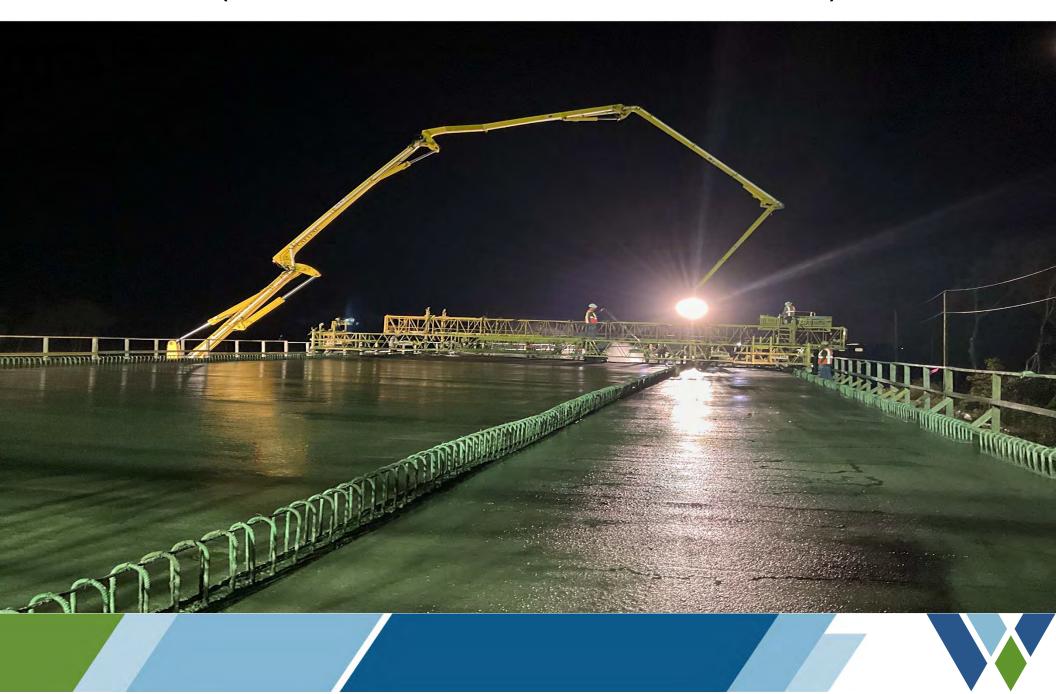


East Wilco Highway - Segment 2 (CR 137 South of Hutto and CR 404)



East Wilco Highway - Segment 2 (CR 137 South of Hutto and CR 404)

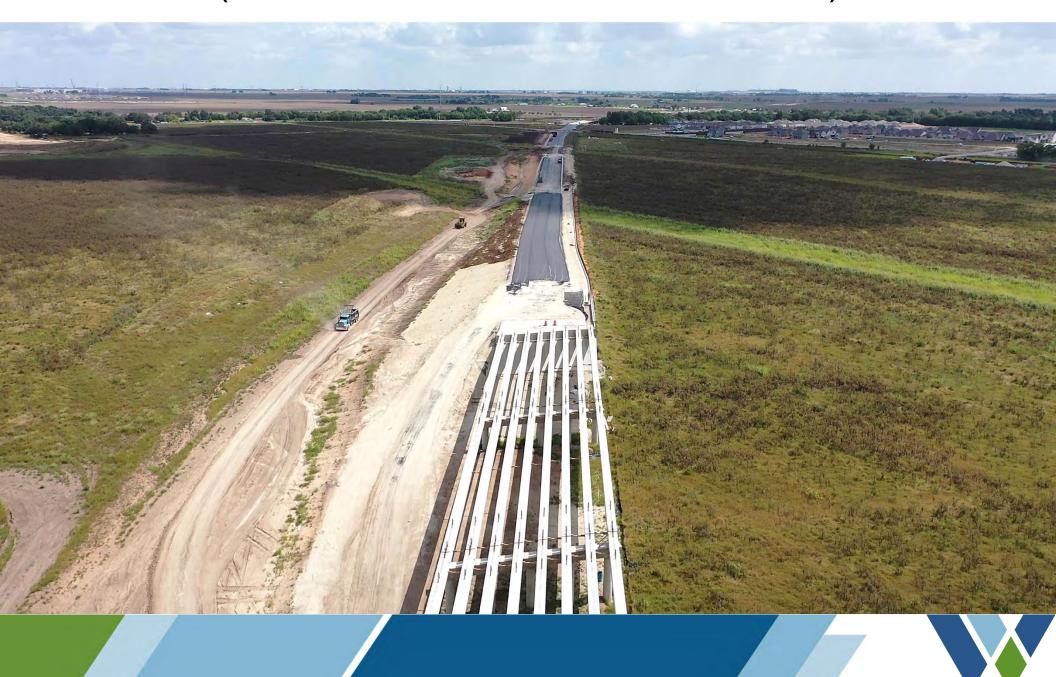

Anticipated Completion Fall 2025




Partnership with the City of Round Rock

Original Contract Amount = \$14,920,847.10

Construction is managed by the City of Round Rock



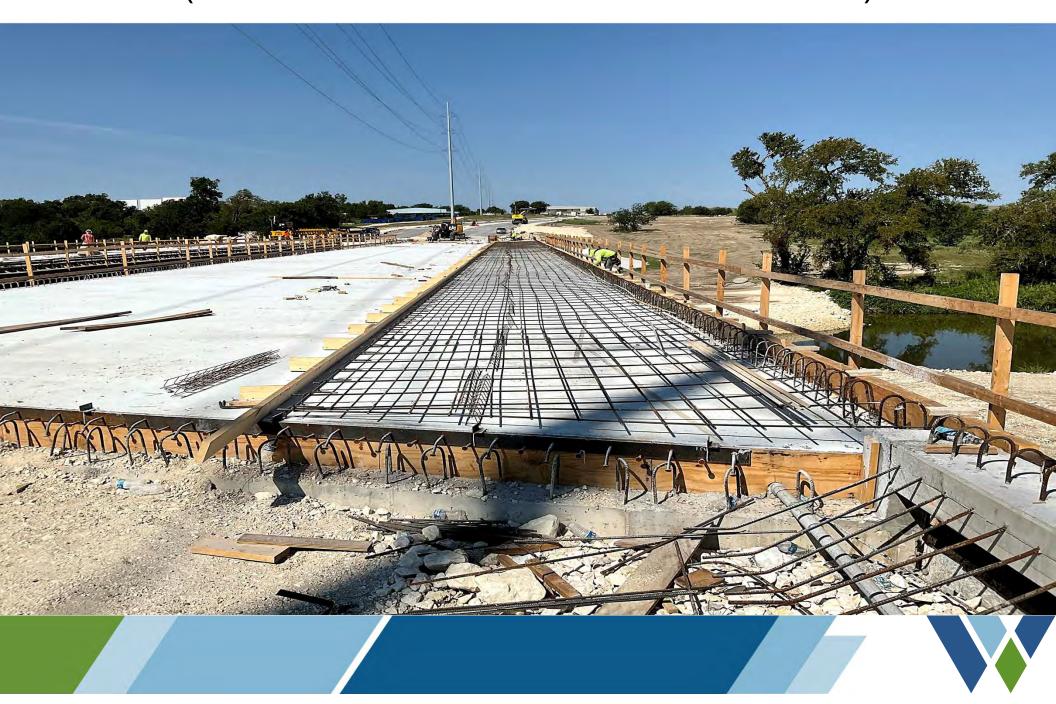






CR 112 Widening (FM 1460/A.W. Grimes to CR 117)

Anticipated Completion Late 2026




Partnership with the City of Round Rock

Original Contract Amount = \$13,119,712.35


Construction is managed by the City of Round Rock



CR 112 Widening (FM 1460/A.W. Grimes to CR 117)

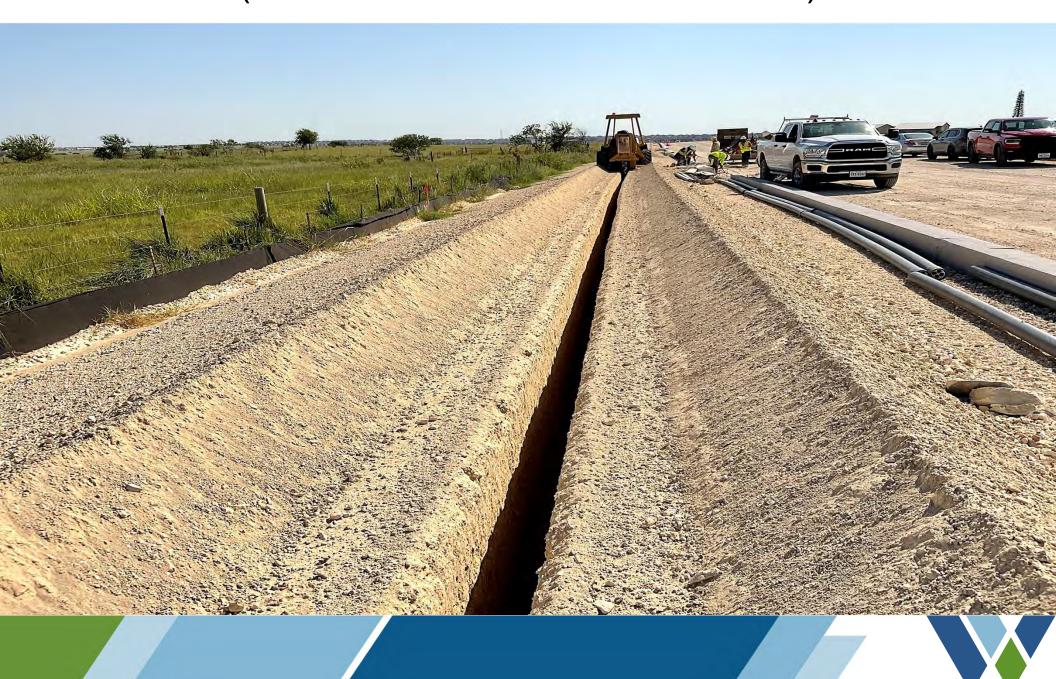

CR 112 Widening (FM 1460/A.W. Grimes to CR 117)

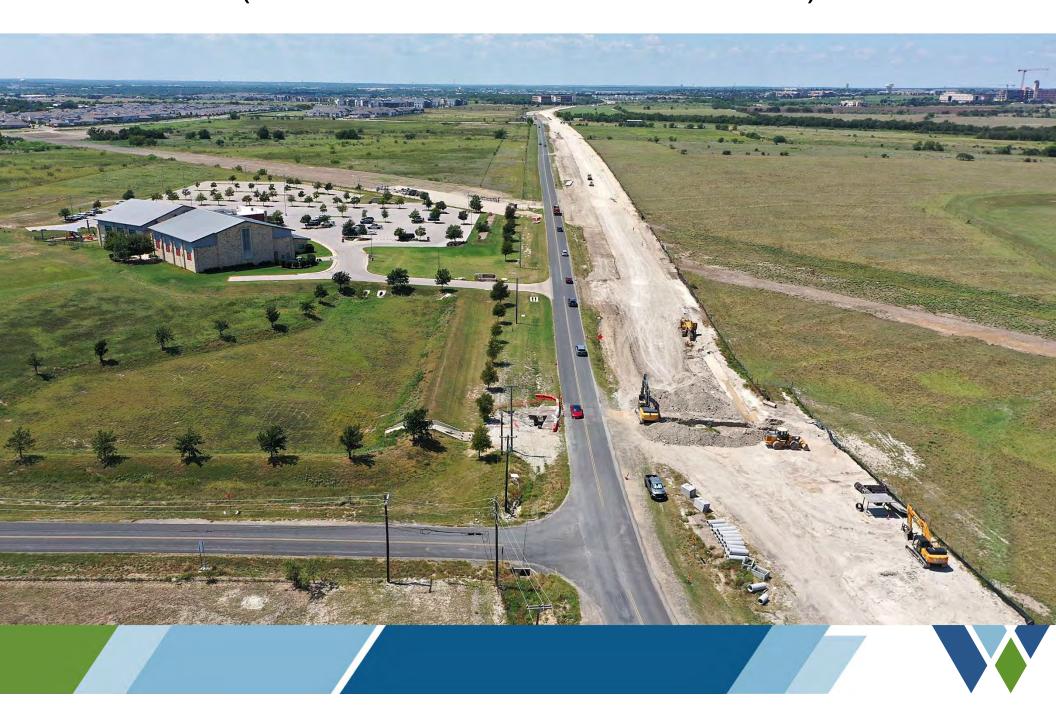

CR 112 Widening (CR 117 to CR 110)

Anticipated Completion Late 2026



Partnership with the City of Round Rock

Original Contract Amount = \$20,434,128.40

Construction is managed by the City of Round Rock



CR 112 Widening (CR 117 to CR 110)




CR 112 Widening (CR 117 to CR 110)



FM 971 (Future Granger High School Turn Lanes)

Anticipated Completion Early 2026



Original Contract Price = \$1,161,629.00

Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$1,161,629.00

Expenditures to Date = \$0.00 (0%)




FM 971 (Future Granger High School Turn Lanes)



FM 971 (Future Granger High School Turn Lanes)



FM 971 (Future Granger High School Turn Lanes)

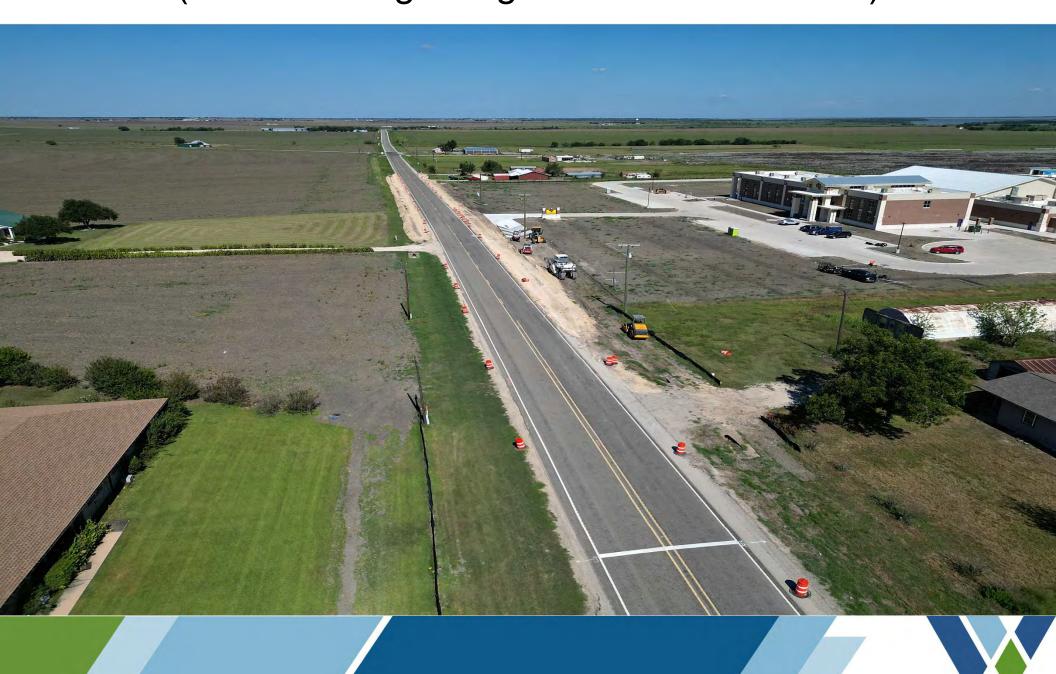

Anticipated Completion Late 2025



Original Contract Price = \$566,829.31

Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$566,829.31

Expenditures to Date = \$51,271.88 (9%)





