




WILLIAMSON COUNTY COMMISSIONERS COURT

ROAD BOND PROGRAM
December 16, 2025


PRECINCT 1

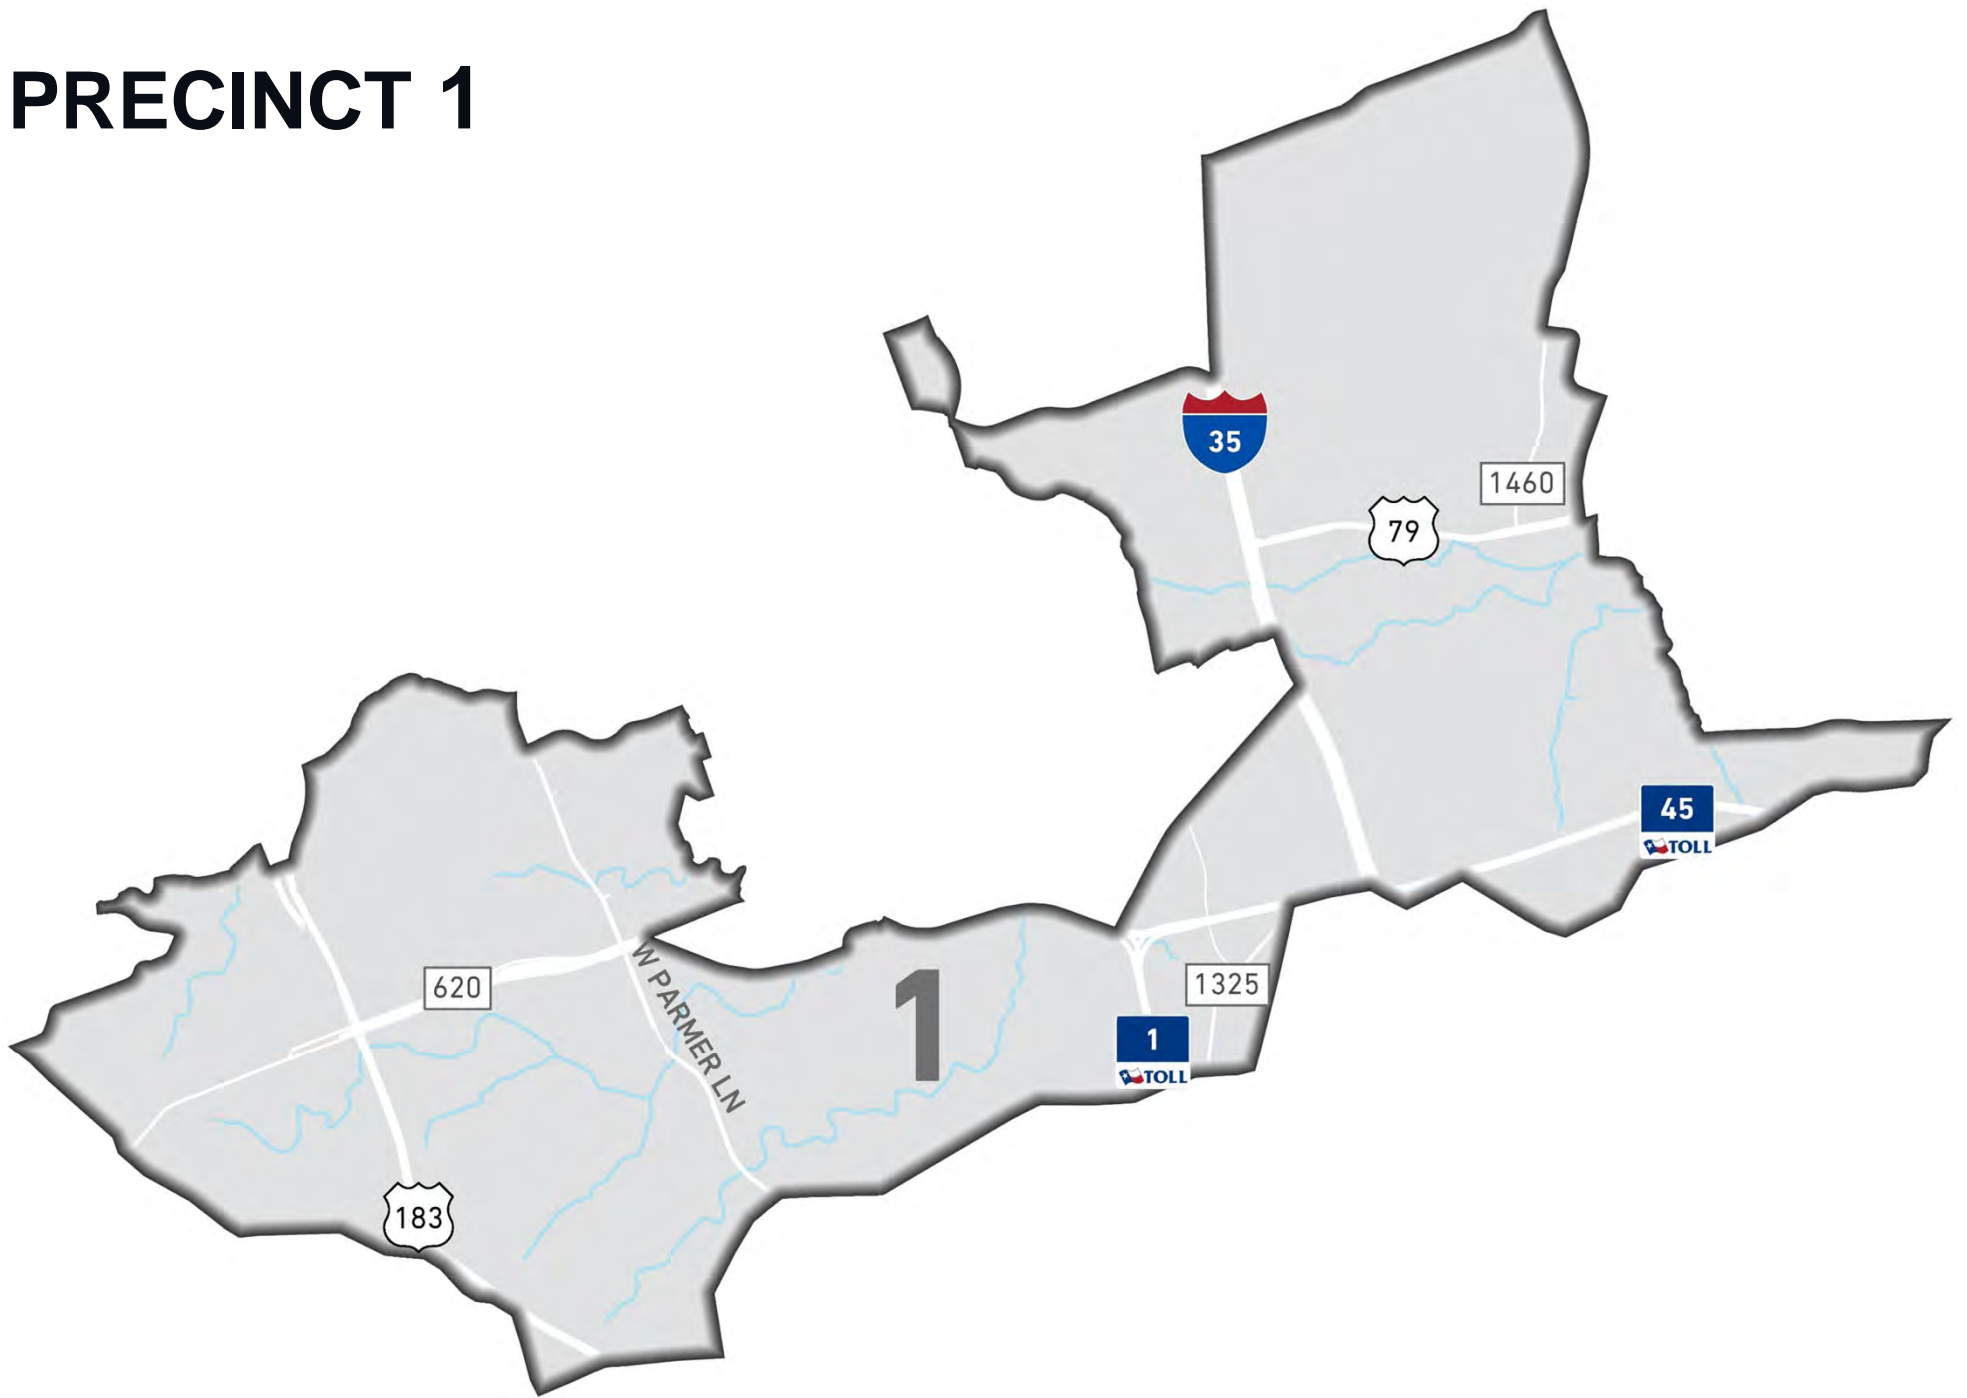

Projects under planning and
design, no active
construction projects.



PRECINCT 2

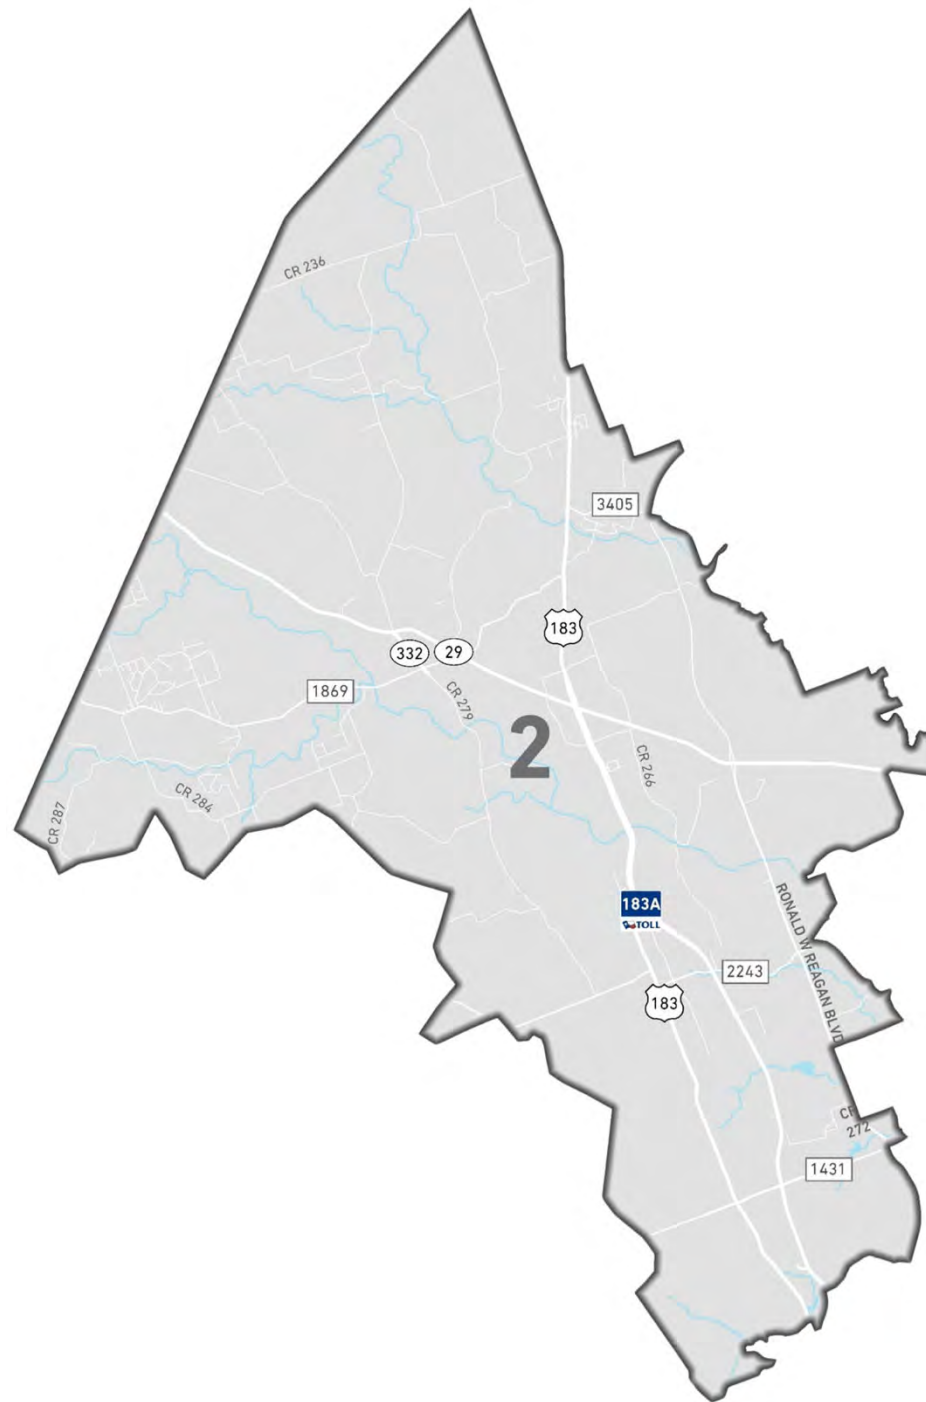

Freedom River Parkway (RM 1869 to CR 279)




Freedom River Parkway (RM 1869 to CR 279)



Ronald Reagan Widening (SH 29 to FM 3405)

Anticipated Completion
Summer 2027

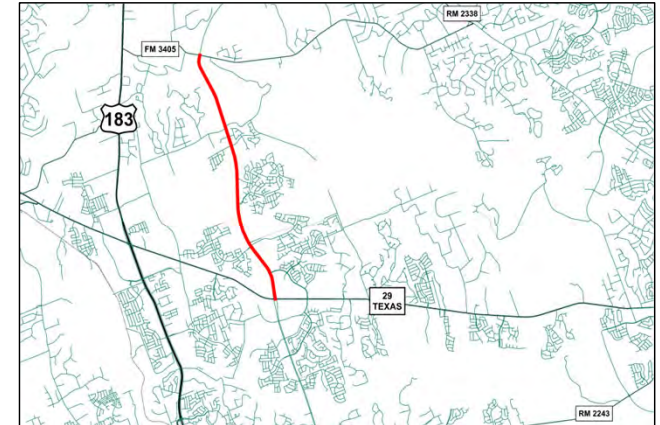

Original Contract Price = \$52,159,299.00

Total Change Orders to Date = \$83,221.75

Adjusted Contract Price = \$52,242,520.75

Expenditures to Date = \$28,709,886.59 (55%)

Ronald Reagan Widening (SH 29 to FM 3405)




Ronald Reagan Widening (SH 29 to FM 3405)



Ronald Reagan Widening (SH 29 to FM 3405)




PRECINCT 3

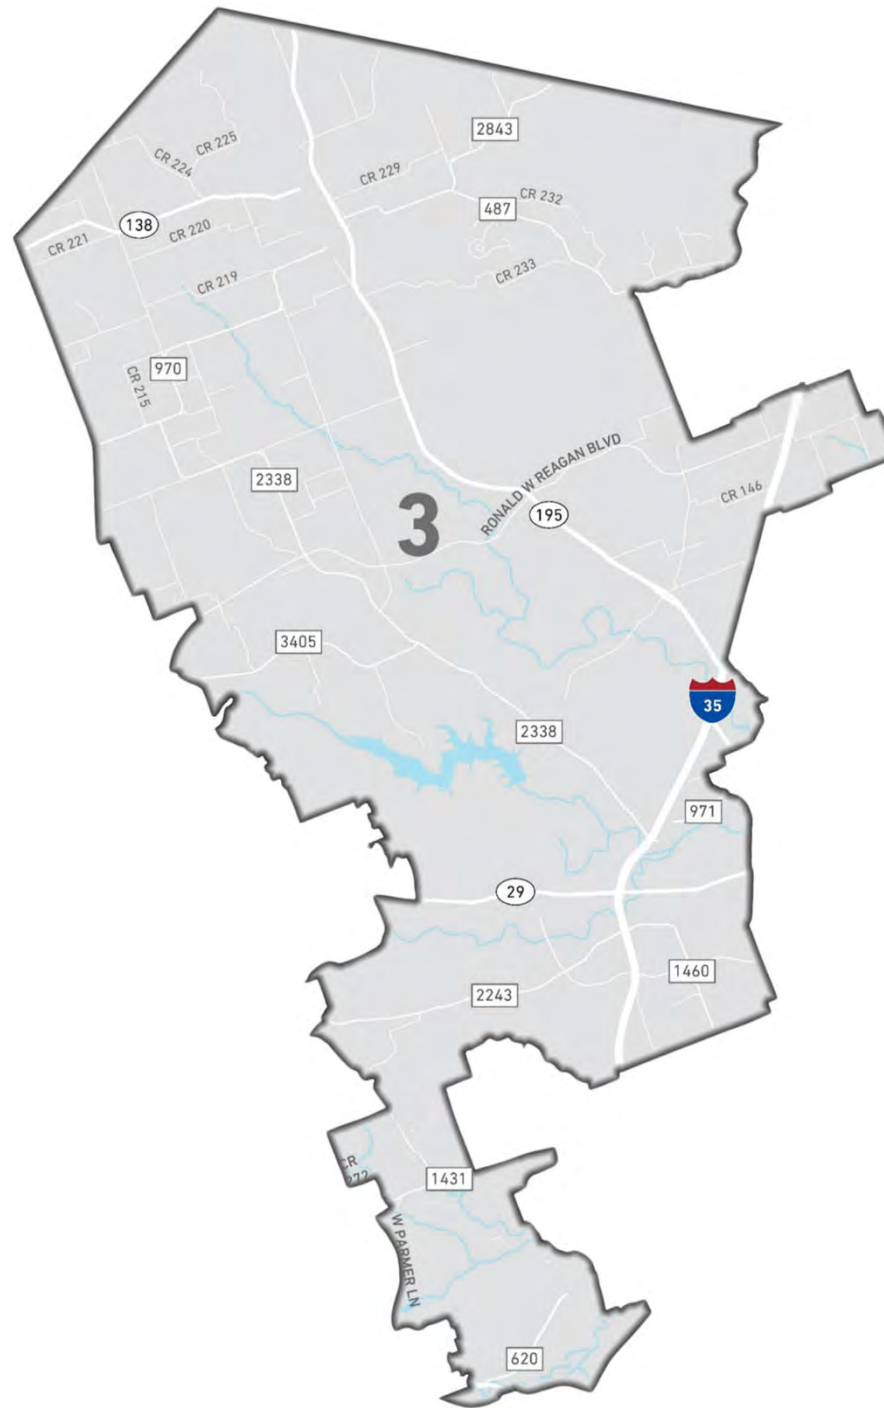

Corridor H/Sam Bass Road (RM 1431 to Wyoming Springs Drive)

Anticipated Completion
Spring 2026

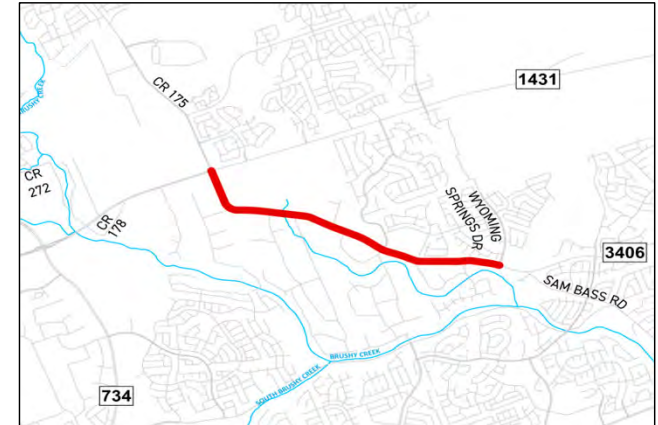

Original Contract Price = \$36,145,959.00

Total Change Orders to Date = -\$1,601,119.76

Adjusted Contract Price = \$34,544,839.24

Expenditures to Date = \$27,934,956.35 (81%)



Corridor H/Sam Bass Road (RM 1431 to Wyoming Springs Drive)



Corridor H/Sam Bass Road (RM 1431 to Wyoming Springs Drive)



Corridor H/Sam Bass Road (RM 1431 to Wyoming Springs Drive)



Wyoming Springs Extension (Brightwater Boulevard/Creek Bend to Sam Bass Road)

Anticipated Completion
Late 2026



Partnership with the City of Round Rock


Original Contract Amount = \$25,917,630.47

Construction is managed by the City of Round Rock

Wyoming Springs Extension (Brightwater Boulevard/Creek Bend to Sam Bass Road)



Wyoming Springs Extension (Brightwater Boulevard/Creek Bend to Sam Bass Road)



Wyoming Springs Extension (Brightwater Boulevard/Creek Bend to Sam Bass Road)



CR 255 (Road and Bridge Funded) (CR 254 to Ronald Reagan Boulevard)

Anticipated Completion
Summer 2026



Original Contract Price = \$20,847,300.93


Total Change Orders to Date = \$192,580.73

Adjusted Contract Price = \$21,039,881.66


Expenditures to Date = \$12,470,979.64 (59%)



CR 255 (Road and Bridge Funded) (CR 254 to Ronald Reagan Boulevard)



CR 255 (Road and Bridge Funded) (CR 254 to Ronald Reagan Boulevard)



CR 255 (Road and Bridge Funded) (CR 254 to Ronald Reagan Boulevard)



Wilco Way (Tracy Chambers Lane to Wilco Way) (Infrastructure Funded)

Anticipated Completion
Early 2026



Original Contract Price = \$2,706,129.45


Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$ 2,706,129.45

Expenditures to Date = \$1,880,805.43 (69%)



Wilco Way (Tracy Chambers Lane to Wilco Way) (Infrastructure Funded)



Wilco Way (Tracy Chambers Lane Extension to Wilco Way) (Infrastructure Funded)



Wilco Way (Tracy Chambers Lane to Wilco Way) (Infrastructure Funded)



SH 195 at Ronald Reagan Boulevard (Single Ramp at Ronald Reagan Boulevard)

Anticipated Completion
Summer 2026



Original Contract Price = \$3,608,141.00


Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$3,608,141.00

Expenditures to Date = \$338,180.64 (9%)




SH 195 at Ronald Reagan Boulevard (Single Ramp at Ronald Reagan Boulevard)



SH 195 at Ronald Reagan Boulevard (Single Ramp at Ronald Reagan Boulevard)




PRECINCT 4

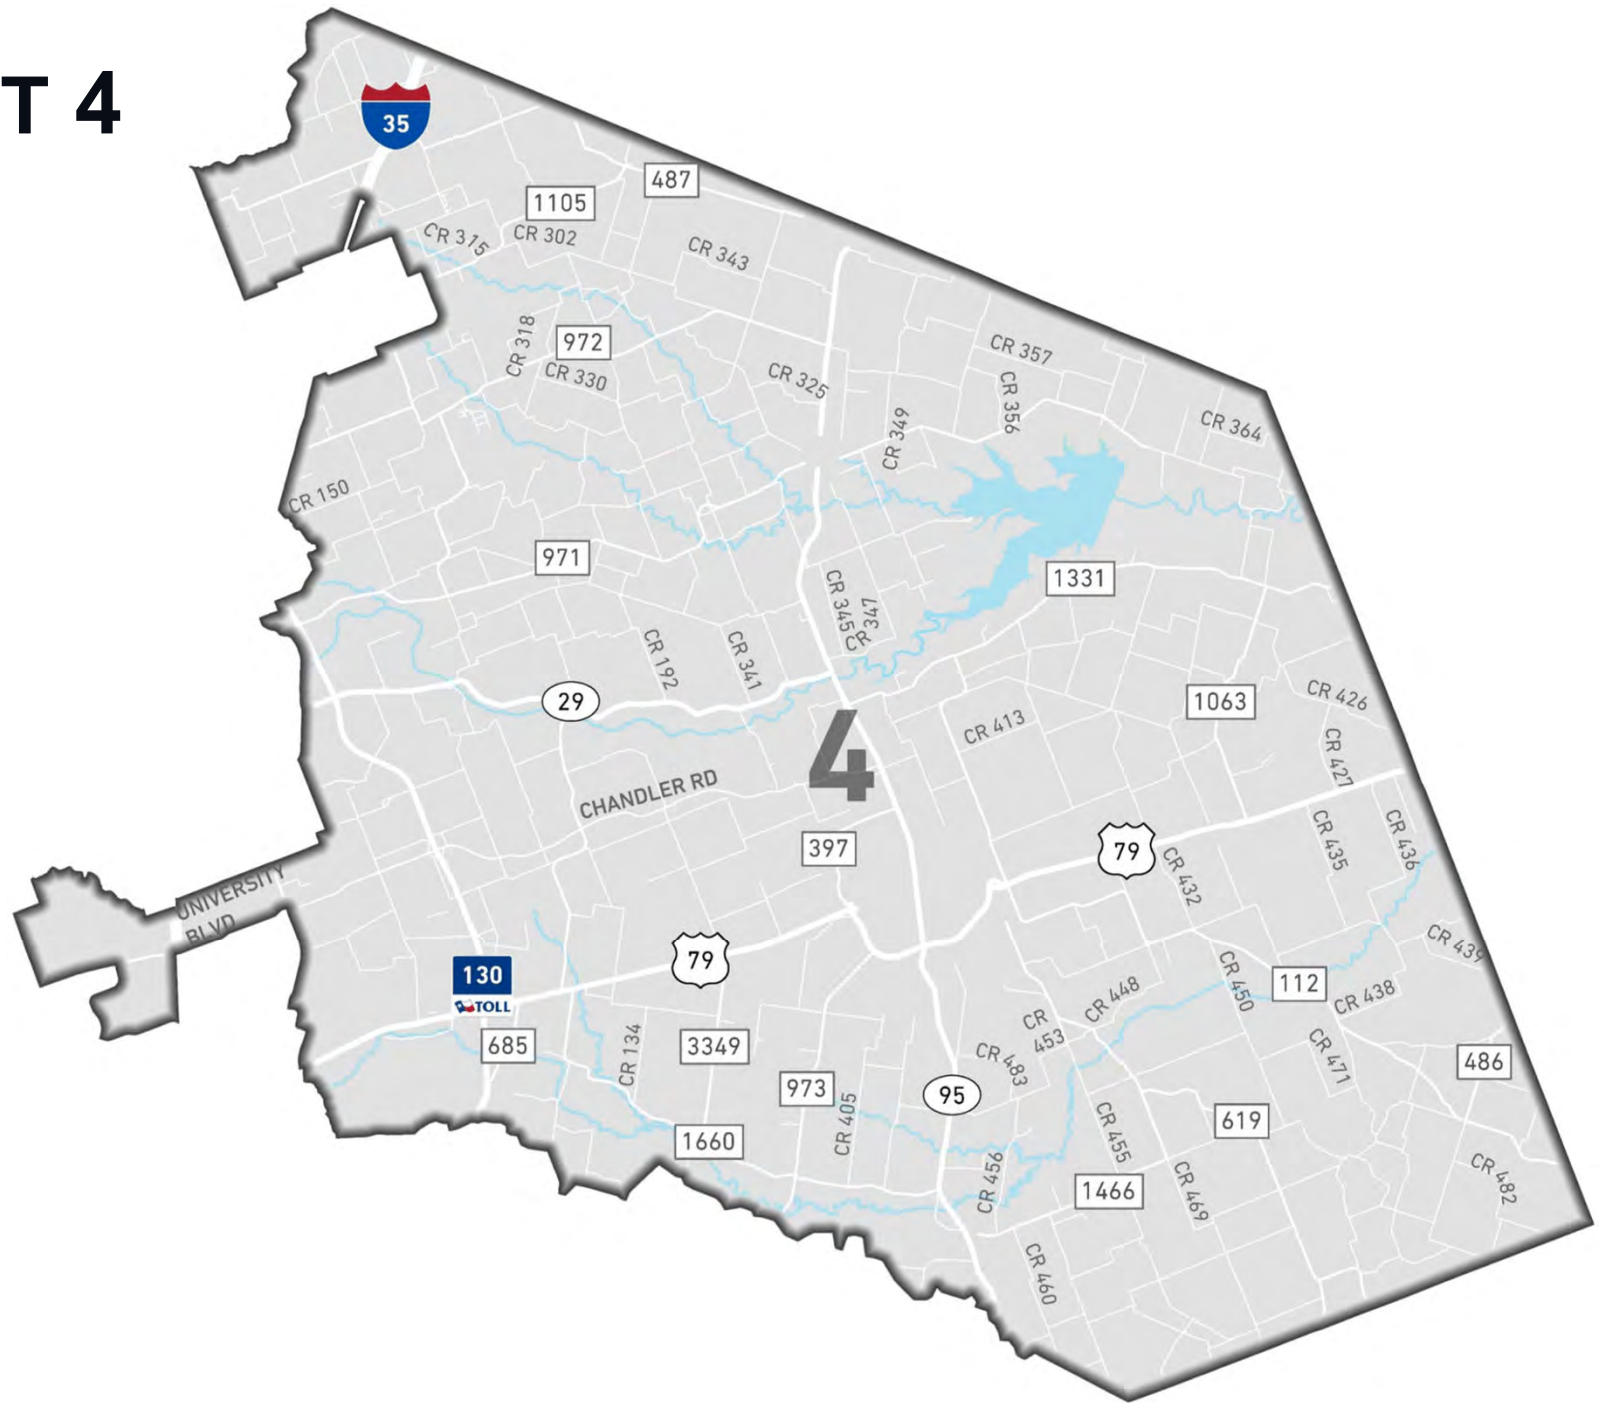

East Wilco Highway (FM 3349/US 79 Interchange) (US 79 to CR 404)

Substantially Complete
June 2025 (Roadwork)

Anticipated Completion
Spring 2027 (Rail Relocation)

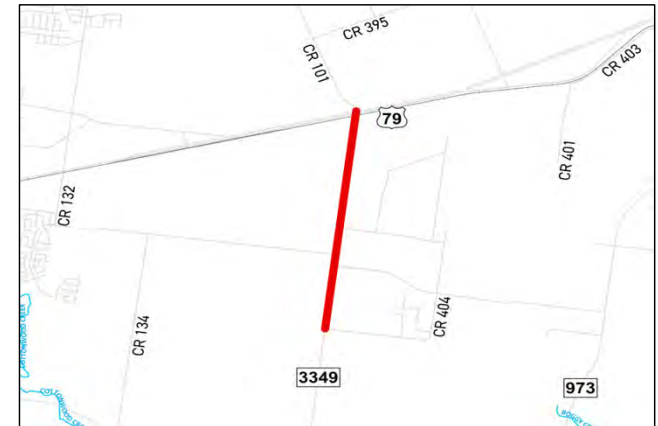

Original Contract Amount = \$81,941,038.13


Total Change Orders = \$3,773,639.65

Adjusted Contract Price = \$85,714,677.78

Expenditures to Date = \$74,025,892.35 (86%)




East Wilco Highway (FM 3349/US 79 Interchange) (US 79 to CR 404)



East Wilco Highway (FM 3349/US 79 Interchange) (US 79 to CR 404)




East Wilco Highway (FM 3349/US 79 Interchange) (US 79 to CR 404)

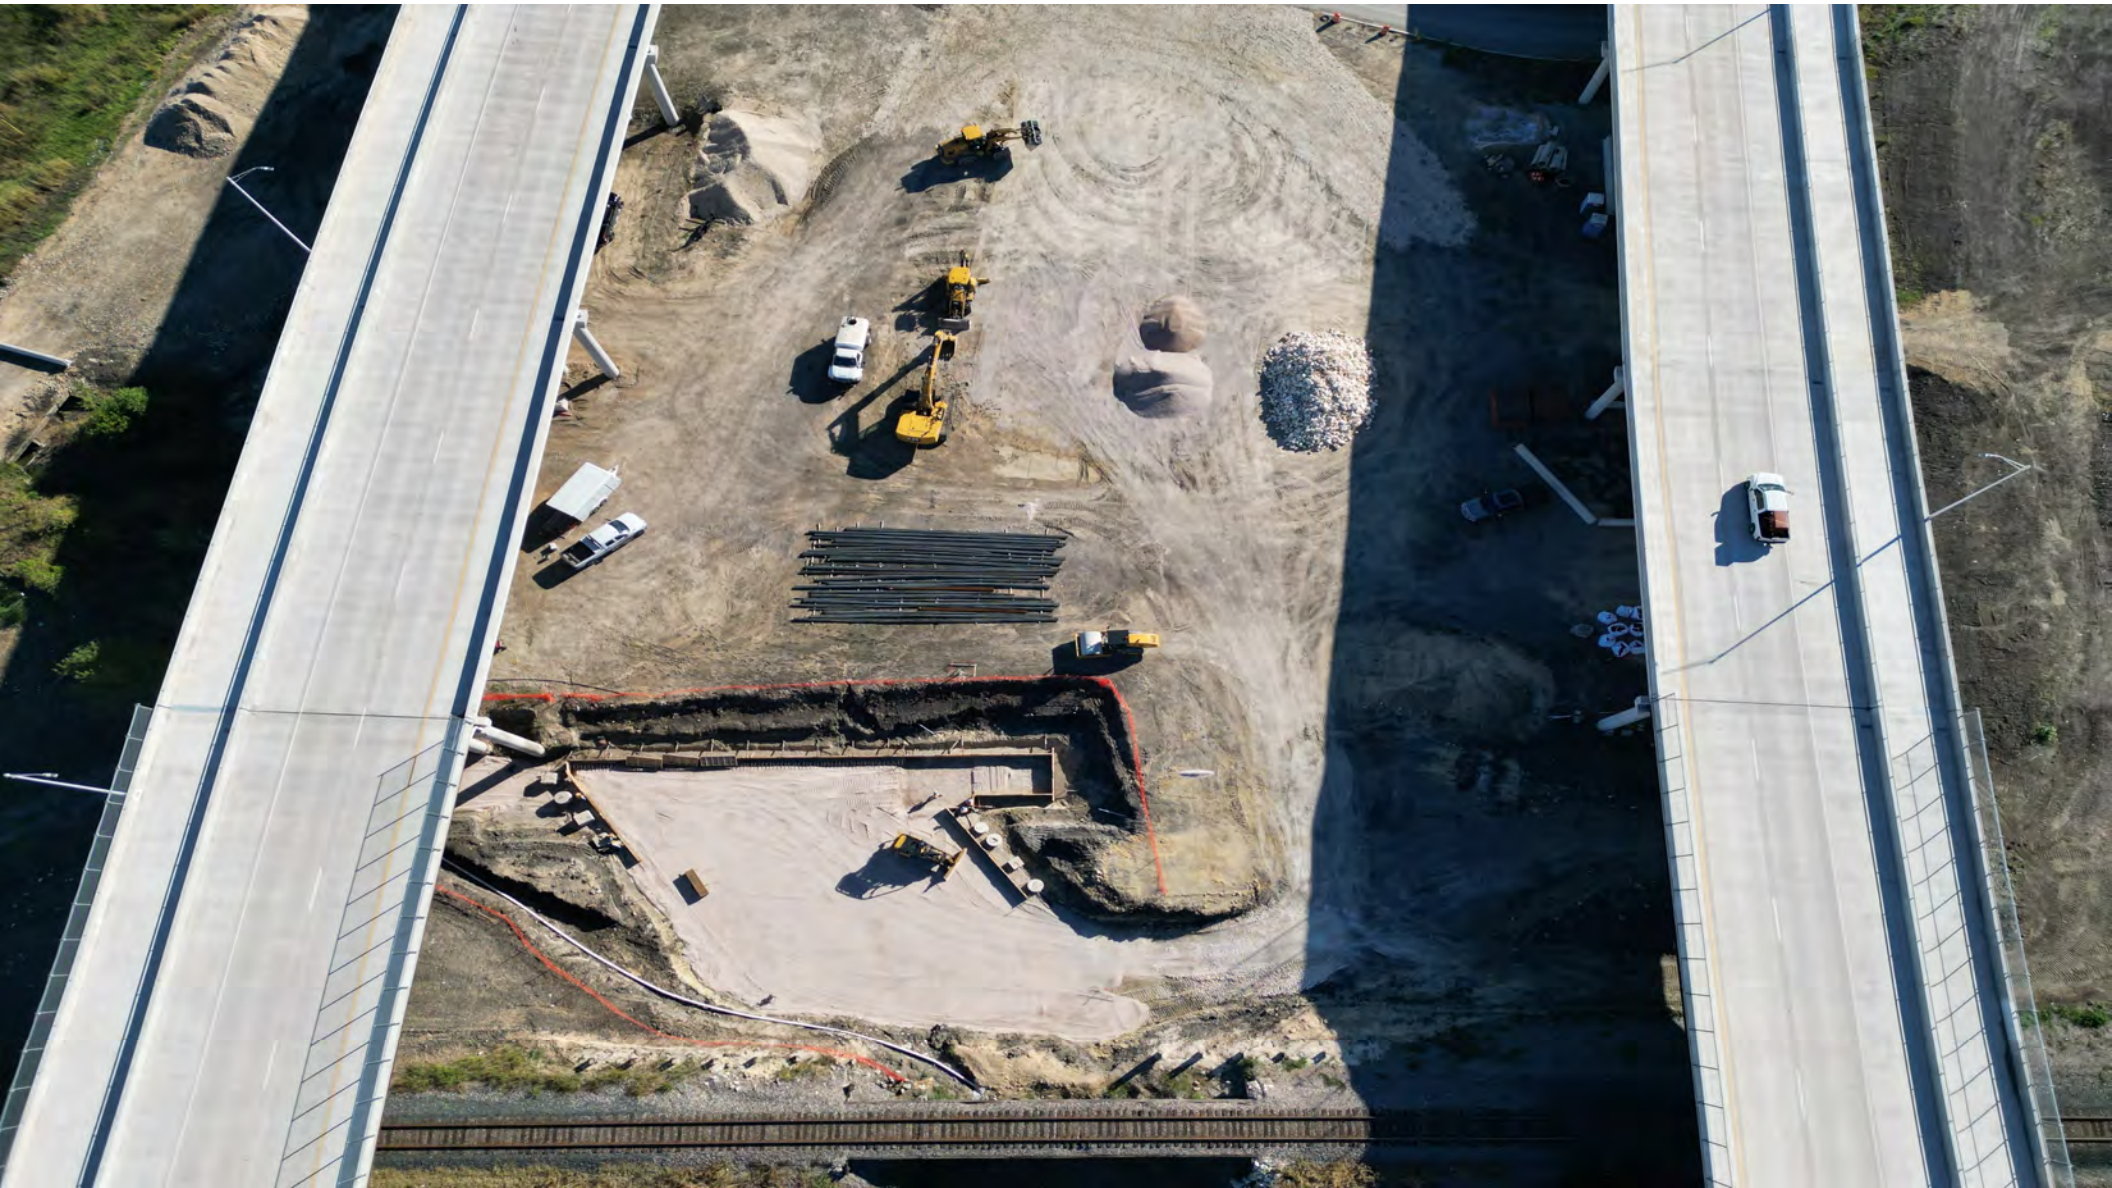

East Wilco Highway - Segment 2 (CR 137 South of Hutto to CR 404)

Anticipated Completion
Summer 2028

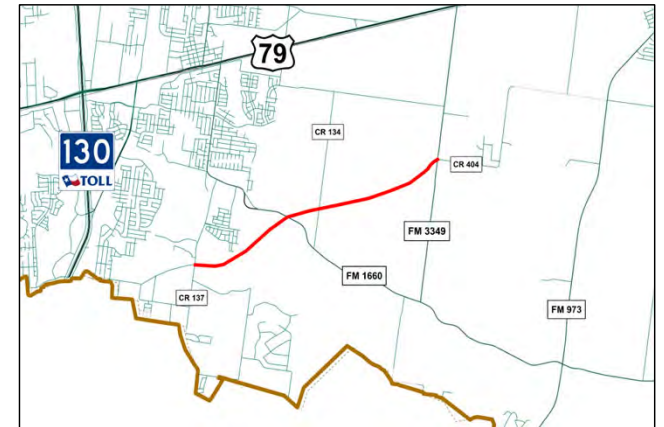

Original contract amount = \$64,407,606.63

Total change orders = -\$1,869,854.64

Adjusted contract price = \$62,537,751.99


Expenditures to date = \$41,406,352.96 (66%)




East Wilco Highway - Segment 2 (CR 137 South of Hutto and CR 404)



East Wilco Highway - Segment 2 (CR 137 South of Hutto and CR 404)




East Wilco Highway - Segment 2 (CR 137 South of Hutto and CR 404)



Old Settlers Boulevard (North Red Bud Lane/CR 122 to CR 110)

Anticipated Completion
Early 2026

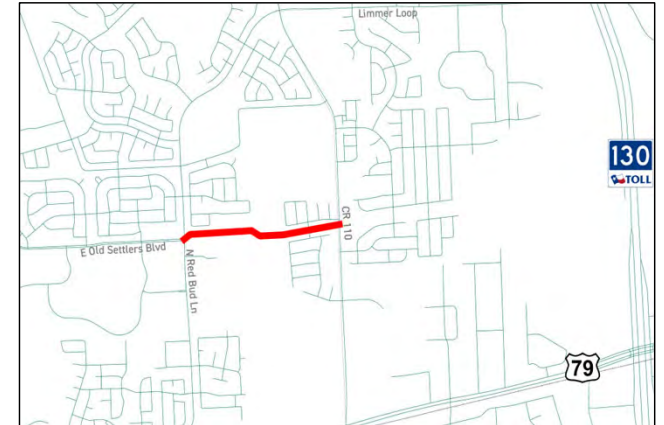

Partnership with the City of Round Rock

Original Contract Amount = \$14,920,847.10

Construction is managed by the City of Round Rock

Old Settlers Boulevard (North Red Bud Lane/CR 122 to CR 110)



Old Settlers Boulevard (North Red Bud Lane/CR 122 to CR 110)



CR 112 Widening (FM 1460/A.W. Grimes to CR 117)

Anticipated Completion
Late 2026



Partnership with the City of Round Rock

Original Contract Amount = \$13,119,712.35

Construction is managed by the City of Round Rock

CR 112 Widening (FM 1460/A.W. Grimes to CR 117)



CR 112 Widening (FM 1460/A.W. Grimes to CR 117)



CR 112 Widening (FM 1460/A.W. Grimes to CR 117)



CR 112 Widening (CR 117 to CR 110)

Anticipated Completion
Late 2026



Partnership with the City of Round Rock

Original Contract Amount = \$20,434,128.40

Construction is managed by the City of Round Rock



CR 112 Widening (CR 117 to CR 110)




CR 112 Widening (CR 117 to CR 110)



FM 971 (Future Granger High School Turn Lanes)

Substantially Complete
October 2025

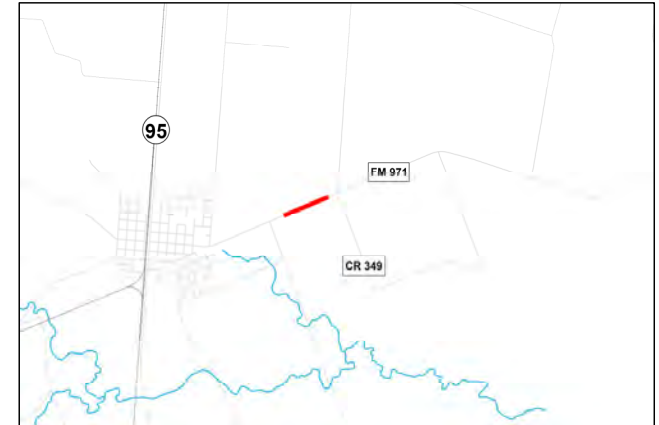

Original Contract Price = \$1,161,629.00

Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$1,161,629.00


Expenditures to Date = \$431,249.50 (37%)



FM 971 (Future Granger High School Turn Lanes)




FM 971 (Future Granger High School Turn Lanes)



Sonterra Boulevard (IH-35 Frontage Road & Sonterra Boulevard Intersection)

Substantially Complete
October 2025

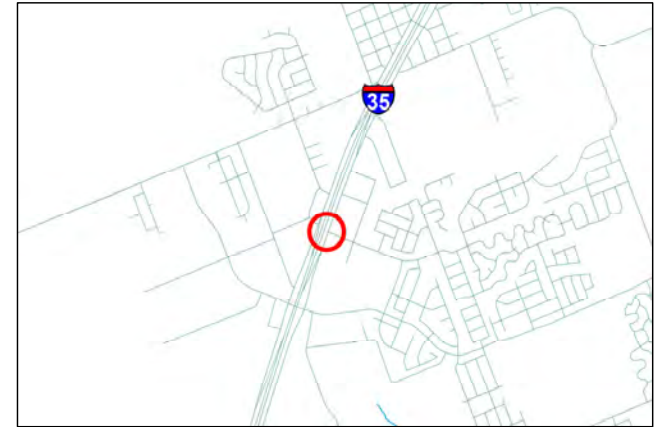

Original Contract Price = \$566,829.31

Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$566,829.31

Expenditures to Date = \$511,130.93 (91%)



Sonterra Boulevard (IH-35 Frontage Road & Sonterra Boulevard Intersection)



Road Bond Projects

Anticipated 2026 Construction Letting Dates

PROJECT	LETTING DATE
CR 258	Early 2026
East Wilco Highway, Seg 2	Early 2026
Pond Springs Drainage Improvements	Early 2026
CR 138	Early 2026
North Barker Street	Early 2026
Ronald Reagan Blvd. Widening, Seg D1 and D2	Spring 2026
CR 314 Safety Improvements	Spring 2026
Seward Junction North Loop (East)	Spring 2026
Salt Lake, Brook and Front Street	Spring 2026
Bagdad Road/CR 279	Spring 2026



Road Bond Projects

Anticipated 2026 Construction Letting Dates (Cont.)

PROJECT	LETTING DATE
Schultz Lane	Summer 2026
Ronald Reagan Blvd. Widening, Seg C1	Summer 2026
Ronald Reagan Blvd. Widening, Seg C2	Summer 2026
Parmer Lane at SH 45	Summer 2026
West Main Street	Summer 2026
CR 458	Summer 2026
Freedom River Parkway (East)	Summer 2026
Freedom River Parkway (West)	Fall 2026
Chandler Road (FM 1660 Overpass)	Fall 2026
Red Bud Lane Widening	Fall 2026
CR 201	Late 2026

