

Williamson County Commissioners Court

Road Bond and Pass Through Financing Programs June 20, 2017










Precinct 1





Anticipated Completion Spring 2018

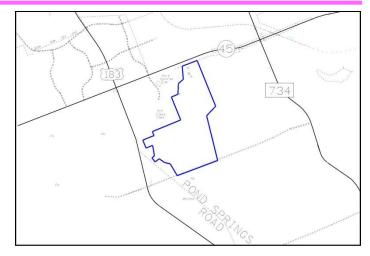

Original Contract Price = \$3,556,659.50

Total Change Orders to Date = \$89,812.83

Adjusted Contract Price = \$3,646,472.33

Expenditures to Date = \$2,352,435.35 (65%)
















Anticipated Completion Fall 2017

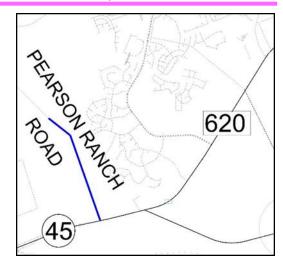


Original Contract Price = \$4,516,178.77

Total Change Orders to Date = -\$81,068.70

Adjusted Contract Price = \$4,435,110.07

Expenditures to Date = \$2,464,356.55 (56%)



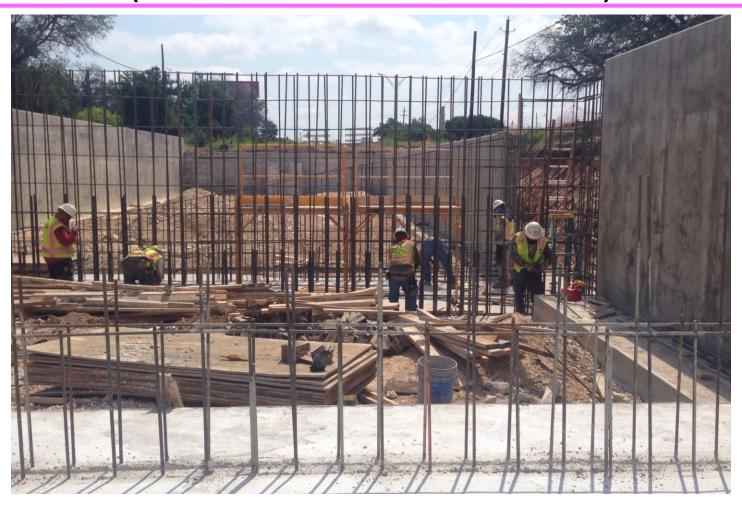












RM 620 Phase 2 (Wyoming Springs to Deep Wood Dr)

Anticipated Completion Spring 2018

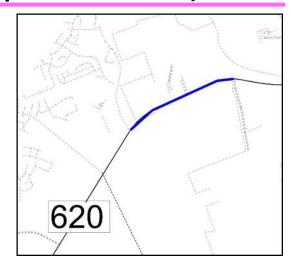

Original Contract Price = \$6,082,225.70

Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$6,082,225.70

Expenditures to Date = \$1,931,099.00 (32%)



RM 620 Phase 2 (Wyoming Springs to Deep Wood Dr.)





RM 620 Phase 2 (Wyoming Springs to Deep Wood Dr.)






RM 620 Phase 2 (Wyoming Springs to Deep Wood Dr.)






Precinct 2





Anticipated Completion Fall 2017

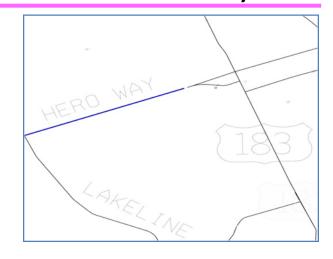

Partnership with the City of Leander
Original Contract Price = \$22,648,112.00
WilCo Contribution = \$9,150,000.00
Construction managed by the City of Leander
















Anticipated Completion
Summer 2017

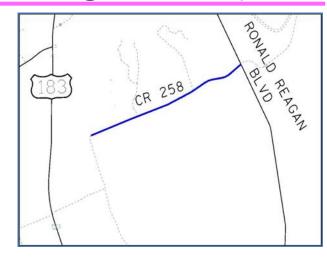

Original Contract Price = \$5,808,856.58

Total Change Orders to Date = \$172,159.69

Adjusted Contract Price = \$5,981,016.27

Expenditures to Date = \$4,901,710.74 (82%)
















Anderson Mill Road (Gasper Bend to RM 1431/Whitestone Blvd.)

Anticipated Completion Summer 2018

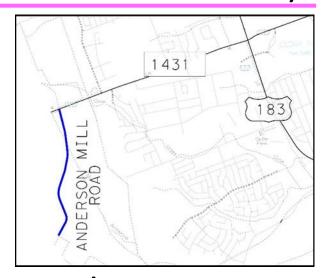

Partnership with the City of Cedar Park

Original Contract Amount = \$8,300,000.00

WilCo Contribution = 50% of total project cost, \$4,150,000.00

Construction is managed by the City of Cedar Park



Anderson Mill Road (Gaspar Bend to RM 1431/Whitestone Blvd.)





Anderson Mill Road (Gaspar Bend to RM 1431/Whitestone Blvd.)





Anderson Mill Road (Gaspar Bend to RM 1431/Whitestone Blvd.)






Precinct 3





FM 1460 North (North of University to Quail Valley Drive)

Anticipated Completion Late 2017

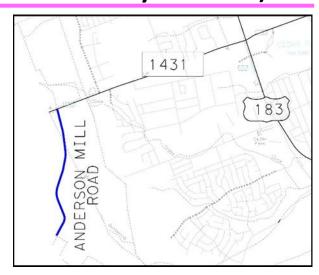

Partnership with TXDOT and the City of Georgetown

Original Contract Amount = \$21,519,391.66

WilCo Contribution = \$4,500,000.00

Construction is managed by TxDOT



FM 1460 North (North of University to Quail Valley Drive)





FM 1460 North (North of University to Quail Valley Drive)






FM 1460 North (North of University to Quail Valley Drive)





Precinct 4

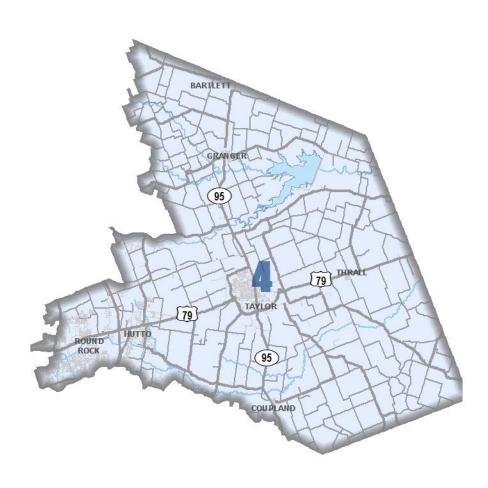



Anticipated Completion
Summer 2018



Original Contract Amount = \$11,224,589.02

Total Change Orders = \$0.00

Adjusted Contract Price = \$11,224,589.02

Expenditures to Date = \$2,911,457.00 (26%)











