

Williamson County Commissioners Court

Road Bond Program November 20, 2018










Precinct 1





Anticipated Completion Early 2019




Original Contract Price = \$2,529,398.54 Total Change Orders to Date = \$6,873.42 Adjusted Contract Price = \$2,536,271.96 Expenditures to Date = \$1,705,705.56 (67%)









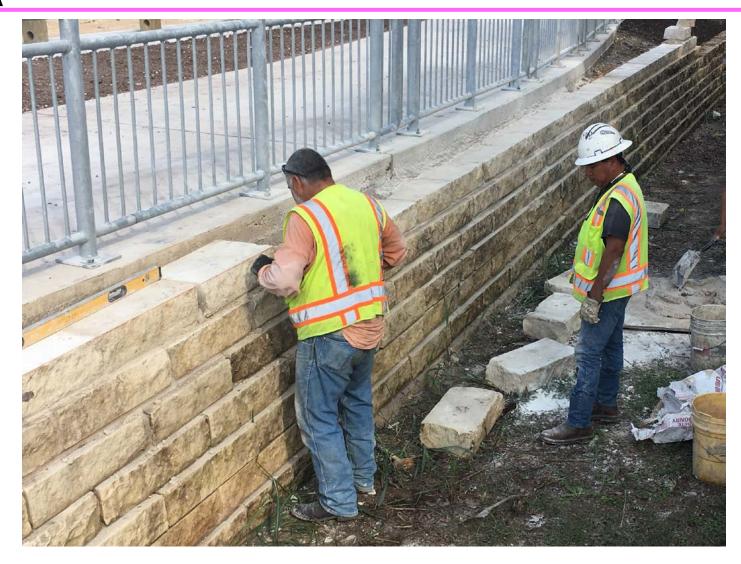








Anticipated Completion Late 2018

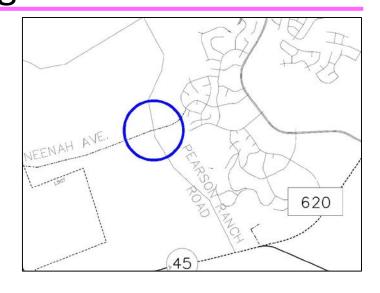

Original Contract Price = \$267,031.15

Total Change Orders to Date = \$15,000.00

Adjusted Contract Price = \$282,031.15

Expenditures to Date = \$10,598.51 (4%)

















Precinct 2

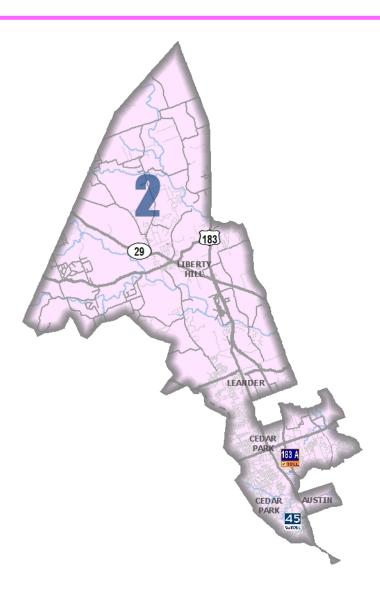



Anderson Mill Road (Gasper Bend to RM 1431/Whitestone Blvd.)

Anticipated Completion Late 2018

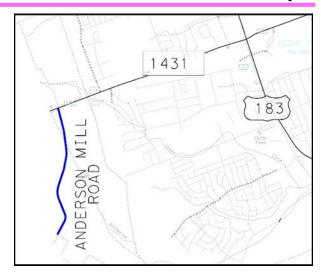


Partnership with the City of Cedar Park Original Contract Amount = \$8,300,000.00

WilCo Contribution = 50% of total project cost, \$4,150,000.00

Construction is managed by the City of Cedar Park



Anderson Mill Road (Gaspar Bend to RM 1431/Whitestone Blvd.)

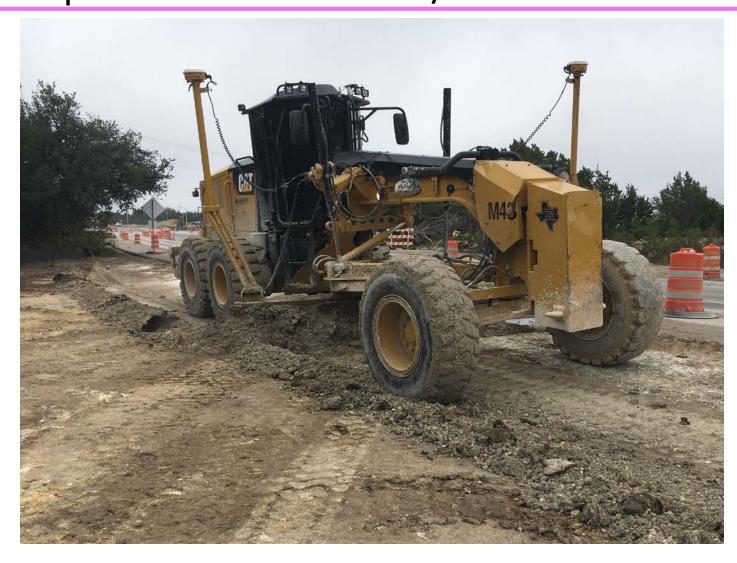




Anderson Mill Road (Gaspar Bend to RM 1431/Whitestone Blvd.)





Anticipated Completion Early 2019

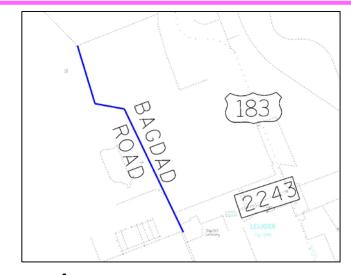

Partnership with the City of Leander

Original Contract Amount = \$8,091,140.30

WilCo Contribution = 50% of total project cost, \$4,903,000.00

Construction is managed by the City of Leander
















New Hope Drive (Cottonwood Creek to Reagan Blvd)

Anticipated Completion Fall 2018

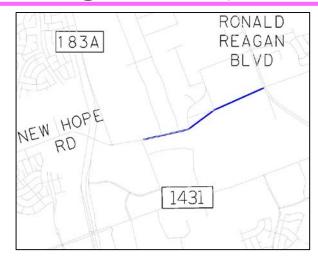

Partnership with the City of Cedar Park

Original Contract Amount = \$7,829,323.40

WilCo Contribution = \$1,300,000.00

Construction is managed by the City of Cedar Park



New Hope Drive (Cottonwood Creek to Reagan Blvd)





New Hope Drive (Cottonwood Creek to Reagan Blvd)






New Hope Drive (Cottonwood Creek to Reagan Blvd)





CR 200 at Bold Sundown (Intersection Improvements)

Anticipated Completion Fall 2018

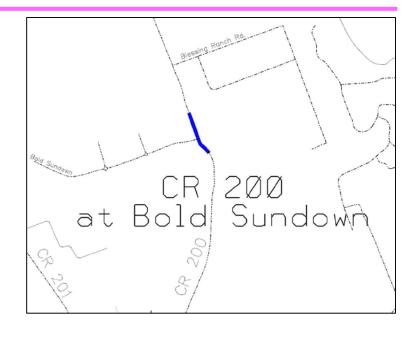

Original Contract Price = \$368,861.80


Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$368,861.80

Expenditures to Date = \$327,754.50 (89%)



CR 200 at Bold Sundown (Intersection Improvements)

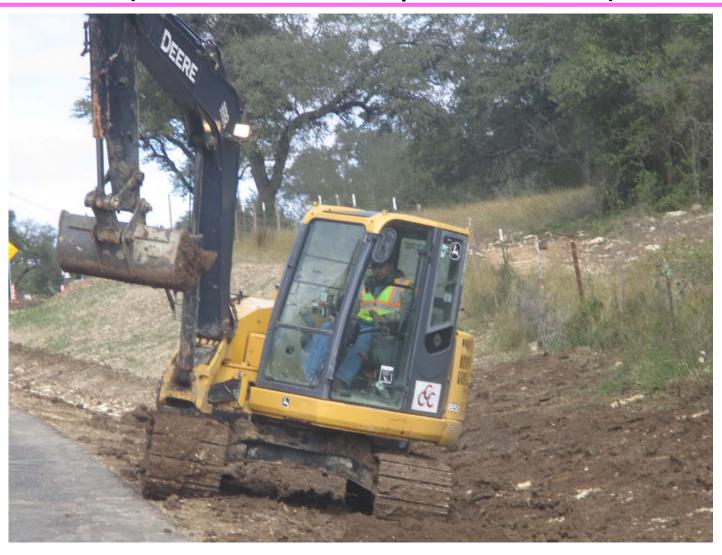




CR 200 at Bold Sundown (Intersection Improvements)





CR 279 (Bagdad Road) at River Ranch Park ²⁶ (2500 ft of Bagdad Road and Park Road)

Anticipated Completion Early 2020

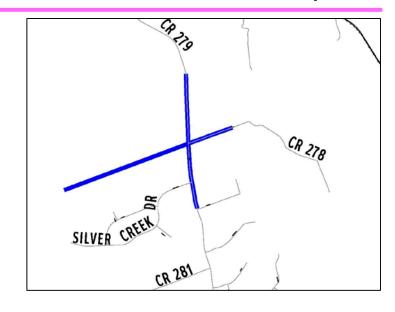

Original Contract Price = \$2,959,000.00

Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$2,959,000.00

Expenditures to Date = \$0.00 (0%)




CR 279 (Bagdad Road) at River Ranch Park ²⁷ (2500 ft of Bagdad Road and Park Road)





San Gabriel Road Bridge at Lackey Creek (Remuda Drive to San Gabriel Ranch Road)

Anticipated Completion Spring 2019

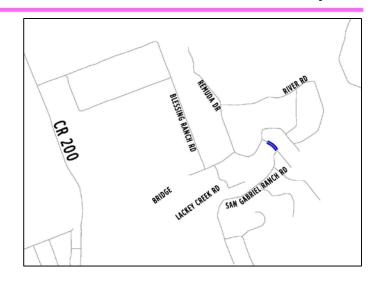

Original Contract Price = \$1,425,301.90 Total Change Orders to Date = \$0.00 Adjusted Contract Price = \$1,425,301.90 Expenditures to Date = \$0.00 (0%)





San Gabriel Road Bridge at Lackey Creek (Remuda Drive to San Gabriel Ranch Road)






San Gabriel Road Bridge at Lackey Creek (Remuda Drive to San Gabriel Ranch Road)





Ronald Reagan Boulevard at Santa Rita Turn Lanes

Anticipated Completion Early 2019

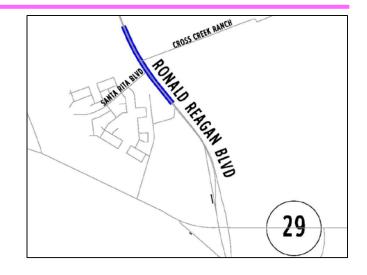

Original Contract Price = \$420,608.60 Total Change Orders to Date = \$0.00 Adjusted Contract Price = \$420,608.60 Expenditures to Date = \$9,152.90 (2%)



Ronald Reagan Boulevard at Santa Rita Turn Lanes






Ronald Reagan Boulevard at Santa Rita Turn Lanes






Precinct 3

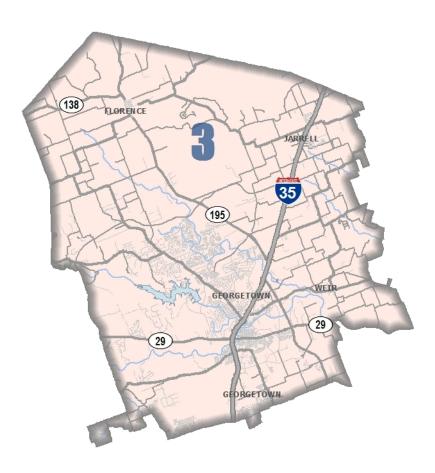



FM 1460 North (North of University to Quail Valley Drive)

Anticipated Completion Fall 2018

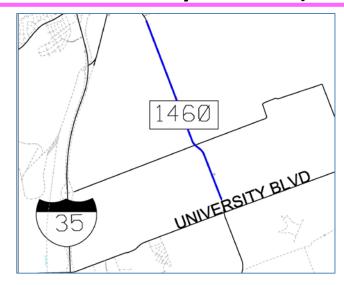

Partnership with TXDOT and the City of Georgetown

Original Contract Amount = \$21,519,391.66

WilCo Contribution = \$4,500,000.00

Construction is managed by TxDOT



FM 1460 North (North of University to Quail Valley Drive)






FM 1460 North (North of University to Quail Valley Drive)





Anticipated Completion Fall 2018



Partnership with the City of Georgetown

Original Contract Amount = \$5,599,200.86

Total Change Orders to Date = \$114,077.58

WilCo Contribution = \$5,713,278.44

Construction is managed by the City of Georgetown
















Anticipated Completion Late 2019

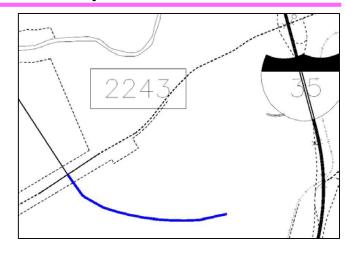

Original Contract Amount = \$8,087,943.77

Total Change Orders = \$0.00

Adjusted Contract Price = \$8,087,943.77

Expenditures to Date = \$0.00 (0%)

















Precinct 4

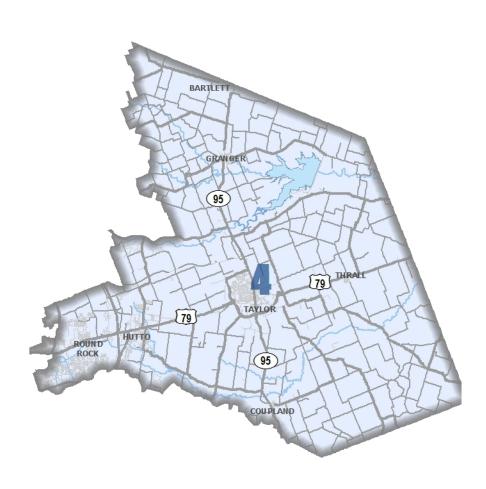



Anticipated Completion Spring 2019

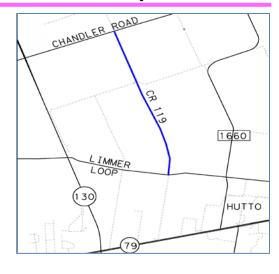

Original Contract Amount = \$6,640,302.71

Total Change Orders = \$0.00


Adjusted Contract Price = \$6,640,302.71

Expenditures to Date = \$4,079,608.04 (61%)







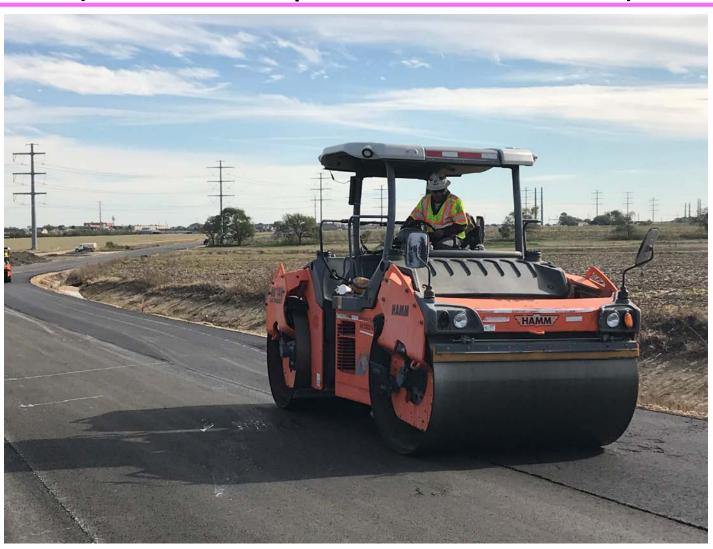








Roundville Lane (A.W. Grimes to EBFR of SH 45)

Anticipated Completion Fall 2018

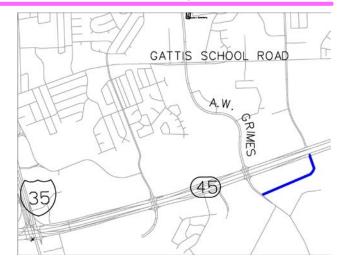

Partnership with the City of Round Rock
Original Contract Amount = \$2,699,825.69
WilCo Contribution = \$1,500,000.00
Construction is managed by the City of
Round Rock



Roundville Lane (A.W. Grimes to EBFR of SH 45)





Roundville Lane (A.W. Grimes to EBFR of SH 45)

