


BOARD OF SUPERVISORS


NOVEMBER 7, 2023

COUNTY ROAD 98

BIKE & SAFETY IMPROVEMENT PROJECT

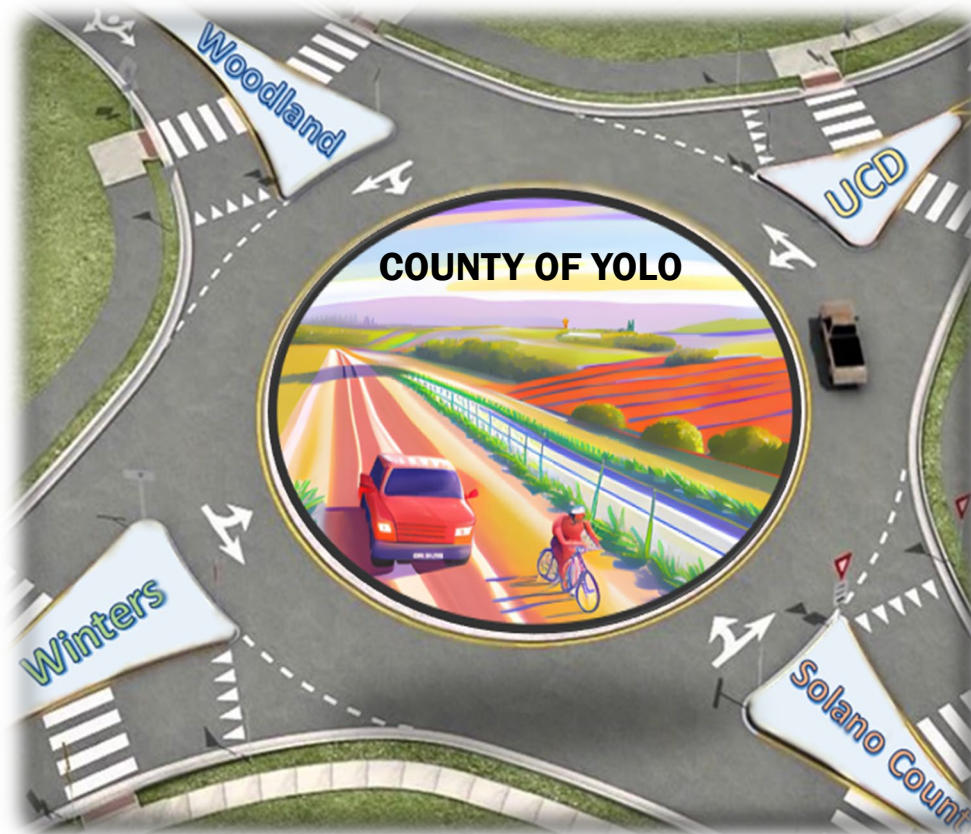

TODD RIDDIOUGH, PRINCIPAL CIVIL ENGINEER
YOLO COUNTY, PUBLIC WORKS

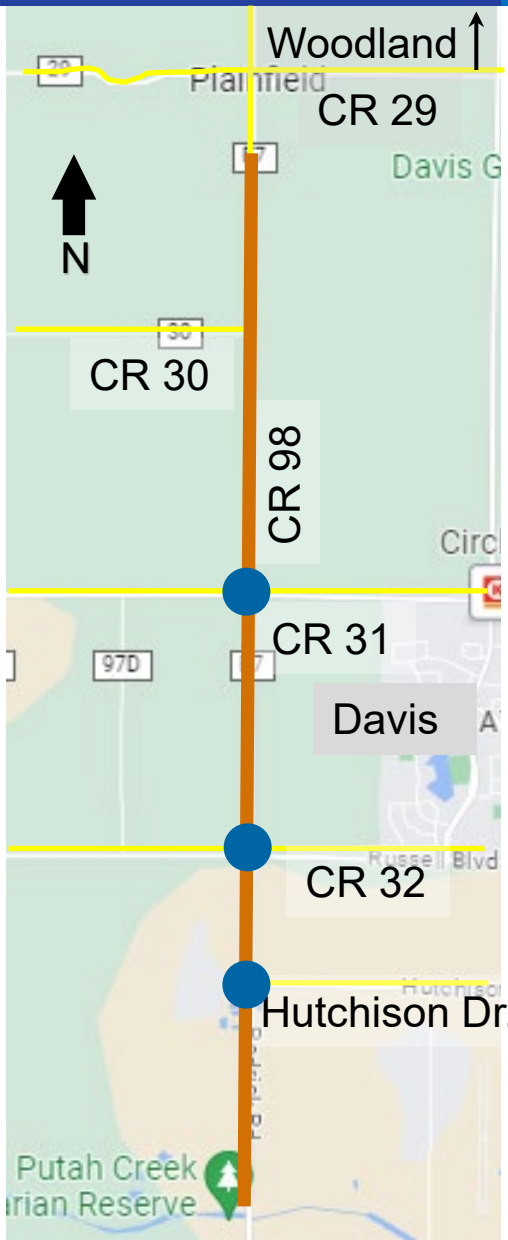

BACKGROUND

PHASE I


- **IMPROVE SAFETY ALONG CORRIDOR FOR ALL MODES OF TRANSPORTATION**

SCOPE

- **ROAD RECONSTRUCTION (4.1 MI)**
- **BIKE LANES (6 FT)**
- **ROUNABOUTS (3)**
 - AT CR 31
 - AT CR 32
 - AT HUTCHISON DR.
- **WAY FINDING**
- **AESTHETIC TREATMENT**

TIMING

- **5 PUBLIC MEETINGS**
 - MARCH 2, 2013, FEBRUARY 7, 2017, SEPTEMBER 5, 2018, OCTOBER 2, 2018, FEBRUARY 12, 2020
- **BOARD APPROVALS**
 - DECEMBER 11, 2018 – PROJECT APPROVAL
 - APRIL 26, 2022 – CEQA CERTIFICATION

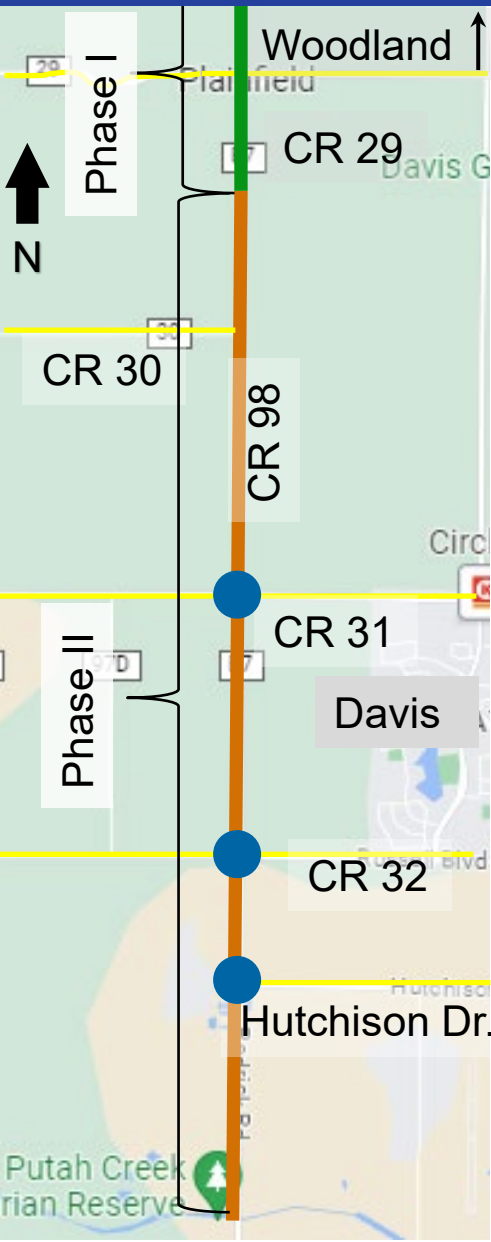


BACKGROUND

- **RIGHT OF WAY INITIATION**
 - **DECEMBER 7, 2022**

COST

PHASE	AVAILABLE FUNDING	TOTAL
PHASE I – COMPLETED (2014)	N/A	\$13,260,400
PHASE II - DESIGN	\$6,700,000	\$6,700,000
PHASE II - CONSTRUCTION	\$8,725,000	\$37,100,000
TOTAL		\$57,060,400

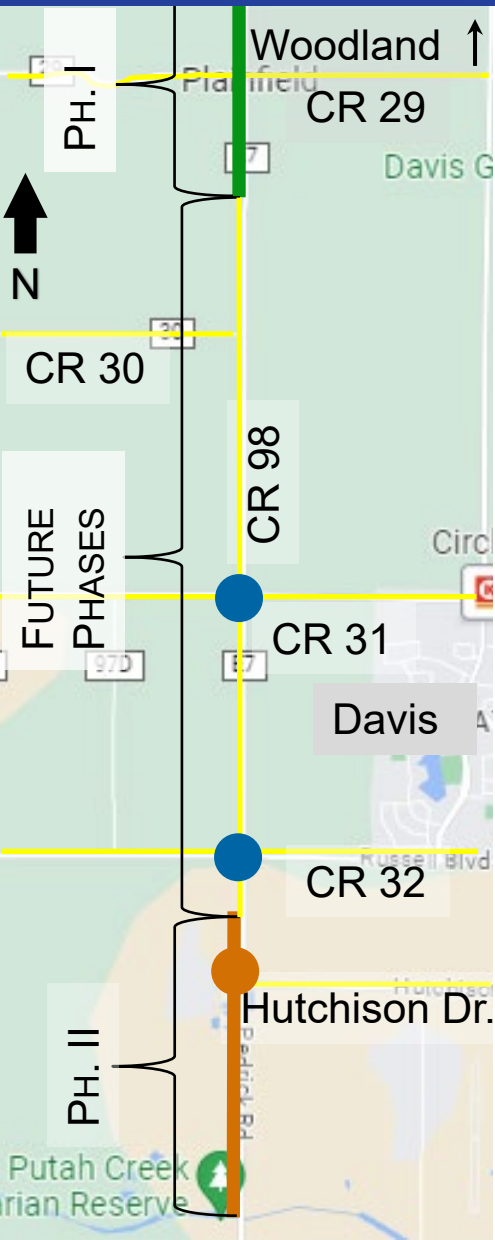

PROPOSED PHASING

PHASE	TOTAL
PHASE I – COMPLETED (2014)	\$13,260,400
PHASE II - DESIGN	\$6,700,000
PHASE II – CONSTRUCTION (MODIFIED)	\$7,000,000
PHASE III – CONSTRUCTION (MODIFIED)	\$30,100,000
TOTAL	\$57,060,400

NEXT STEPS

- **BOARD APPROVES MODIFIED PROJECT PHASING**
- **COMPLETE RIGHT OF WAY ACQUISITION (EXPECTED LATE 2024)**
- **CLOSE CONSTRUCTION FUNDING GAP TO PROVIDE CONSTRUCTION FUNDING FOR FUTURE PHASES**
