




# Administrator's Report

September 1, 2022 – CTOC Meeting





# NORTHERN PARKWAY

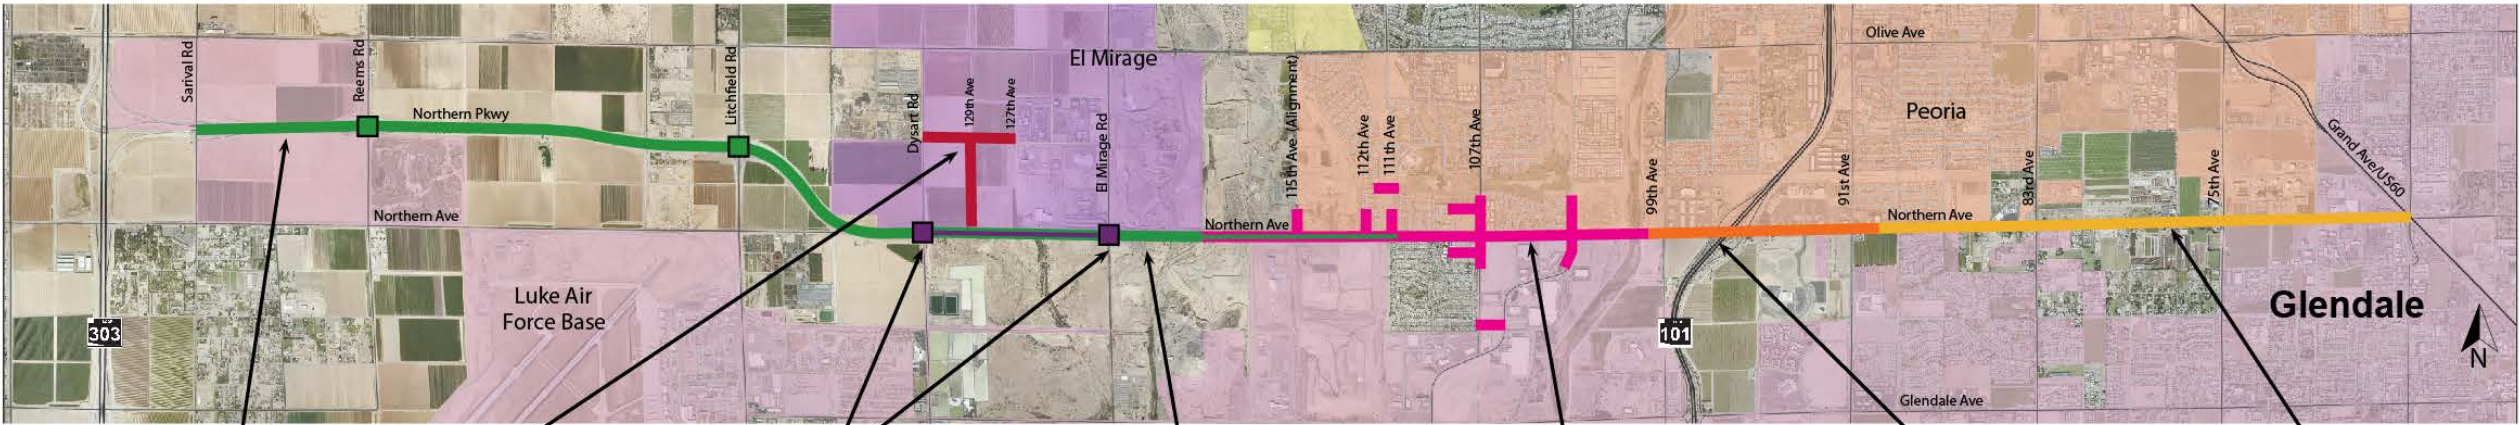

**TT0195: Sarival Ave to Dysart Rd**  
Completed 2013

**TT0498: El Mirage Alternative Access**  
Construction: Fall 2022 (Start)


**TT0427: Dysart Rd Overpass  
El Mirage Rd Overpass**  
Construction: Substantially complete  
Open to traffic August 2022

**TT0347: Dysart Rd to 111th Ave  
Agua Fria River Bridge**  
Completed 2021

**TT0600: Agua Fria River to 99th Ave**  
Final Design: Underway  
Construction: Fall 2025 (Start)

**TT0372: 99th Ave to 87th Ave**  
Final Design: Underway  
Construction: Spring 2026 (Start)

**TT0573: Loop 101 to Grand Ave**  
Scoping: Complete  
Construction: No available funding

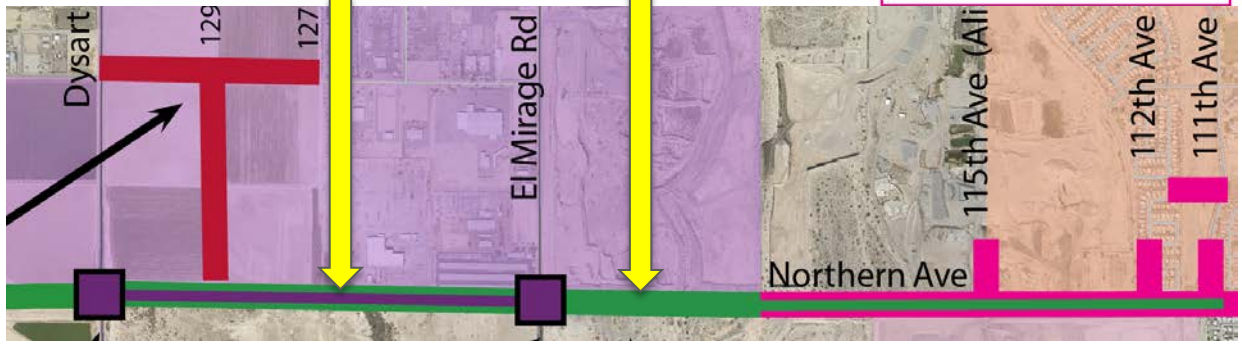



# NORTHERN PARKWAY

---

- Dysart & El Mirage overpasses/mainline
  - 99.5% Complete
  - Open to traffic in late August 26, 2022
  - Ribbon cutting on October 25, 2022 (tentative)
- El Mirage Alternative Access
  - Construction Management consultant April 2022
  - Construction start delayed due to readvertisement
- 99<sup>th</sup> Avenue to 87<sup>th</sup> Avenue
  - 60% Design plans under development
- Agua Fria River to 99<sup>th</sup> Avenue
  - Public meeting likely in Fall 2022



# NORTHERN PARKWAY

