



# Williamson County Commissioners Court


---

Road Bond Program

January 28, 2020



# Precinct 1




## North Mays Extension (Paloma Drive to Oakmont Drive)

---

3

Anticipated Completion  
Summer 2020

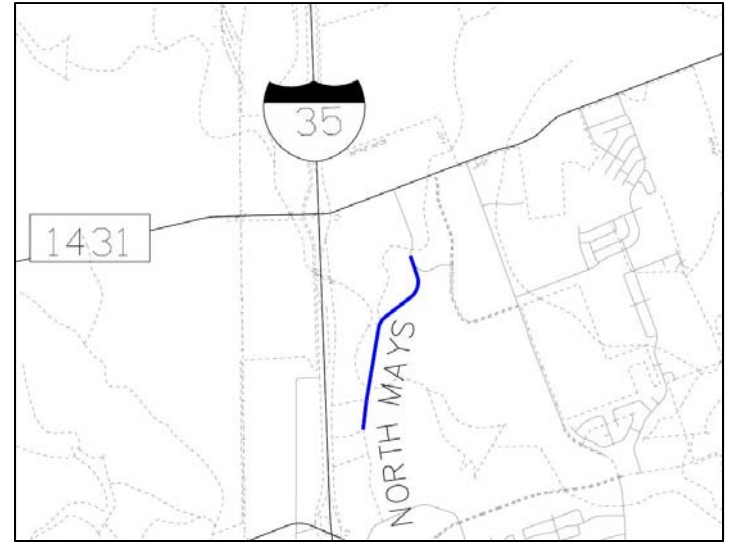

Original Contract Price = \$10,775,835.75

Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$10,775,835.75

Expenditures to Date = \$7,186,077.86 (67%)

# North Mays Extension (Paloma Drive to Oakmont Drive)

4



# North Mays Extension (Paloma Drive to Oakmont Drive)


5



# North Mays Extension (Paloma Drive to Oakmont Drive)



# Precinct 2

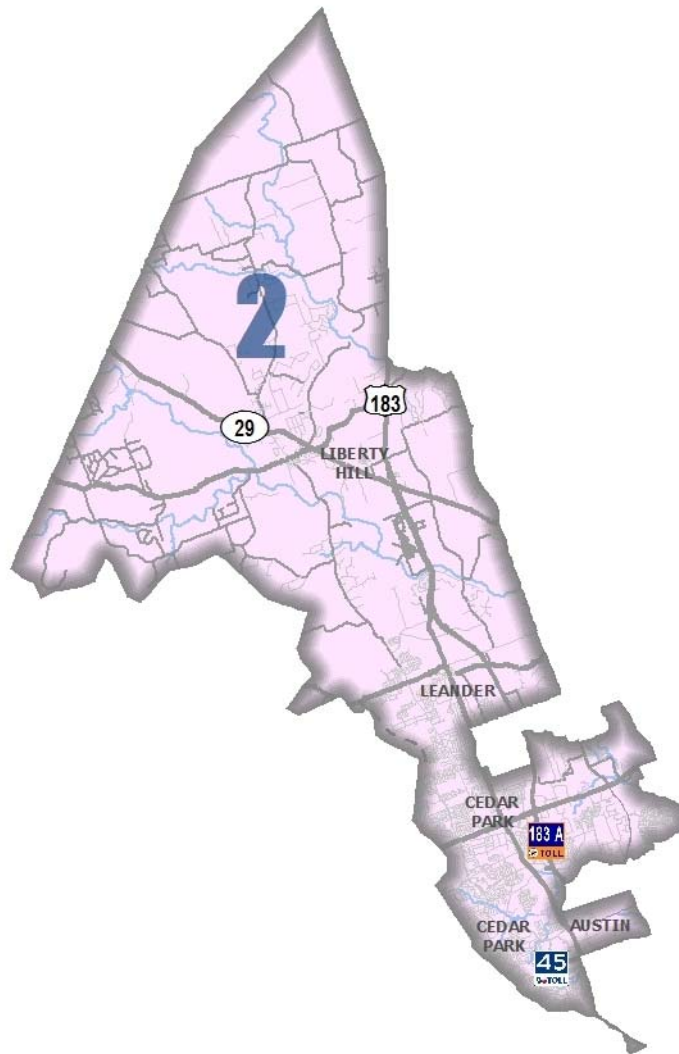




## Bagdad Road (CR 279) at CR 278 (River Ranch County Park Road)

8

Anticipated Completion  
Early 2020

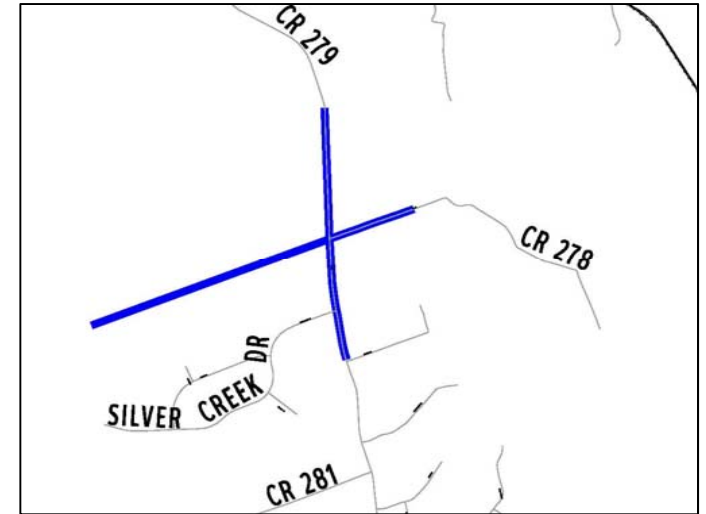

Original Contract Price = \$2,959,000.00

Total Change Orders to Date = \$53,416.00

Adjusted Contract Price = \$3,012,416.00

Expenditures to Date = \$2,001,133.76 (66%)

# Bagdad Road (CR 279) at CR 278 (River Ranch County Park Road)

9



# Bagdad Road (CR 279) at CR 278 (River Ranch County Park Road)

10



# Bagdad Road (CR 279) at CR 278 (River Ranch County Park Road)


11





# San Gabriel Ranch Road Bridge at Lackey Creek <sup>12</sup>

Anticipated Completion  
Early 2020

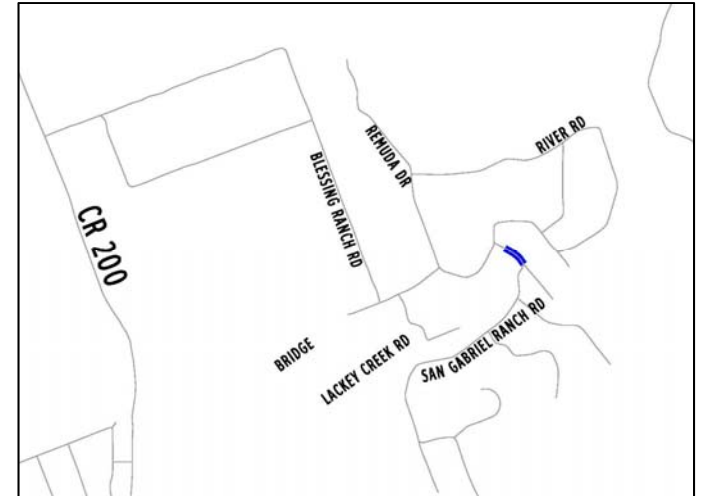

Original Contract Price = \$1,425,301.90

Total Change Orders to Date = \$16,166.09

Adjusted Contract Price = \$1,441,467.99

Expenditures to Date = \$1,202,614.79 (83%)

# San Gabriel Ranch Road Bridge at Lackey<sup>13</sup> Creek



# San Gabriel Ranch Road Bridge at Lackey<sup>14</sup> Creek




# San Gabriel Ranch Road Bridge at Lackey Creek<sup>15</sup>



# Seward Junction Improvements

Anticipated Completion  
Late 2020

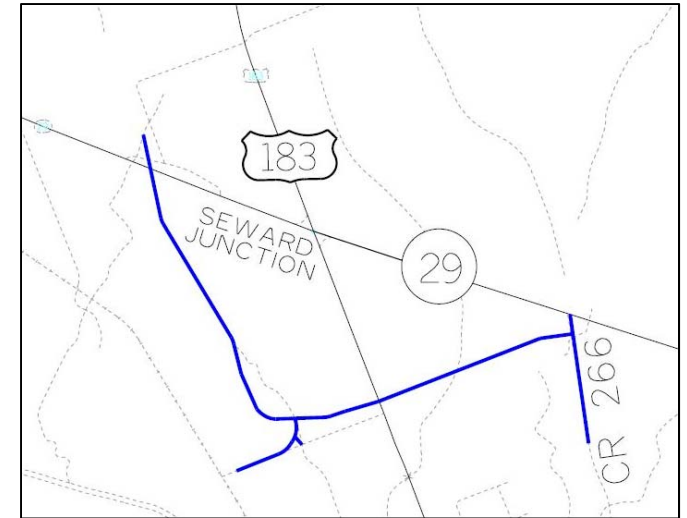

Original Contract Price = \$13,270,258.10

Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$13,270,258.10

Expenditures to Date = \$5,252,684.92 (40%)

# Seward Junction Improvements




# Seward Junction Improvements



# Seward Junction Improvements



# Precinct 3




## Southwest Bypass Segment 2 (Southbound IH 35 to RM 2243)

---

21

Anticipated Completion  
Spring 2020

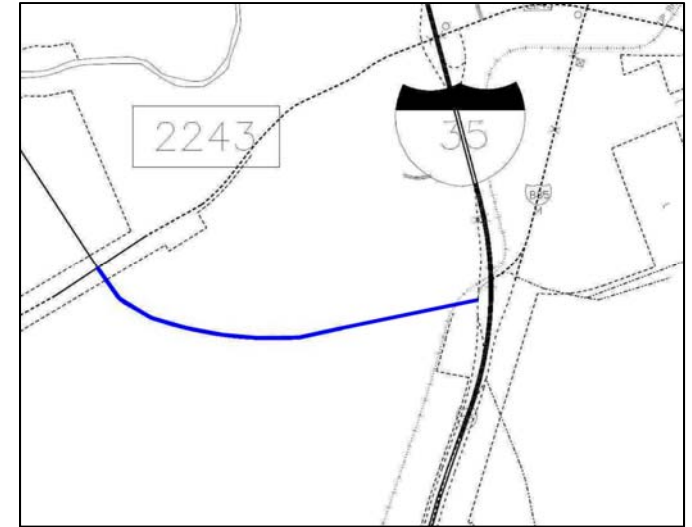

Original Contract Amount = \$8,087,943.77


Total Change Orders = \$0.00

Adjusted Contract Price = \$8,087,943.77

Expenditures to Date = \$6,648,852.90 (82%)

## Southwest Bypass Segment 2 (Southbound IH 35 to RM 2243)

22

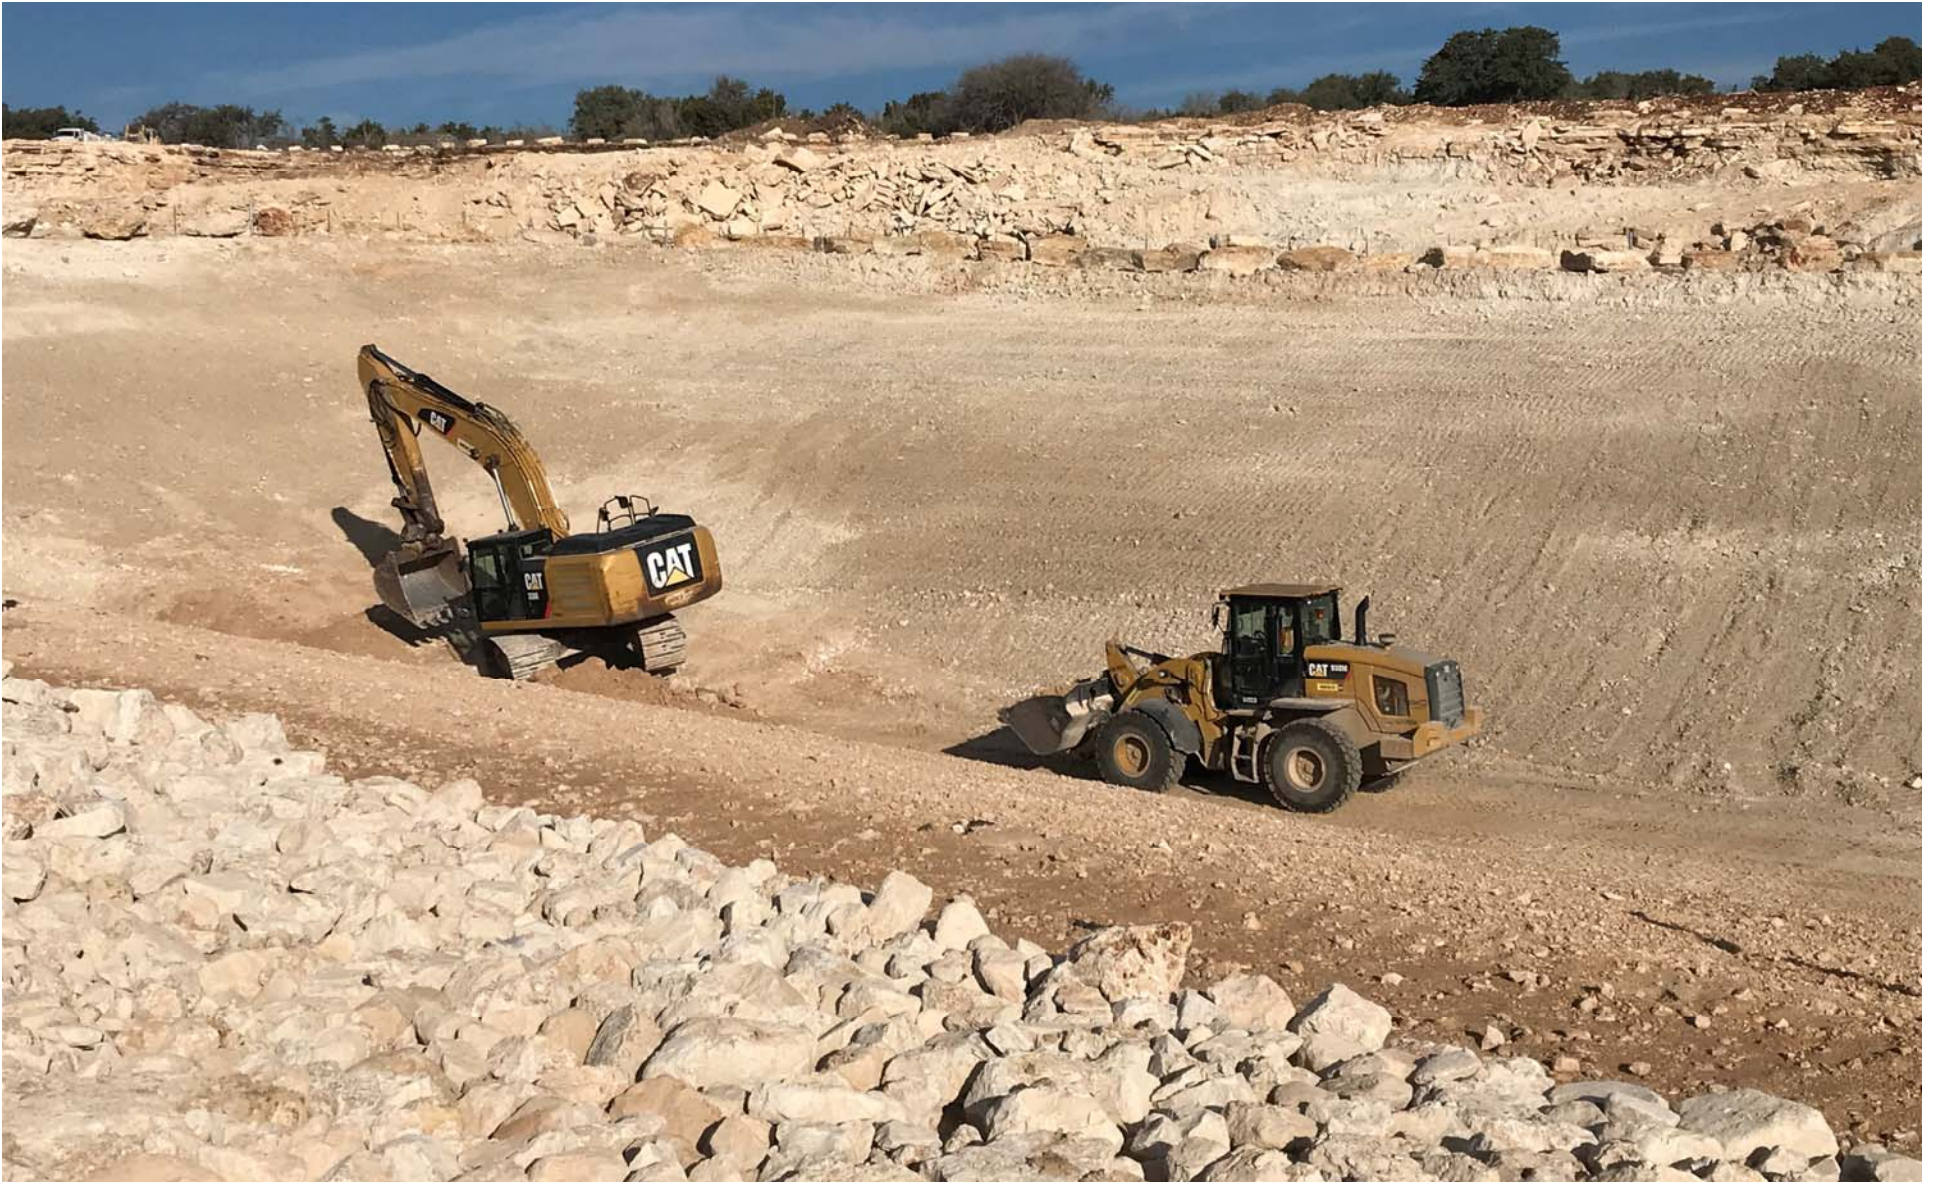

## Southwest Bypass Segment 2 (Southbound IH 35 to RM 2243)

23



## Southwest Bypass Segment 2 (Southbound IH 35 to RM 2243)

24




## CR 305 at IH 35 (Bridge Replacement)

---

25

Substantially Complete

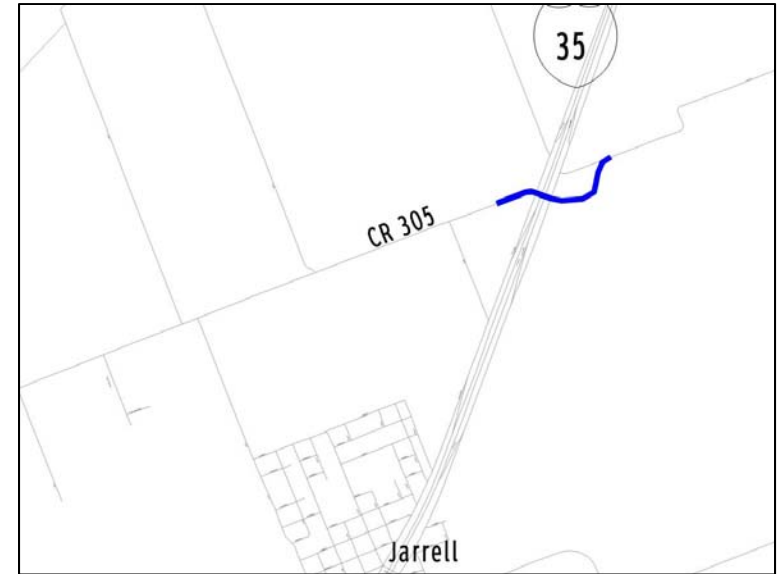

Partnership with TxDOT

Original Contract Amount = \$6,748,948.60

Construction is managed by TxDOT

# CR 305 at IH 35 (Bridge Replacement)



# CR 305 at IH 35 (Bridge Replacement)

27






# IH 35 Ramp Reversals and Frontage Road Conversion <sup>28</sup>

---

Anticipated Completion  
Late 2020

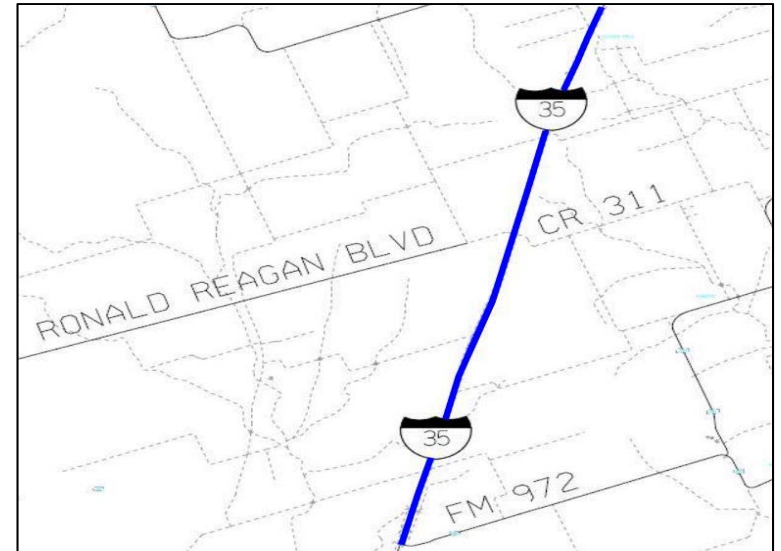

Partnership with TxDOT

Original Contract Amount = \$13,145,762.51

Construction is managed by TxDOT

# IH 35 Ramp Reversals and Frontage Road Conversion<sup>29</sup>



# IH 35 Ramp Reversals and Frontage Road<sup>30</sup> Conversion



# IH 35 Ramp Reversals and Frontage Road Conversion<sup>31</sup>




# Ronald Reagan Boulevard at IH 35 (Bridge Replacement)

---

32

Anticipated Completion  
Early 2021

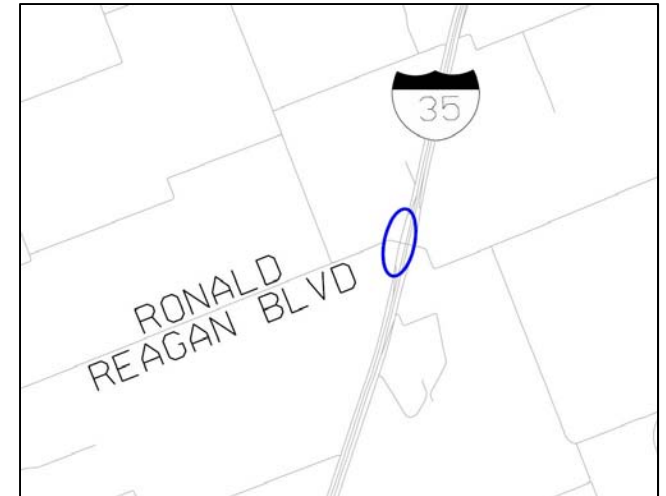

Partnership with TxDOT

Original Contract Amount = \$15,048,229.93

Construction is managed by TxDOT

# Ronald Reagan Boulevard at IH 35 (Bridge Replacement)

33



# Ronald Reagan Boulevard at IH 35 (Bridge Replacement)

34



# Ronald Reagan Boulevard at IH 35 (Bridge Replacement)

35




## CR 176 at RM 2243 (RM 2243 to Parkside Parkway)

---

36

Anticipated Completion  
Spring 2020

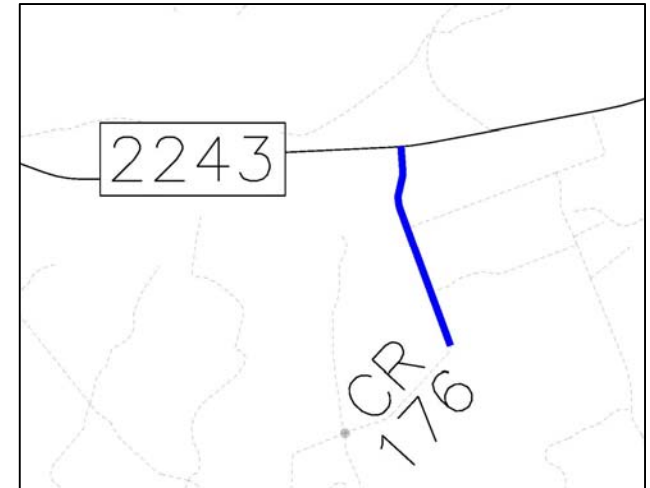

Original Contract Amount = \$2,447,560.00

Total Change Orders = \$208,869.67

Adjusted Contract Price = \$2,656,429.67

Expenditures to Date = \$1,264,228.51 (52%)

## CR 176 at RM 2243 (RM 2243 to Parkside Parkway)



## CR 176 at RM 2243 (RM 2243 to Parkside Parkway)




## Limestone Terrace & Quarry Rim (Sonterra Boulevard to IH 35 Frontage Road)

---

39

Anticipated Completion  
Early 2020

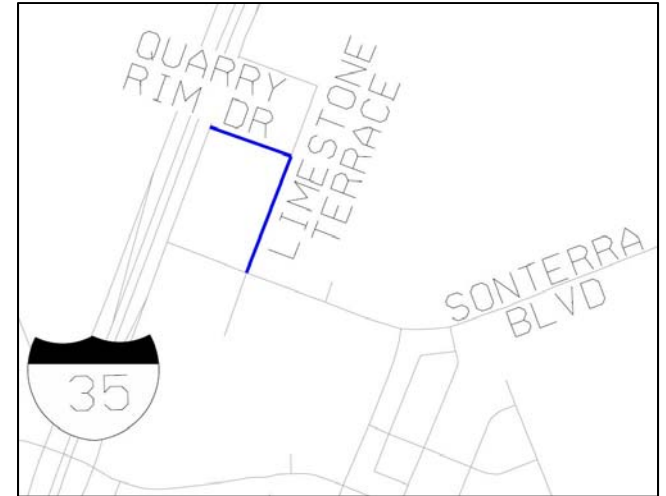

Original Contract Amount = \$1,060,707.70

Total Change Orders = \$44,272.00

Adjusted Contract Price = \$1,104,979.70

Expenditures to Date = \$1,026,859.92 (93%)

## Limestone Terrace & Quarry Rim (Sonterra Boulevard to IH 35 Frontage Road)




# Limestone Terrace & Quarry Rim (Sonterra Boulevard to IH 35 Frontage Road)



## Limestone Terrace & Quarry Rim (Sonterra Boulevard to IH 35 Frontage Road)




# Precinct 4

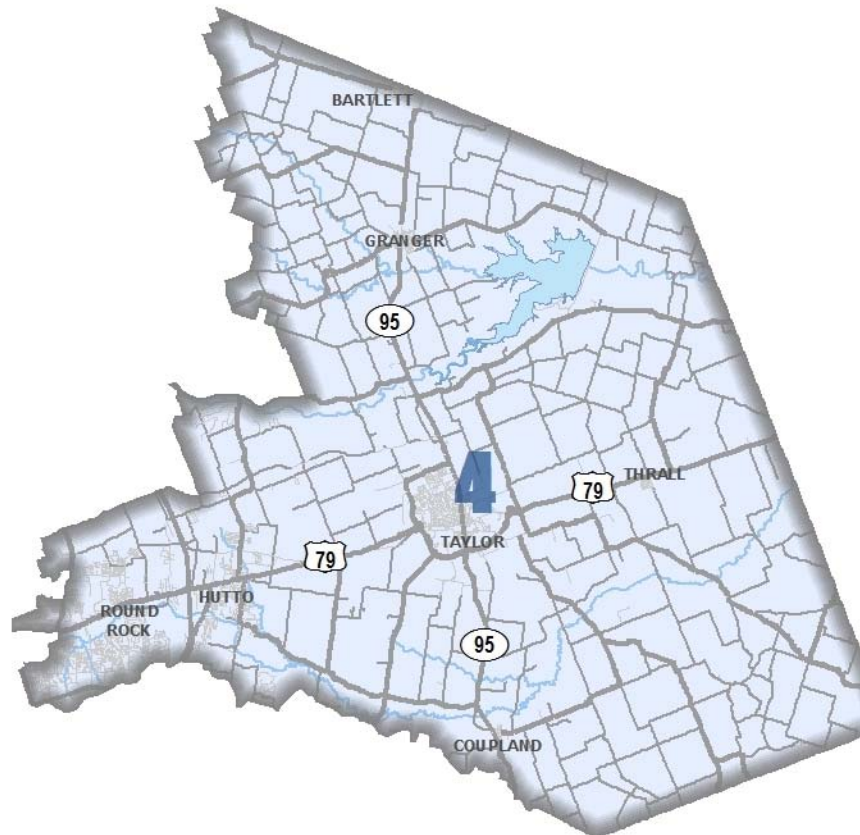

## CR 110 Middle (Limmer Loop to CR 107)

Anticipated Completion  
Summer 2020

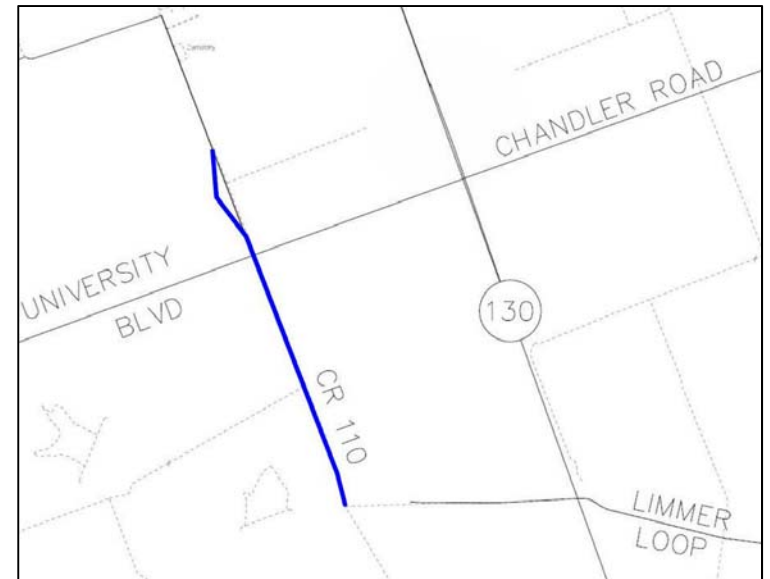

Original Contract Amount = \$8,910,862.73

Total Change Orders = \$66,291.83

Adjusted Contract Price = \$8,977,154.56

Expenditures to Date = \$3,515,392.04 (39%)

## CR 110 Middle (Limmer Loop to CR 107)



## CR 110 Middle (Limmer Loop to CR 107)



## CR 110 Middle (Limmer Loop to CR 107)

