




Williamson County Commissioners Court

Road Bond Program

July 20, 2021




Precinct 1

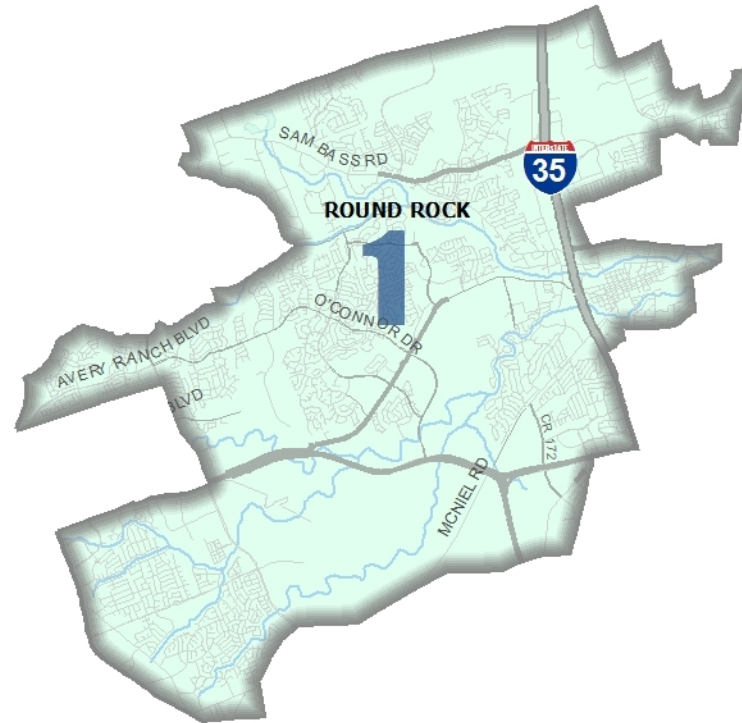

Forest North Phase 3 Drainage Improvements

Anticipated Completion
Early 2022

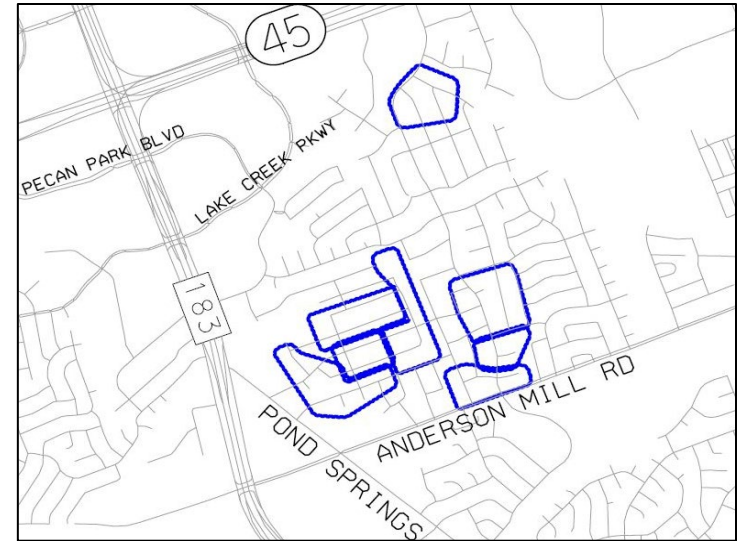

Original Contract Price = \$4,793,058.15

Total Change Orders to Date = \$87,744.37

Adjusted Contract Price = \$4,880,802.52

Expenditures to Date = \$3,247,749.14 (67%)

Forest North Phase 3 Drainage Improvements



Forest North Phase 3 Drainage Improvements




Forest North Phase 3 Drainage Improvements



O'Connor Traffic Signals

(Morgan Hill Trail, Liberty Walk, Great Oaks)

Anticipated Completion
Summer 2021

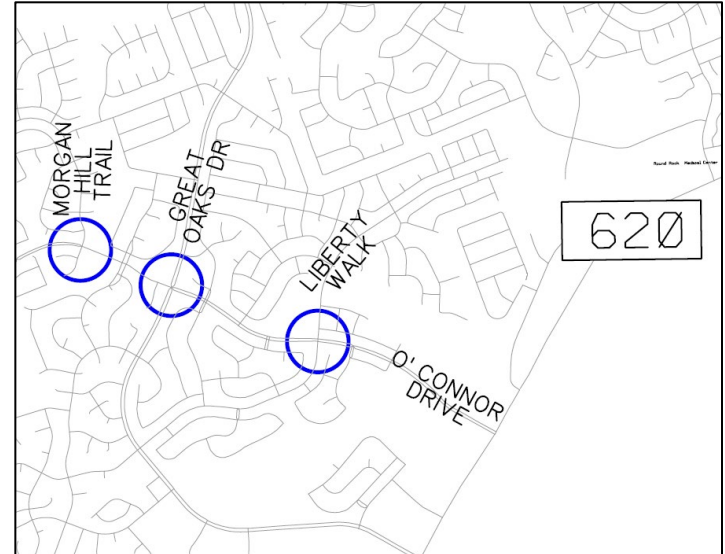

Original Contract Price = \$853,503.50

Total Change Orders to Date = \$131,055.38

Adjusted Contract Price = \$984,558.88

Expenditures to Date = \$776,076.14 (79%)

O'Connor Traffic Signals (Morgan Hill Trail, Liberty Walk, Great Oaks)



O'Connor Traffic Signals (Morgan Hill Trail, Liberty Walk, Great Oaks)




O'Connor Traffic Signals (Morgan Hill Trail, Liberty Walk, Great Oaks)



Hairy Man Road / Brushy Creek Road Safety Improvements

Anticipated Completion
Winter 2021

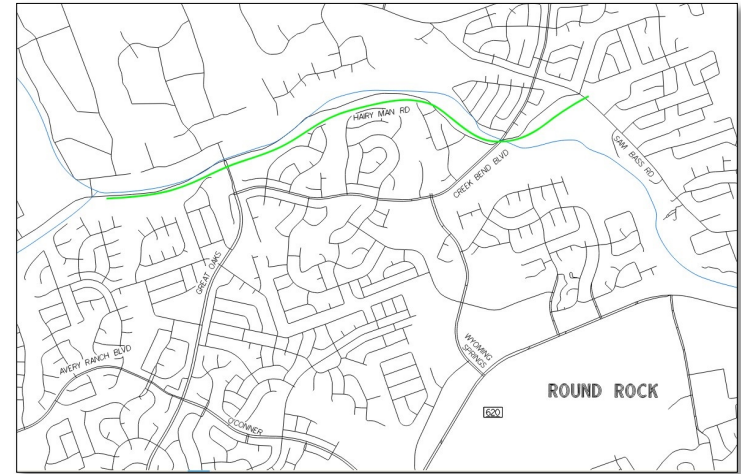

Original Contract Price = \$3,964,380.00

Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$3,964,380.00

Expenditures to Date = \$1,357,425.72 (34%)

Hairy Man Road / Brushy Creek Road Safety Improvements




Hairy Man Road / Brushy Creek Road Safety Improvements



Hairy Man Road / Brushy Creek Road Safety Improvements




Precinct 2




All construction projects are
substantially complete

Precinct 3

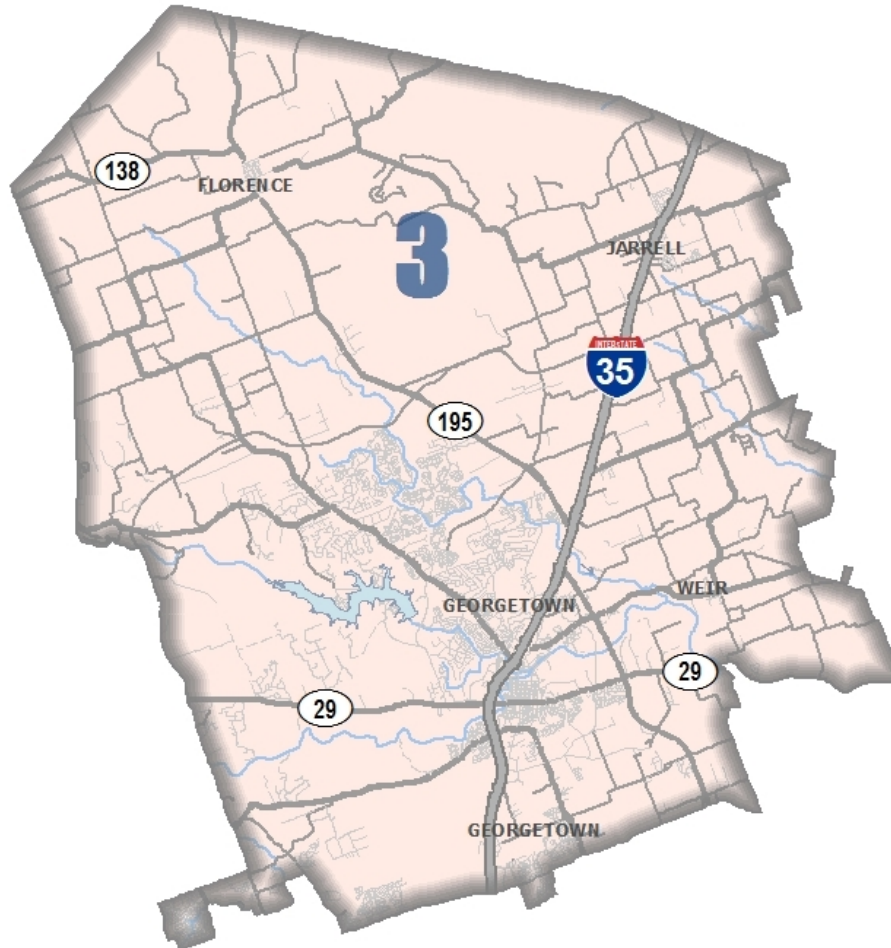

Ronald Reagan Boulevard at IH 35 (Bridge Replacement)

Anticipated Completion
Fall 2021

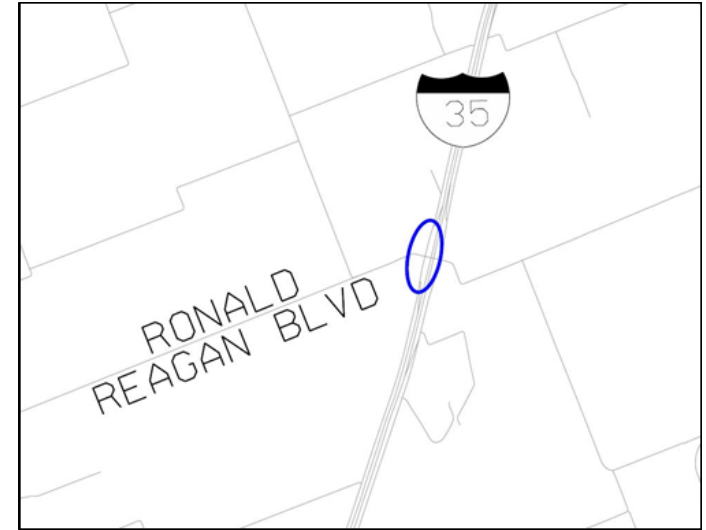

Partnership with TxDOT

Original Contract Amount = \$15,048,229.93

Construction is managed by TxDOT



Ronald Reagan Boulevard at IH 35 (Bridge Replacement)




Ronald Reagan Boulevard at IH 35 (Bridge Replacement)



Ronald Reagan Boulevard at IH 35 (Bridge Replacement)




Precinct 4

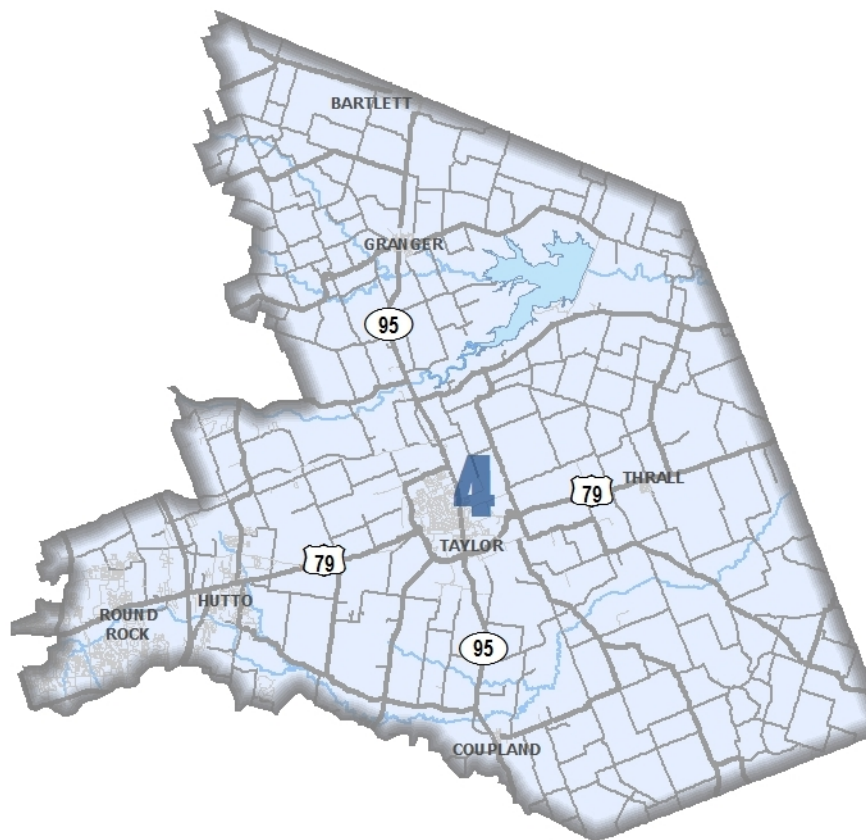

(US 79 to North of Chandler Road)

Anticipated Completion
Winter 2021

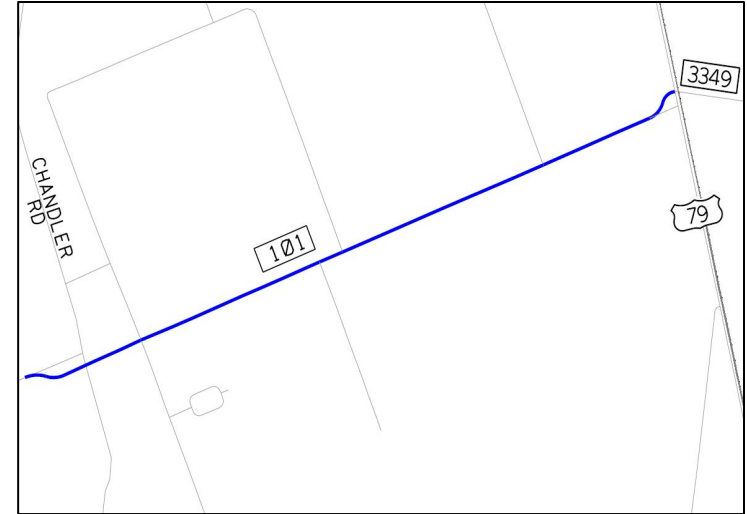

Original Contract Amount = \$13,092,842.00

Total Change Orders = \$0.00

Adjusted Contract Price = \$13,092,842.00

Expenditures to Date = \$6,735,532.21 (51%)

CR 101 (US 79 to North of Chandler Road)



CR 101 (US 79 to North of Chandler Road)



CR 101 (US 79 to North of Chandler Road)

