




# Williamson County Commissioners Court

---

Road Bond Program  
September 21, 2021



# Precinct 1

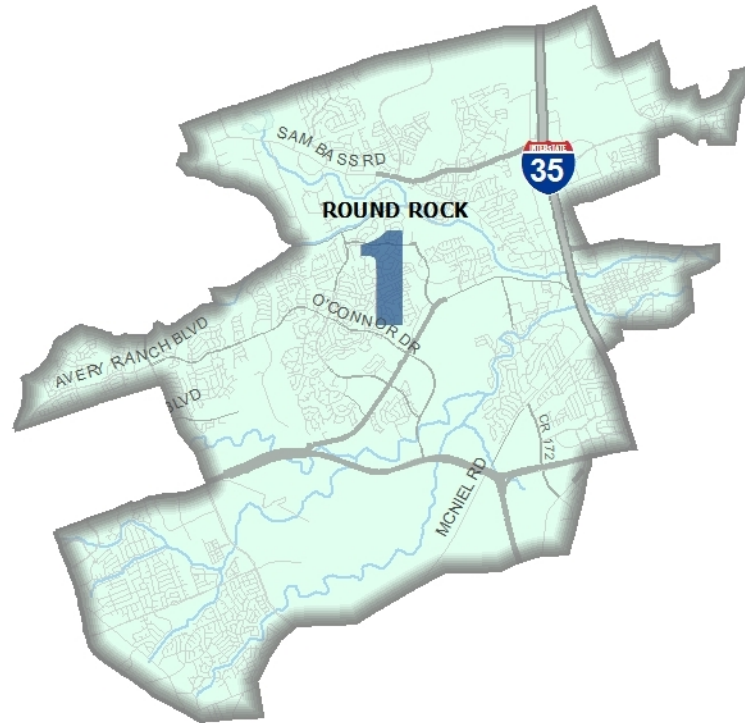




# RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)

---

3

Anticipated Completion  
Summer 2022

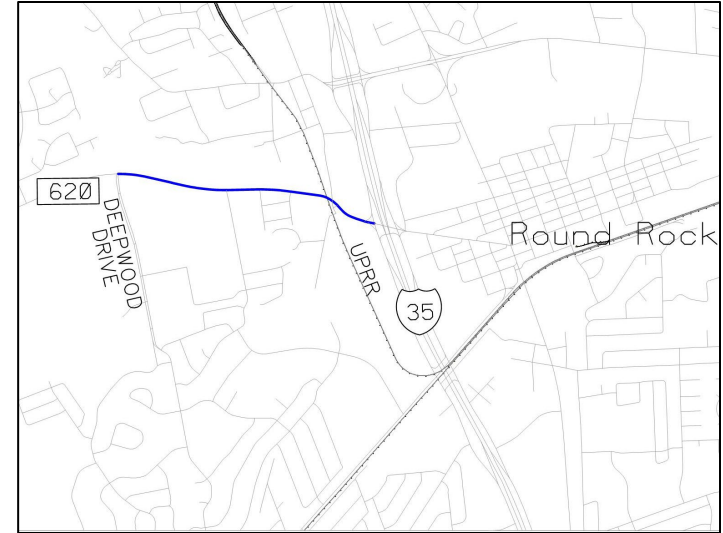

Partnership with TxDOT and the City of Round Rock  
Original Contract Amount = \$27,468,703.67  
Construction is managed by TxDOT

# RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)





# RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)






# RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)



# Forest North Phase 3 Drainage Improvements

Anticipated Completion  
Early 2022

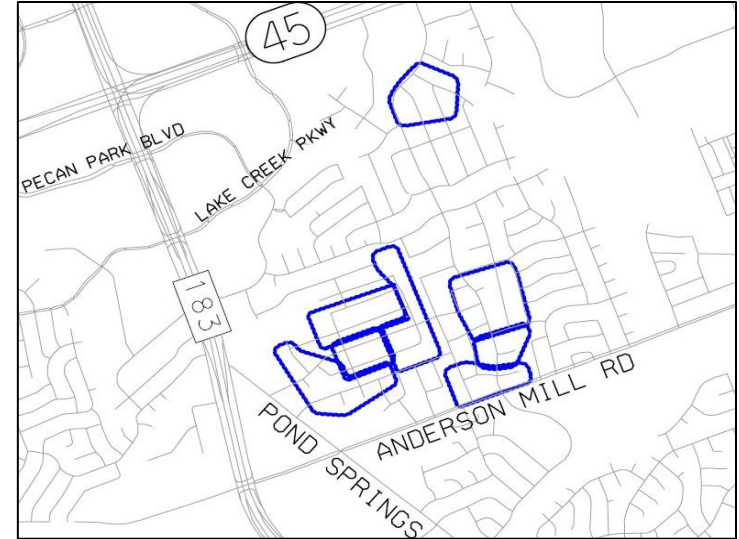

Original Contract Price = \$4,793,058.15

Total Change Orders to Date = \$87,744.37

Adjusted Contract Price = \$4,880,802.52

Expenditures to Date = \$3,787,788.99 (78%)



# Forest North Phase 3 Drainage Improvements





# Forest North Phase 3 Drainage Improvements





# Forest North Phase 3 Drainage Improvements






# O'Connor Traffic Signals

## (Morgan Hill Trail, Liberty Walk, Great Oaks)

---

Anticipated Completion  
Fall 2021

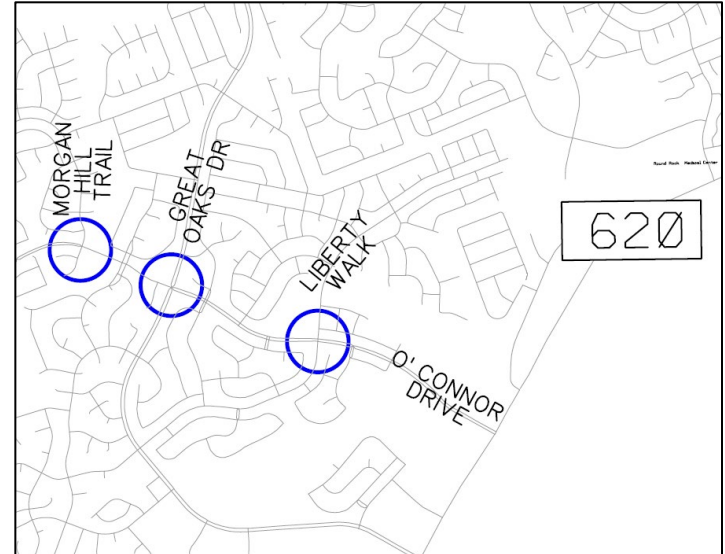

Original Contract Price = \$853,503.50

Total Change Orders to Date = \$131,055.38

Adjusted Contract Price = \$984,558.88

Expenditures to Date = \$792,333.64 (80%)



# O'Connor Traffic Signals (Morgan Hill Trail, Liberty Walk, Great Oaks)





# O'Connor Traffic Signals (Morgan Hill Trail, Liberty Walk, Great Oaks)






# O'Connor Traffic Signals (Morgan Hill Trail, Liberty Walk, Great Oaks)



# Hairy Man Road / Brushy Creek Road Safety Improvements

---

Anticipated Completion  
Winter 2021

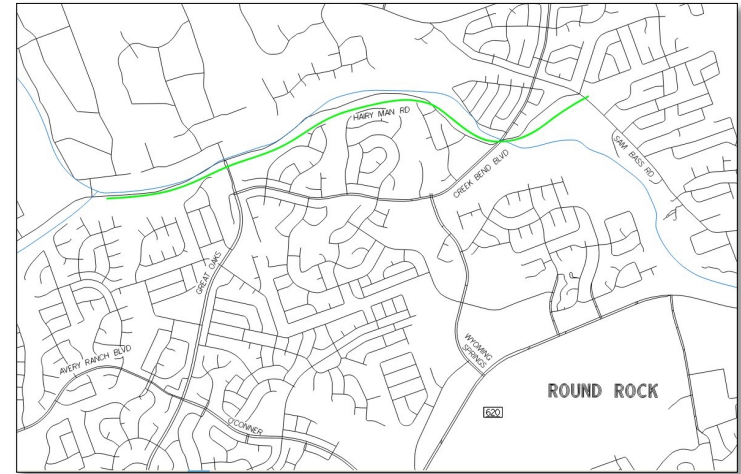

Original Contract Price = \$3,964,380.00

Total Change Orders to Date = \$9,904.00

Adjusted Contract Price = \$3,974,284.00

Expenditures to Date = \$3,121,917.92 (79%)



# Hairy Man Road / Brushy Creek Road Safety Improvements





# Hairy Man Road / Brushy Creek Road Safety Improvements






# Hairy Man Road / Brushy Creek Road Safety Improvements





# University Boulevard Widening (IH 35 to Sunrise Road)

Anticipated Completion  
Early 2022

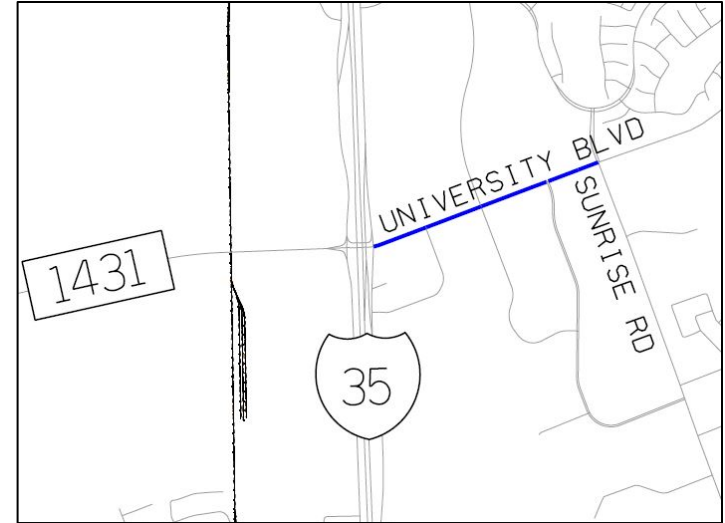

Partnership with the City of Round Rock

Original Contract Amount = \$12,135,410.45

Construction is managed by the City of Round Rock

# University Boulevard Widening (IH 35 to Sunrise Road)





# University Boulevard Widening (IH 35 to Sunrise Road)






# University Boulevard Widening (IH 35 to Sunrise Road)




# Precinct 2



All construction projects are substantially complete.




# Precinct 3



# Ronald Reagan Boulevard at IH 35 (Bridge Replacement)

---

Anticipated Completion  
Fall 2021

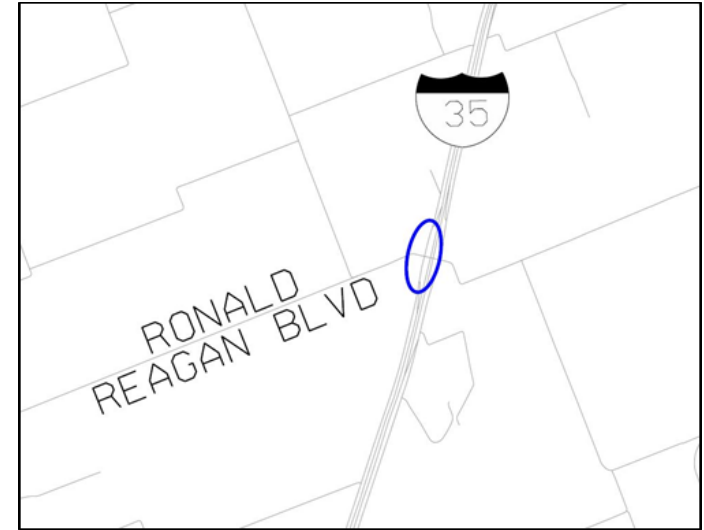

Partnership TxDOT

Original Contract Amount = \$15,048,229.93

Construction is managed by TxDOT

# Ronald Reagan Boulevard at IH 35 (Bridge Replacement)





# Ronald Reagan Boulevard at IH 35 (Bridge Replacement)






# Ronald Reagan Boulevard at IH 35 (Bridge Replacement)



## (DB Woods Intersection)

Anticipated Completion  
Fall 2022

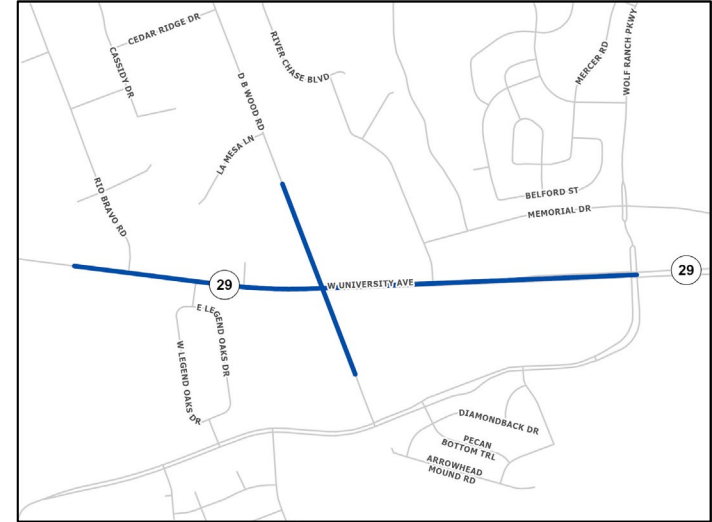

Partnership TxDOT

Original Contract Amount = \$5,548,287.93

Construction is managed by TxDOT



# SH 29 (DB Woods Intersection)





# SH 29 (DB Woods Intersection)






# SH 29 (DB Woods Intersection)



# Precinct 4

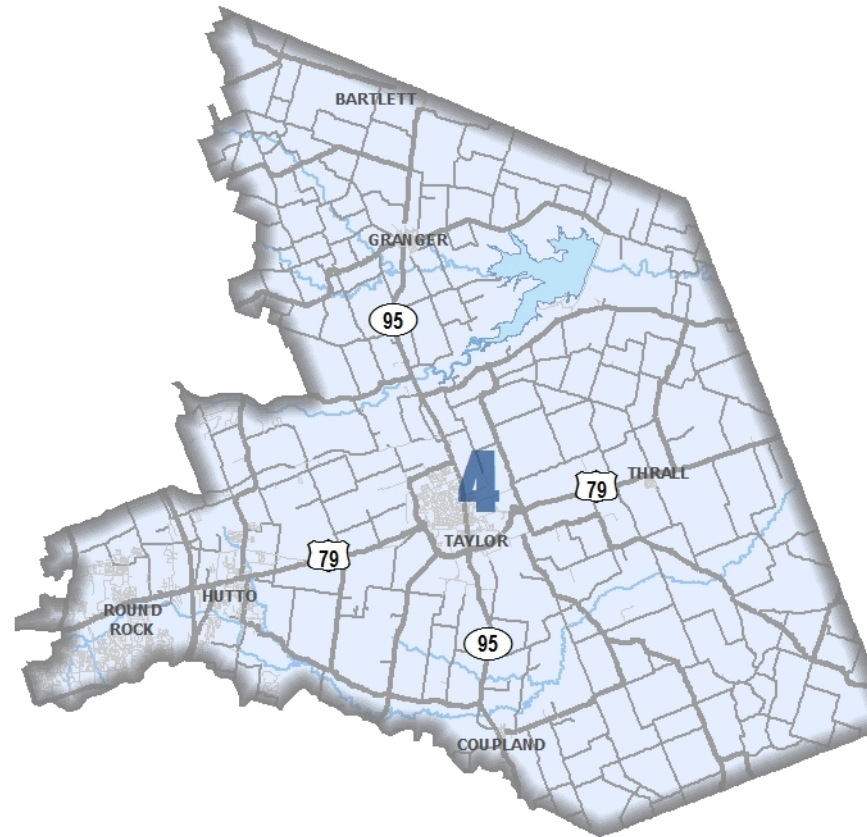




## (US 79 to North of Chandler Road)

---

Anticipated Completion

Fall 2021

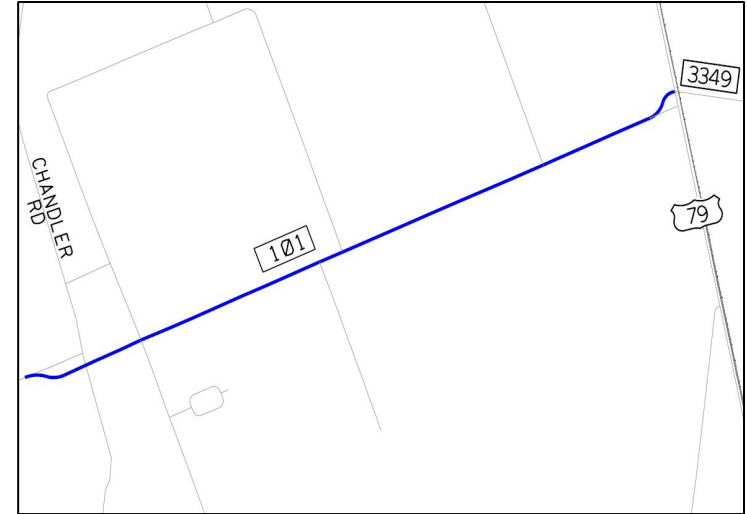

Original Contract Amount = \$13,092,842.00

Total Change Orders = \$0.00

Adjusted Contract Price = \$13,092,842.00

Expenditures to Date = \$7,835,075.13 (59%)



# CR 101 (US 79 to North of Chandler Road)





# CR 101 (US 79 to North of Chandler Road)





# CR 101 (US 79 to North of Chandler Road)






# Southeast Loop Segment 1, Phase 1 (Corridor E1) (CR 138 to CR 137)

38

Anticipated Completion  
Fall 2022

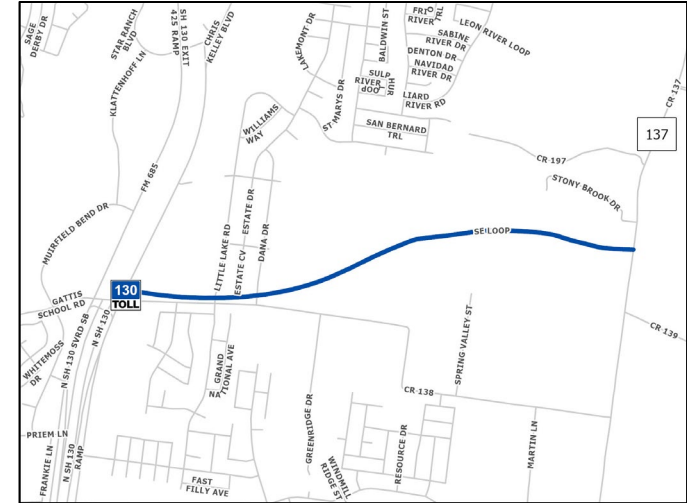

Original Contract Amount = \$11,526,789.09

Total Change Orders = \$148,710.35

Adjusted Contract Price = \$11,675,499.44

Expenditures to Date = \$852,678.96 (7%)



# Southeast Loop Segment 1, Phase 1 (Corridor E1) (CR 138 to CR 137)





# Southeast Loop Segment 1, Phase 1 (Corridor E1) (CR 138 to CR 137)






# Southeast Loop Segment 1, Phase 1 (Corridor E1) (CR 138 to CR 137)





# University Boulevard Expansion (Chandler Road)

Anticipated Completion  
Spring 2022

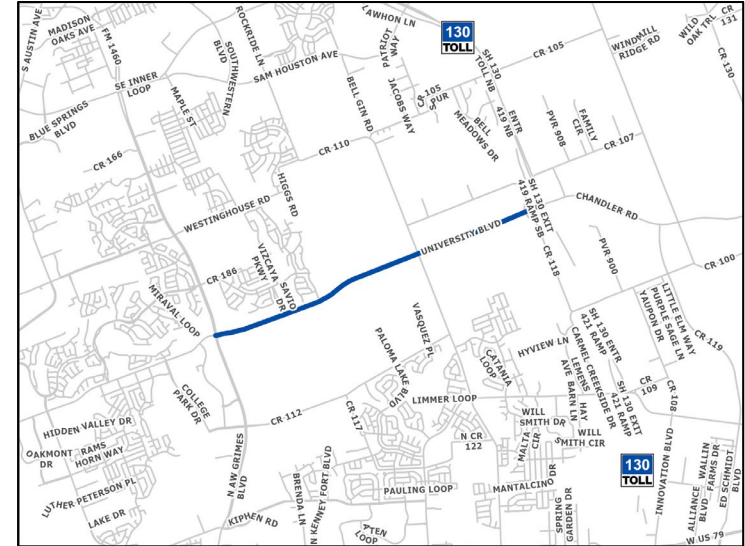

Partnership with the City of Round Rock

Original Contract Amount = \$11,104,890.49

Construction is managed by the City of Round Rock



# University Boulevard Expansion (Chandler Road)





# University Boulevard Expansion (Chandler Road)





# University Boulevard Expansion (Chandler Road)

