




Williamson County Commissioners Court

Road Bond Program
October 19, 2021




Precinct 1

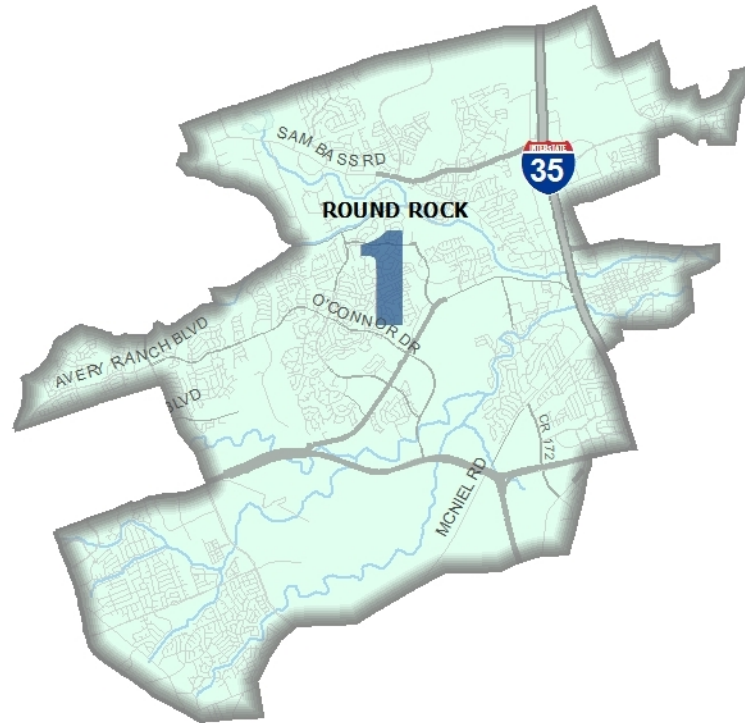

RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)

3

Anticipated Completion
Summer 2022

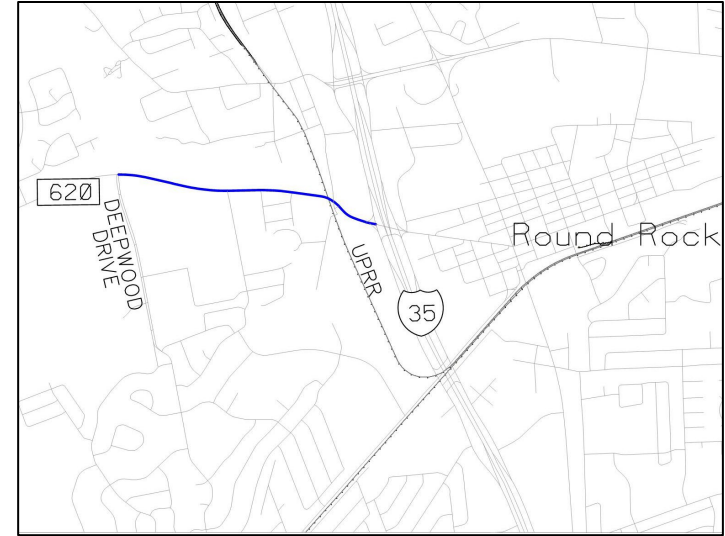

Partnership with TxDOT and the City of Round Rock
Original Contract Amount = \$27,468,703.67
Construction is managed by TxDOT

RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)



RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)




RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)



Forest North Phase 3 Drainage Improvements

Anticipated Completion
Early 2022

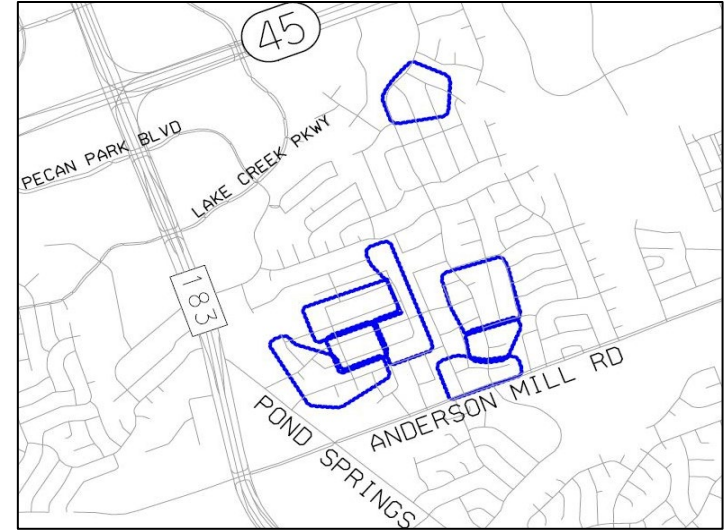

Original Contract Price = \$4,793,058.15

Total Change Orders to Date = \$87,744.37

Adjusted Contract Price = \$4,880,802.52

Expenditures to Date = \$3,787,788.99 (78%)

Forest North Phase 3 Drainage Improvements



Forest North Phase 3 Drainage Improvements




Forest North Phase 3 Drainage Improvements



O'Connor Traffic Signals

(Morgan Hill Trail, Liberty Walk, Great Oaks)

Anticipated Completion
Fall 2021

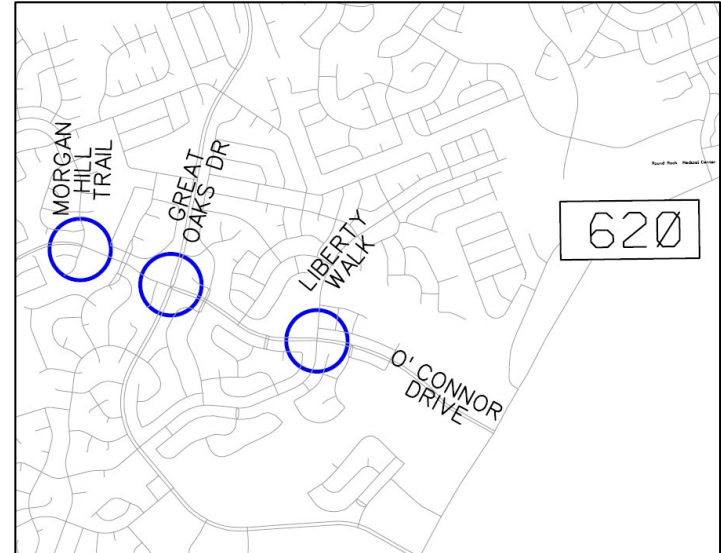

Original Contract Price = \$853,503.50

Total Change Orders to Date = \$168,601.88

Adjusted Contract Price = \$1,022,105.38

Expenditures to Date = \$923,502.51 (90%)

O'Connor Traffic Signals (Morgan Hill Trail, Liberty Walk, Great Oaks)



O'Connor Traffic Signals (Morgan Hill Trail, Liberty Walk, Great Oaks)




O'Connor Traffic Signals (Morgan Hill Trail, Liberty Walk, Great Oaks)



Hairy Man Road / Brushy Creek Road Safety Improvements

Anticipated Completion
Fall 2021

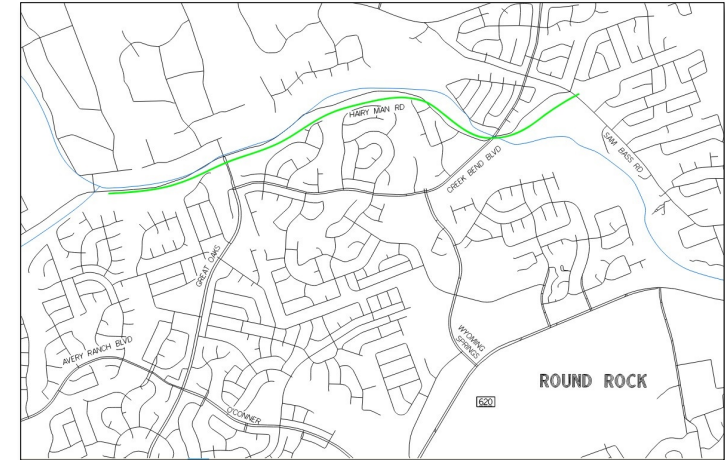

Original Contract Price = \$3,964,380.00

Total Change Orders to Date = \$9,904.00

Adjusted Contract Price = \$3,974,284.00

Expenditures to Date = \$3,121,917.92 (79%)

Hairy Man Road / Brushy Creek Road Safety Improvements



Hairy Man Road / Brushy Creek Road Safety Improvements




Hairy Man Road / Brushy Creek Road Safety Improvements



University Boulevard Widening (IH 35 to Sunrise Road)

Anticipated Completion
Early 2022

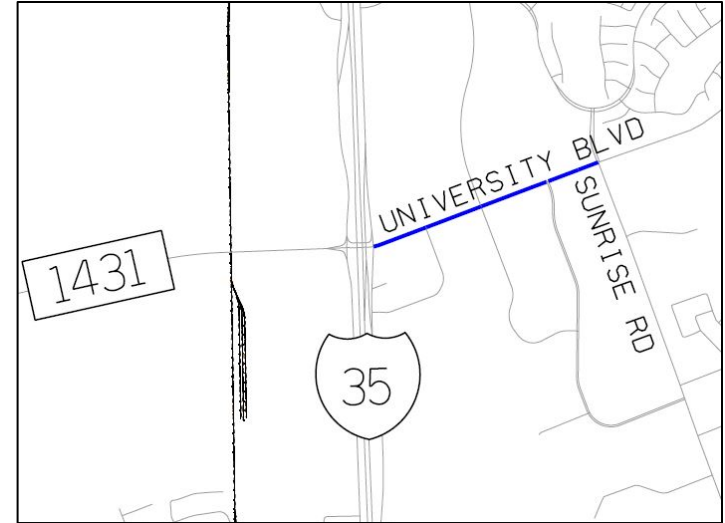

Partnership with the City of Round Rock

Original Contract Amount = \$12,135,410.45

Construction is managed by the City of Round Rock

University Boulevard Widening (IH 35 to Sunrise Road)



University Boulevard Widening (IH 35 to Sunrise Road)




University Boulevard Widening (IH 35 to Sunrise Road)



Great Oaks Bridge at Brushy Creek

Anticipated Completion
Early 2023

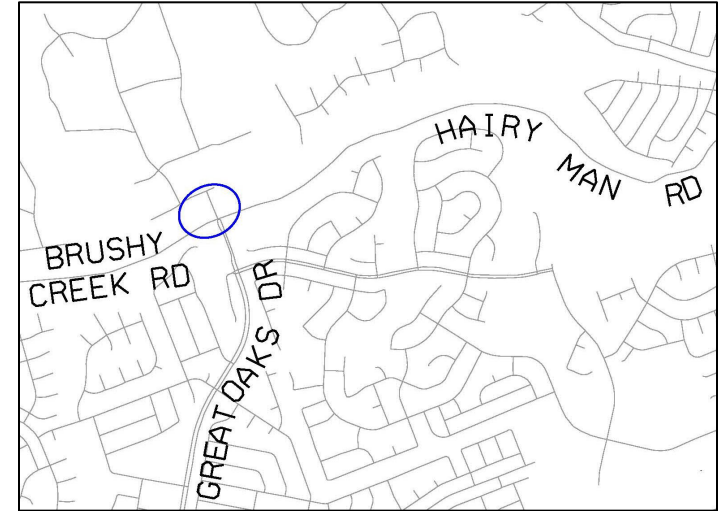

Original Contract Price = \$10,580,634.11

Total Change Orders to Date = \$0

Adjusted Contract Price = \$0

Expenditures to Date = \$0 (0%)

Great Oaks Bridge at Brushy Creek




Great Oaks Bridge at Brushy Creek



Great Oaks Bridge at Brushy Creek




Precinct 2




All construction projects are substantially complete.

Precinct 3

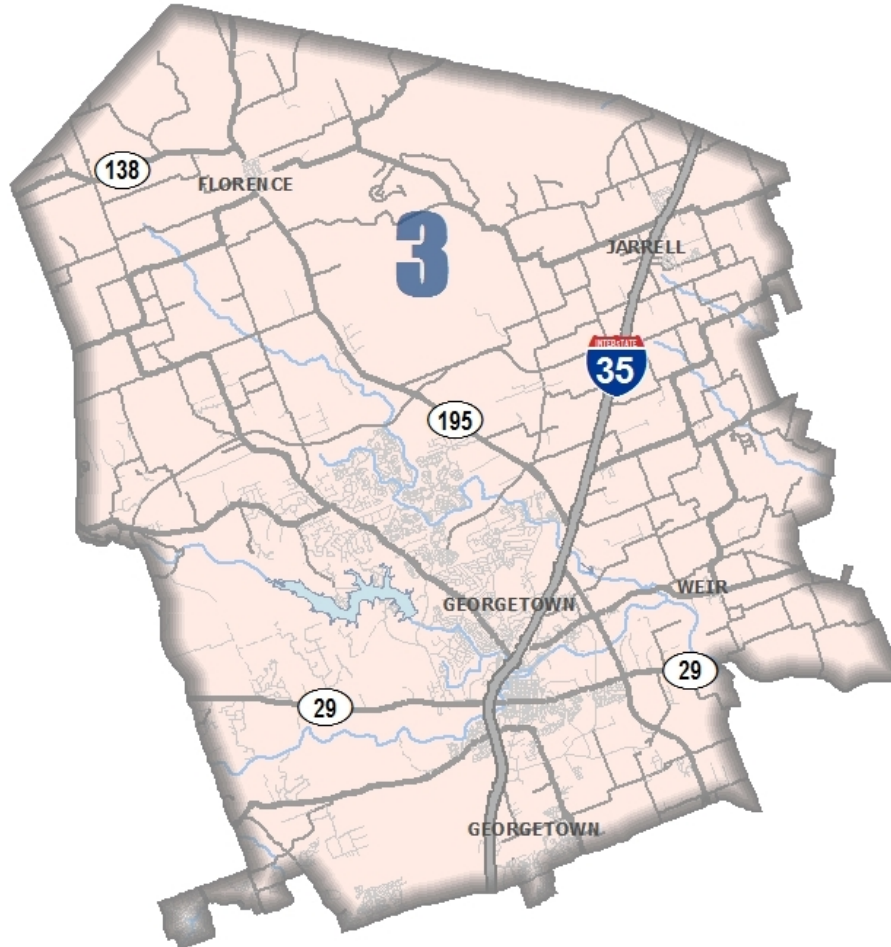

Ronald Reagan Boulevard at IH 35 (Bridge Replacement)

Anticipated Completion
Fall 2021

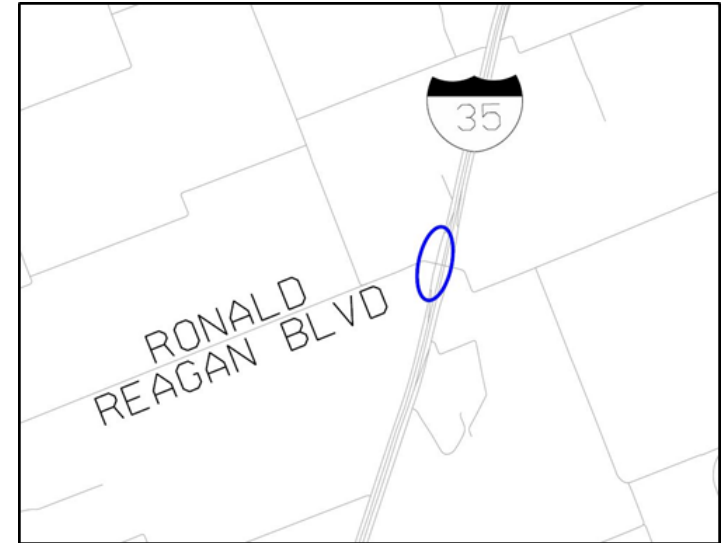

Partnership TxDOT

Original Contract Amount = \$15,048,229.93

Construction is managed by TxDOT

Ronald Reagan Boulevard at IH 35 (Bridge Replacement)



Ronald Reagan Boulevard at IH 35 (Bridge Replacement)




Ronald Reagan Boulevard at IH 35 (Bridge Replacement)



(DB Woods Intersection)

Anticipated Completion
Fall 2022

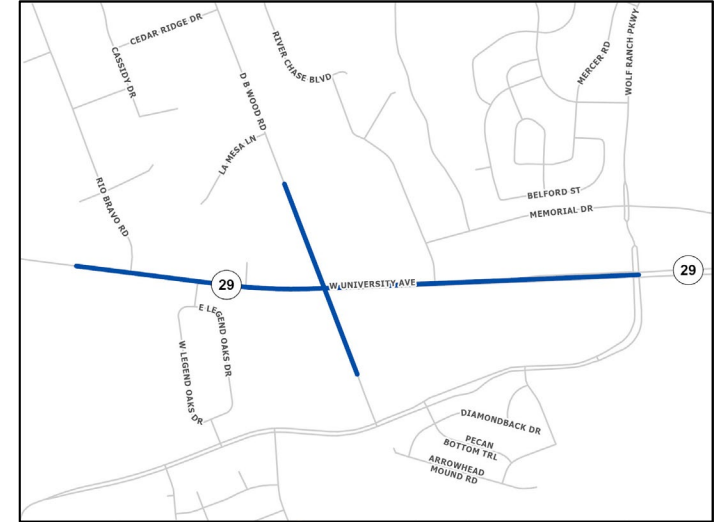

Partnership TxDOT

Original Contract Amount = \$5,548,287.93

Construction is managed by TxDOT

SH 29 (DB Woods Intersection)




SH 29 (DB Woods Intersection)



SH 29 (DB Woods Intersection)




Precinct 4

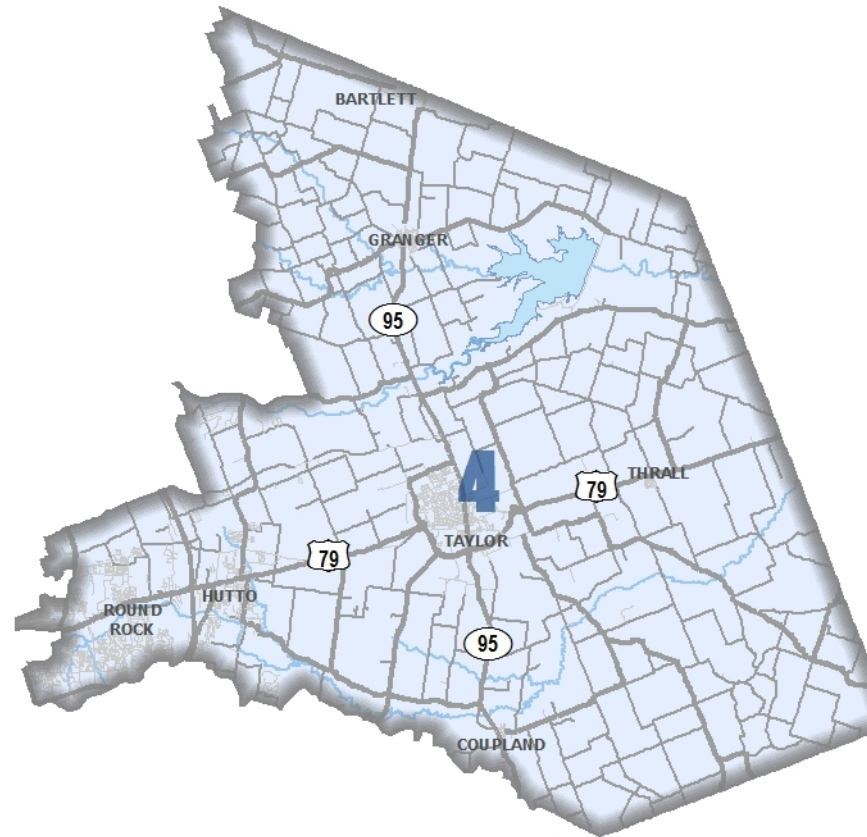

(US 79 to North of Chandler Road)

Anticipated Completion
Fall 2021

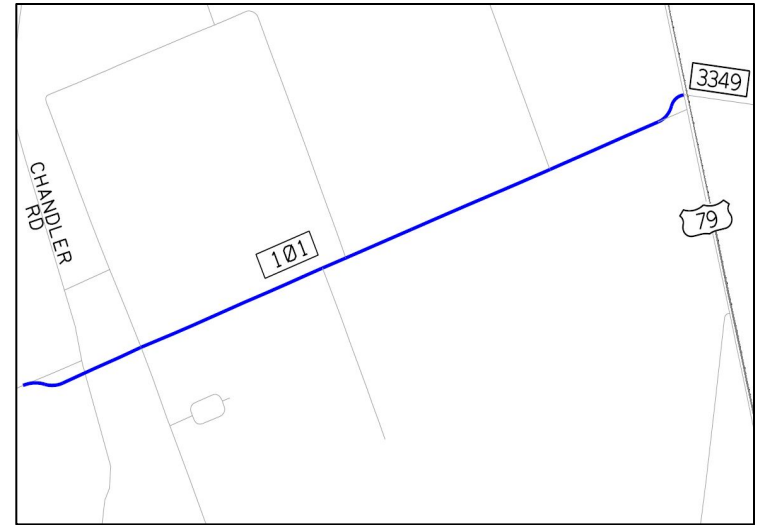

Original Contract Amount = \$13,092,842.00

Total Change Orders = \$-58,067.26

Adjusted Contract Price = \$13,034,774.74

Expenditures to Date = \$9,315,671.01 (71%)

CR 101 (US 79 to North of Chandler Road)



CR 101 (US 79 to North of Chandler Road)




CR 101 (US 79 to North of Chandler Road)



Southeast Loop Segment 1, Phase 1 (Corridor E1) (CR 138 to CR 137)

Anticipated Completion
Spring 2023

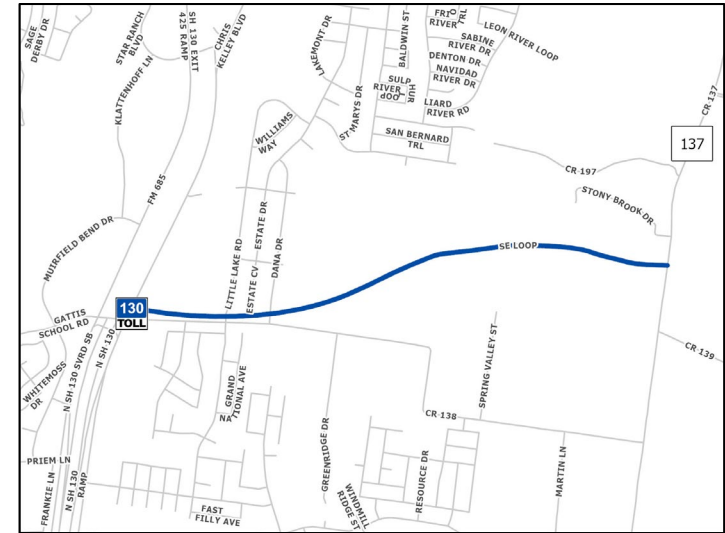

Original Contract Amount = \$11,526,789.09

Total Change Orders = \$148,710.35

Adjusted Contract Price = \$11,675,499.44

Expenditures to Date = \$1,181,291.65 (10%)

Southeast Loop Segment 1, Phase 1 (Corridor E1) (CR 138 to CR 137)



Southeast Loop Segment 1, Phase 1 (Corridor E1) (CR 138 to CR 137)




Southeast Loop Segment 1, Phase 1 (Corridor E1) (CR 138 to CR 137)



University Boulevard Expansion (Chandler Road)

Anticipated Completion
Spring 2022

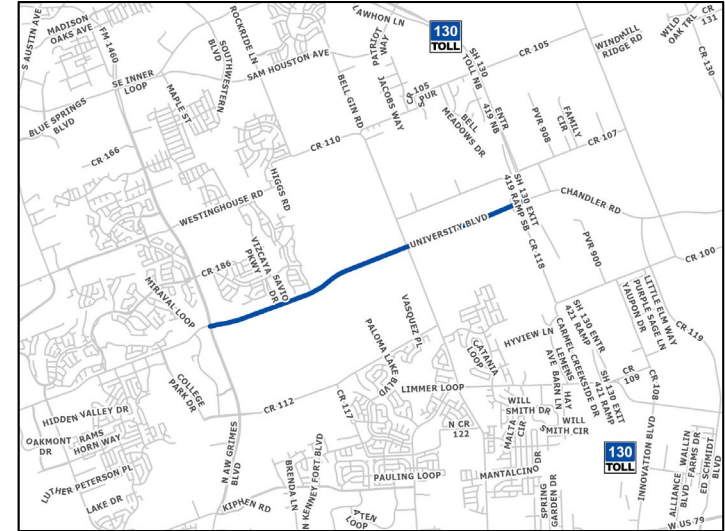

Partnership with the City of Round Rock

Original Contract Amount = \$11,104,890.49

Construction is managed by the City of Round Rock

University Boulevard Expansion (Chandler Road)



University Boulevard Expansion (Chandler Road)



University Boulevard Expansion (Chandler Road)

