



# Williamson County Commissioners Court


---

Road Bond Program

March 22, 2022




# Precinct 1

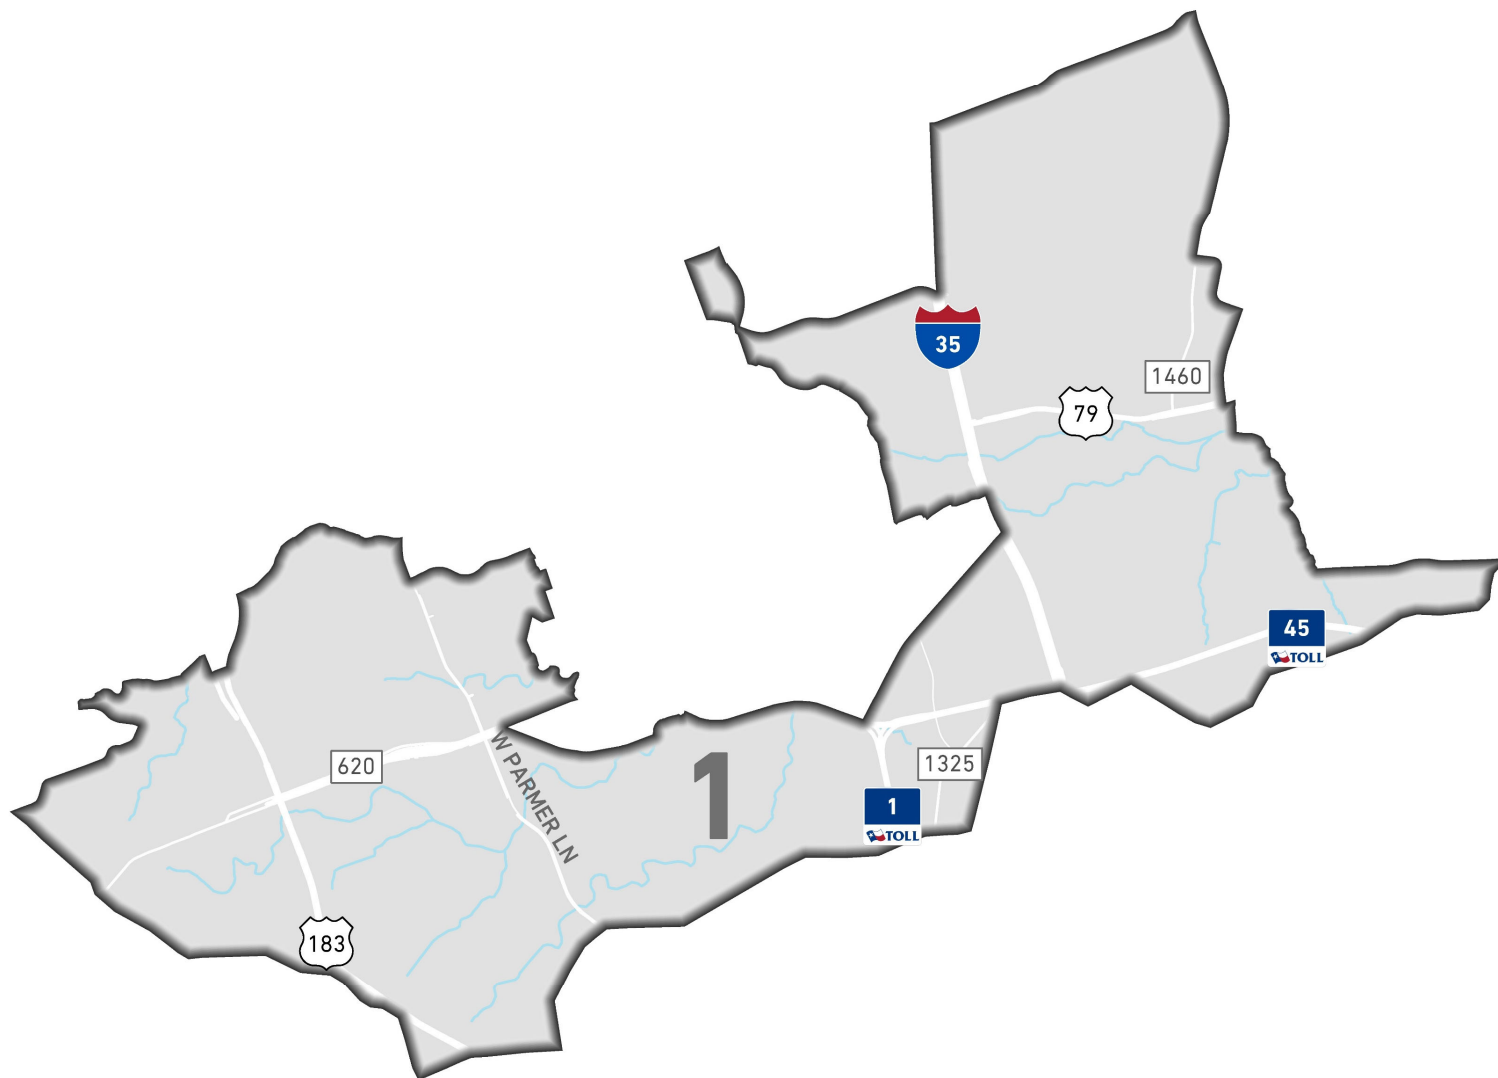

All Precinct 1 Construction Projects are  
Substantially Complete




# Precinct 2

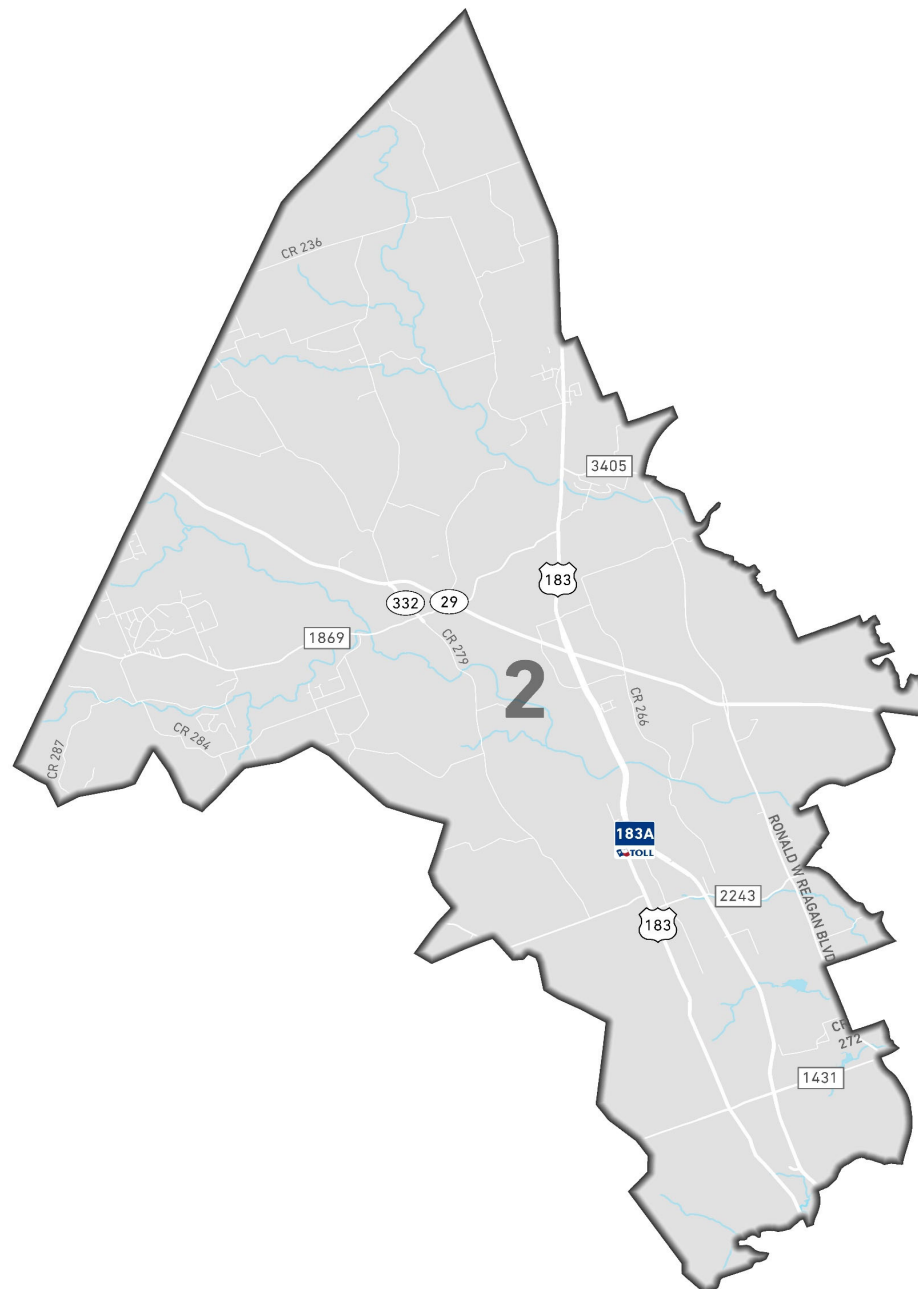

# CR 200 Reconstruction

Anticipated Completion  
Fall 2022

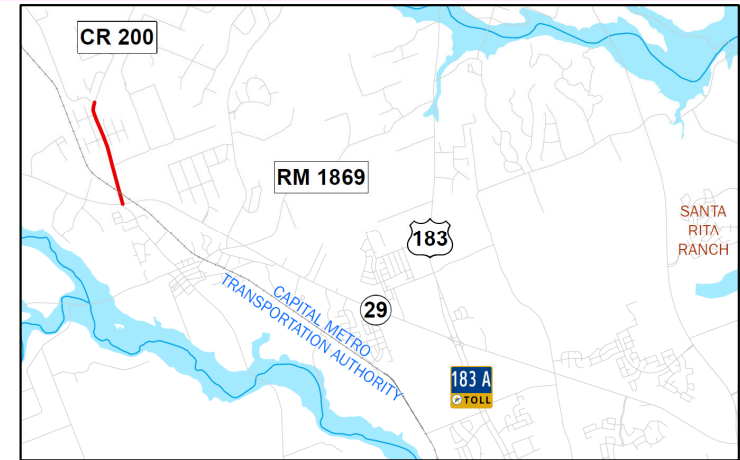

Original Contract Price = \$4,975,515.09

Total Change Orders to Date = \$0

Adjusted Contract Price = \$4,975,515.09

Expenditures to Date = \$987,484.00 (20%)



# CR 200 Reconstruction





# CR 200 Reconstruction






# CR 200 Reconstruction






# Precinct 3

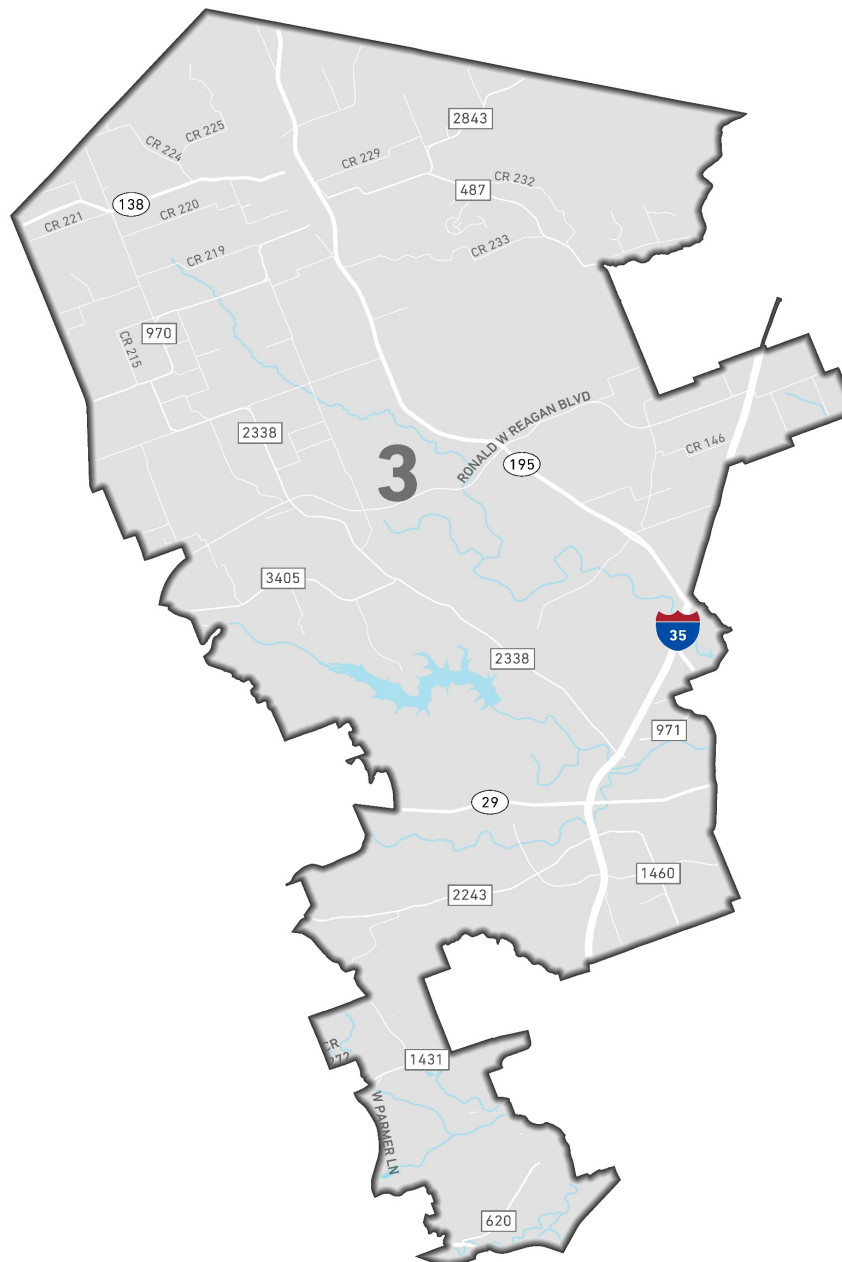

## (DB Woods Intersection)

---

Anticipated Completion  
Spring 2023

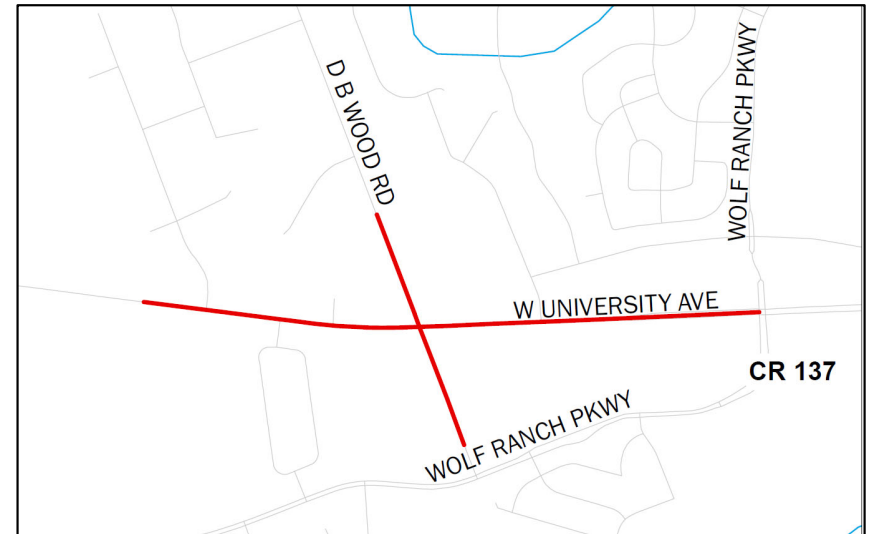

Partnership TxDOT

Original Contract Amount = \$5,548,287.93

Construction is managed by TxDOT

# SH 29 (DB Woods Intersection)





# SH 29 (DB Woods Intersection)






# SH 29 (DB Woods Intersection)



# Great Oaks Bridge at Brushy Creek

Anticipated Completion  
Spring 2023

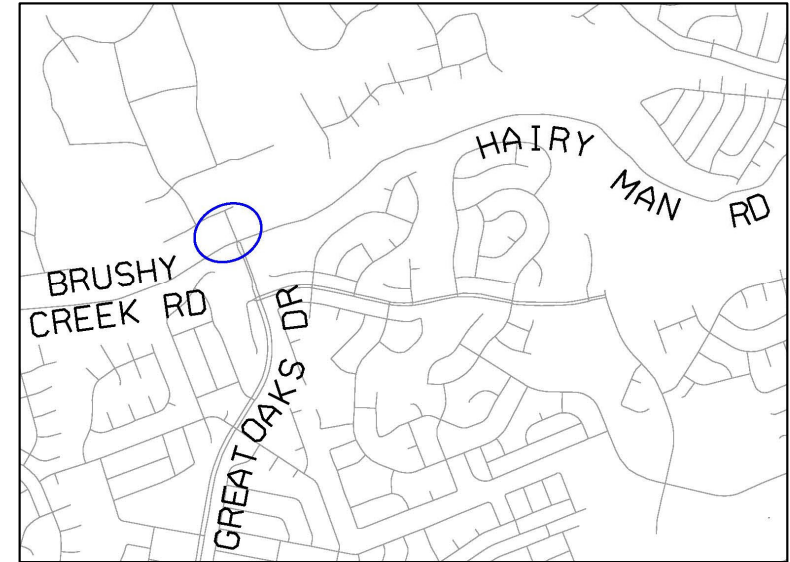

Original Contract Price = \$10,580,634.11  
Total Change Orders to Date = \$0  
Adjusted Contract Price = \$10,580,634.11  
Expenditures to Date = \$1,857,682.26 (18%)



# Great Oaks Bridge at Brushy Creek





# Great Oaks Bridge at Brushy Creek





# Great Oaks Bridge at Brushy Creek






# RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)

---

17

Anticipated Completion  
Summer 2022

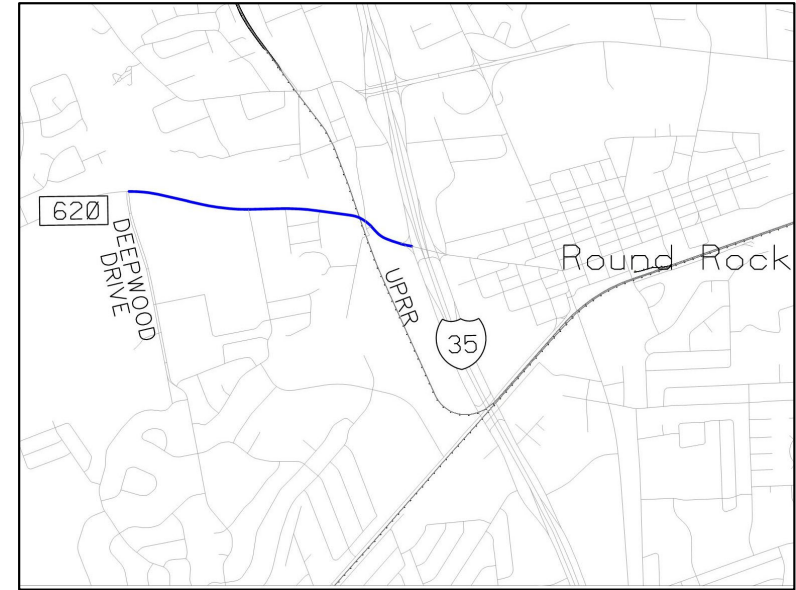

Partnership with TxDOT and the City of Round Rock  
Original Contract Amount = \$27,468,703.67  
Construction is managed by TxDOT

# RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)





# RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)






# RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)



# CR 111 Westinghouse Road

Anticipated Completion  
Early 2023

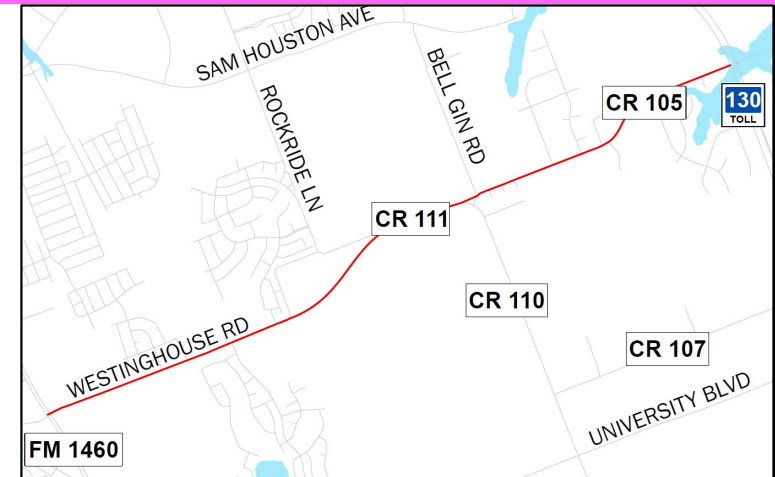

Original Contract Price = \$21,024,332.88

Total Change Orders to Date = \$0

Adjusted Contract Price = \$ 21,024,332.88

Expenditures to Date = \$0.00 (0%)



# CR 111 Westinghouse Road






# CR 111 Westinghouse Road





# CR 111 Westinghouse Road



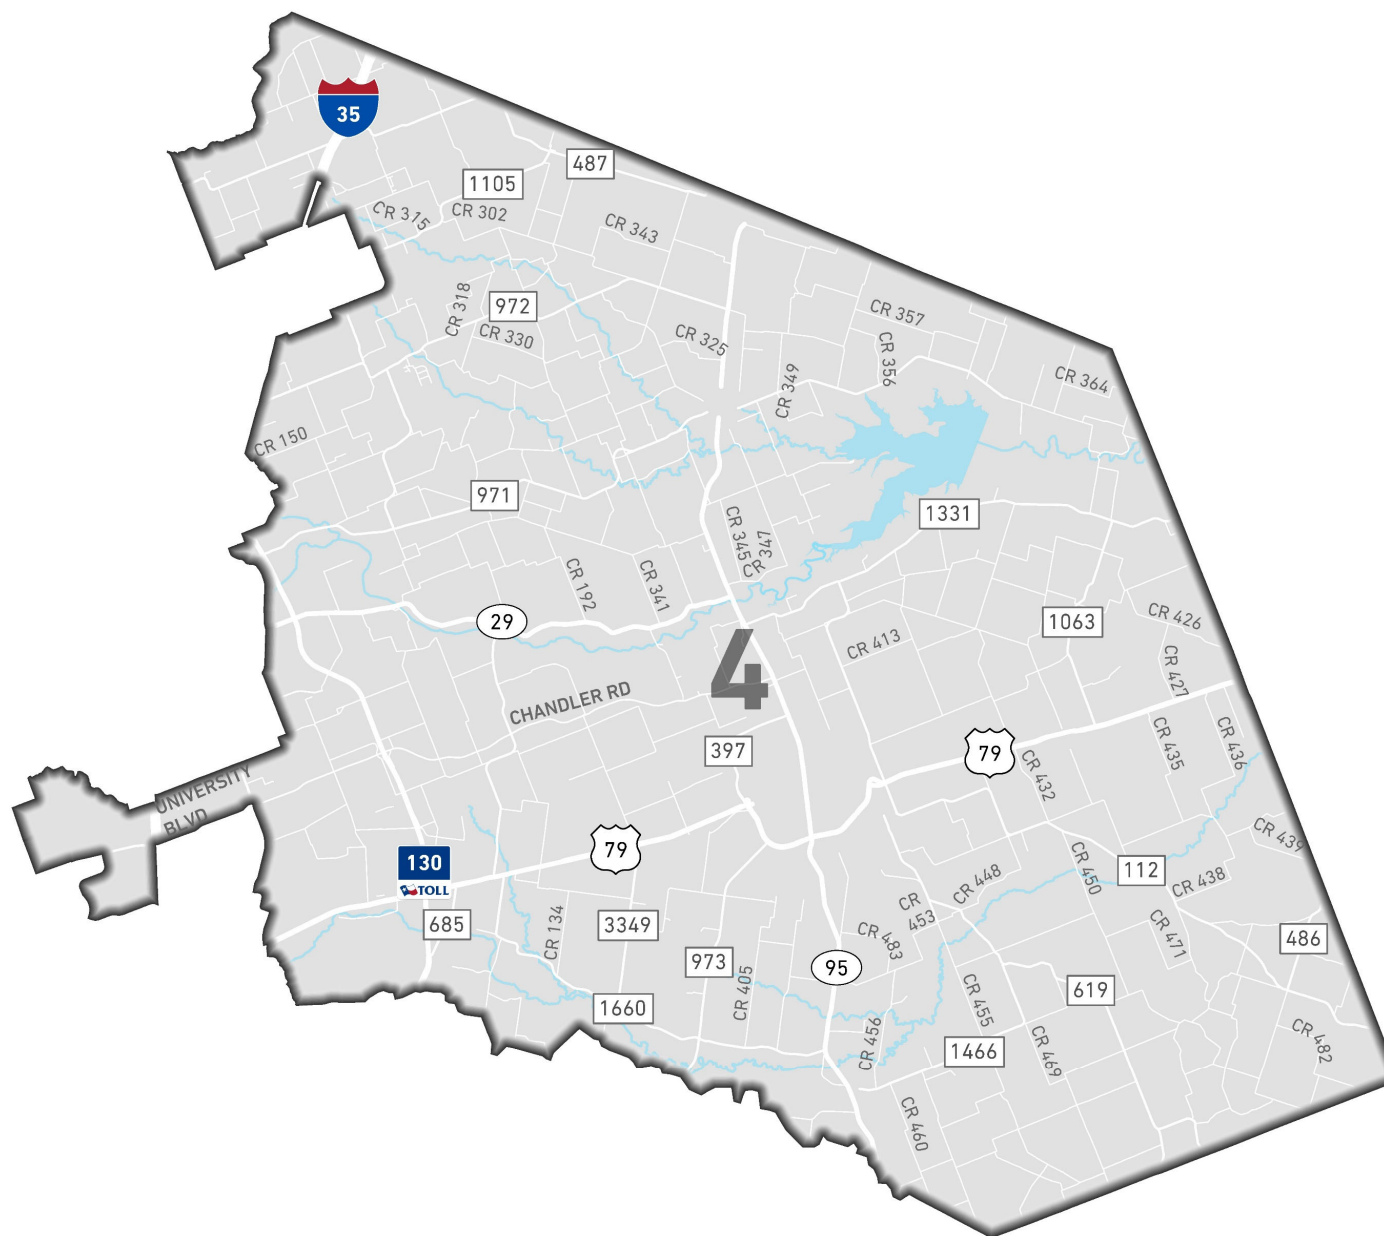

## (US 79 to North of Chandler Road)

---

Anticipated Completion  
Early 2022



Original Contract Amount = \$13,092,842.00

Total Change Orders = \$-58,067.26

Adjusted Contract Price = \$13,034,774.74

Expenditures to Date = \$11,123,699.23 (85%)



# CR 101 (US 79 to North of Chandler Road)





# CR 101 (US 79 to North of Chandler Road)








# CR 101 (US 79 to North of Chandler Road)



# Southeast Loop Segment 1, Phase 1 (Corridor E1) (CR 138 to CR 137)

Anticipated Completion  
Early 2023

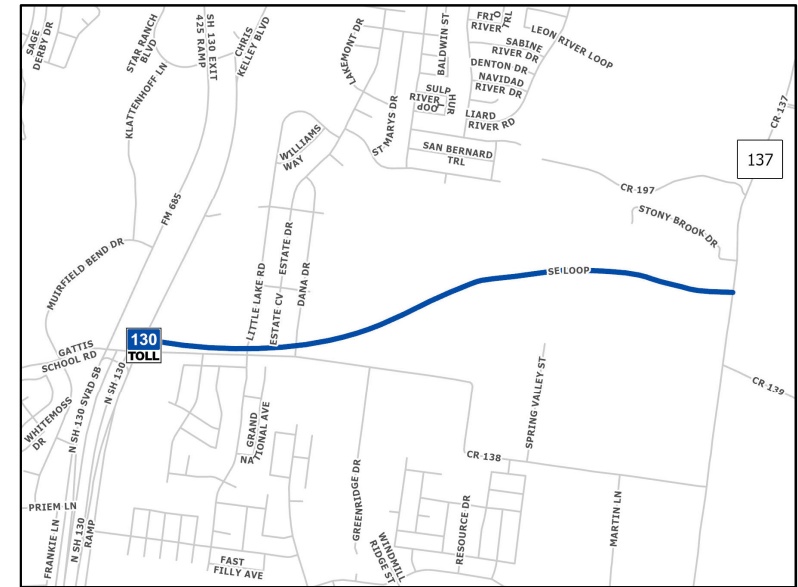

Original Contract Amount = \$11,526,789.09

Total Change Orders = \$148,710.35

Adjusted Contract Price = \$11,675,499.44

Expenditures to Date = \$3,226,936.84 (28%)



# Southeast Loop Segment 1, Phase 1 (Corridor E1) (CR 138 to CR 137)





# Southeast Loop Segment 1, Phase 1 (Corridor E1) (CR 138 to CR 137)






# Southeast Loop Segment 1, Phase 1 (Corridor E1) (CR 138 to CR 137)





# University Boulevard Expansion (Chandler Road)

Anticipated Completion  
Spring 2022

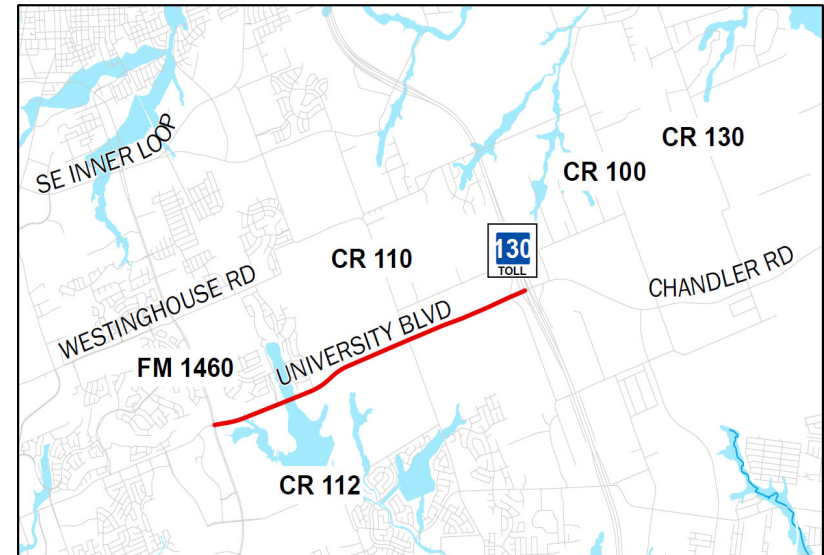

Partnership with the City of Round Rock

Original Contract Amount = \$11,104,890.49

Construction is managed by the City of Round Rock



# University Boulevard Expansion (Chandler Road)





# University Boulevard Expansion (Chandler Road)






# University Boulevard Expansion (Chandler Road)





# Thrall Project (S. Bounds Street)

Completed  
January 2022

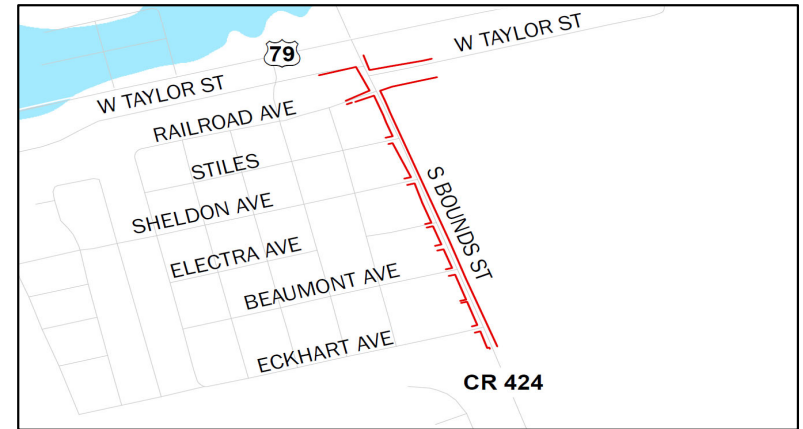

Original Contract Amount = \$889,988.00

Total Change Orders = \$47,437.00

Adjusted Contract Price = \$937,425.00

Expenditures to Date = \$723,474.26 (77%)




# Thrall Project (S. Bounds Street)





# Bartlett Project (Cotrell Street)

Completed  
February 2022

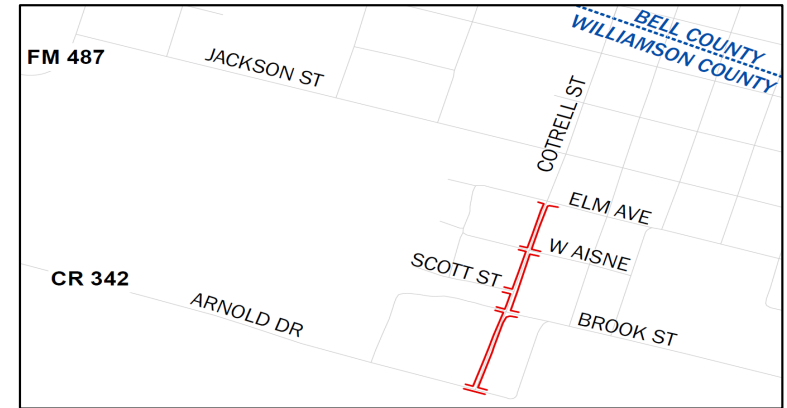

Original Contract Amount = \$419,919.00

Total Change Orders = \$0

Adjusted Contract Price = \$419,919.00

Expenditures to Date = \$0 (0%)



# Bartlett Project (Cotrell Street)





# Bartlett Project (Cotrell Street)








# Bartlett Project (Cotrell Street)





# University Boulevard Widening (IH 35 to Sunrise Road)

Anticipated Completion  
Early 2022

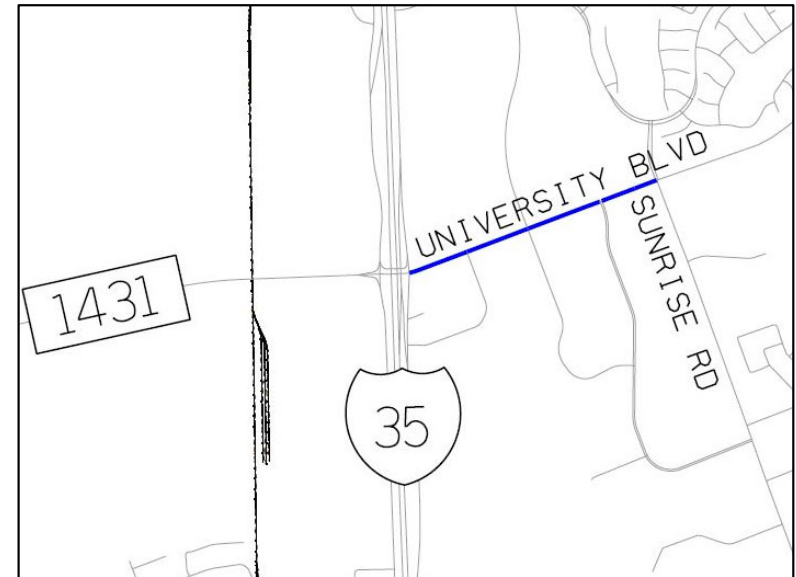

Partnership with the City of Round Rock

Original Contract Amount = \$12,135,410.45

Construction is managed by the City of Round Rock



# University Boulevard Widening (IH 35 to Sunrise Road)





# University Boulevard Widening (IH 35 to Sunrise Road)





# University Boulevard Widening (IH 35 to Sunrise Road)

