



# Williamson County Commissioners Court


---

Road Bond Program

June 21, 2022



# Precinct 1

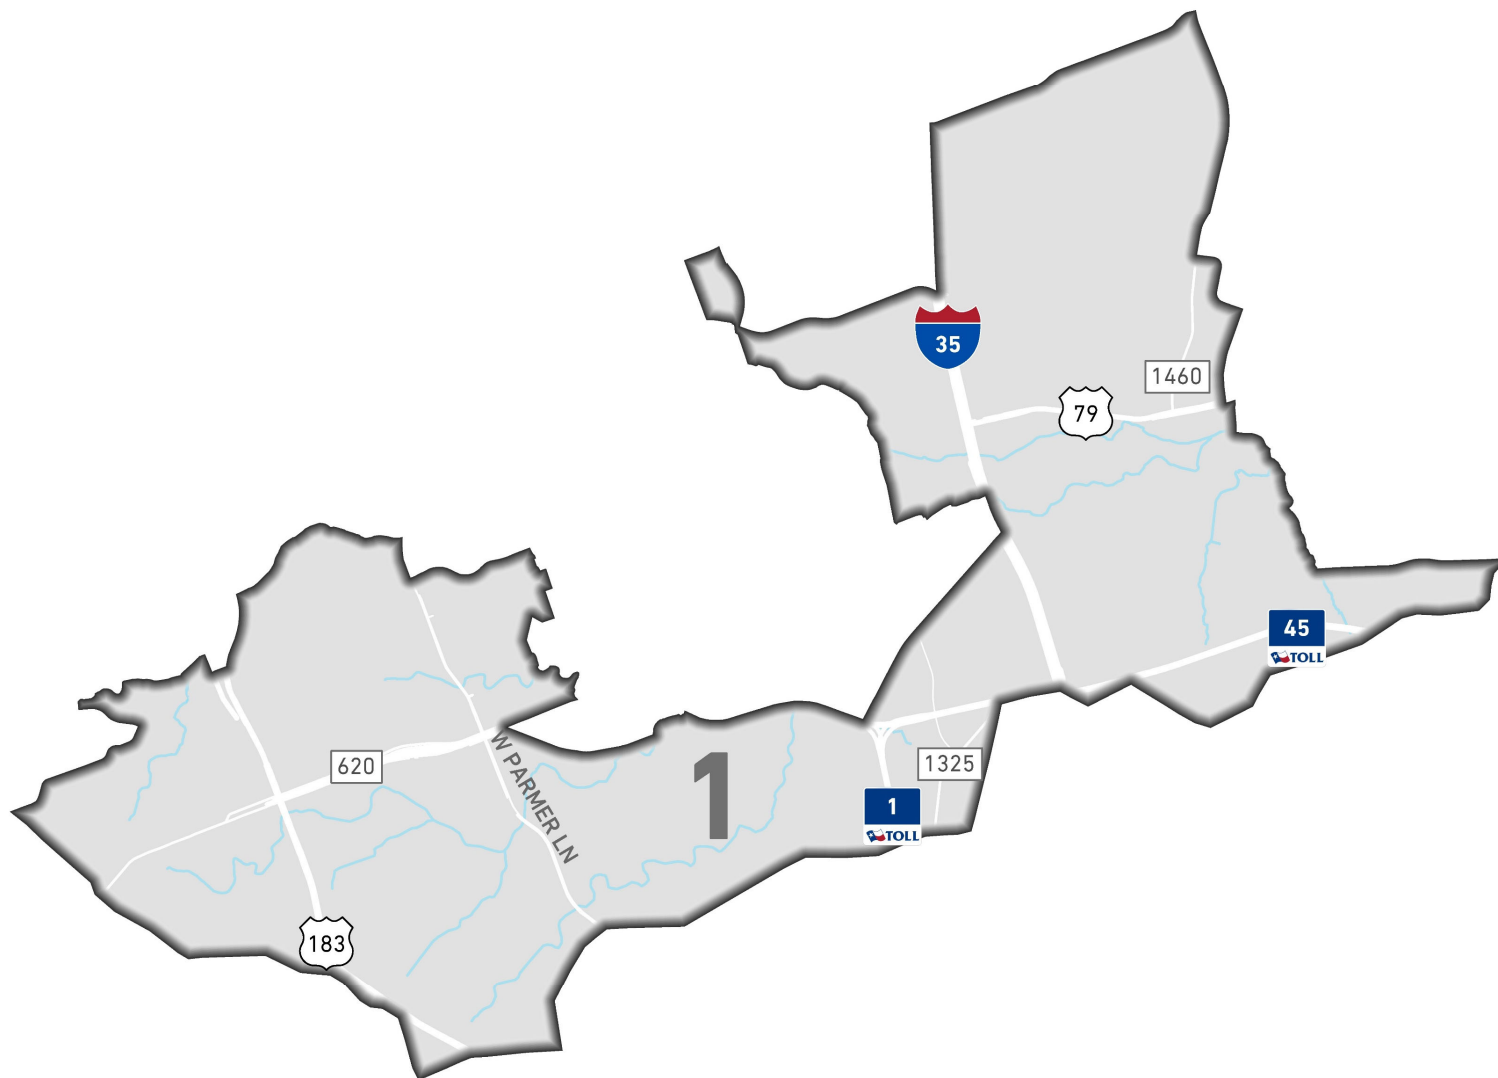




# RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)

---

3

Anticipated Completion  
Summer 2023

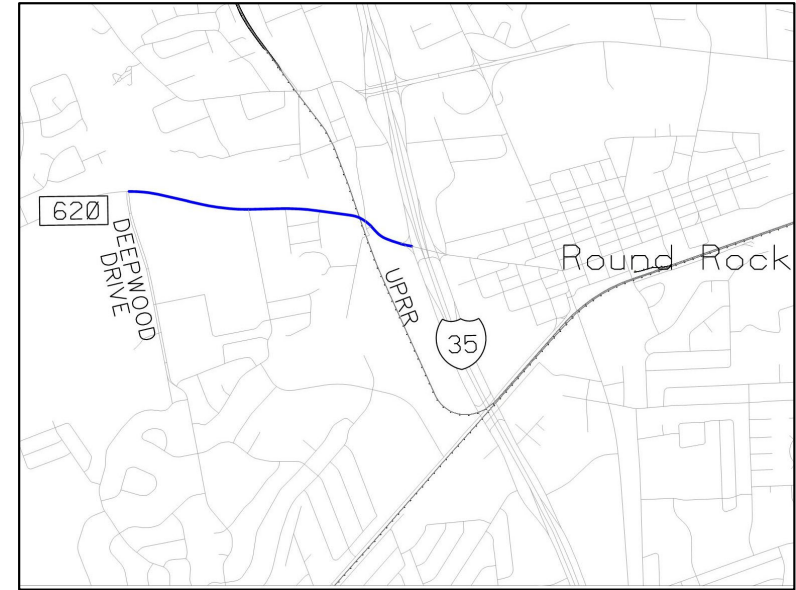

Partnership with TxDOT and the City of Round Rock  
Original Contract Amount = \$27,468,703.67  
Construction is managed by TxDOT

# RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)





# RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)








# RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)




# Precinct 2

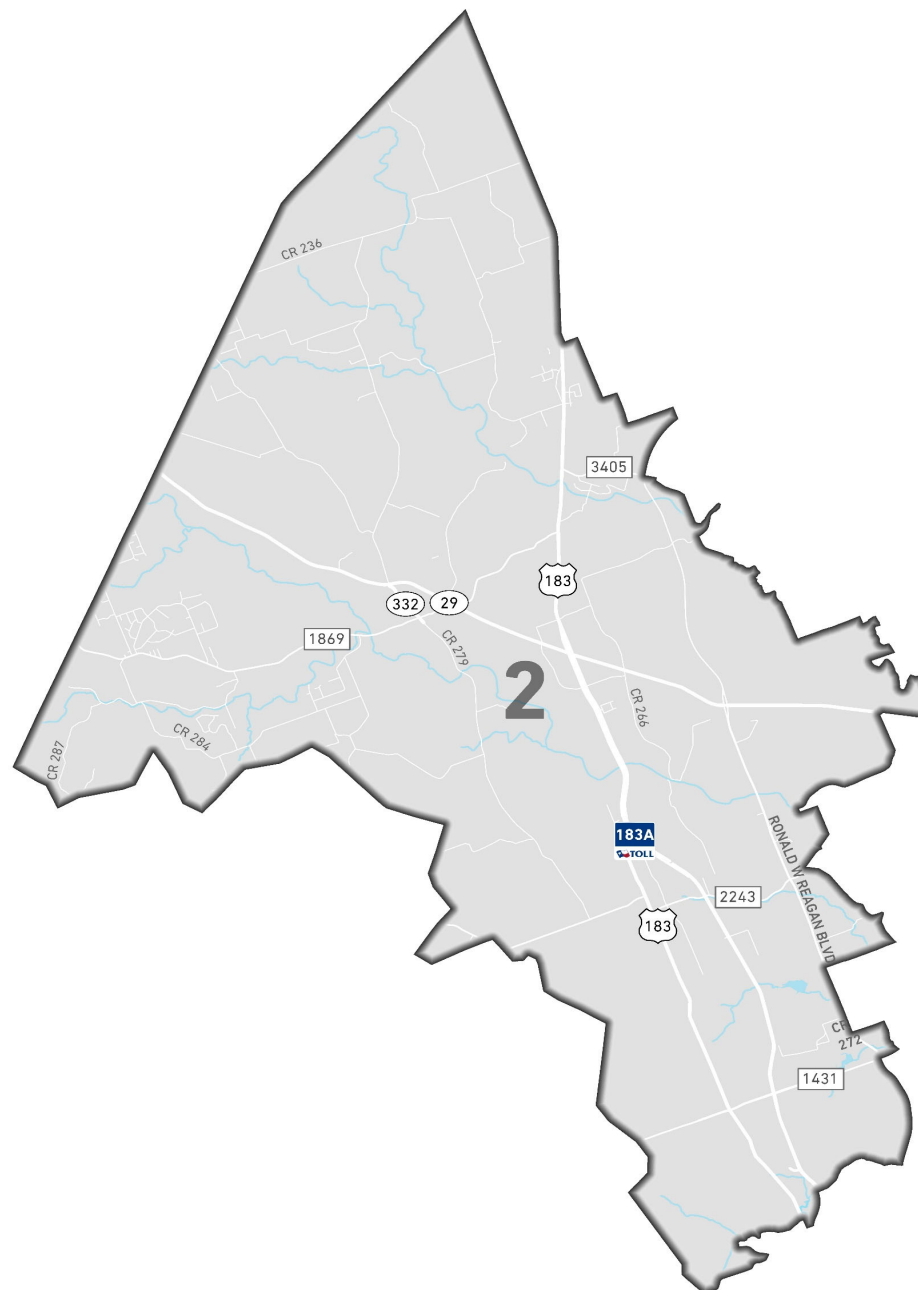

# CR 200 Reconstruction

Anticipated Completion  
Fall 2022

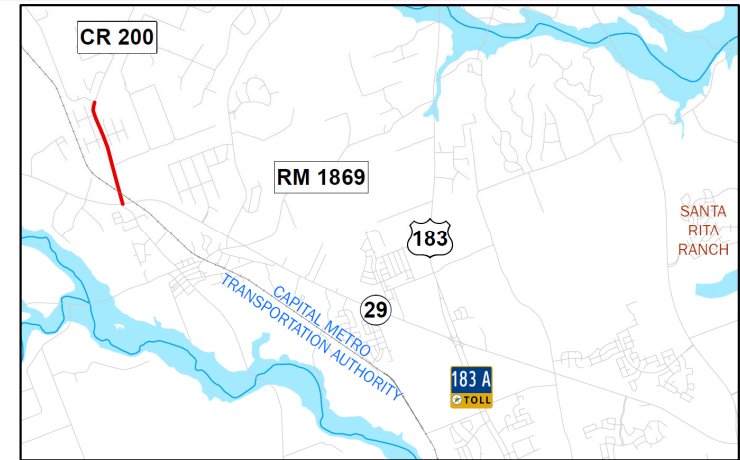

Original Contract Price = \$4,975,515.09

Total Change Orders to Date = \$0

Adjusted Contract Price = \$4,975,515.09

Expenditures to Date = \$2,360,725.41 (47%)



# CR 200 Reconstruction





# CR 200 Reconstruction






# CR 200 Reconstruction






# Precinct 3

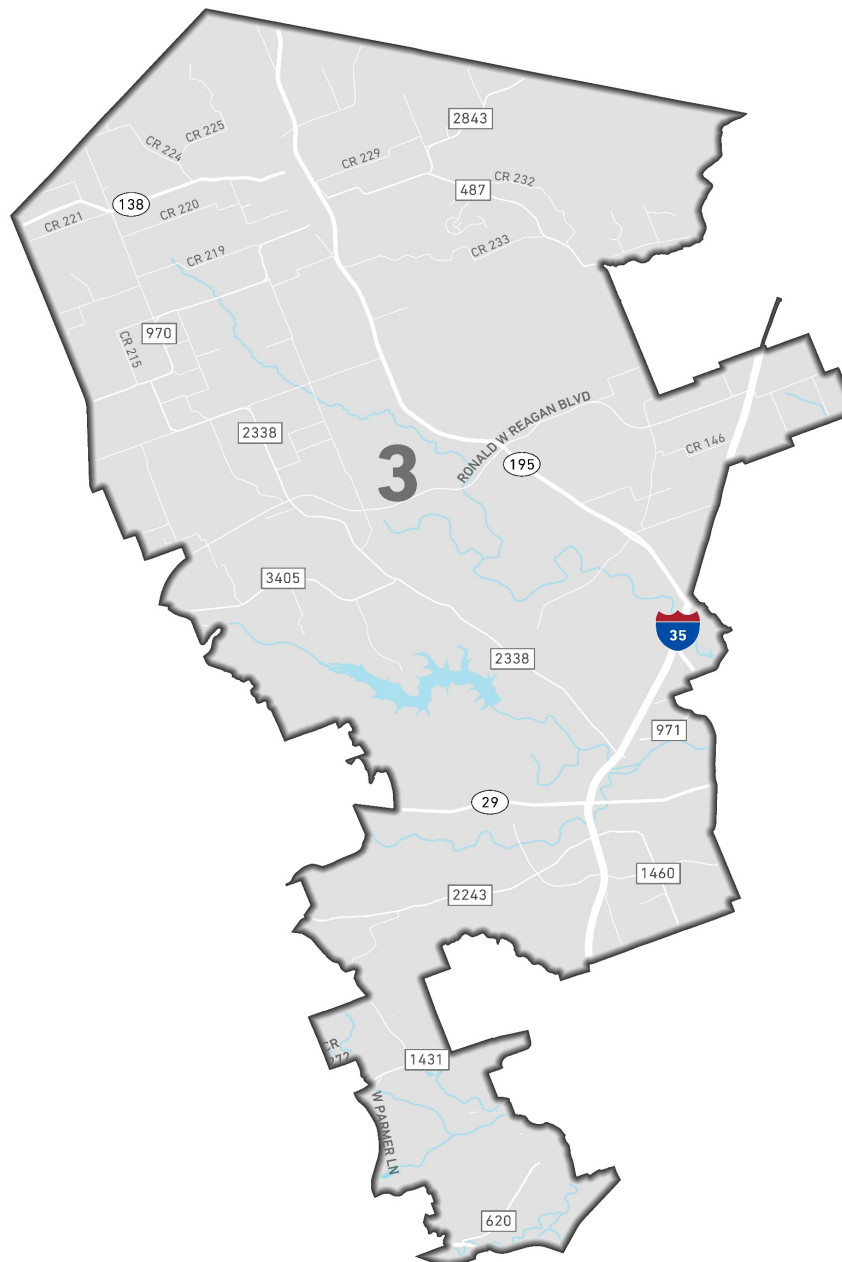

## (DB Woods Intersection)

---

Anticipated Completion  
Spring 2023

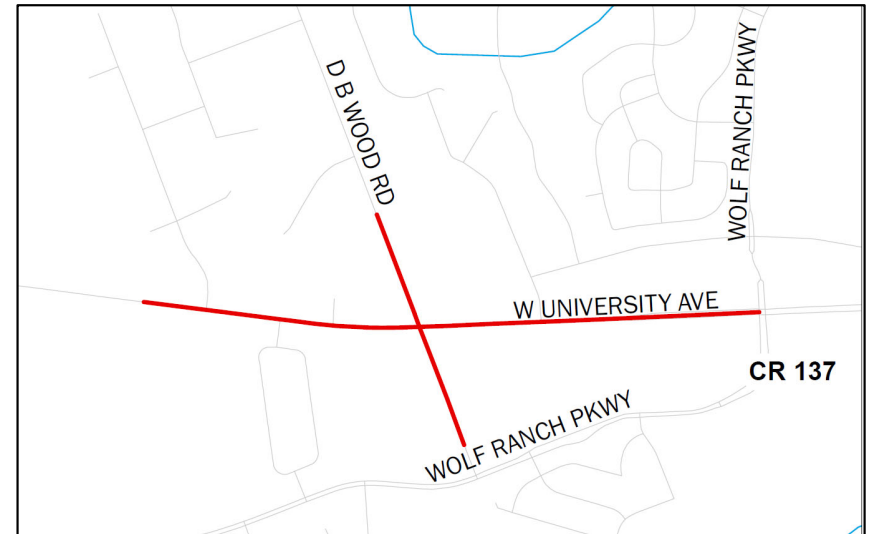

Partnership TxDOT

Original Contract Amount = \$5,548,287.93

Construction is managed by TxDOT



# SH 29 (DB Woods Intersection)





# SH 29 (DB Woods Intersection)






# SH 29 (DB Woods Intersection)





# Great Oaks Bridge at Brushy Creek

Anticipated Completion  
Spring 2023

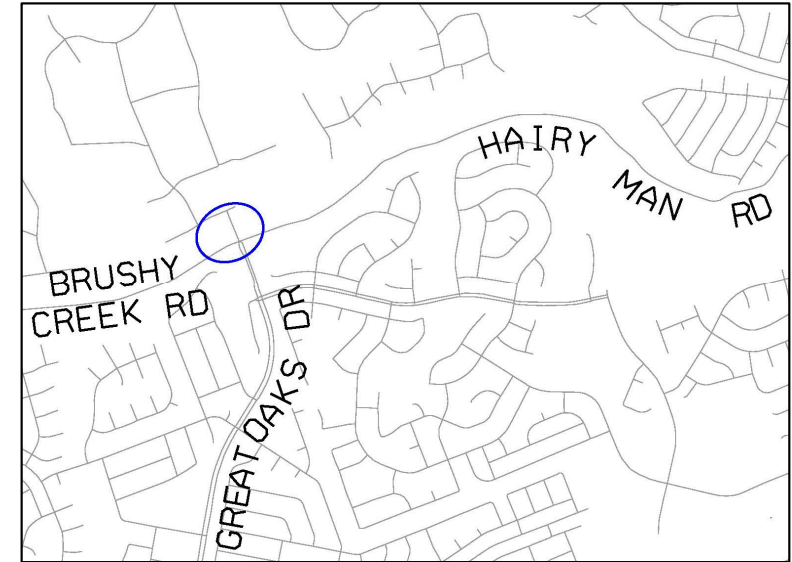

Original Contract Price = \$10,580,634.11  
Total Change Orders to Date = \$29,487.96  
Adjusted Contract Price = \$10,610,122.07  
Expenditures to Date = \$3,776,223.01 (36%)



# Great Oaks Bridge at Brushy Creek





# Great Oaks Bridge at Brushy Creek






# Great Oaks Bridge at Brushy Creek



# CR 111 Westinghouse Road

Anticipated Completion  
Late 2023

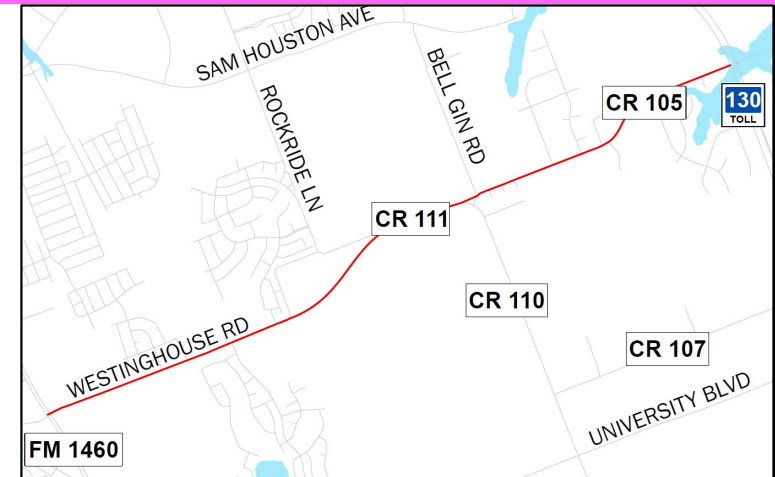

Original Contract Price = \$21,024,332.88

Total Change Orders to Date = \$240,917.84

Adjusted Contract Price = \$ 21,265,250.72

Expenditures to Date = \$3,392,217.16 (16%)



# CR 111 Westinghouse Road





# CR 111 Westinghouse Road






# CR 111 Westinghouse Road






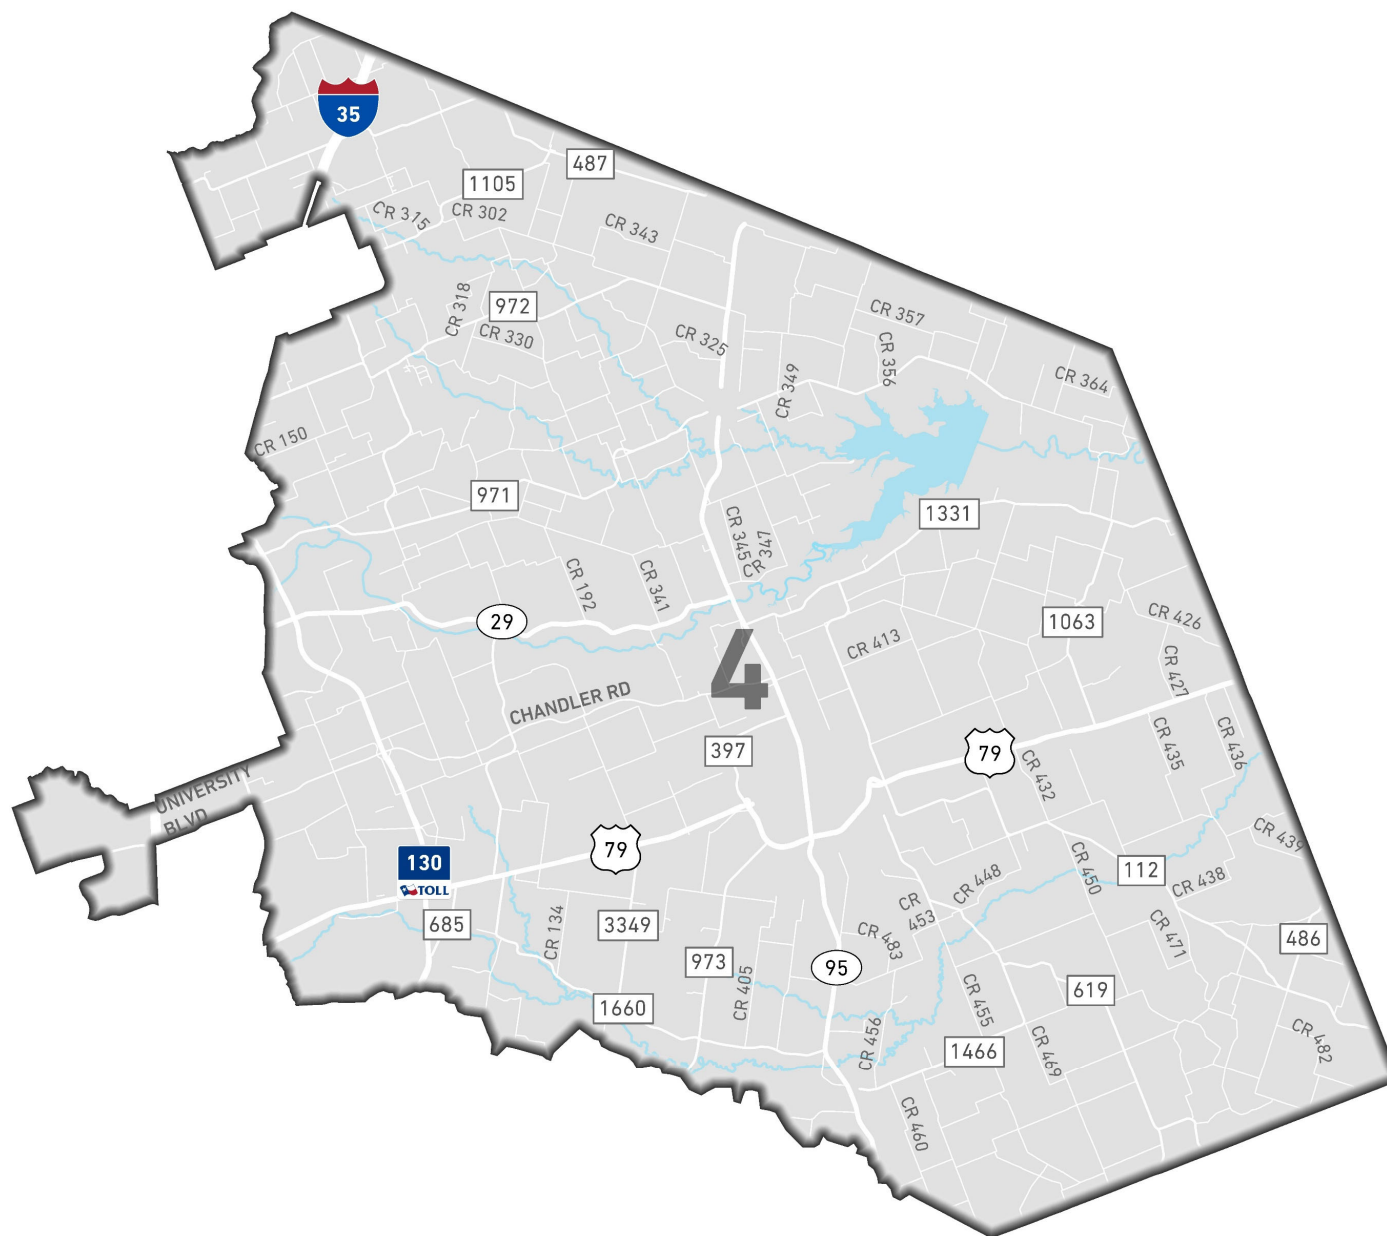

# Southeast Loop Segment 1, Phase 1 (Corridor E1) (CR 138 to CR 137)

Anticipated Completion  
Early 2023

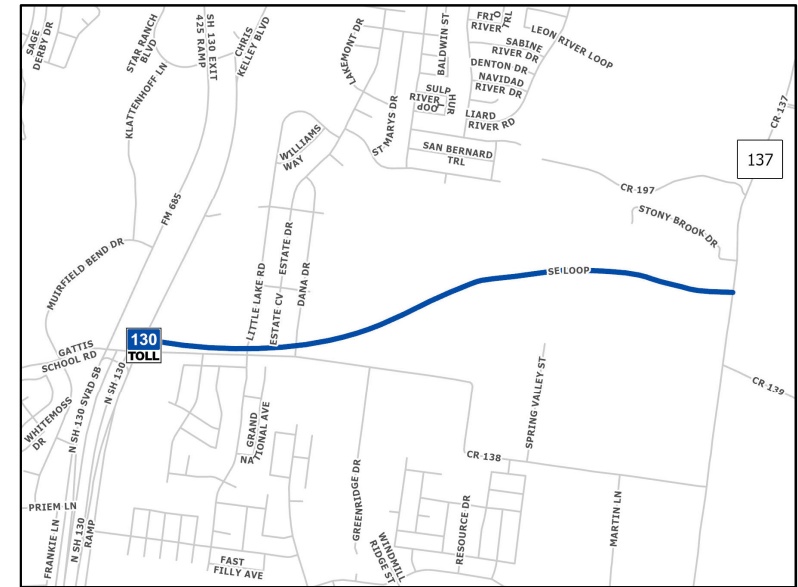

Original Contract Amount = \$11,526,789.09

Total Change Orders = \$148,710.35

Adjusted Contract Price = \$11,675,499.44

Expenditures to Date = \$4,957,122.97 (42%)



# Southeast Loop Segment 1, Phase 1 (Corridor E1) (CR 138 to CR 137)





# Southeast Loop Segment 1, Phase 1 (Corridor E1) (CR 138 to CR 137)






# Southeast Loop Segment 1, Phase 1 (Corridor E1) (CR 138 to CR 137)



# University Boulevard Expansion (Chandler Road)

Anticipated Completion  
Late 2022

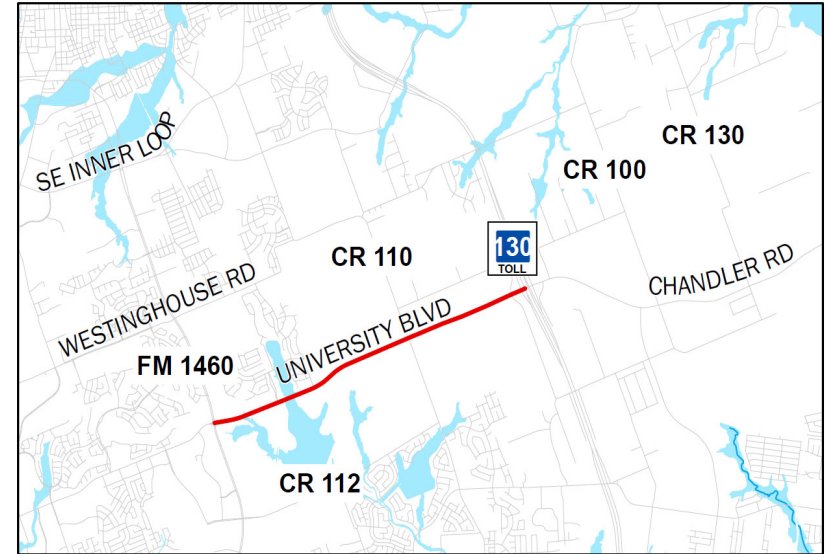

Partnership with the City of Round Rock

Original Contract Amount = \$11,104,890.49

Construction is managed by the City of Round Rock



# University Boulevard Expansion (Chandler Road)






# University Boulevard Expansion (Chandler Road)



# Davilla Street Culvert Replacement (Davilla Street at Walton Avenue)

Anticipated Completion  
Summer 2022

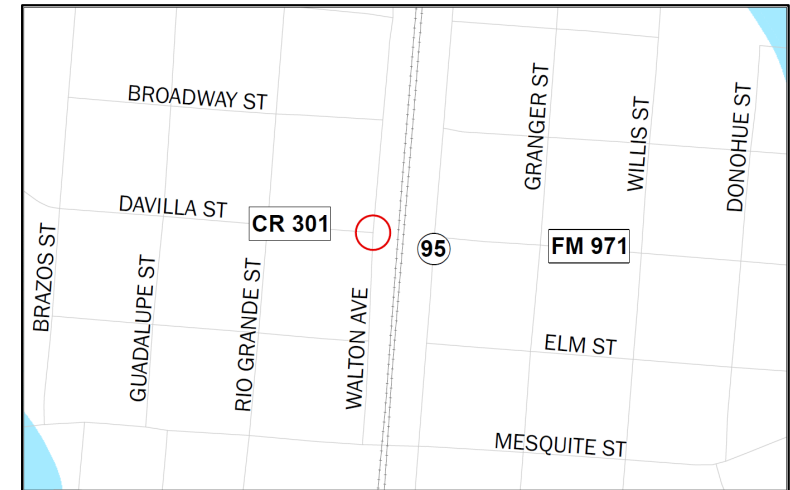

Original Contract Amount = \$664,464.00

Total Change Orders = \$0.00

Adjusted Contract Price = \$664,464.00

Expenditures to Date = \$0.00 (0%)



# Davilla Street Culvert Replacement (Davilla Street at Walton Avenue)





# Davilla Street Culvert Replacement (Davilla Street at Walton Avenue)






# Davilla Street Culvert Replacement (Davilla Street at Walton Avenue)





# Coupland Street Project (South Broad and Muery)

Anticipated Completion  
Summer 2022

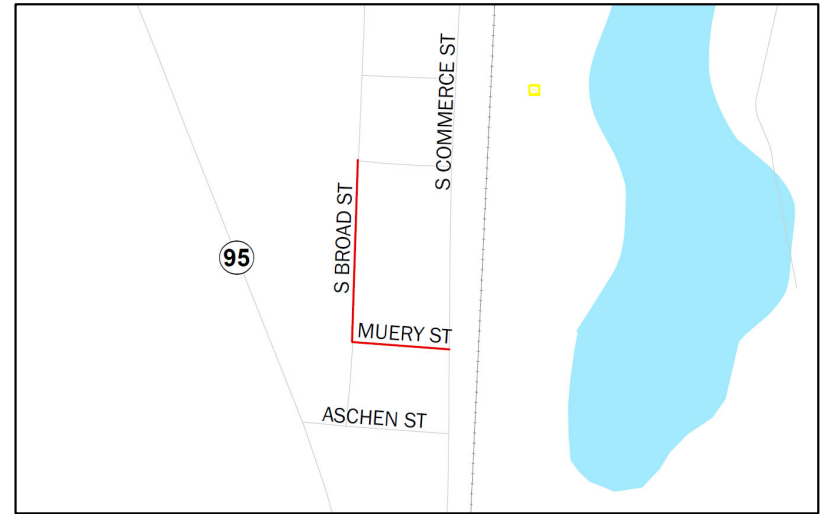

Original Contract Amount = \$519,919.00

Total Change Orders = \$0.00

Adjusted Contract Price = \$519,919.00

Expenditures to Date = \$0.00 (0%)



# Coupland Street Project (South Broad and Muery)





# Coupland Street Project (South Broad and Muery)






# Coupland Street Project (South Broad and Muery)





# CR 401 Reconstruction

Anticipated Completion  
Summer 2023

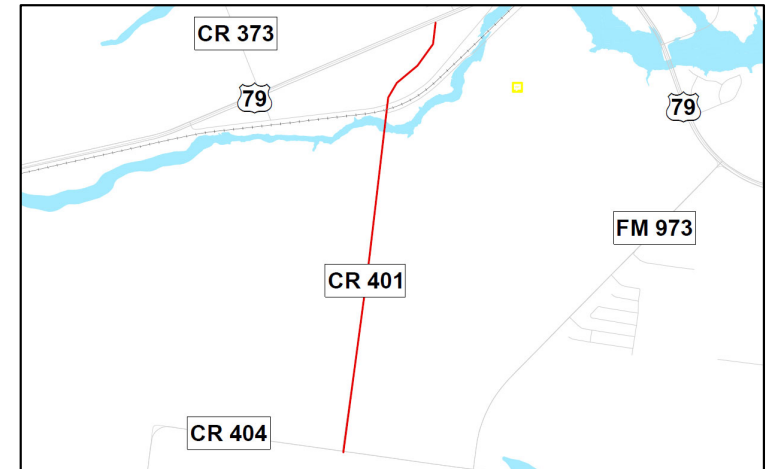

Original Contract Amount = \$12,673,200.94

Total Change Orders = \$0.00

Adjusted Contract Price = \$ 12,673,200.94

Expenditures to Date = \$601,500.00 (5%)



# CR 401 Reconstruction






# CR 401 Reconstruction





# Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)

Anticipated Completion  
Spring 2023

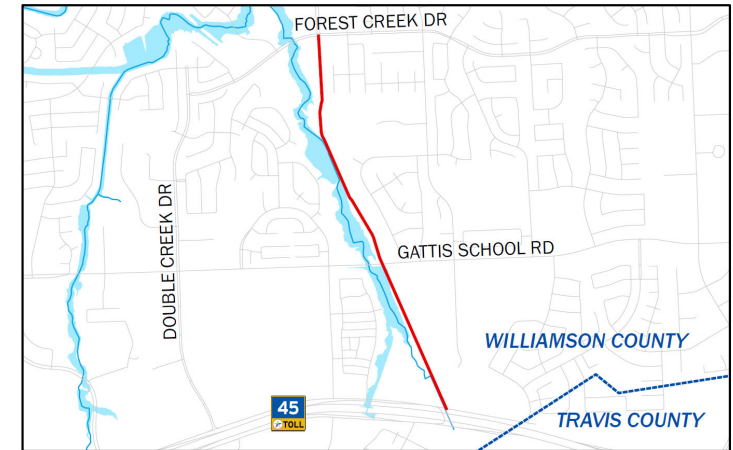

Partnership with the City of Round Rock

Original Contract Amount = \$23,409,120.97

Construction is managed by the City of Round Rock



# Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)





# Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)






# Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)





# University Boulevard Widening (IH 35 to Sunrise Road)

Anticipated Completion  
Spring 2023

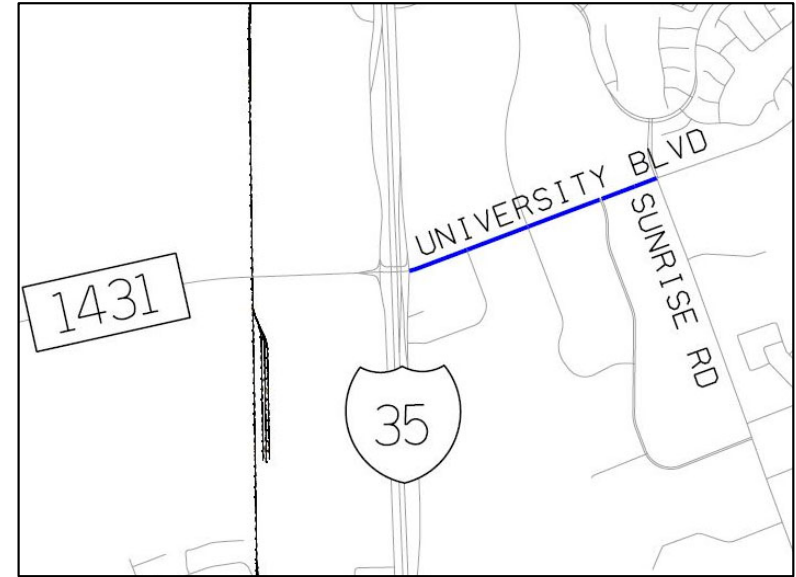

Partnership with the City of Round Rock

Original Contract Amount = \$12,135,410.45

Construction is managed by the City of Round Rock



# University Boulevard Widening (IH 35 to Sunrise Road)





# University Boulevard Widening (IH 35 to Sunrise Road)





# University Boulevard Widening (IH 35 to Sunrise Road)

