


Williamson County Commissioners Court

Road Bond Program September 20, 2022






Precinct 1

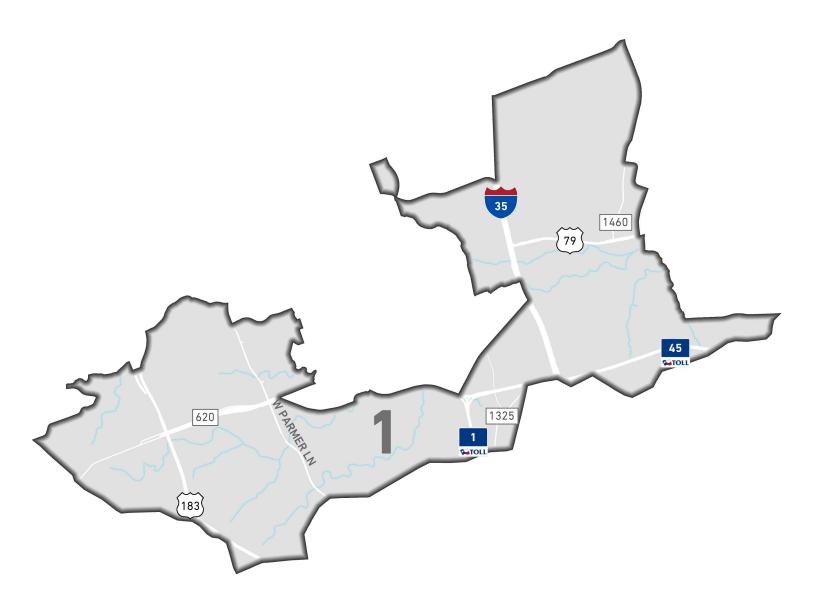



RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)

Anticipated Completion Summer 2023

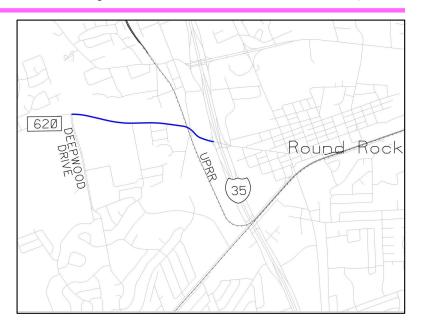

Partnership with TxDOT and the City of Round Rock Original Contract Amount = \$27,468,703.67 Construction is managed by TxDOT



RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)





RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)






RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)






Precinct 2

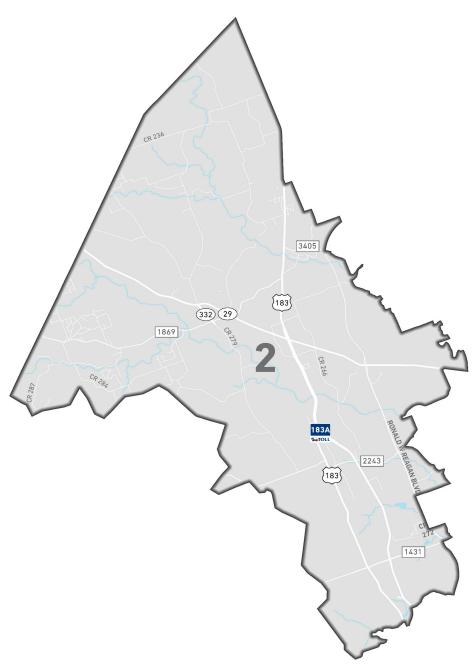



Anticipated Completion Fall 2022

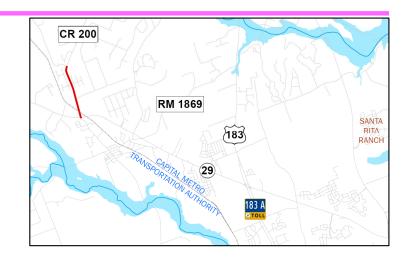

Original Contract Price = \$4,975,515.09

Total Change Orders to Date = \$0

Adjusted Contract Price = \$4,975,515.09

Expenditures to Date = \$3,246,927.06 (65%)

















Precinct 3

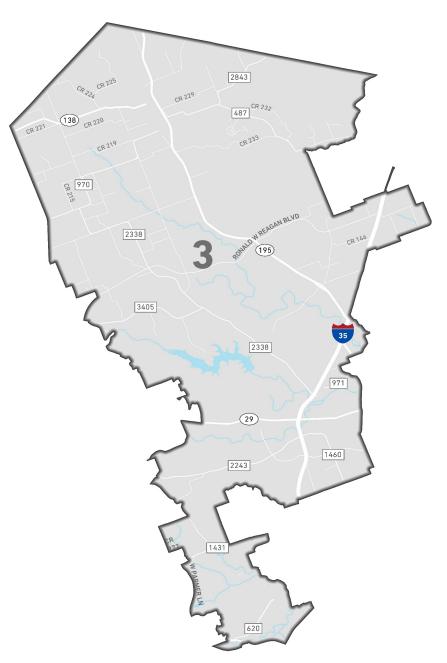



SH 29 (DB Wood Intersection)

Anticipated Completion
Spring 2023

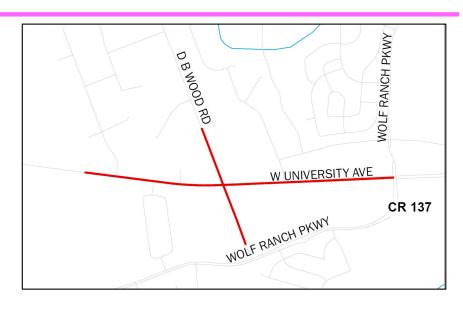

Partnership TxDOT

Original Contract Amount = \$5,548,287.93

Construction is managed by TxDOT



SH 29 (DB Wood Intersection)






SH 29 (DB Wood Intersection)





Anticipated Completion
Spring 2023

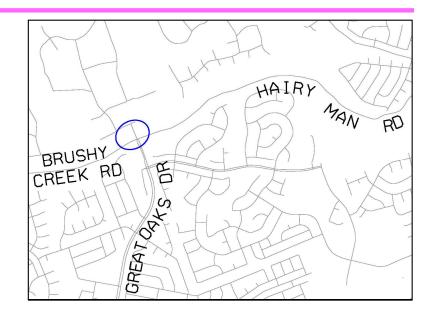


Original Contract Price = \$10,580,634.11

Total Change Orders to Date = \$29,487.96

Adjusted Contract Price = \$10,610,122.07

Expenditures to Date = \$4,682,954.23 (44%)



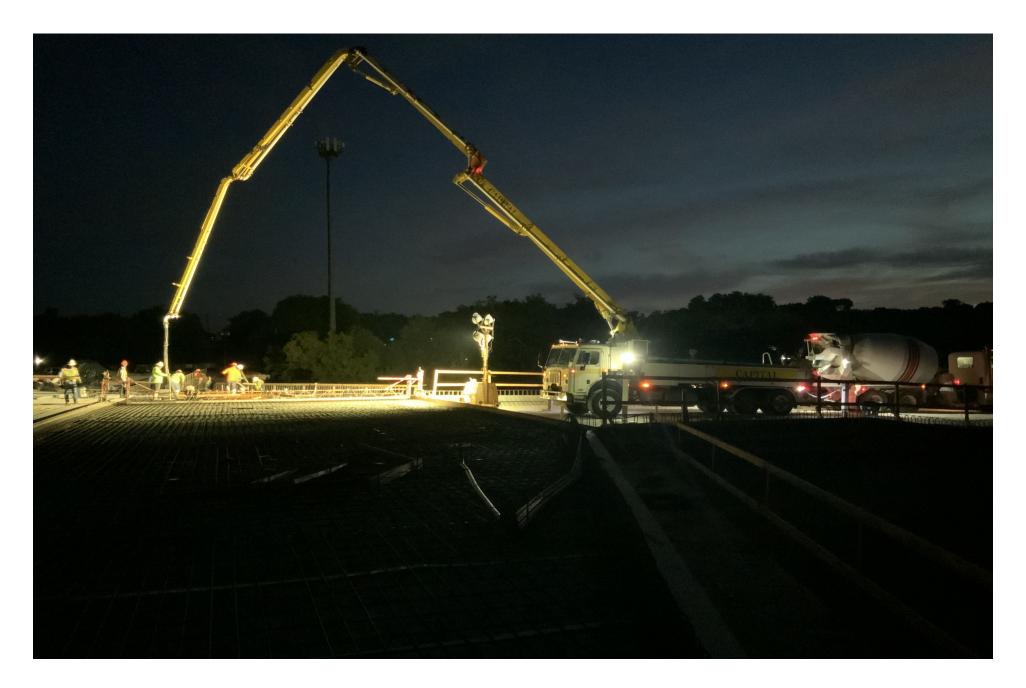












Anticipated Completion
Spring 2024

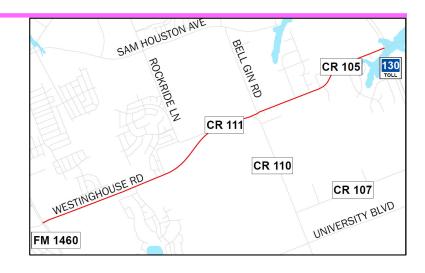

Original Contract Price = \$21,024,332.88

Total Change Orders to Date = \$715,492.44

Adjusted Contract Price = \$21,739,825.32

Expenditures to Date = \$6,036,744.64 (28%)
















Southwest Bypass Extension

Anticipated Completion
Summer 2023

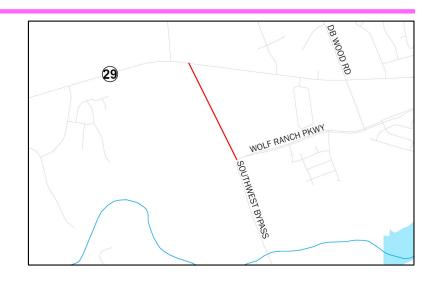

Original Contract Price = \$4,288,543.00

Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$4,288,543.00

Expenditures to Date = \$0.00 (0%)




Southwest Bypass Extension






Precinct 4

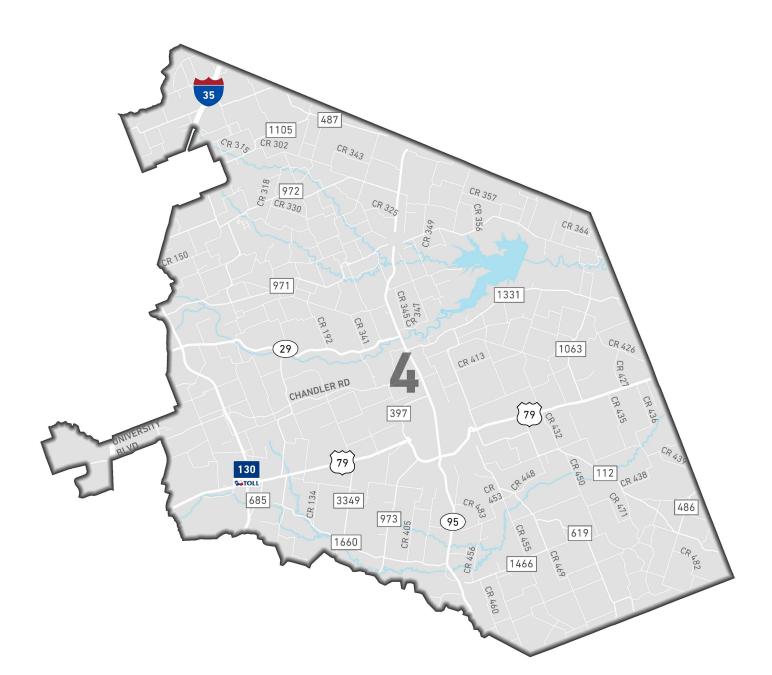



Anticipated Completion Early 2023

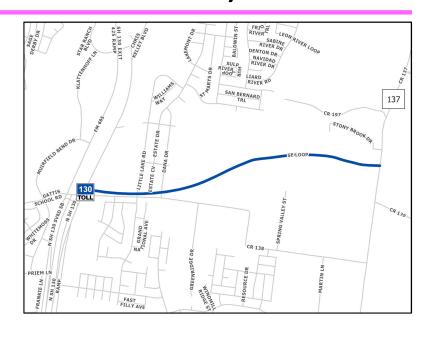

Original Contract Amount = \$11,526,789.09

Total Change Orders = \$148,710.35


Adjusted Contract Price = \$11,675,499.44

Expenditures to Date = \$6,785,856.46 (58%)








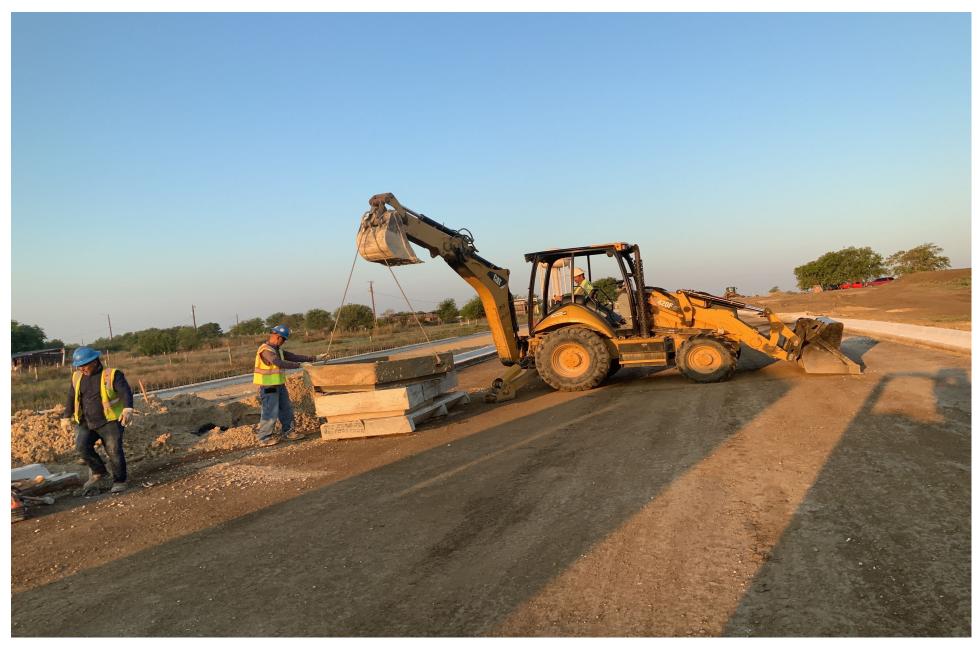




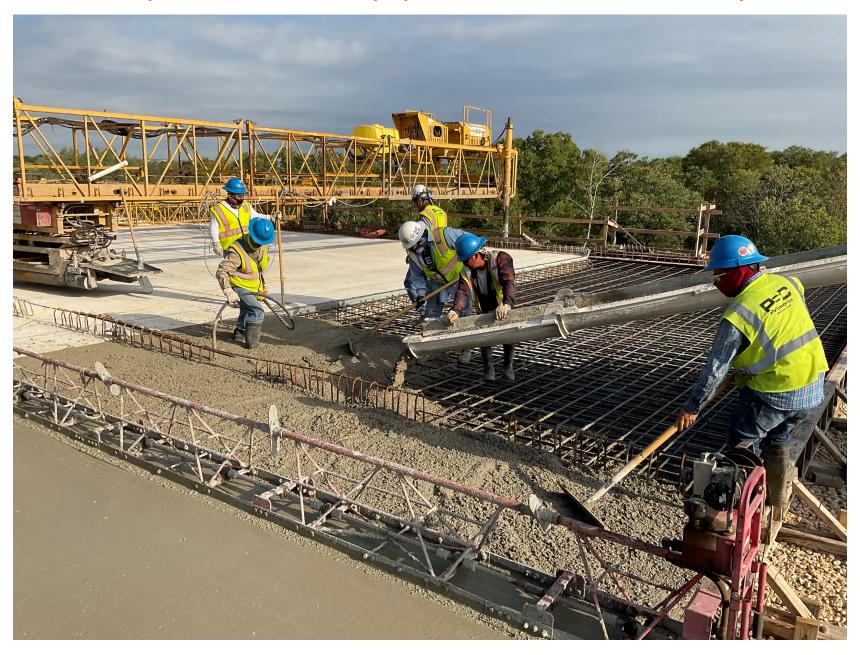



University Boulevard Expansion (Chandler Road)

Anticipated Completion Late 2022

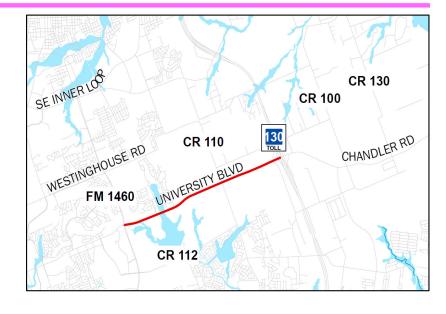

Partnership with the City of Round Rock

Original Contract Amount = \$11,104,890.49

Construction is managed by the City of Round Rock



University Boulevard Expansion (Chandler Road)






University Boulevard Expansion (Chandler Road)





Anticipated Completion Summer 2023

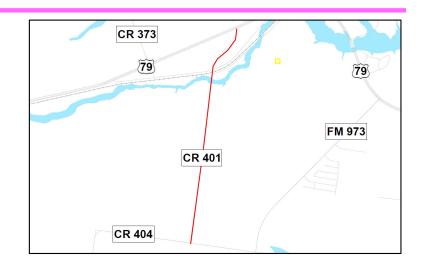

Original Contract Amount = \$12,673,200.94

Total Change Orders = \$0.00


Adjusted Contract Price = \$ 12,673,200.94

Expenditures to Date = \$3,155,362.82 (25%)







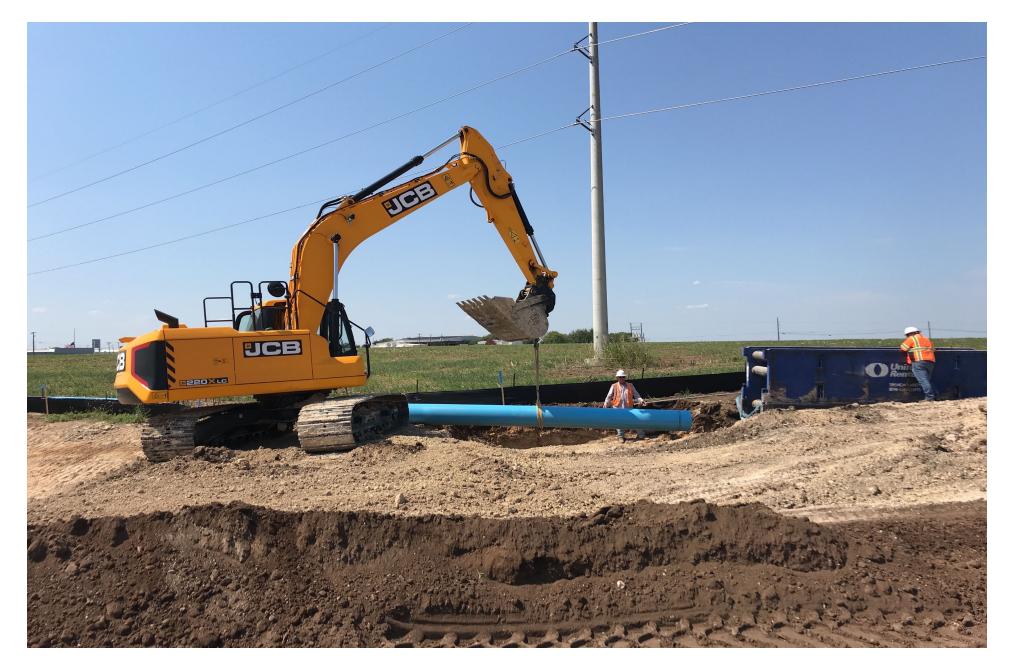




CR 401 Reconstruction





Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)

Anticipated Completion Winter 2023

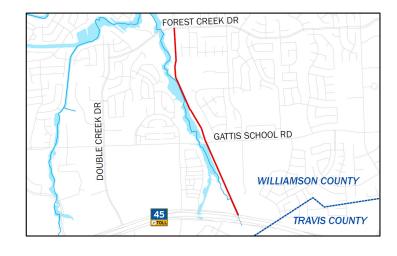

Partnership with the City of Round Rock

Original Contract Amount = \$23,409,120.97

Construction is managed by the City of Round Rock



Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)






Kenney Fort Boulevard – Seg. 2 and 3 (Forest Creek Drive to SH 45)





Anticipated Completion
Summer 2022

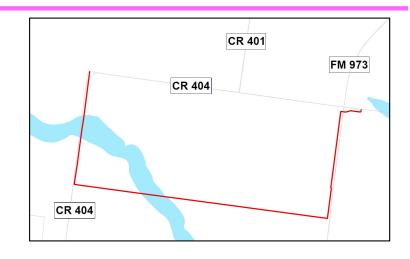


Original Contract Amount = \$4,759,838.25

Total Change Orders = \$392,689.25

Adjusted Contract Price = \$5,152,527.50

Expenditures to Date = \$3,294,672.53 (64%)



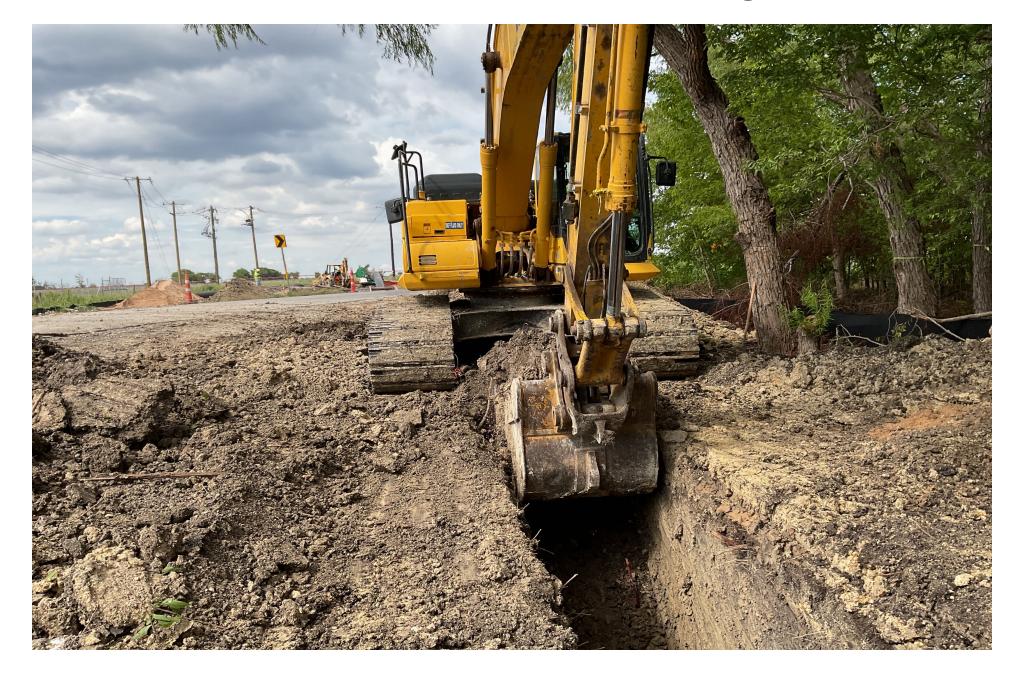












University Boulevard Widening (IH 35 to Sunrise Road)

Anticipated Completion
Spring 2023

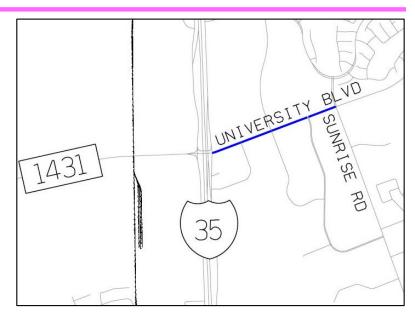

Partnership with the City of Round Rock

Original Contract Amount = \$12,135,410.45

Construction is managed by the City of Round Rock



University Boulevard Widening (IH 35 to Sunrise Road)






University Boulevard Widening (IH 35 to Sunrise Road)





Future County Road (CR 404 to FM 973)

Anticipated Completion Fall 2023

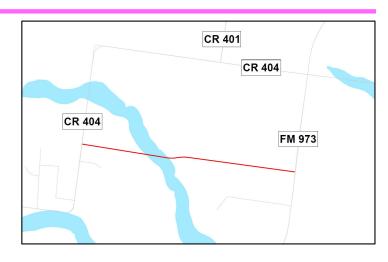

Original Contract Amount = \$11,289,929.00 Total Change Orders = \$0.00 Adjusted Contract Price = \$11,289,929.00 Expenditures to Date = \$0.00 (0%)



Future County Road (CR 404 to FM 973)

