


Williamson County Commissioners Court

Road Bond Program
June 27, 2023





Precinct 1

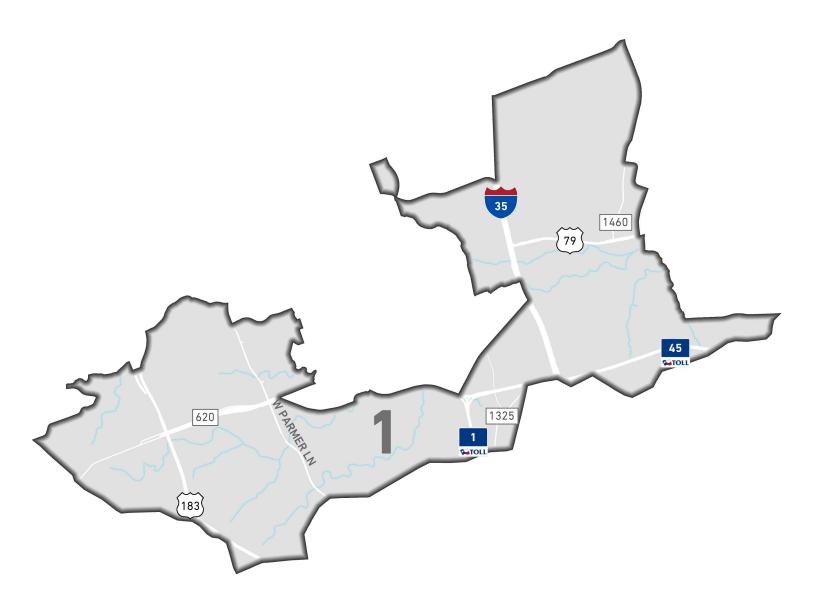



RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)

Anticipated Completion Fall 2023



Partnership with TxDOT and the City of Round Rock Original Contract Amount = \$27,468,703.67 Construction is managed by TxDOT



RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)





RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)






RM 620 at Railroad / Chisholm Trail (IH 35 Frontage Road to Deep Wood Drive)






Precinct 2

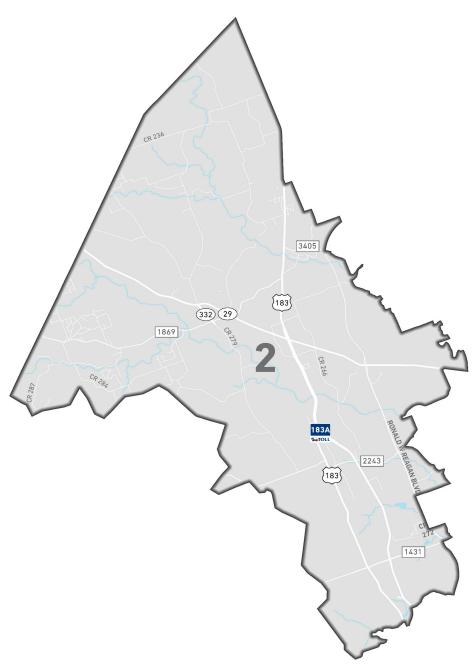



Anticipated Completion Early 2024

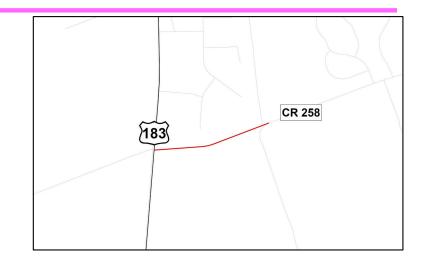

Original Contract Price = \$5,836,754.36

Total Change Orders to Date = \$422,565.69

Adjusted Contract Price = \$6,259,320.05

Expenditures to Date = \$2,064,359.81 (33%)
















Ronald Reagan at Elizabeth Park Temporary Signals

Anticipated Completion Fall 2023



Original Contract Price = \$215,902.22

Total Change Orders to Date = \$28,245.75

Adjusted Contract Price = \$ 245,147.97

Expenditures to Date = \$105,566.20 (43%)



Ronald Reagan at Elizabeth Park Temporary Signals






Ronald Reagan at Elizabeth Park Temporary Signals






Precinct 3

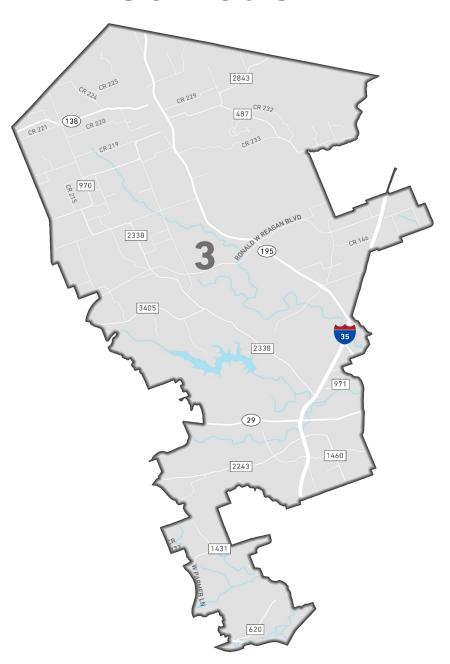



Anticipated Completion
Summer 2023

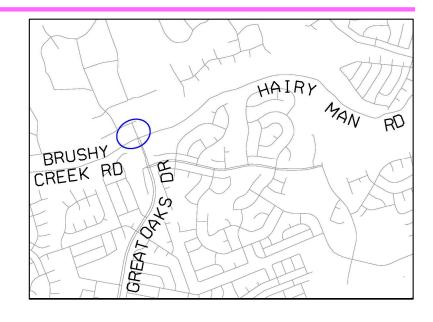


Original Contract Price = \$10,580,634.11

Total Change Orders to Date = \$172,301.30

Adjusted Contract Price = \$10,752,935.41

Expenditures to Date = \$8,706,010.67 (81%)




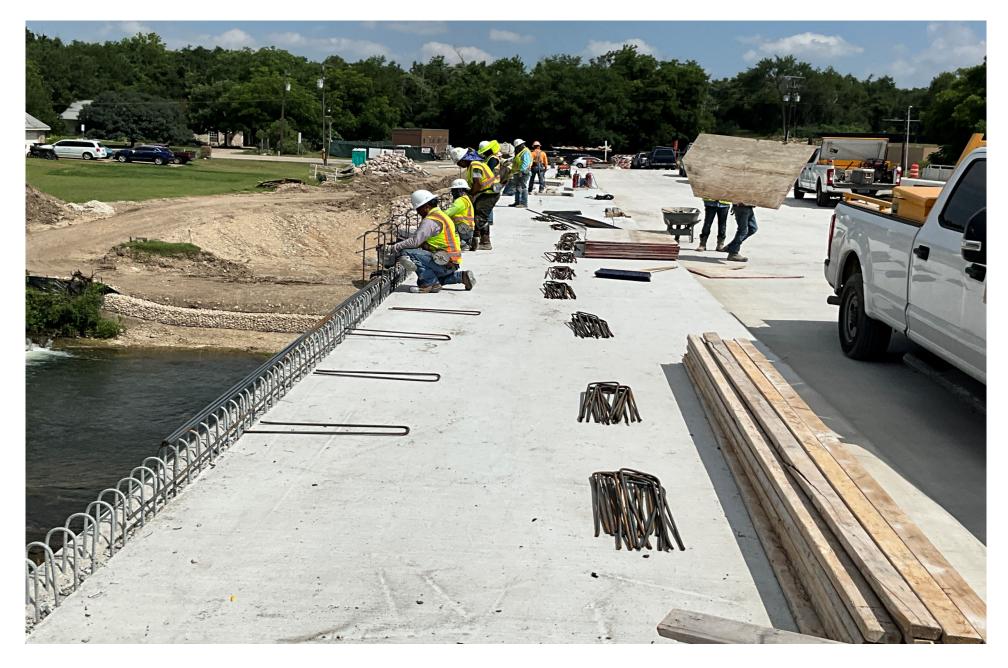








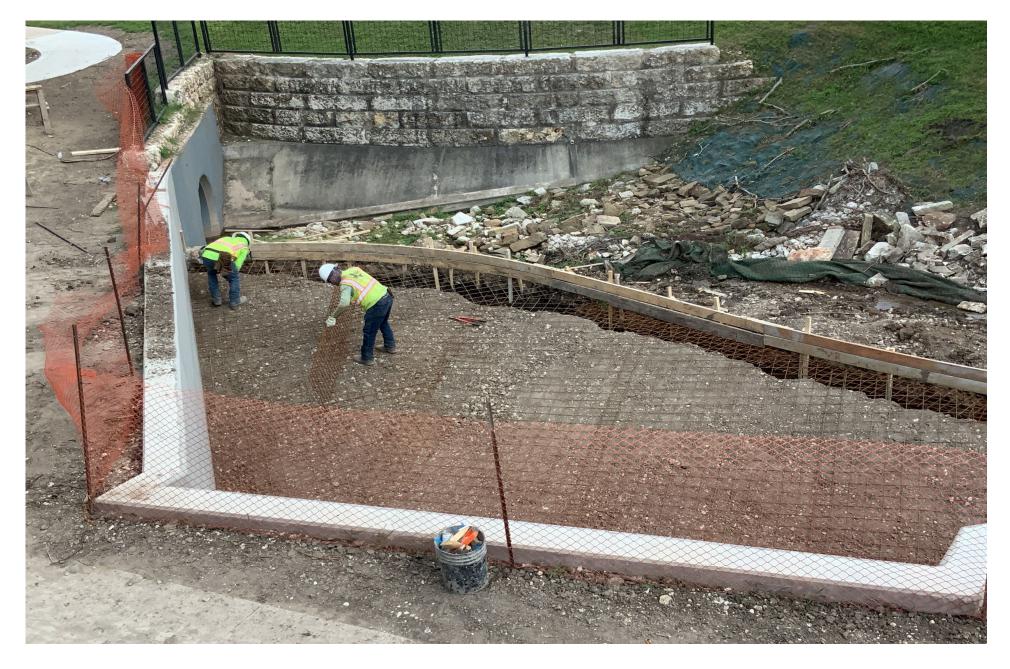



Anticipated Completion
Spring 2024

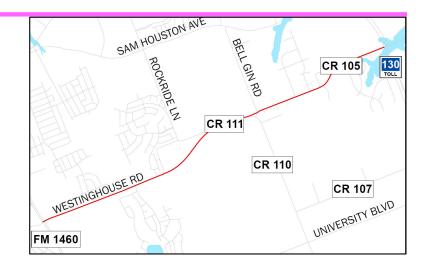

Original Contract Price = \$21,024,332.88

Total Change Orders to Date = \$1,099,708.30


Adjusted Contract Price = \$22,124,041.18

Expenditures to Date = \$14,419,961.23 (65%)







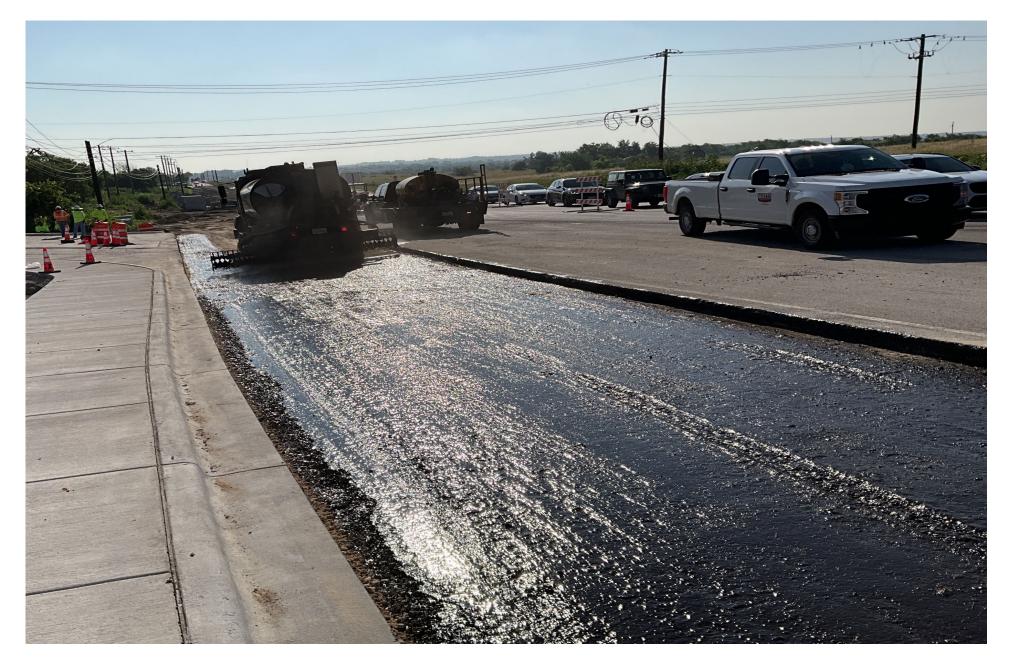








Anticipated Completion
Summer 2023

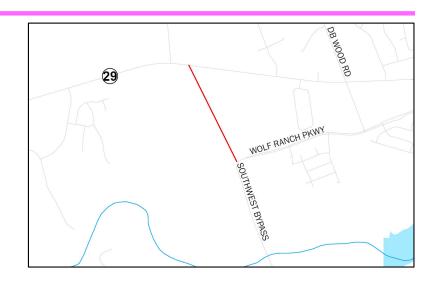

Original Contract Price = \$4,288,543.00

Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$4,288,543.00

Expenditures to Date = \$3,252,999.45 (76%)
















Anticipated Completion
Spring 2024

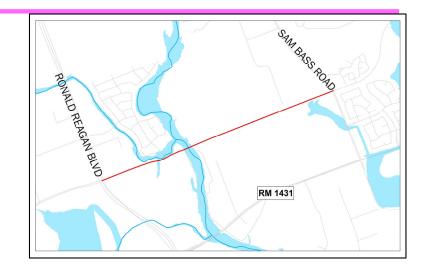

Partnership with the City of Cedar Park

Original Contract Amount = \$22,619,961.16

Construction is managed by the City of Cedar Park
















Anticipated Completion
Spring 2024

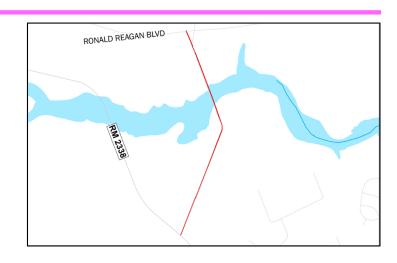

Original Contract Price = \$6,969,195.21

Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$6,969,195.21

Expenditures to Date = \$975,061.78 (14%)
















Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)

Anticipated Completion Fall 2025

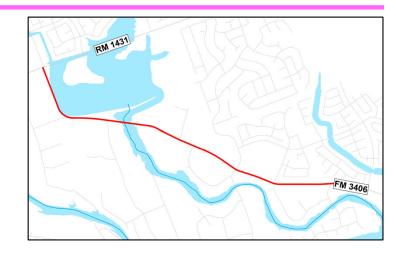

Original Contract Price = \$36,145,959.00

Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$36,145,959.00

Expenditures to Date = \$23,439.50 (0%)



Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)






Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)






Precinct 4

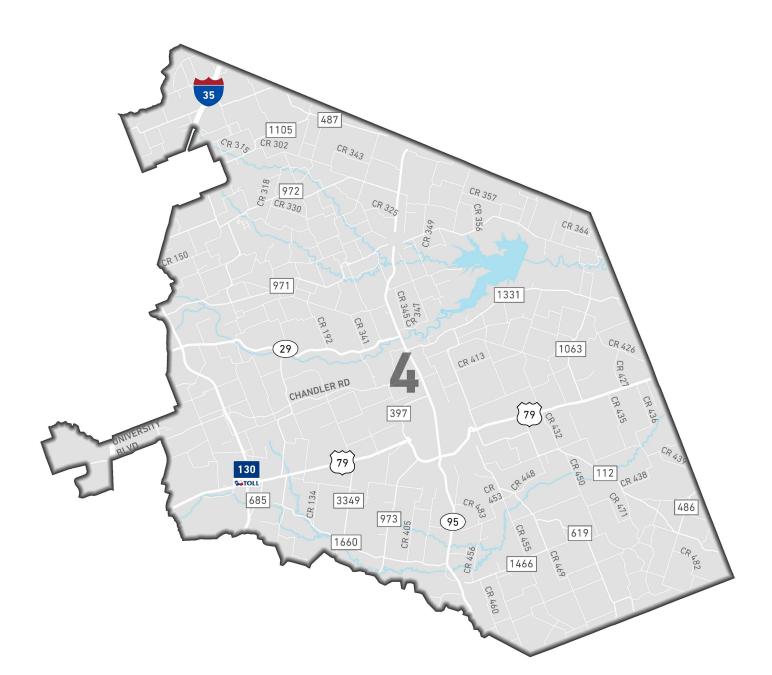



East Wilco Highway (Southeast Loop Segment 1) (Corridor E1) (CR 138 to CR 137)

Anticipated Completion
Summer 2023

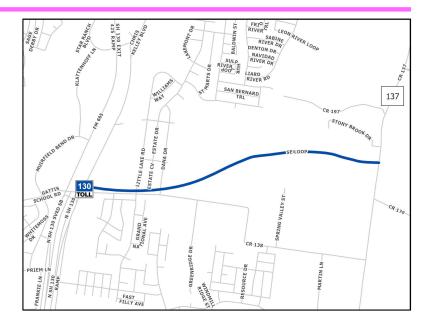

Original Contract Amount = \$11,526,789.09

Total Change Orders = \$555,757.32

Adjusted Contract Price = \$12,082,546.41

Expenditures to Date = \$10,687,329.95 (89%)



East Wilco Highway (Southeast Loop Segment 1) (Corridor E1) (CR 138 to CR 137)





East Wilco Highway (Southeast Loop Segment 1) (Corridor E1) (CR 138 to CR 137)






East Wilco Highway (Southeast Loop Segment 1) (Corridor E1) (CR 138 to CR 137)





University Boulevard Expansion (Chandler Road)

Anticipated Completion
Spring 2023

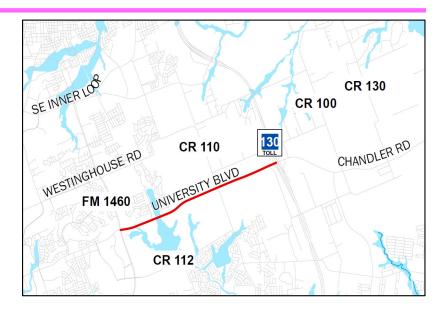

Partnership with the City of Round Rock

Original Contract Amount = \$11,104,890.49

Construction is managed by the City of Round Rock




University Boulevard Expansion (Chandler Road)





Anticipated Completion Summer 2023

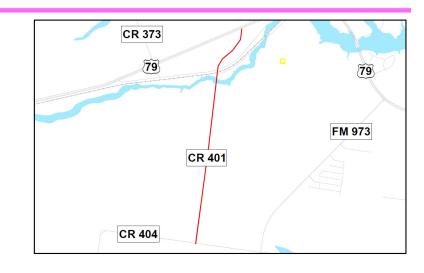

Original Contract Amount = \$12,673,200.94

Total Change Orders = \$830,893.84

Adjusted Contract Price = \$13,504,094.78

Expenditures to Date = \$10,338,944.61 (77%)
















Anticipated Completion Late 2023

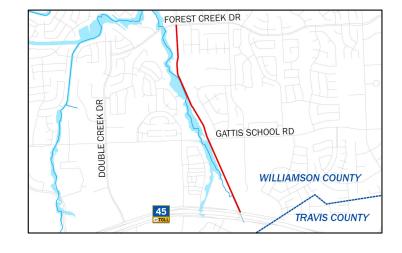

Partnership with the City of Round Rock

Original Contract Amount = \$23,409,120.97

Construction is managed by the City of Round Rock
















Samsung Highway (Future County Road) (CR 404 to FM 973)

Anticipated Completion Fall 2023

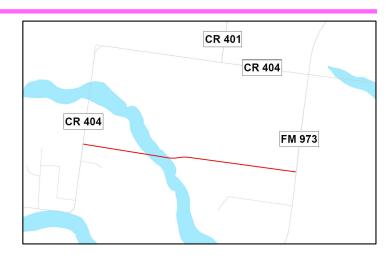

Original Contract Amount = \$11,289,929.00 Total Change Orders = \$41,260.00 Adjusted Contract Price = \$11,331,189.00 Expenditures to Date = \$8,359,530.85 (74%)



Samsung Highway (Future County Road) (CR 404 to FM 973)





Samsung Highway (Future County Road) (CR 404 to FM 973)






Samsung Highway (Future County Road) (CR 404 to FM 973)





East Wilco Highway FM 3349 / US 79 Interchange (US 79 to CR 404)

Anticipated Completion
Summer 2025 (Roadwork)

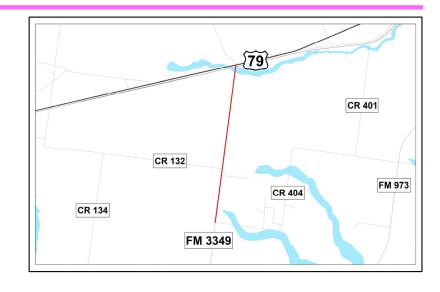

Original Contract Amount = \$81,941,038.13

Total Change Orders = \$1,007,354.41

Adjusted Contract Price = \$82,948,392.54

Expenditures to Date = \$14,654,225.24 (18%)



East Wilco Highway (FM 3349 / US 79) Interchange (US 79 to CR 404)





East Wilco Highway (FM 3349 / US 79) Interchange (US 79 to CR 404)






East Wilco Highway (FM 3349 / US 79) Interchange (US 79 to CR 404)





Anticipated Completion
Summer 2024



Original Contract Amount = \$17,694,262.46

Total Change Orders = \$0.00

Adjusted Contract Price = \$17,694,262.46

Expenditures to Date = \$2,379,761.59 (13%)
















Anticipated Completion
Summer 2023



Original Contract Amount = \$4,622,143.93

Total Change Orders = \$0.00

Adjusted Contract Price = \$4,622,143.93

Expenditures to Date = \$1,809,782.06 (39%)
















Anticipated Completion Fall 2023



Original Contract Amount = \$5,917,275.00 Total Change Orders = \$35,830.59 Adjusted Contract Price = \$5,953,105.59 Expenditures to Date = \$1,422,269.00 (24%)
















Samsung Highway (CR 404 Realignment) (FM 3349 to CR 404)

Anticipated Completion Early 2024



Original Contract Amount = \$5,139,487.45

Total Change Orders = \$0.00

Adjusted Contract Price = \$5,139,487.45

Expenditures to Date = \$0.00 (0%)



Samsung Highway (CR 404 Realignment) (FM 3349 to CR 404)






Samsung Highway (CR 404 Realignment) (FM 3349 to CR 404)





Anticipated Completion
Summer 2023



Original Contract Amount = \$2,796,832.80 Total Change Orders = \$0.00 Adjusted Contract Price = \$2,796,832.80

Expenditures to Date = \$117,081.00 (4%)











