




WILLIAMSON COUNTY COMMISSIONERS COURT

ROAD BOND PROGRAM
February 25, 2025


PRECINCT 1

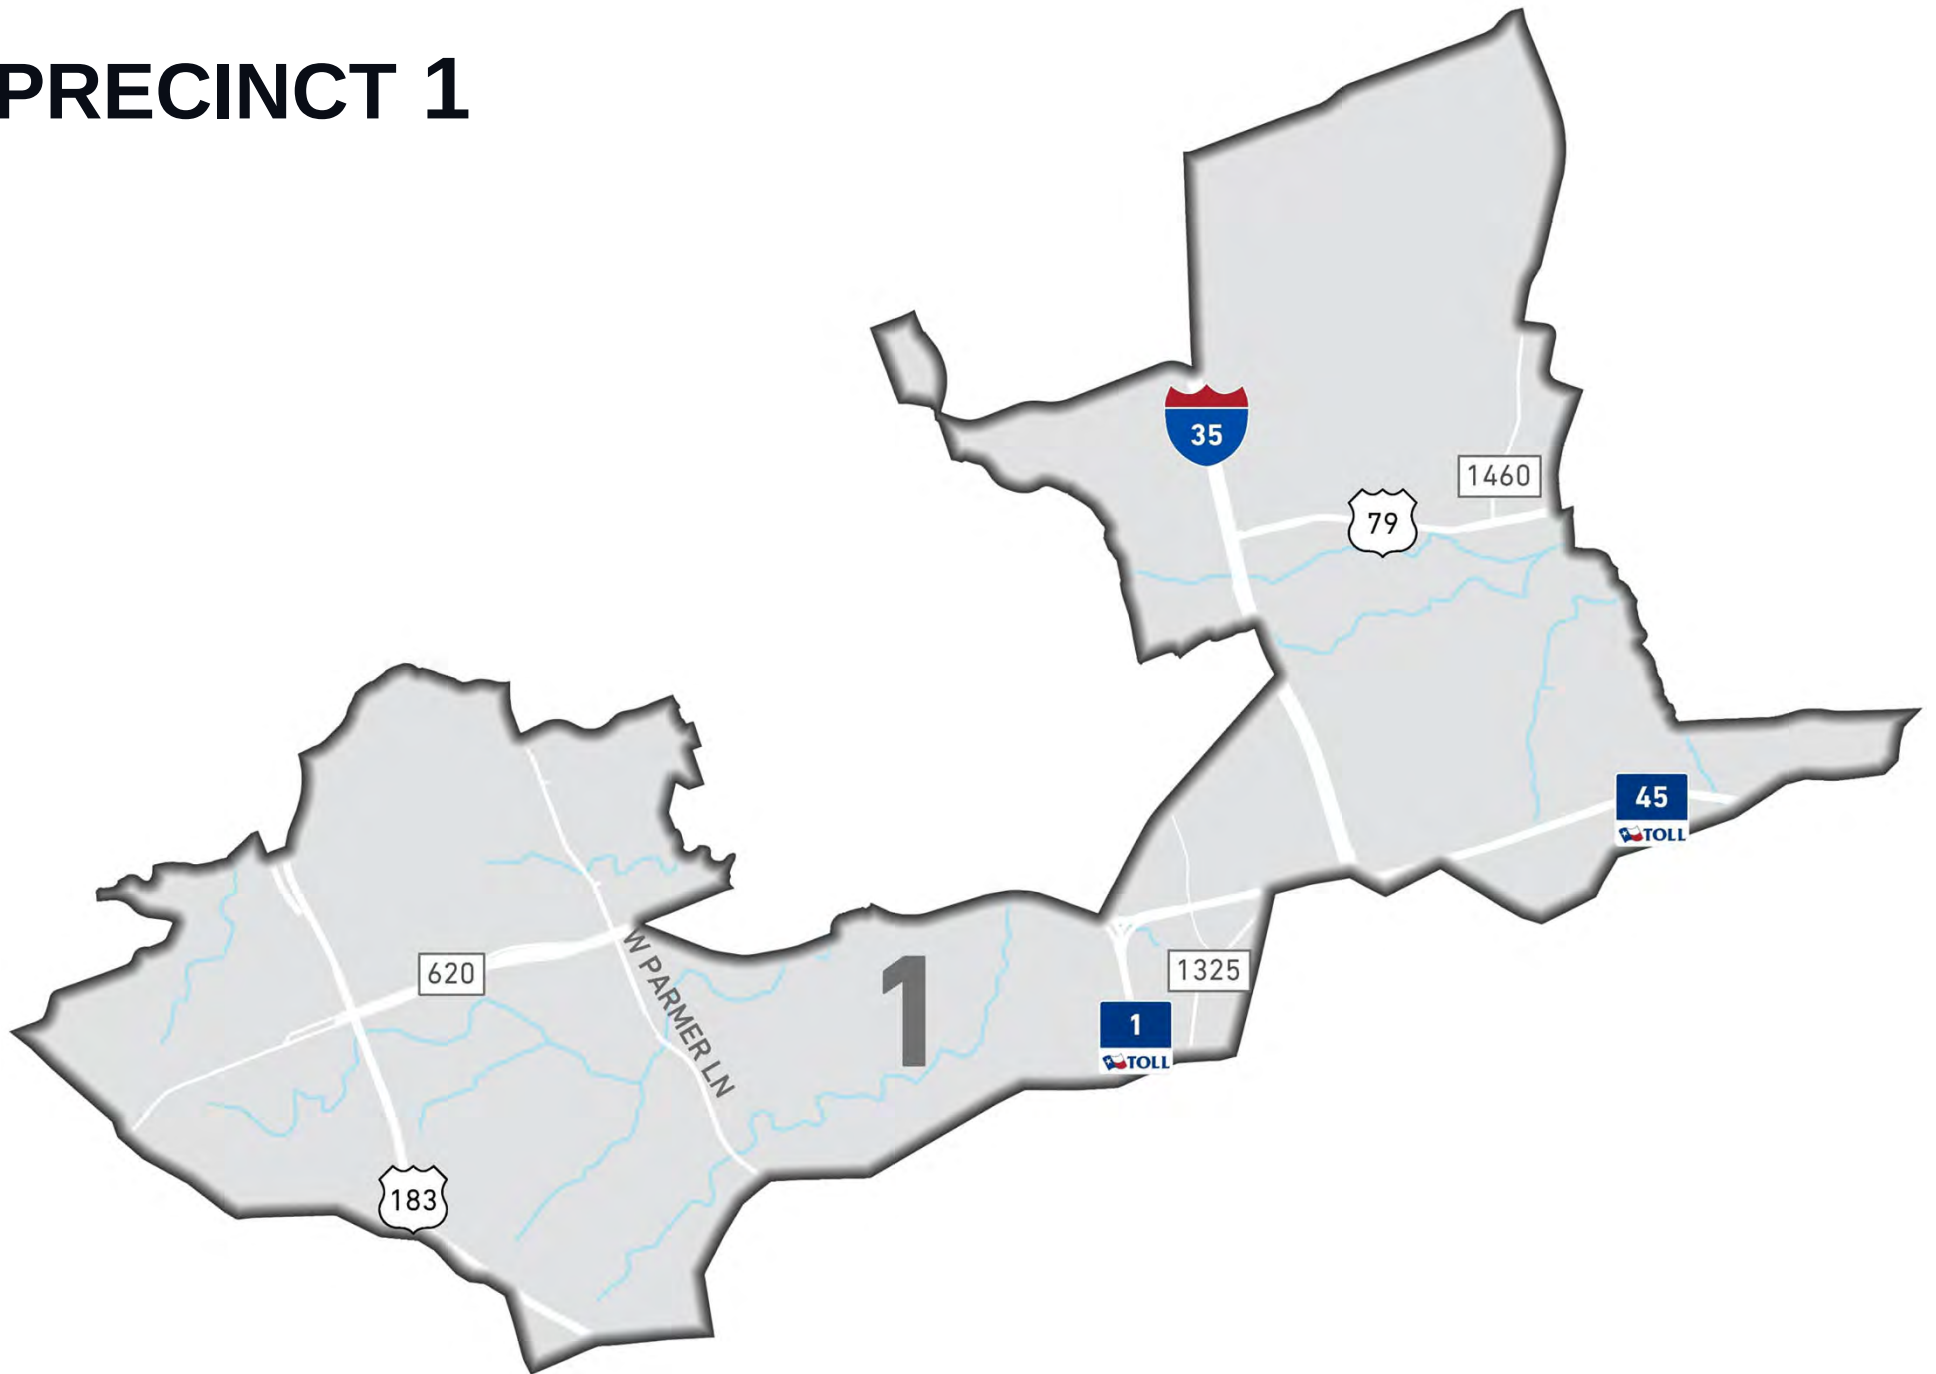

Projects under planning and
design, no active
construction projects.



PRECINCT 2

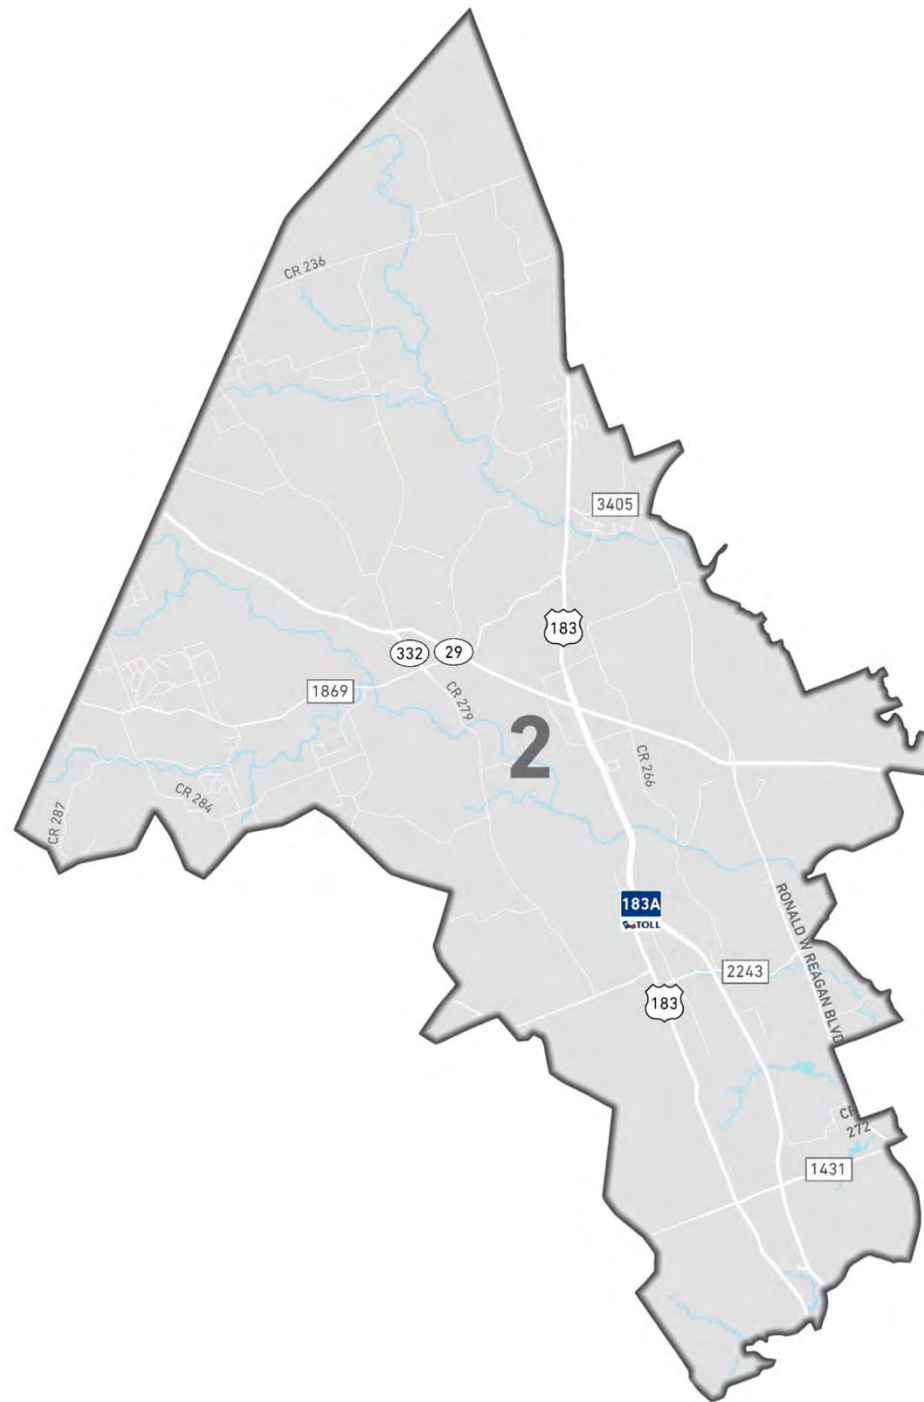

Liberty Hill (SH 29) Bypass (RM 1869 to CR 279)

Anticipated Completion
Late 2025




Original contract amount = \$14,149,449.00

Total change orders = \$280,462.00

Adjusted contract price = \$14,429,911.00

Expenditures to date = \$9,119,835.34 (63%)

Liberty Hill (SH 29) Bypass (RM 1869 to CR 279)



Liberty Hill (SH 29) Bypass (RM 1869 to CR 279)




Liberty Hill (SH 29) Bypass (RM 1869 to CR 279)



Ronald Reagan Widening (SH 29 to FM 3405)

Anticipated Completion
Summer 2027

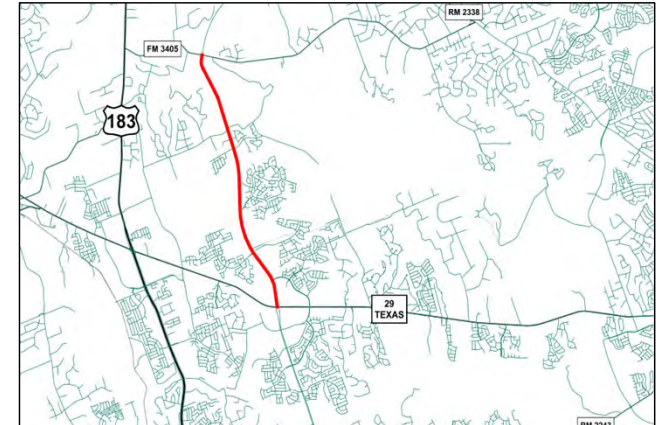

Original Contract Price = \$52,159,299.00

Total Change Orders to Date = \$203,752.50

Adjusted Contract Price = \$52,363,051.50

Expenditures to Date = \$11,535,462.47 (22%)



Ronald Reagan Widening (SH 29 to FM 3405)



Ronald Reagan Widening (SH 29 to FM 3405)




Ronald Reagan Widening (SH 29 to FM 3405)





Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)

Anticipated Completion
Fall 2025

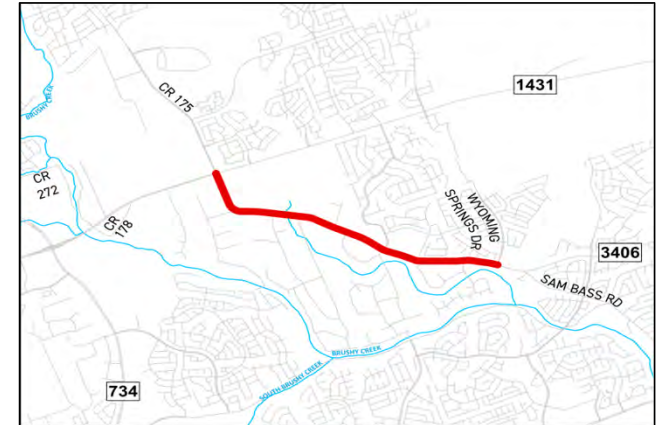

Original Contract Price = \$36,145,959.00

Total Change Orders to Date = -\$2,192,985.66

Adjusted Contract Price = \$33,952,973.34

Expenditures to Date = \$19,164,811.65 (56%)



Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)



Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)




Corridor H/Sam Bass (RM 1431 to Wyoming Springs Drive)



Wyoming Springs Extension (Brightwater Boulevard/Creek Bend to Sam Bass Road)

Anticipated Completion
Late 2026

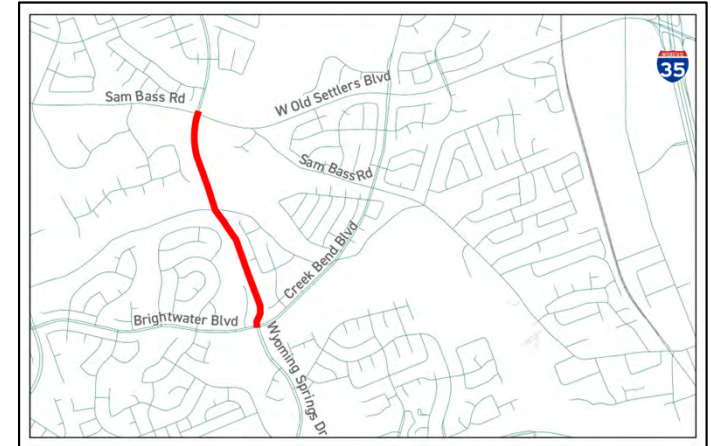

Partnership with the City of Round Rock


Original Contract Amount = \$25,917,630.47

Construction is managed by the City of Round Rock

Wyoming Springs Extension (Brightwater Boulevard/Creek Bend to Sam Bass Road)




Wyoming Springs Extension (Brightwater Boulevard/Creek Bend to Sam Bass Road)



CR 255 (CR 254 to Ronald Reagan Boulevard)

Anticipated Completion
Summer 2026

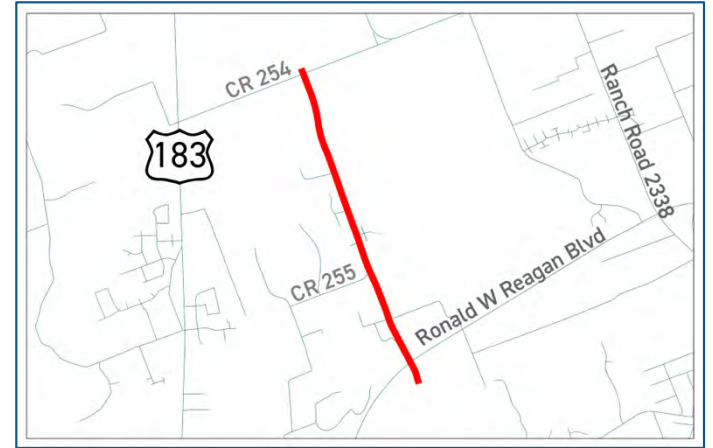

Original Contract Price = \$20,847,300.93

Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$20,847,300.93

Expenditures to Date = \$0.00 (0%)



CR 255

(CR 254 to Ronald Reagan Boulevard)




A detailed map of Township 4, showing a network of roads and highways. The map includes the following features:

- Highways:**
 - Interstate 35 (I-35) at the top left.
 - State Route 29 (SR-29) running horizontally across the middle.
 - State Route 79 (SR-79) running vertically through the center.
 - State Route 95 (SR-95) at the bottom center.
 - State Route 130 (SR-130) at the bottom left, marked with a "TOLL" sign.
- Roads:** Numerous County Routes (CR) are labeled, including CR 150, CR 318, CR 302, CR 343, CR 325, CR 349, CR 356, CR 364, CR 375, CR 330, CR 347, CR 341, CR 413, CR 426, CR 427, CR 435, CR 436, CR 439, CR 438, CR 471, CR 482, CR 469, CR 460, CR 456, CR 453, CR 448, CR 450, CR 452, CR 437, CR 397, CR 314, CR 405, CR 406, CR 407, CR 408, CR 409, CR 410, CR 411, CR 412, CR 413, CR 414, CR 415, CR 416, CR 417, CR 418, CR 419, CR 420, CR 421, CR 422, CR 423, CR 424, CR 425, CR 426, CR 427, CR 428, CR 429, CR 430, CR 431, CR 432, CR 433, CR 434, CR 435, CR 436, CR 437, CR 438, CR 439, CR 440, CR 441, CR 442, CR 443, CR 444, CR 445, CR 446, CR 447, CR 448, CR 449, CR 450, CR 451, CR 452, CR 453, CR 454, CR 455, CR 456, CR 457, CR 458, CR 459, CR 460, CR 461, CR 462, CR 463, CR 464, CR 465, CR 466, CR 467, CR 468, CR 469, CR 470, CR 471, CR 472, CR 473, CR 474, CR 475, CR 476, CR 477, CR 478, CR 479, CR 480, CR 481, CR 482, CR 483, CR 484, CR 485, CR 486, CR 487, CR 488, CR 489, CR 490, CR 491, CR 492, CR 493, CR 494, CR 495, CR 496, CR 497, CR 498, CR 499.

- Water Bodies:** Several blue lines represent creeks and rivers, and a larger blue area represents a lake or reservoir in the upper right quadrant.
- Other Features:**
- A large black number "4" is centered on the map.
- A road labeled "CHANDLER RD" runs horizontally across the middle.
- A road labeled "UNIVERSITY BLVD" runs vertically on the left side.
- Various numbered markers (e.g., 1105, 487, 972, 971, 1331, 1063, 685, 3349, 973, 1660, 1466, 619, 486) are placed along the roads.


East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)

Anticipated Completion
Summer 2025 (Roadwork)

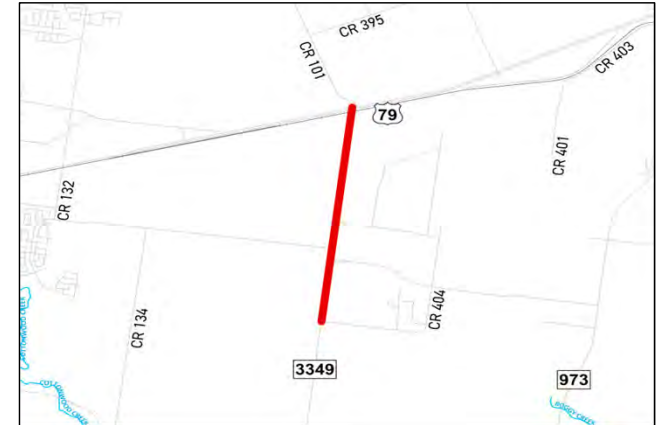

Original Contract Amount = \$81,941,038.13

Total Change Orders = \$2,335,980.09

Adjusted Contract Price = \$84,277,018.22

Expenditures to Date = \$64,593,396.73 (76%)



East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)



East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)




East Wilco Highway (FM 3349 / US 79 Interchange) (US 79 to CR 404)



East Wilco Highway - Segment 2 (CR 137 South of Hutto to CR 404)

Anticipated Completion
Summer 2028

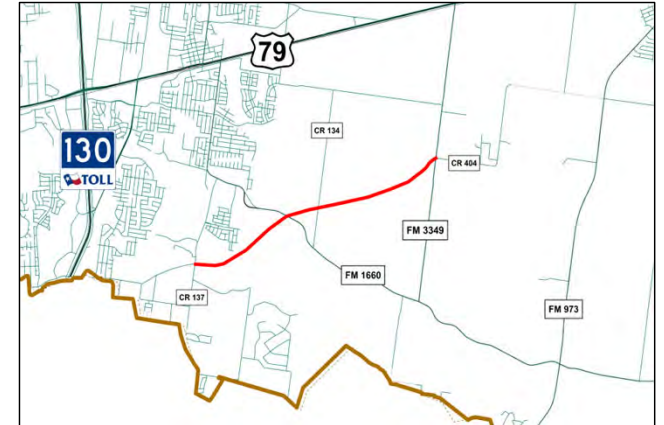

Original contract amount = \$64,407,606.63

Total change orders = \$0.00

Adjusted contract price = \$64,407,606.63

Expenditures to date = \$13,669,845.49 (21%)



East Wilco Highway - Segment 2 (CR 137 South of Hutto and CR 404)



East Wilco Highway - Segment 2 (CR 137 South of Hutto and CR 404)




East Wilco Highway - Segment 2 (CR 137 South of Hutto and CR 404)



Bud Stockton Extension (Traffic Signal at FM 487)

Anticipated Completion
Early 2025

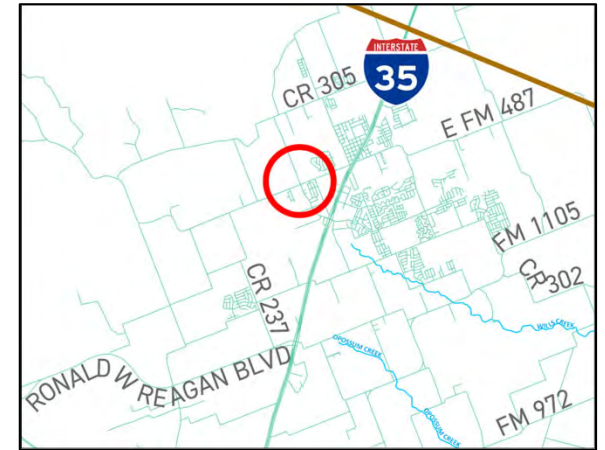

Original Contract Amount = \$553,983.00

Total Change Orders = \$0.00

Adjusted Contract Price = \$ 553,983.00


Expenditures to Date = \$169,350.00 (31%)

Bud Stockton Extension (Traffic Signal at FM 487)



Old Settlers Boulevard (North Red Bud Lane/CR 122 to CR 110)

Anticipated Completion
Fall 2025

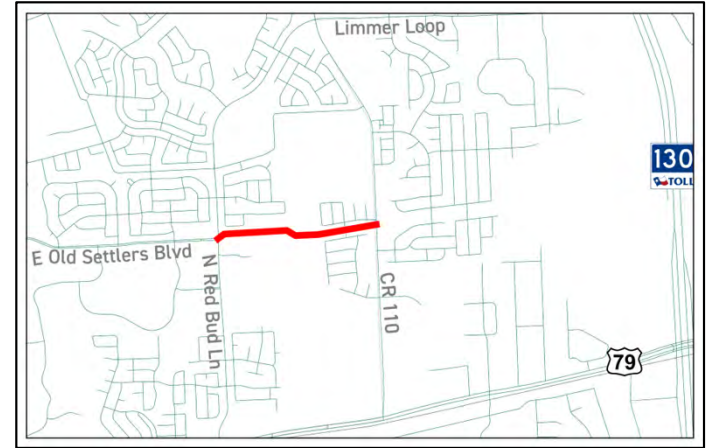


Partnership with the City of Round Rock

Original Contract Amount = \$14,920,847.10

Construction is managed by the City of Round Rock



Old Settlers Boulevard (North Red Bud Lane/CR 122 to CR 110)




Old Settlers Boulevard (North Red Bud Lane/CR 122 to CR 110)



CR 112 Widening (FM 1460 / A.W. Grimes to CR 117)

Anticipated Completion
Late 2026

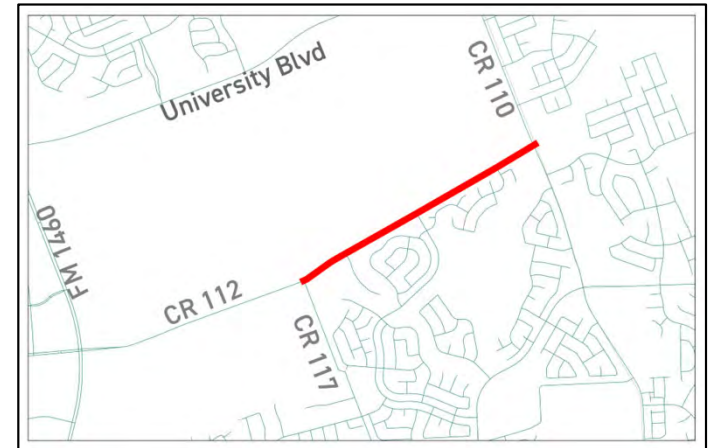

Partnership with the City of Round Rock

Original Contract Amount = \$13,119,712.35


Construction is managed by the City of Round Rock

CR 112 Widening (FM 1460 / A.W. Grimes to CR 117)



CR 112 Widening (CR 117 to CR 110)

Anticipated Completion
Late 2026

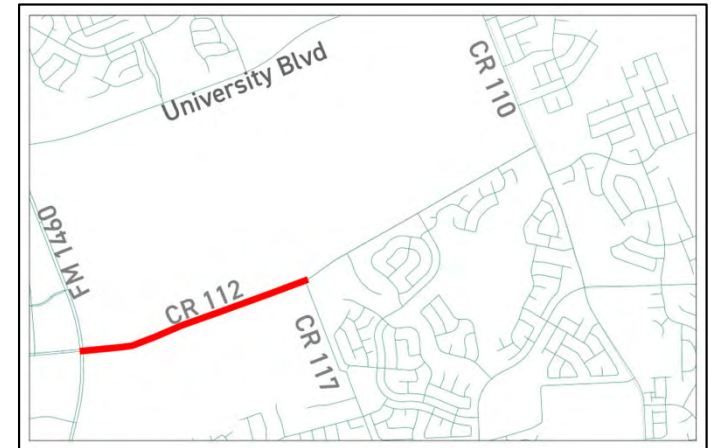

Partnership with the City of Round Rock

Original Contract Amount = \$20,434,128.40

Construction is managed by the City of Round Rock



CR 112 Widening (CR 117 to CR 110)

