

**2025/26 ROAD FUND PROJECT LIST  
CAPITAL IMPROVEMENT PROGRAM**

The following bridge and road improvement projects are budgeted for fiscal year 2025/26. Some projects are carryovers from prior fiscal years. Construction projects are contracted through a competitive bidding process with private contractors.

**1 BRIDGE IMPROVEMENT/REPLACEMENT PROJECTS**

- a. County Road 41 over Cache Creek (Rumsey) Bridge Replacement ..... \$7,500,000

Construction Phase

Sources of Financing: Federal ..... \$7,500,000

Environmental & Engineering Phase	Right of Way Phase	Construction
100% complete	100% complete	0%

Estimated Completion of Construction: February 2028

- b. County Road 95A Stevenson Bridge over Putah Creek Rehabilitation..... \$50,000

Preliminary Engineering and Right of Way Phases (Solano County-managed project)

Sources of Financing: County Road Fund ..... \$50,000

Environmental & Engineering Phase	Right of Way Phase	Construction
99% complete	90% complete	0%

Estimated Completion of Engineering & Right of Way: December 2025

- c. Road 40 over Cache Creek (Low Water Crossing) Bridge Replacement..... \$0

Final invoice to Caltrans to close out project

Sources of Financing: Federal ..... \$0

Environmental & Engineering Phase	Construction
100%	100%

Construction Project Accepted by Board of Supervisors December 6, 2022

- d. County Road 96 over Dry Slough Bridge Replacement..... \$150,000

Preliminary Engineering and Right of Way Phases

Sources of Financing: Federal ..... \$150,000

Environmental & Engineering Phase	Right of Way Phase	Construction
95% complete	75% complete	0%

Estimated Completion of Engineering and Right of Way Phases: March 2026

- e. County Road 96 over Union School Slough Bridge Replacement..... \$200,000

Preliminary Engineering and Right of Way Phases

Sources of Financing: Federal ..... \$200,000

Environmental & Engineering Phase	Right of Way Phase	Construction
95% complete	0%	0%

Estimated Completion of Engineering and Right of Way Phases: December 2026

- f. County Road 49 over Hamilton Creek Bridge Replacement..... \$150,000  
 Preliminary Engineering and Right of Way Phases  
 Sources of Financing: Federal ..... \$150,000

Engineering Phase	Right of Way Phase	Construction
95% complete FY25-26	10% complete FY25-26	0%

Estimated Completion of Engineering and Right of Way Phases: December 2026

- g. County Road 29 over Dry Slough Bridge Replacement..... \$500,000  
 Final Engineering, Right of Way, & Construction Phases  
 Sources of Financing: Federal ..... \$500,000

Environmental & Engineering Phase	Right of Way Phase	Construction
95% complete FY25-26	90% complete FY25-26	0%

Estimated Completion of Final Engineering & Right of Way: March 2026

Estimated Completion of Construction: February 2027

- h. County Road 29 over Chickahominy Slough Bridge Replacement..... \$200,000  
 Preliminary Engineering and Environmental Phase  
 Sources of Financing: Federal ..... \$200,000

Environmental & Engineering Phase	Right of Way Phase	Construction
5% complete FY25-26	0%	0%

Estimated Completion of Environmental & Engineering: December 2027

- i. Grant/SR128/Russell Blvd Bike & Ped Improvements..... \$550,000  
 Preliminary Engineering and Right of Way Phases  
 Source of Financing: Federal..... \$500,000  
 County Road Fund ..... \$50,000

Engineering Phase	Right of Way Phase	Construction
0% complete FY25-26	0%	0%

Estimated Completion of Right of Way & Engineering: December 2027

- j. CR32A Railroad Crossing Relocation and Grade Separation Project ..... \$1,100,000  
 Preliminary Engineering and Environmental Phase  
 Source of Financing: County Road Fund ..... \$100,000  
 Federal..... \$500,000  
 State..... \$500,000

Engineering Phase	Right of Way Phase	Construction
0% complete FY25-26	0%	0%

Estimated Completion of Environmental & Engineering: June 2028

## 2 ROAD IMPROVEMENT PROJECTS

- a. Madison Flood Mitigation ..... \$400,000  
 Preliminary Engineering & Environmental Phases for the Madison, Esparto and State  
 Route 16 Flood Risk Reduction Project  
 Sources of Financing: Madison Flood Mitigation Fund ..... \$400,000

Engineering Phase	Right of Way Phase	Construction
10% complete FY25-26	0%	0%

Estimated Completion of 10% level Environmental & Engineering: July 2025

- b. CR98 Bike & Safety Improvement, Phase 2, CR29 to Solano County ..... \$1,700,000  
 Preliminary Engineering & Right of Way Phases  
 Source of Financing: Federal (RSTP) ..... \$1,500,000  
 County Road Fund ..... \$200,000

Environmental & Engineering Phase	Right of Way Phase	Construction
90% complete FY25-26	50% complete FY25-26	0%

Estimated Completion of Right of Way & Engineering: December 2026

- c. CR 41 Washout Realignment Project ..... \$0  
 Preliminary Engineering & Environmental, and Construction Phases  
 Source of Financing: None identified to date ..... \$0  
 (Previously used General Fund – Road Contingency funding for earlier efforts)

Environmental & Engineering Phase	Right of Way Phase	Construction
75% complete FY25-26	5% complete FY25-26	0%

Estimated Completion of Environmental & Engineering: Unknown; unfunded to date

- d. 2023 Road Rehabilitation Project ..... \$10,000  
 Warranty Period  
 Source of Financing: SB1 Road Maint. & Rehabilitation Account ..... \$10,000

Environmental & Engineering Phase	Construction
100%	100%

Estimated Completion of Construction: July 2025

- e. 2024 Annual Striping Contract ..... \$100,000  
 Preliminary Engineering, Environmental, and Construction Phases  
 Source of Financing: SB1 Road Maint. & Rehabilitation Account ..... \$100,000

Environmental & Engineering Phase	Construction
90% complete FY25-26	0%

Determine roads to receive treatment: Summer 2024



Estimated Completion of Construction: June 2026

- f. 2024 Road Resurfacing Project ..... \$10,000  
Warranty Period  
Source of Financing: SB1 Road Maint. & Rehabilitation Account ..... \$10,000

Environmental & Engineering Phase	Construction
100% complete	100%


Estimated Completion of Construction: July 2025

- g. HSIP-CR102 Bike & Safety Improvements Project..... \$350,000  
Preliminary Engineering and Construction Phases  
Source of Financing: State HSIP Funds ..... \$300,000  
County Road Fund ..... \$50,000

Environmental & Engineering Phase	Construction
75% complete  FY25-26	0%  FY25-26


Estimated Completion of Engineering: March 2026

- h. Safe Streets 4 All Grant, County Safety Action Plan ..... \$250,000  
Develop countywide safety action plan  
Source of Financing: Federal Funds ..... \$200,000  
County Road Fund ..... \$50,000

Engineering Study	Environmental & Engineering Phase	Right of Way
0%  FY25-26	0%	0%


Estimated Completion of Plan: December 2026

- i. East Esparto Sidewalk Study and Design ..... \$180,000  
Predesign engineering study  
Source of Financing: Federal Funds ..... \$150,000  
County Road Fund ..... \$30,000

Engineering Study	Environmental & Engineering Phase	Right of Way
0%  FY25-26	0%	0%


Estimated Completion of Study: December 2026

- j. 2025 Pavement Preservation Project ..... \$10,100,000  
Construction Phase  
Source of Financing: SB1 Road Maint. & Rehabilitation Account .. \$6,100,000  
County Road Fund ..... \$4,000,000

Environmental & Engineering Phase	Construction
100% complete	0%  FY25-26

Estimated Completion of Construction: January 2026

- k. Bridge Preventive Maintenance Project 1..... \$3,000,000  
Preliminary Engineering and Construction Phases  
Source of Financing: County Road Fund ..... \$3,000,000

Environmental & Engineering Phase	Construction
75% complete  FY25-26	0%

Estimated Completion of Construction: January 2026

1. Clarksburg Branch Line Extension Project..... \$20,000  
 Preliminary Engineering & Environmental, and Right of way Phases  
 (Currently City of West Sacramento-managed project)  
 Source of Financing: County Road Fund..... \$20,000

Environmental & Engineering Phase	Right of Way Phase	Construction
5% complete FY25-26	0%	0%

Estimated Completion of Environmental, Engineering & Right of way: June 2028

- m. Yolo County Public Works Yard Pavement Rehabilitation Project ..... \$100,000  
 Preliminary Engineering and Construction Phases  
 Source of Financing: County Road Fund ..... \$100,000

Environmental & Engineering Phase	Construction
20% complete FY25-26	0%

Estimated Completion of Construction: January 2027

- n. Bridge Preventive Maintenance Project 2..... \$200,000  
 Preliminary Engineering, Environmental, and Construction Phases  
 Source of Financing: County Road Fund ..... \$200,000

Environmental & Engineering Phase	Construction
10% complete FY25-26	0%

Estimated Completion of Environmental & Engineering: January 2027

- o. 2026 Pavement Preservation Project ..... \$800,000  
 Preliminary Engineering, Environmental, and Construction Phases  
 Source of Financing: SB1 Road Maint. & Rehabilitation Account ..... \$300,000  
 County Road Fund ..... \$500,000

Environmental & Engineering Phase	Construction
1% complete FY25-26	0%

Estimated Completion of Construction: January 2027

- p. Road Slope Stability Project..... \$200,000  
 Preliminary Engineering, Environmental, and Construction Phases  
 Source of Financing: County Road Fund ..... \$200,000

Environmental & Engineering Phase	Construction
0% FY25-26	0%

Estimated Completion of Engineering and Environmental Phase: December 2027


- q. CUPCAA Striping Contract(s)..... \$200,000  
 Construction Phase  
 Source of Financing: County Road Fund ..... \$200,000

Environmental & Engineering Phase	Construction
0% FY25-26	0%

Determine roads to receive treatment: Summer 2025

Estimated Completion of Construction: June 2026

r. CUPCCAA Chip Seal Contract(s) ..... \$400,000  
 Construction Phase  
 Source of Financing: County Road Fund ..... \$400,000

Environmental & Engineering Phase	Construction
0%  FY25-26	0%


Determine roads to receive treatment: Summer 2025  
 Estimated Completion of Construction: June 2026

# ROAD FUND PROJECT SITE MAPS

PROJECT: 1a

ROAD NO. OR NAME: County Road 41 Bridge over Cache Creek (Rumsey Bridge)

BRIDGE NO.: 22C-003

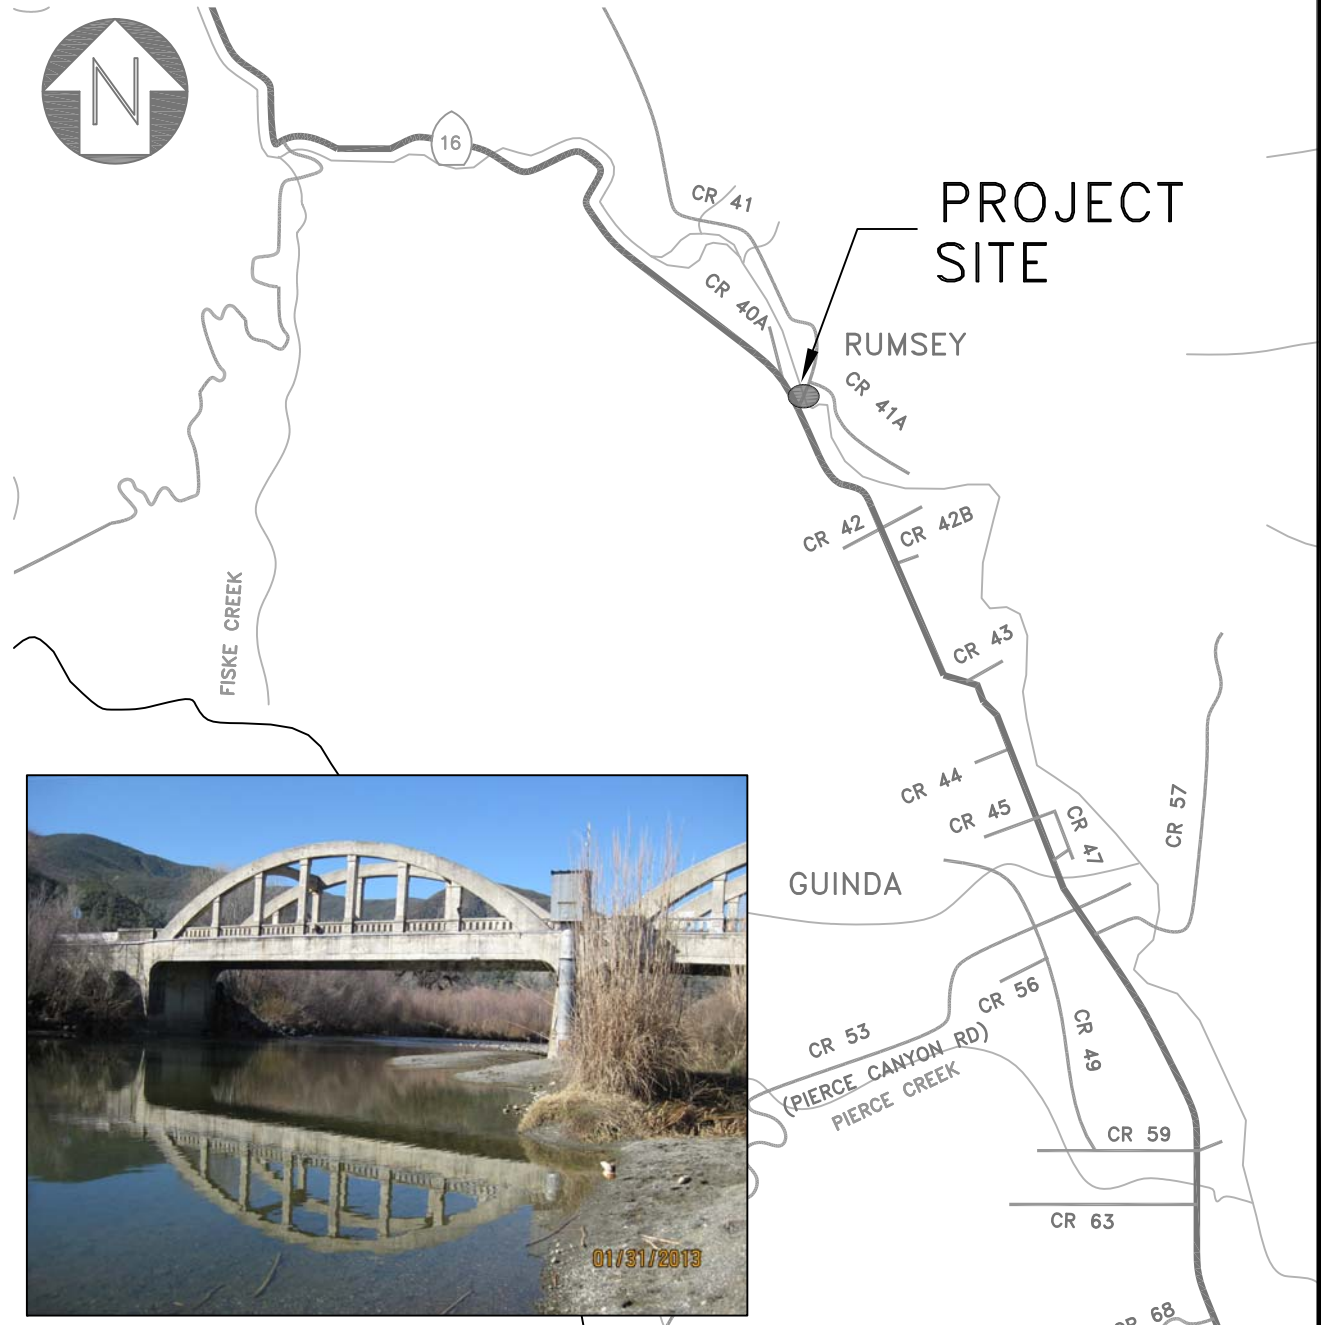

DESCRIPTION OF WORK: Construction Phase.

NOTES: 100% Reimbursement from Federal Funds.

# ROAD FUND PROJECT SITE MAPS

## PROJECT 1b

ROAD NO. OR NAME: CR 95A (Stevenson's) Bridge over Putah Creek (Solano/Yolo Bridge);  
Bridge Rehabilitation

BRIDGE NO.: 23C-092



DESCRIPTION OF WORK: Preliminary Engineering & Right of Way Phases. (Solano County is  
managing project.)


NOTES: Yolo County contributes 1/2 of local match from Road Fund, per Agreement 05-19.

# ROAD FUND PROJECT SITE MAPS

PROJECT: 1c

ROAD NO. OR NAME: Road 40 Bridge over Cache Creek (Low Water Crossing)

BRIDGE NO.: 22C-003

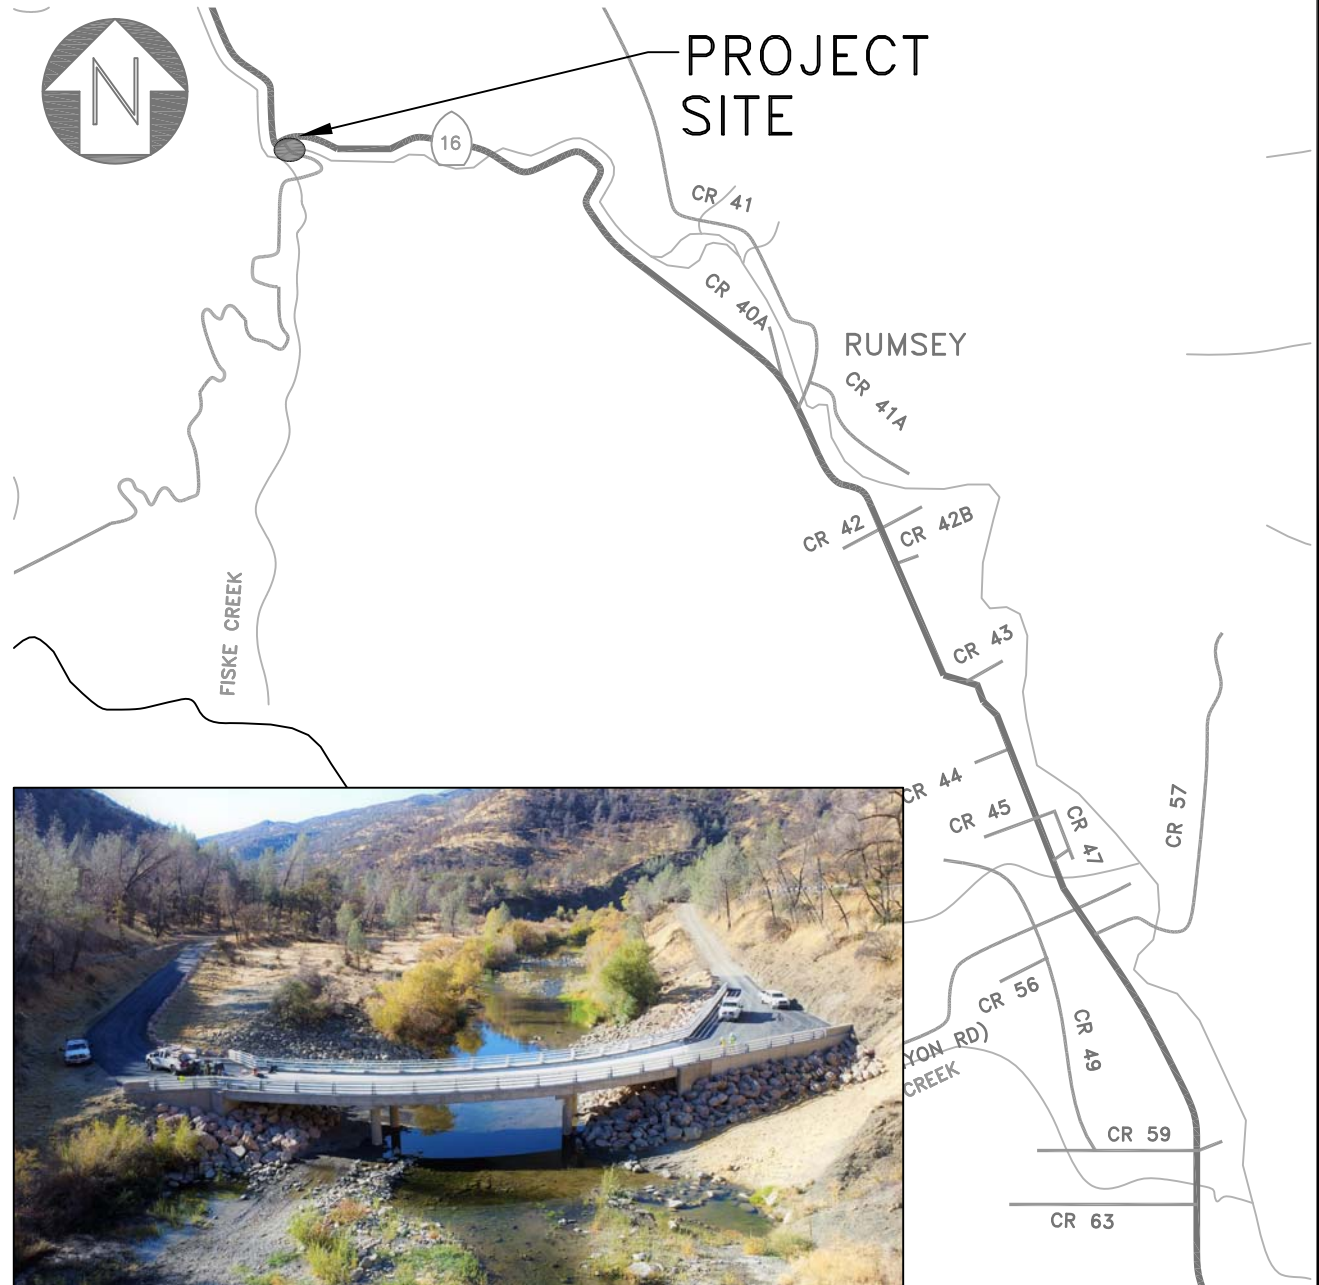

DESCRIPTION OF WORK: Final invoice to Caltrans to close out project.

NOTES: 100% Reimbursement from State and federal Funds for Construction

# ROAD FUND PROJECT SITE MAPS

PROJECT: 1d

ROAD NO. OR NAME: County Road 96 Bridge over Dry Slough; Bridge Replacement

BRIDGE NO.: 22C-127



ERS



SOLANO COUNTY

DESCRIPTION OF WORK: Preliminary Engineering and Right of Way Phases.

NOTES: 100% Reimbursement from Federal Funds.




# ROAD FUND PROJECT SITE MAPS

## PROJECT: 1f

ROAD NO. OR NAME: County Road 49 Bridge over Hamilton Creek; Bridge Replacement

BRIDGE NO.: 22C-095

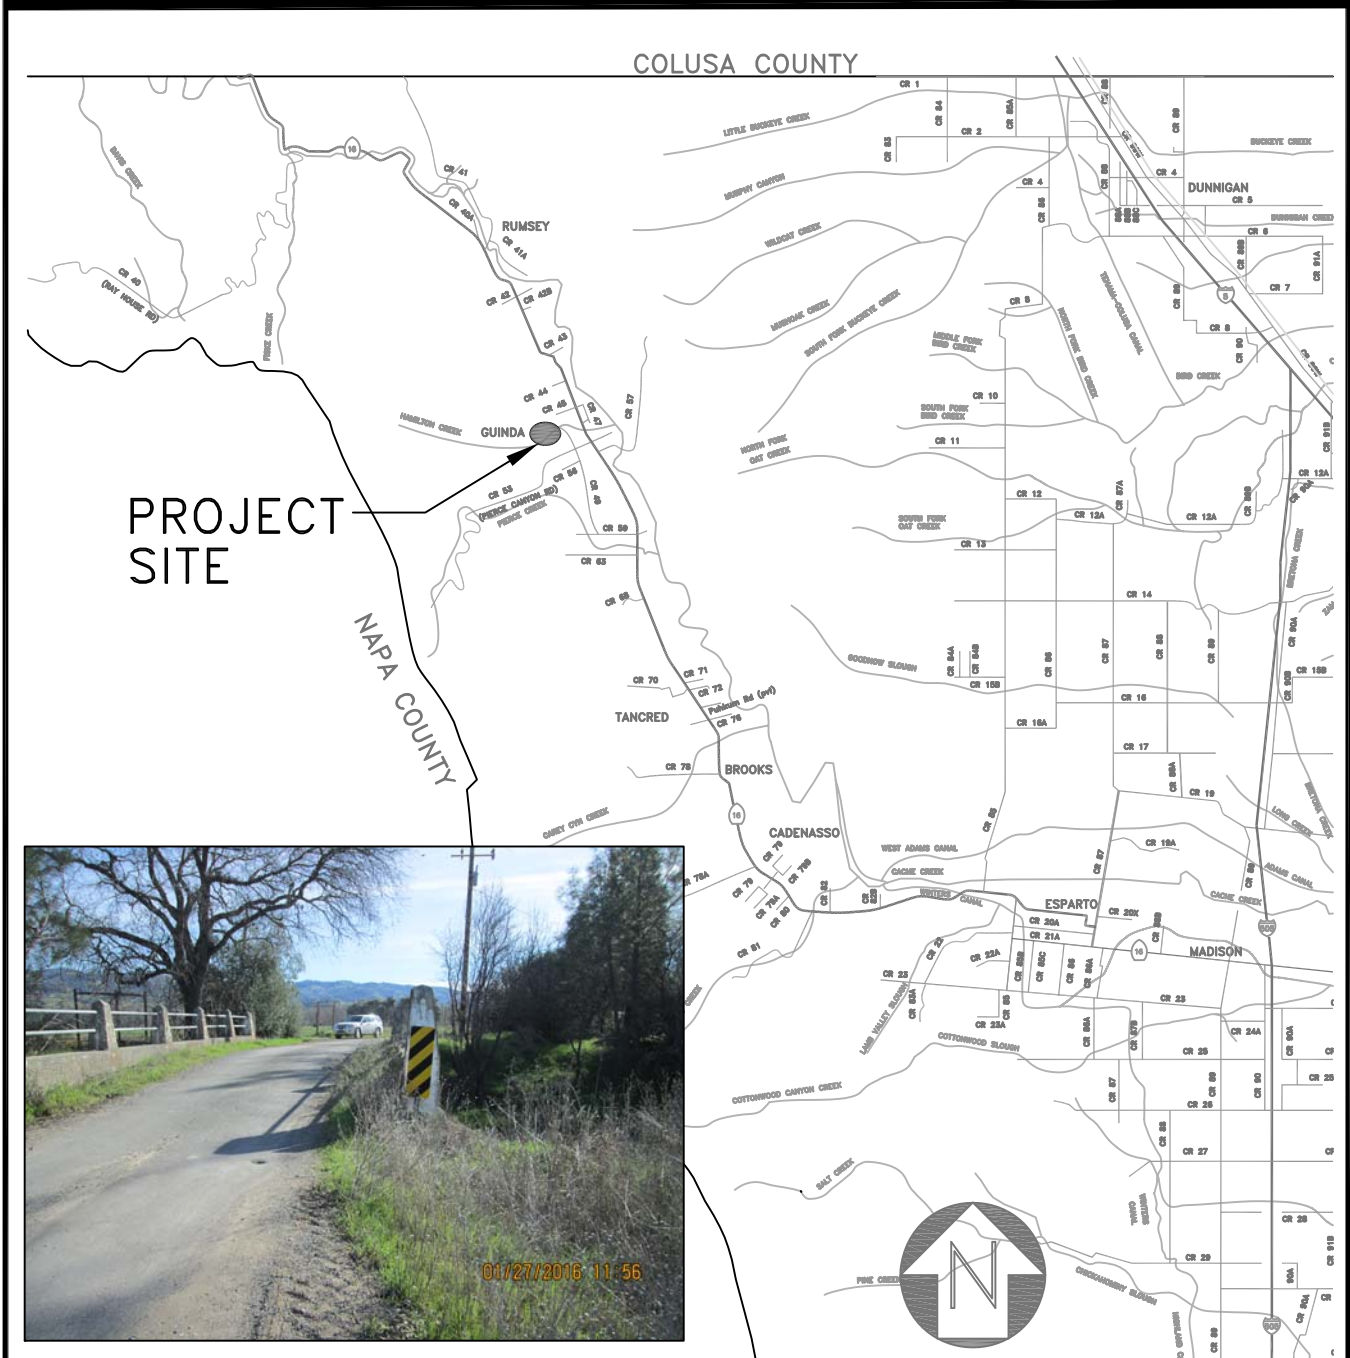

DESCRIPTION OF WORK: Preliminary Engineering and Right of Way Phases.

NOTES: 100% Reimbursement from Federal Funds.

# ROAD FUND PROJECT SITE MAPS

PROJECT: 1g

ROAD NO. OR NAME: County Road 29 Bridge over Dry Slough; Bridge Replacement

BRIDGE NO.: 22C-117



DESCRIPTION OF WORK: Final Engineering, Right of Way and Construction Phases.

NOTES: 100% Reimbursement from Federal Funds.

# ROAD FUND PROJECT SITE MAPS

PROJECT: 1h

ROAD NO. OR NAME: County Road 29 Bridge over Chickahominy Slough; Bridge Replacement

BRIDGE NO.: 22C-105




DESCRIPTION OF WORK: Preliminary Engineering & Environmental Phases.

NOTES: 100% Reimbursement from Federal Funds.

# ROAD FUND PROJECT SITE MAPS

PROJECT: 1i

ROAD NO. OR NAME: Grant/SR128/Russell Blvd Bike & Ped Improvements

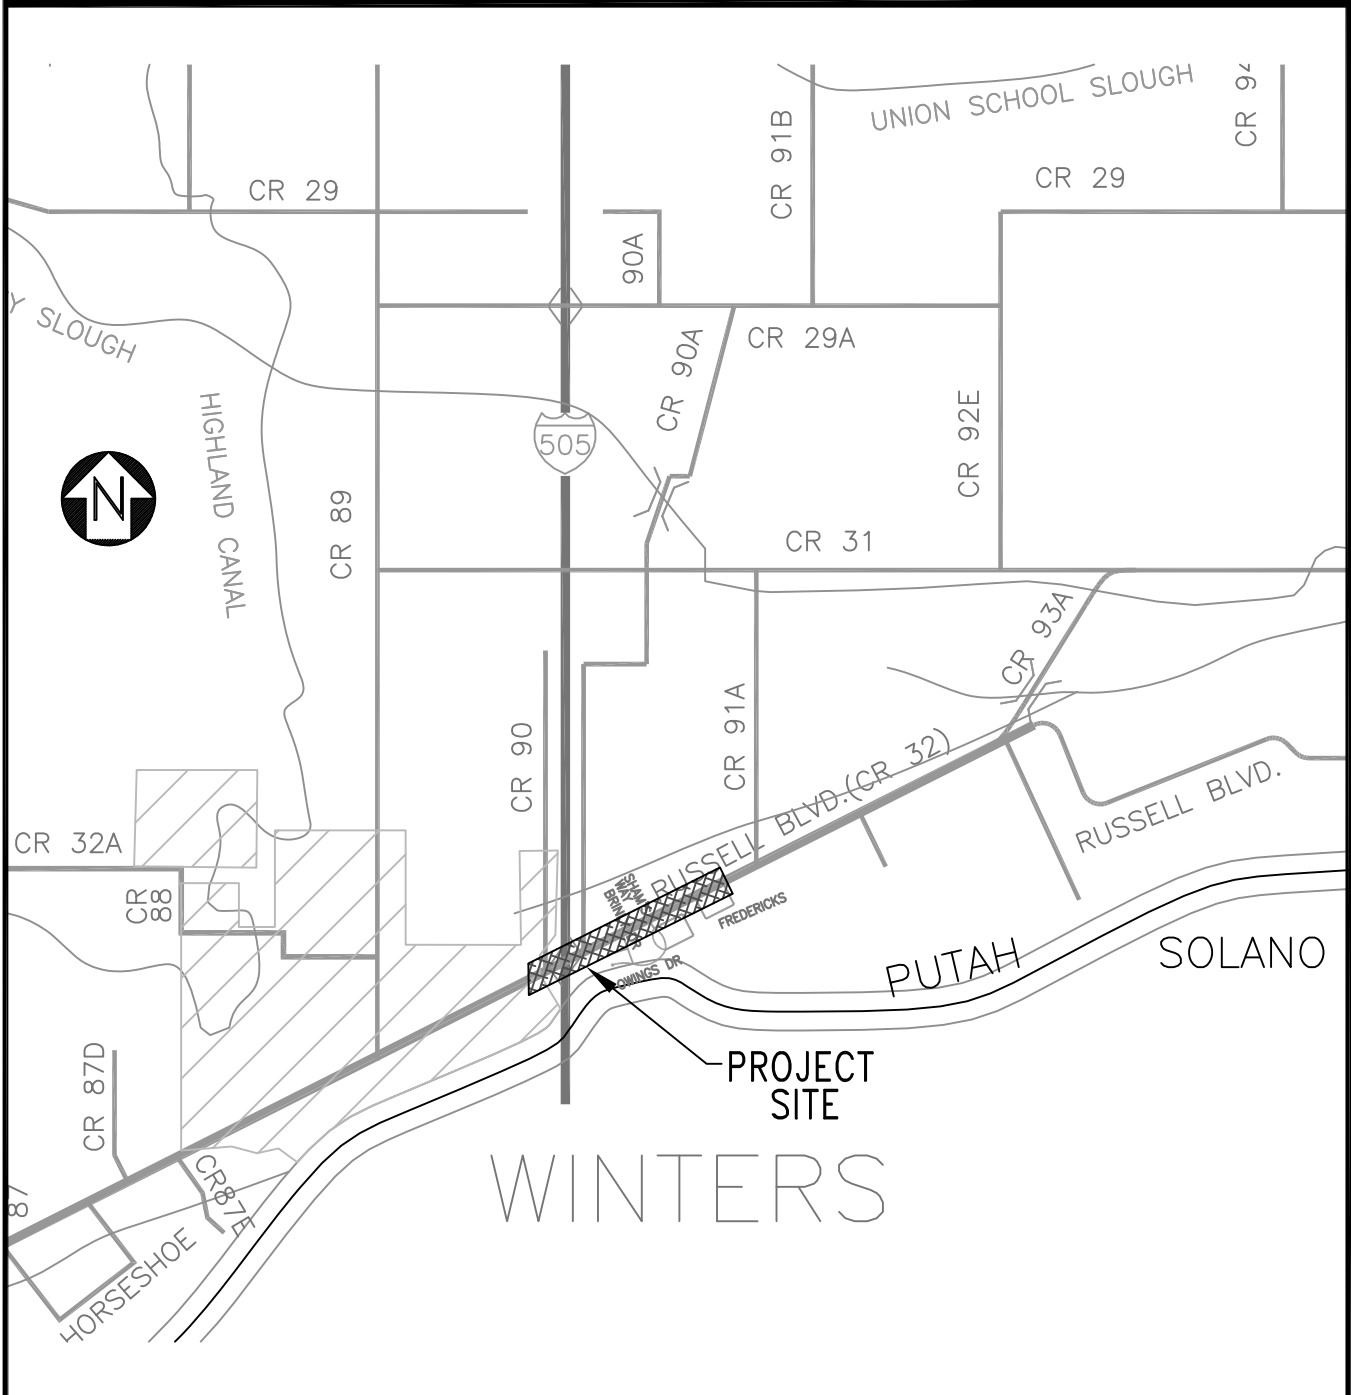

DESCRIPTION OF WORK: Preliminary Engineering and Right of Way Phases.

NOTES: Federal Earmark Funds and County Road Funds.

# ROAD FUND PROJECT SITE MAPS

PROJECT: 1j

ROAD NO. OR NAME: County Road 32A Railroad Crossing Relocation and Grade Separation Project




DESCRIPTION OF WORK: Preliminary Engineering & Environmental Phase.

NOTES: Federal grant, State grant, and County Road Funds.

# ROAD FUND PROJECT SITE MAPS

## PROJECT 2a

ROAD NO. OR NAME: Madison Flood Mitigation

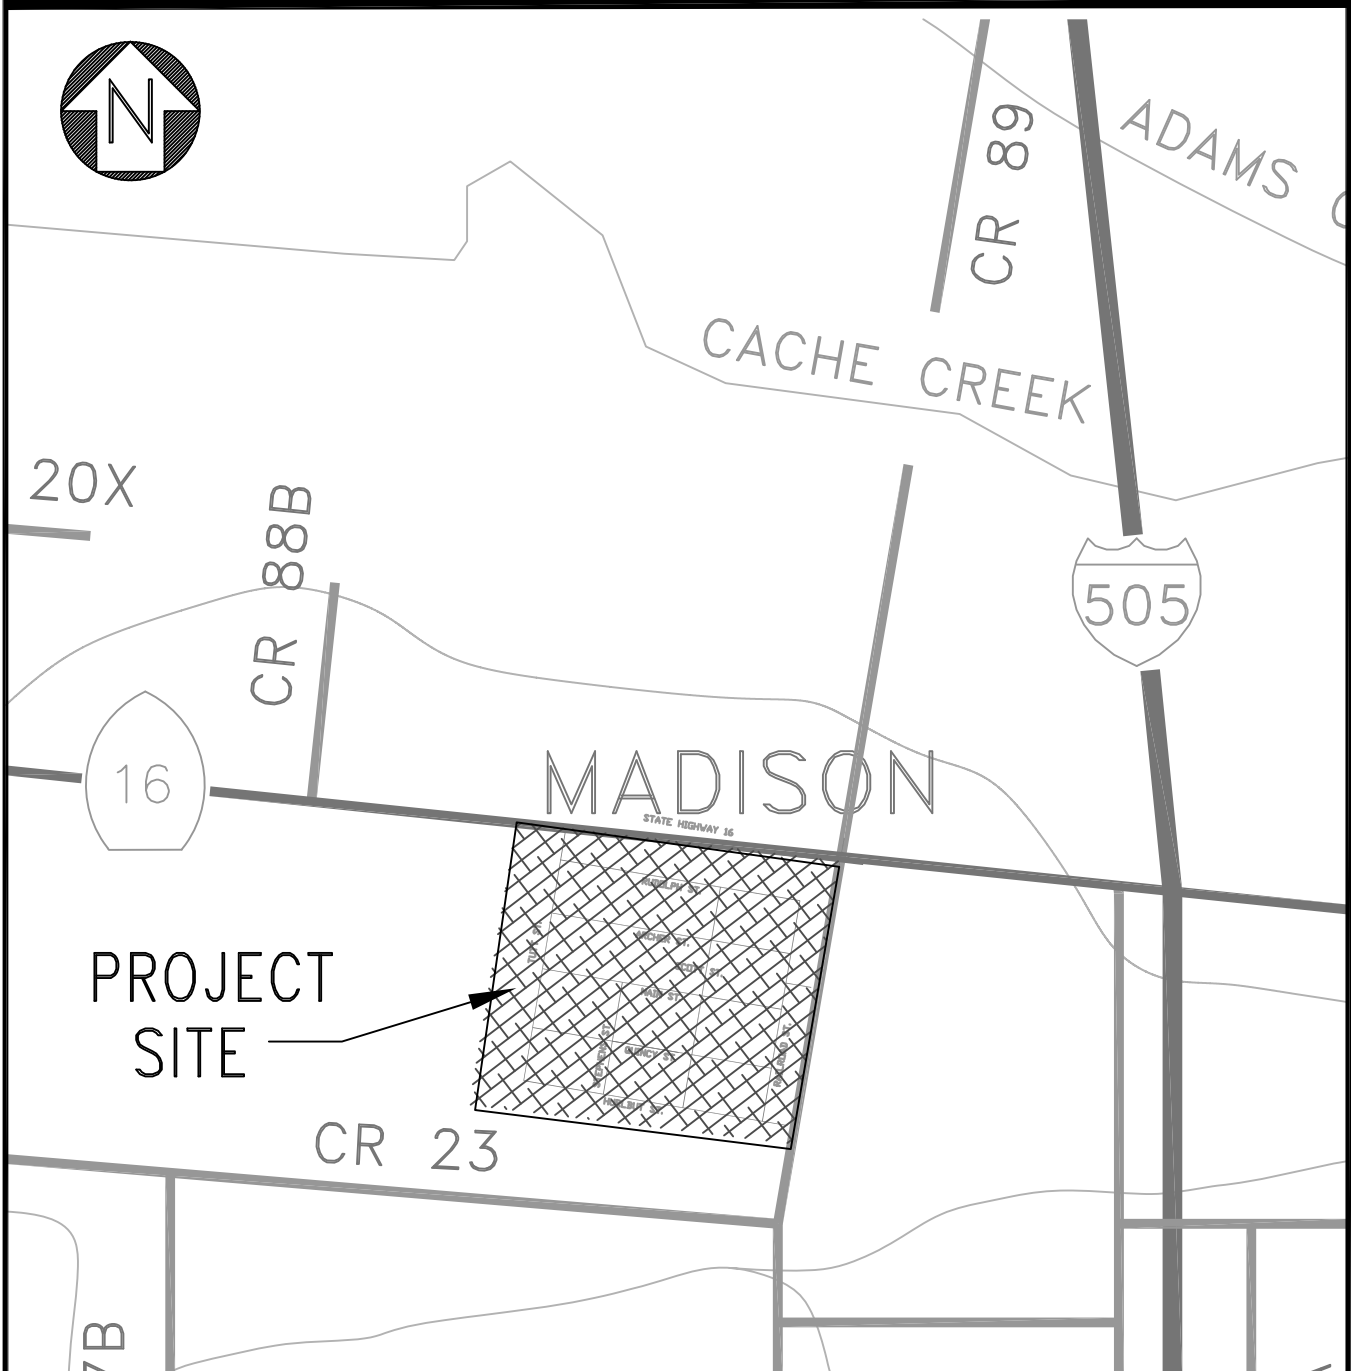

DESCRIPTION OF WORK: Madison, Esparto and State Route 16 Flood Risk Reduction Project Preliminary Engineering and Environmental Phases.

NOTES: Madison Flood Mitigation Fund

# ROAD FUND PROJECT SITE MAPS

PROJECT: 2b

ROAD NO. OR NAME: County Road 98 Bike & Safety Project-Phase 2





DESCRIPTION OF WORK: Environmental, Engineering & Right of Way Phases.

NOTES: 88.53% Reimbursement from Federal funds.

# ROAD FUND PROJECT SITE MAPS

## PROJECT: 2c

ROAD NO. OR NAME: CR 41 Washout Realignment Project

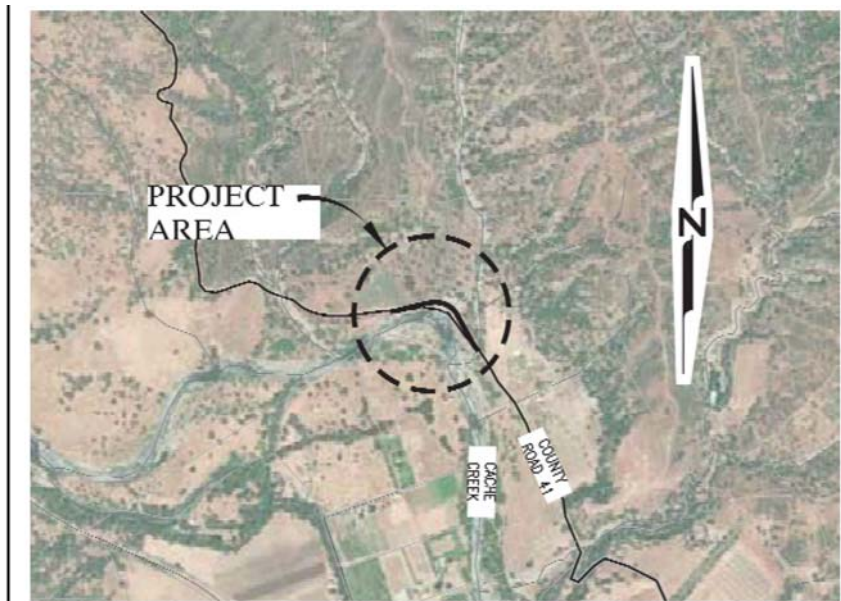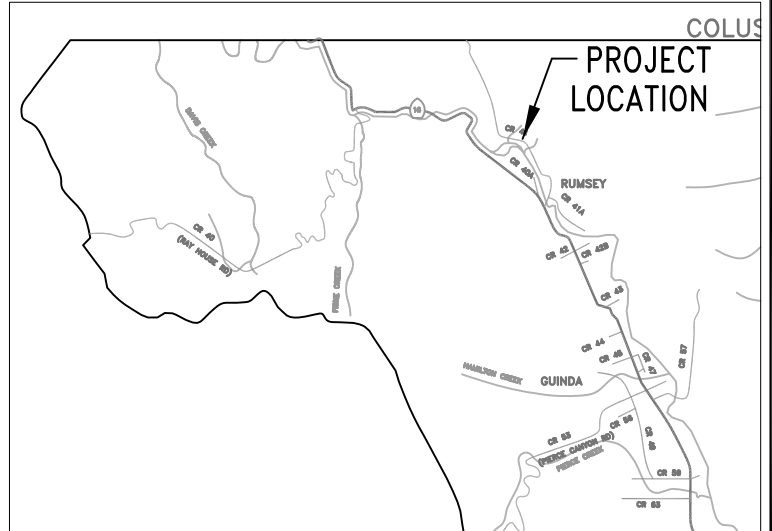

DESCRIPTION OF WORK: Preliminary Engineering, Environmental, Right of Way, and Construction Phases.


NOTES: Currently Unfunded.



# ROAD FUND PROJECT SITE MAPS

PROJECT: 2e

ROAD NO. OR NAME: 2024 Annual Striping Contract

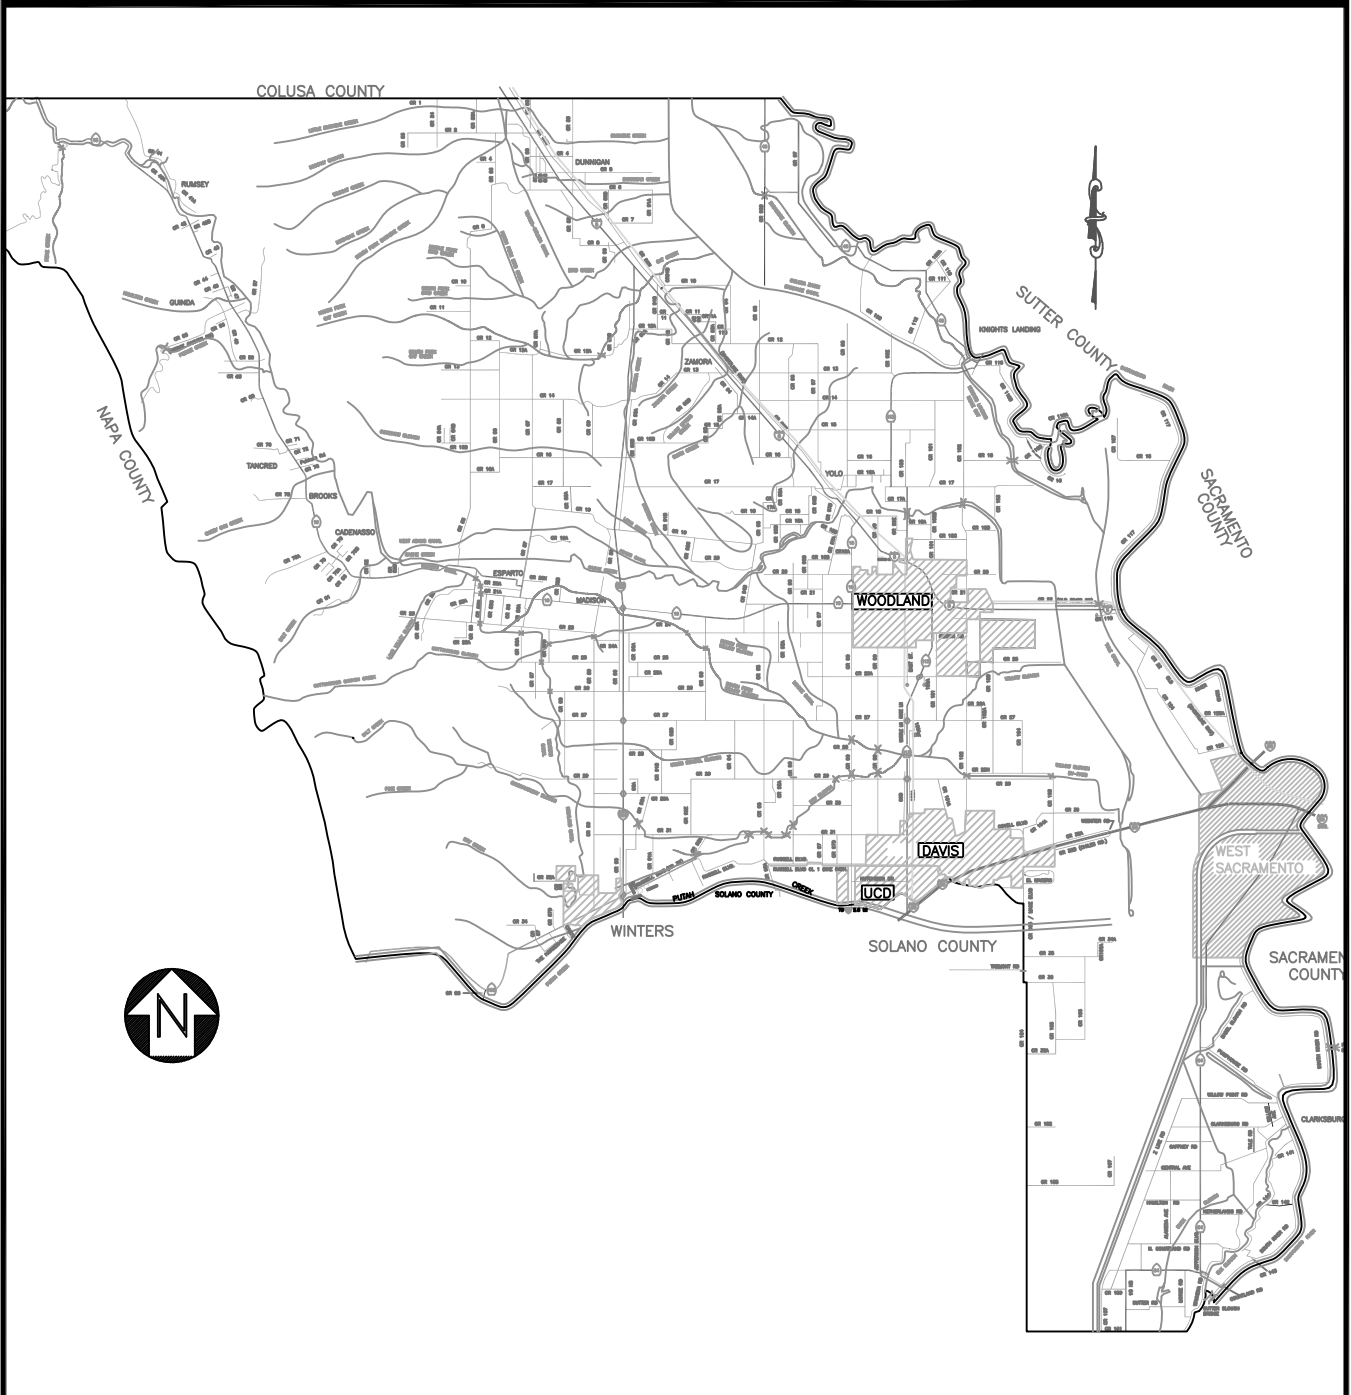


DESCRIPTION OF WORK: Road Striping various County Roads; Preliminary Engineering, Environmental, and Construction Phases.

NOTES: SB1 Road Maintenance & Rehabilitation Account Funds.

# ROAD FUND PROJECT SITE MAPS

PROJECT: 2f

ROAD NO. OR NAME: 2024 Road Resurfacing Project

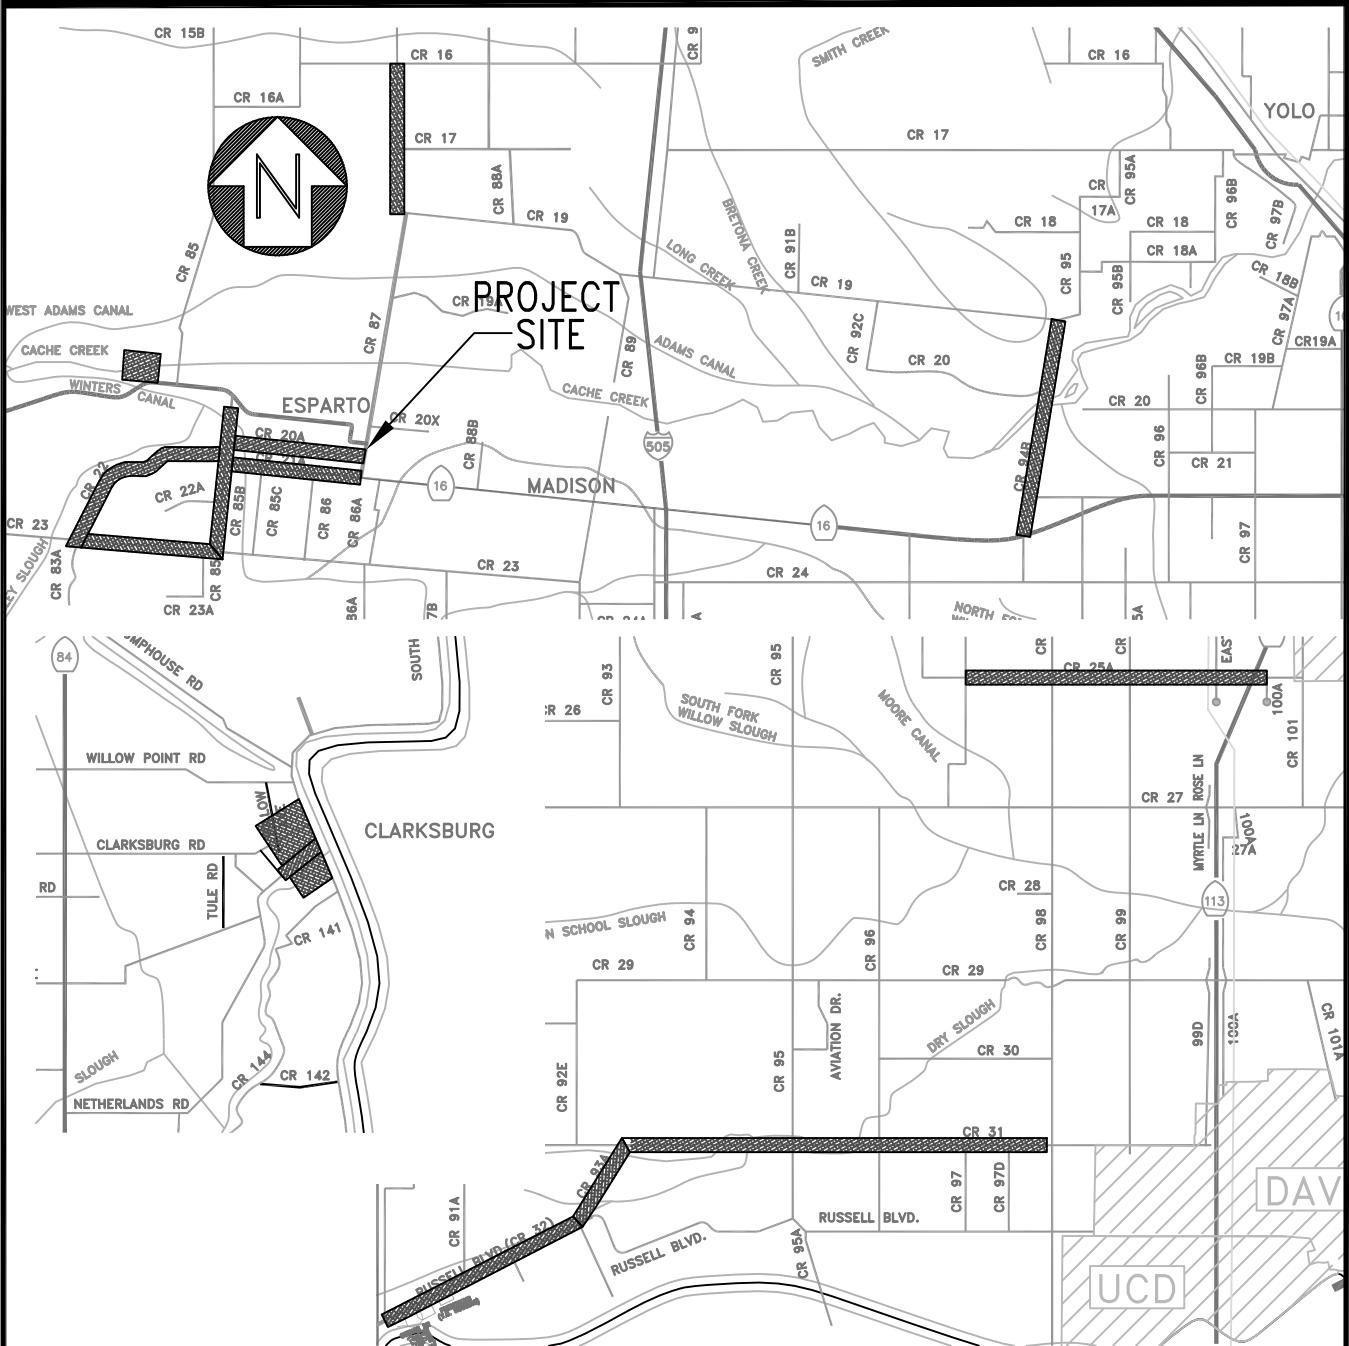


DESCRIPTION OF WORK: Warranty Period.

NOTES: SB1 Road Road Maintenance & Rehabilitation Funds.

# ROAD FUND PROJECT SITE MAPS

PROJECT: 2g

ROAD NO. OR NAME: HSIP - CR102 Bike & Safety Improvement Project

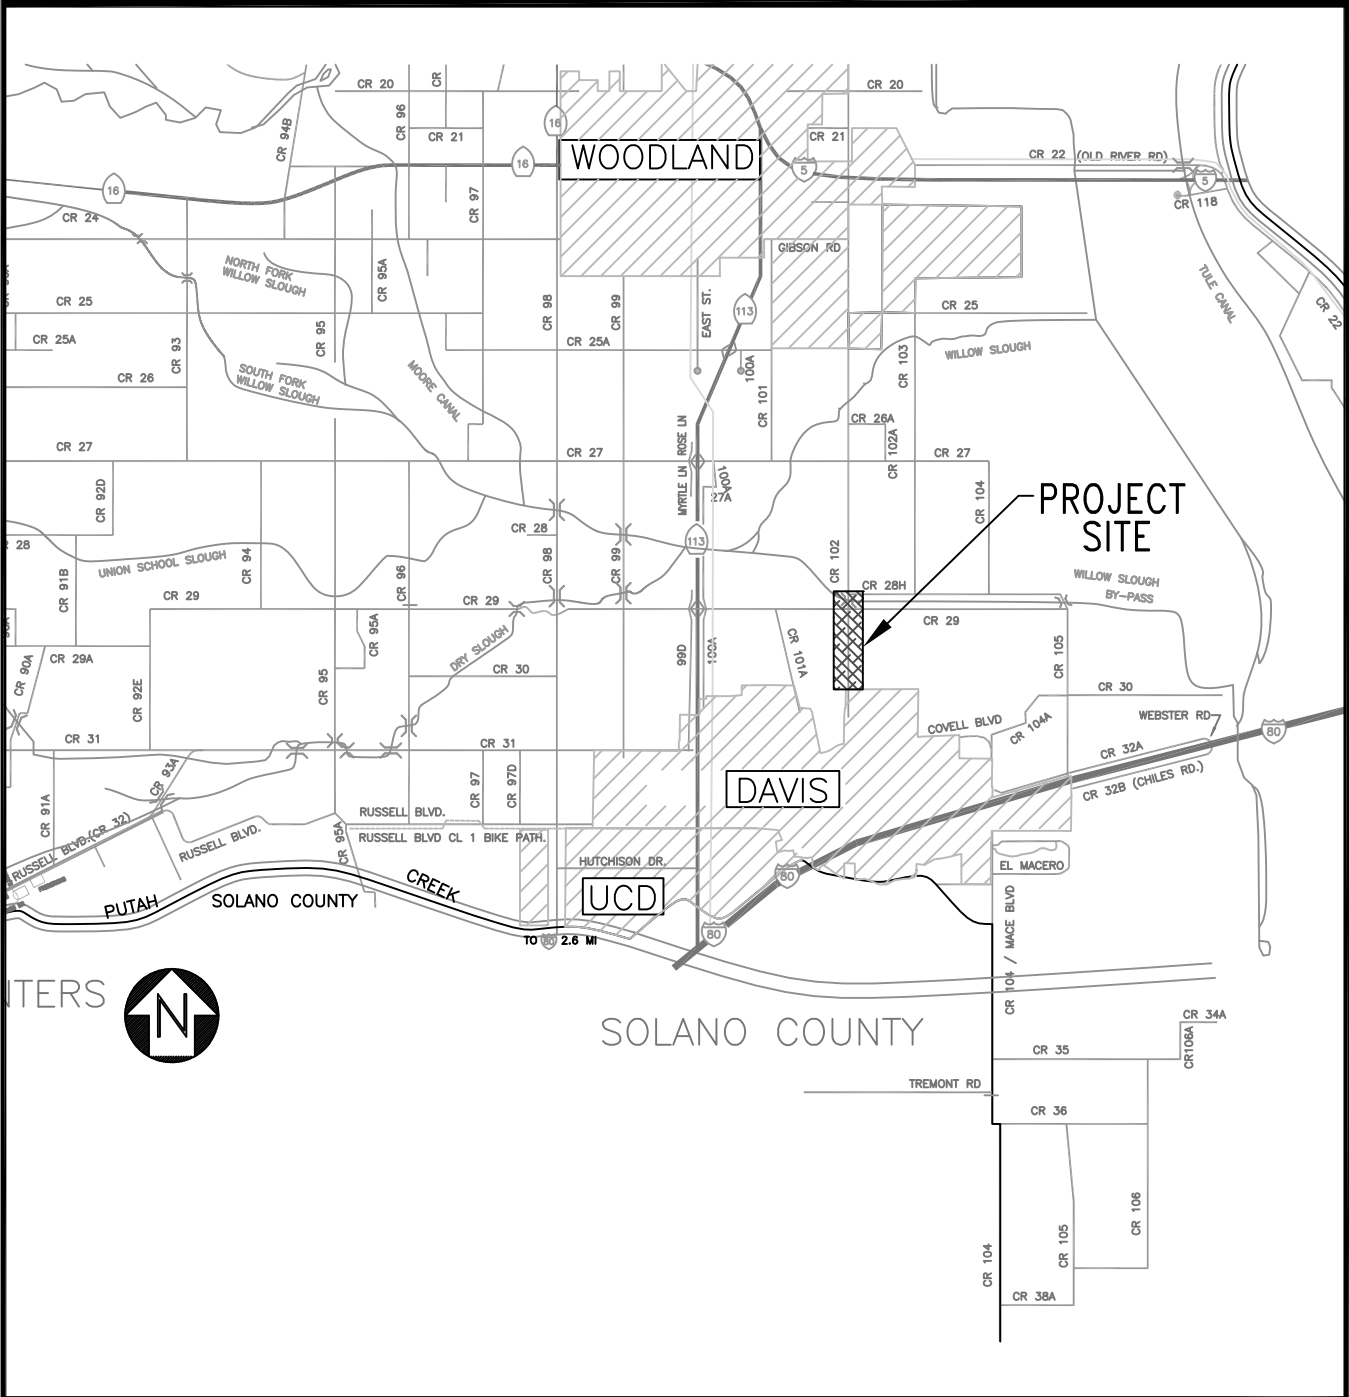


DESCRIPTION OF WORK: Preliminary Engineering, Environmental, and Construction Phases.

NOTES: State HSIP Funds and County Road Funds.

# ROAD FUND PROJECT SITE MAPS

PROJECT: 2h

ROAD NO. OR NAME: Safe Streets 4 All Grant, County Safety Action Plan

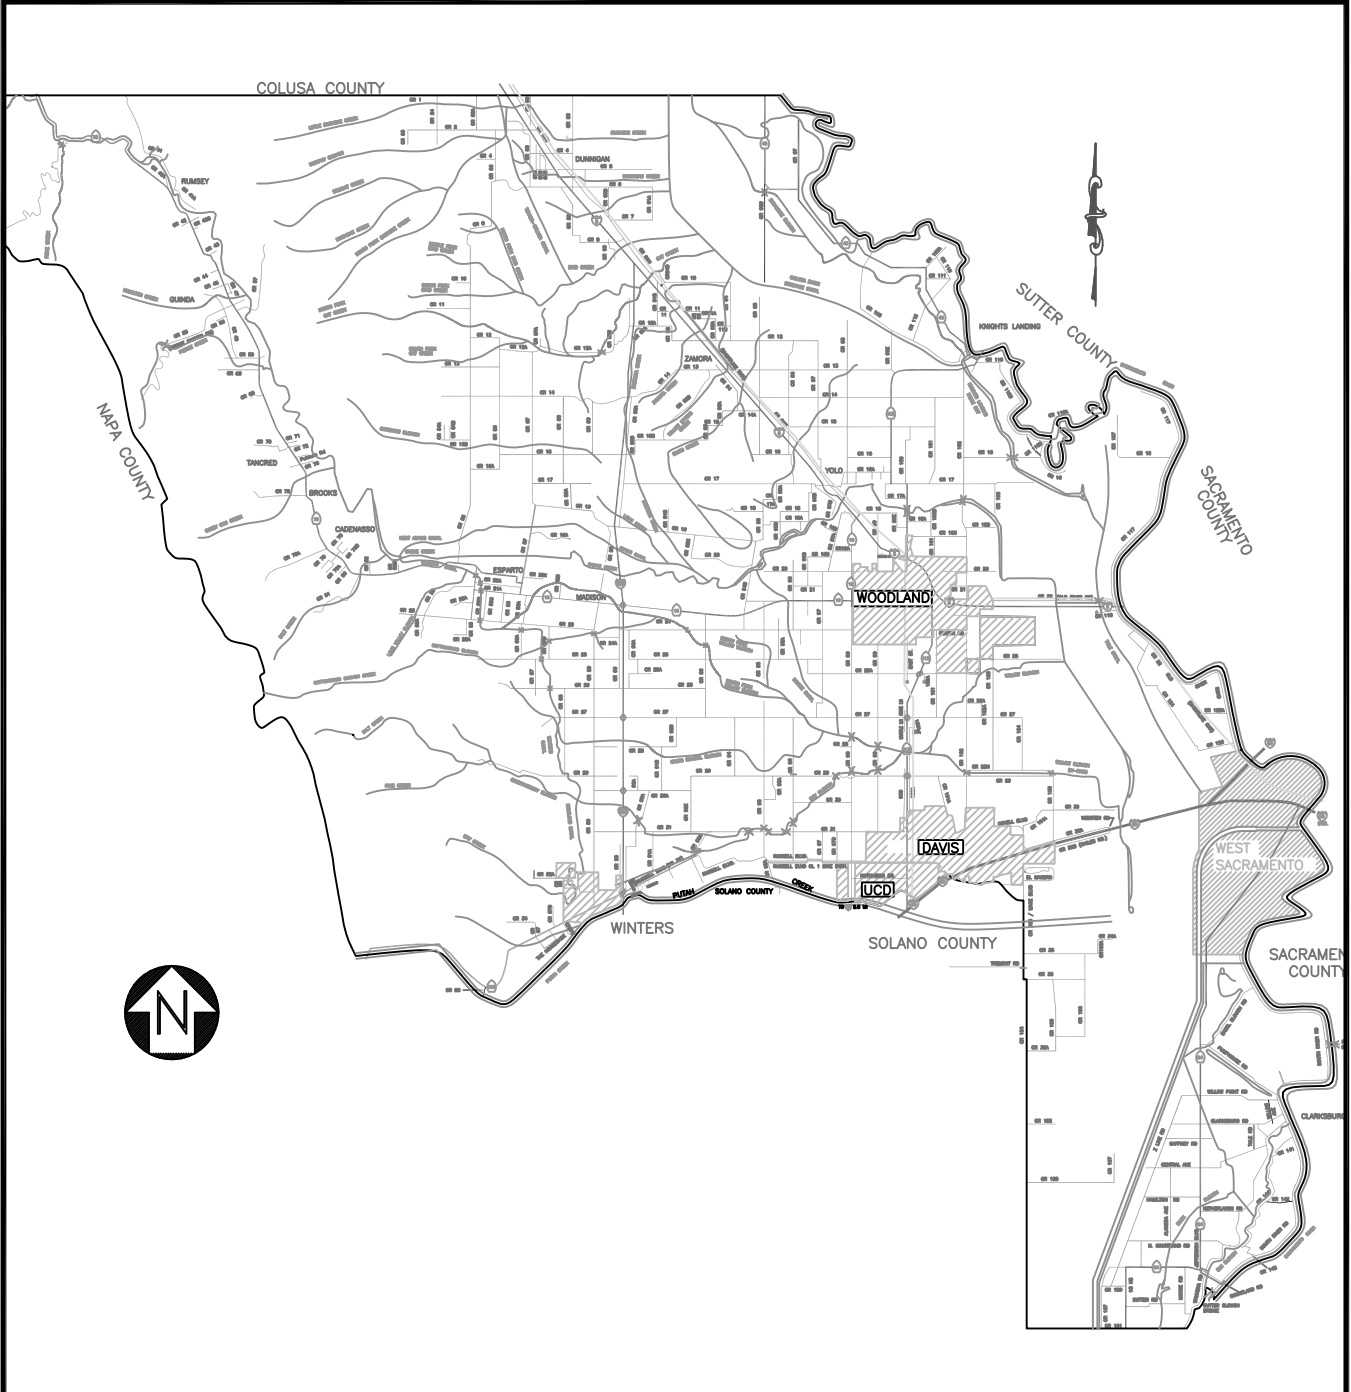


DESCRIPTION OF WORK: Develop Countywide Safety Action Plan.

NOTES: Federal Funds and County Road Funds.

# ROAD FUND PROJECT SITE MAPS

PROJECT: 2i

ROAD NO. OR NAME: East Esparto Sidewalk Study and Design

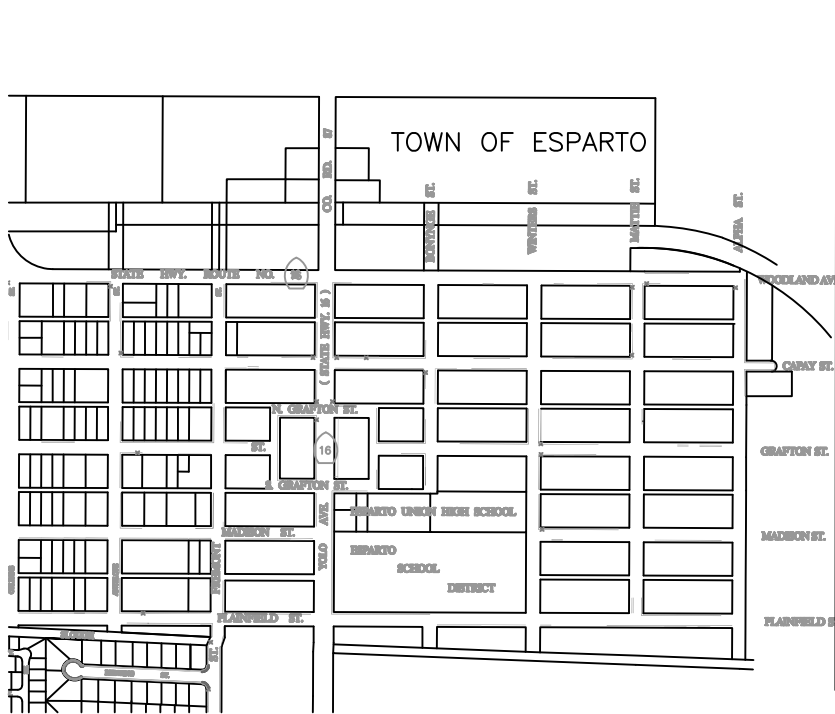

DESCRIPTION OF WORK: Predesign Engineering Study.


NOTES: Federal Funds and County Road Funds.



# ROAD FUND PROJECT SITE MAPS

PROJECT: 2k

ROAD NO. OR NAME: Bridge Preventive Maintenance Project 1

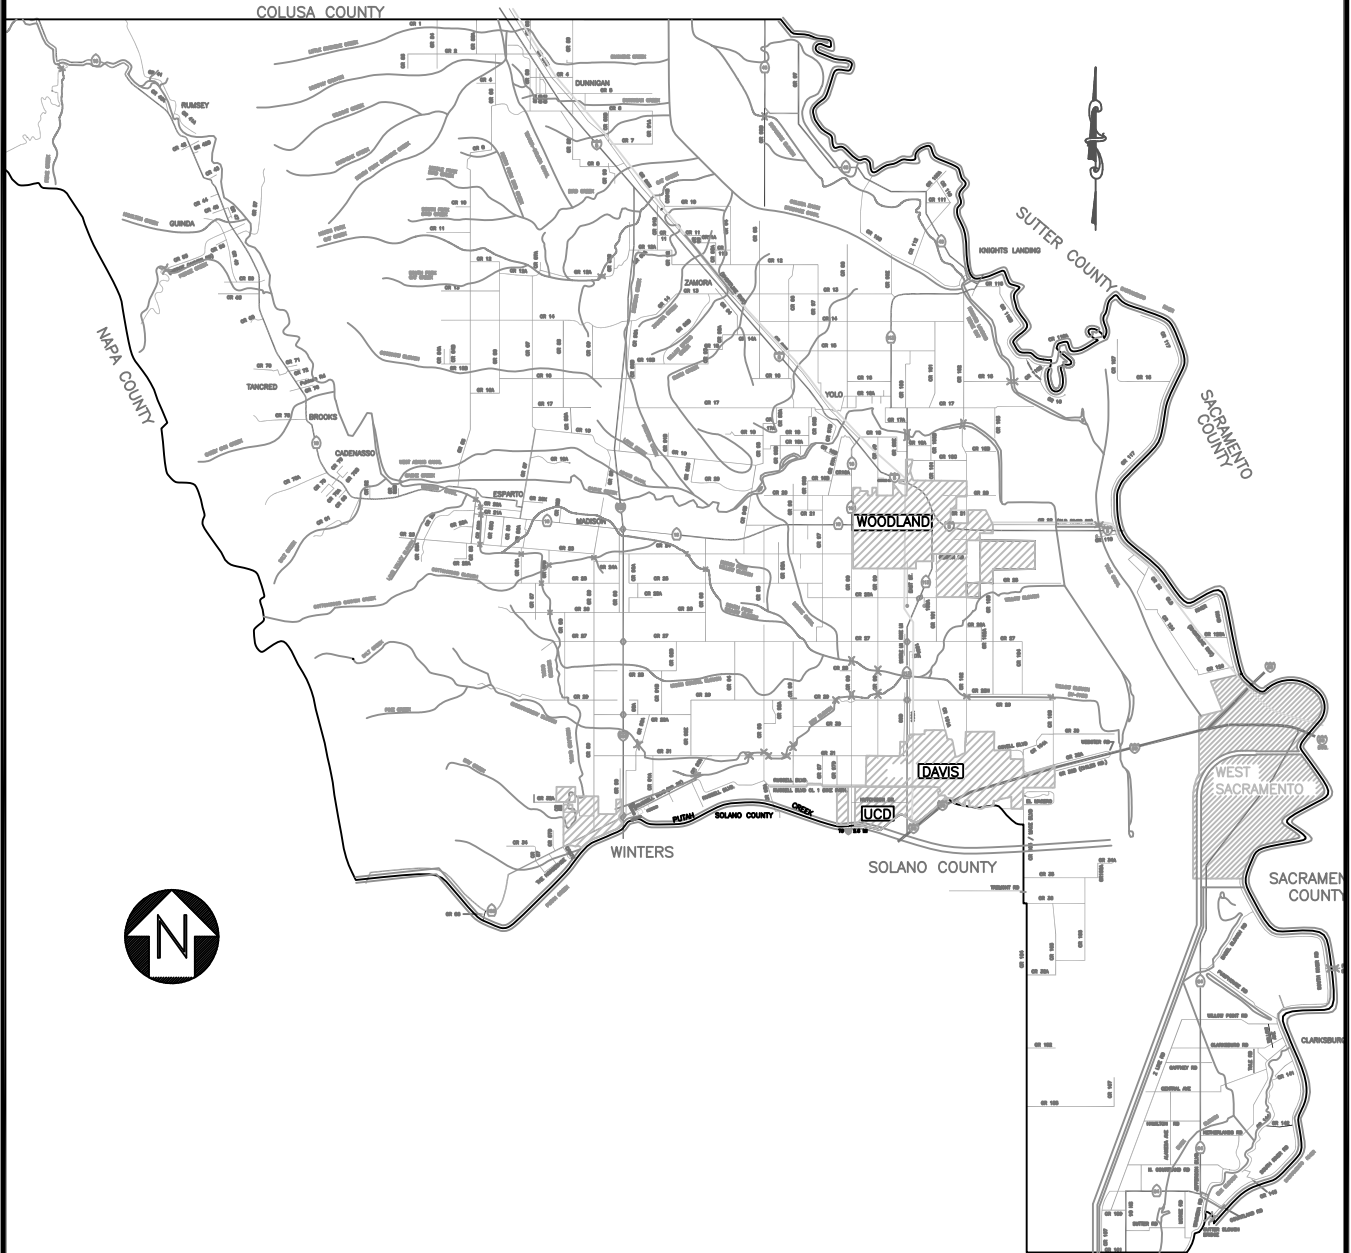


DESCRIPTION OF WORK: Bridge Preventive Maintenance on Several Bridges along various County Roads (Phase 1); Preliminary Engineering, Environmental, and Construction Phases.

NOTES: County Road Funds.

# ROAD FUND PROJECT SITE MAPS

## PROJECT: 21

ROAD NO. OR NAME: Clarksburg Branch Line Extension Project

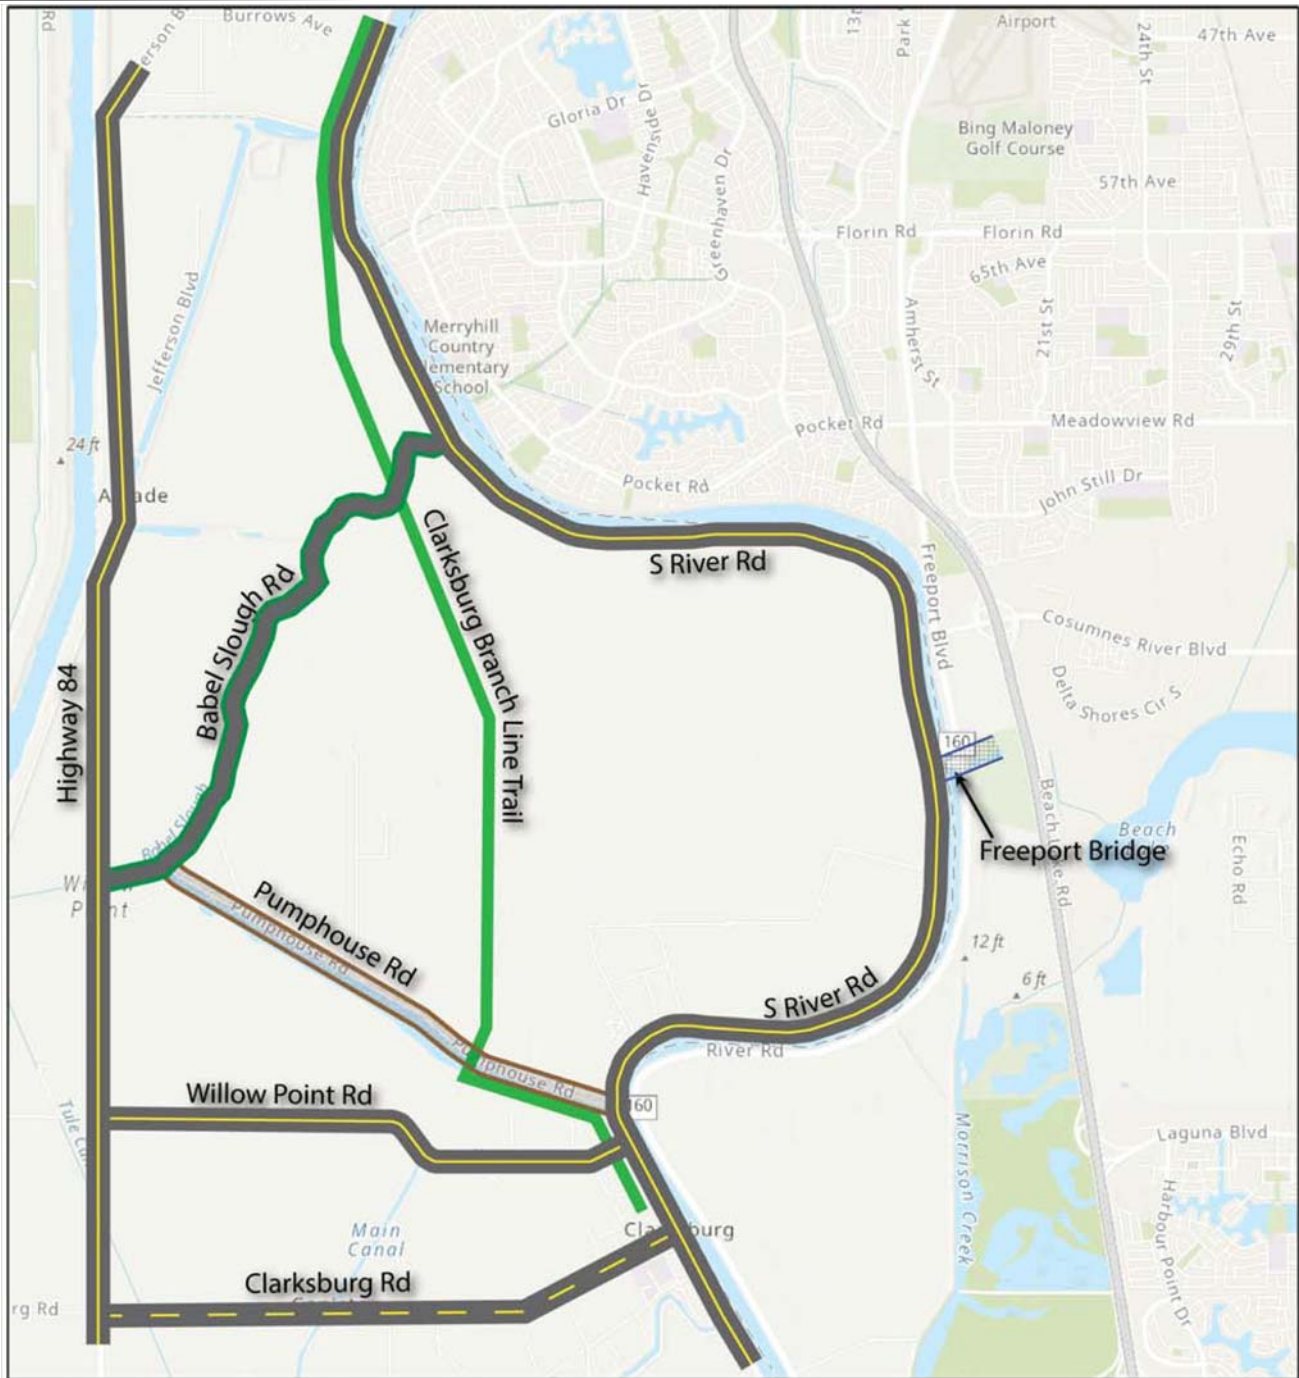


DESCRIPTION OF WORK: Preliminary Engineering, Environmental, and Right of Way Phases.

NOTES: County Road Funds.

# ROAD FUND PROJECT SITE MAPS

PROJECT: 2m

ROAD NO. OR NAME: Yolo County Public Works Yard Pavement Rehabilitation Project

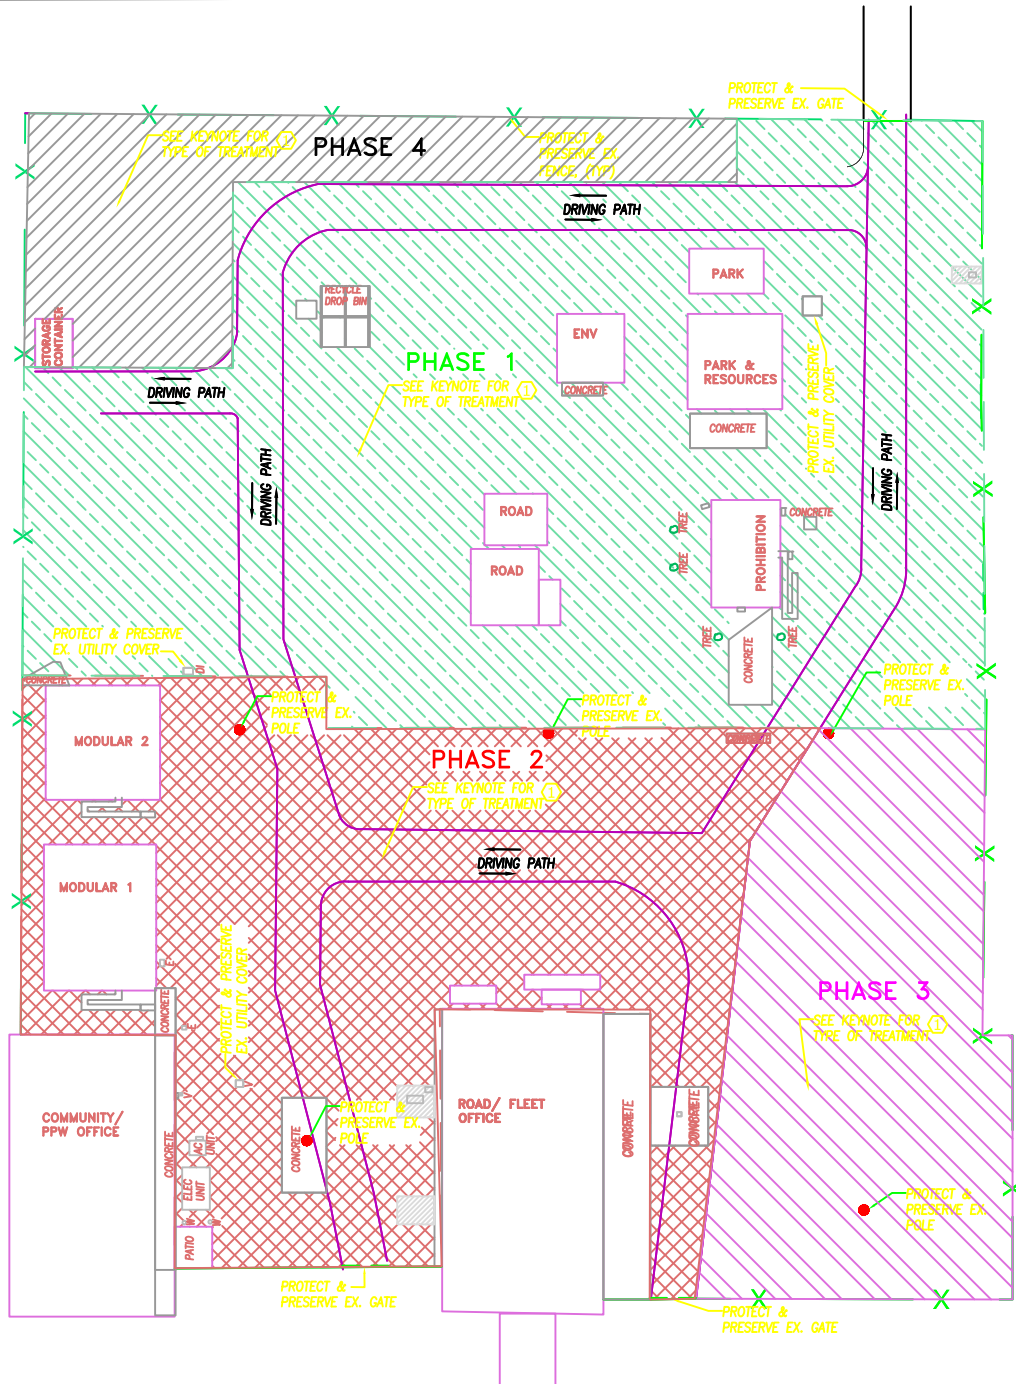


DESCRIPTION OF WORK: Preliminary Engineering and Construction Phases.

NOTES: County Road Funds.

# ROAD FUND PROJECT SITE MAPS

PROJECT: 2n

ROAD NO. OR NAME: Bridge Protective Maintenance Project 2

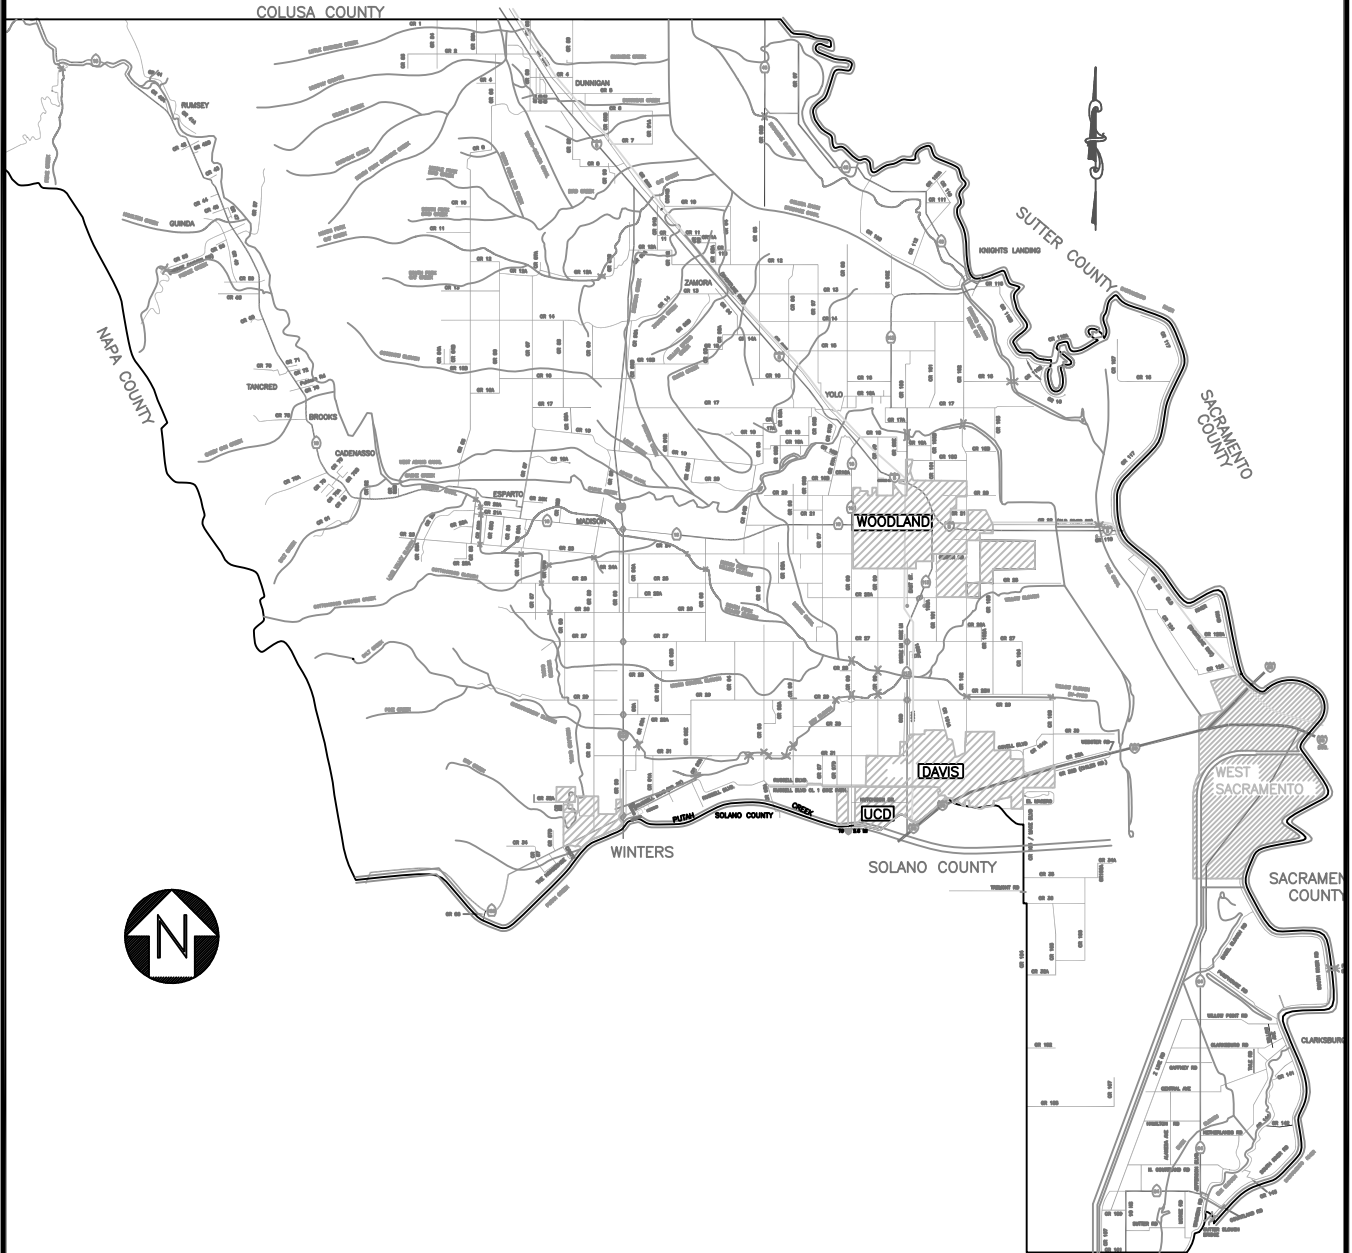


DESCRIPTION OF WORK: Bridge Preventive Maintenance on Several Bridges along various County Roads (Phase 2); Preliminary Engineering, Environmental, and Construction Phases.

NOTES: County Road Funds.

# ROAD FUND PROJECT SITE MAPS

PROJECT: 2o

ROAD NO. OR NAME: 2026 Pavement Preservation Project

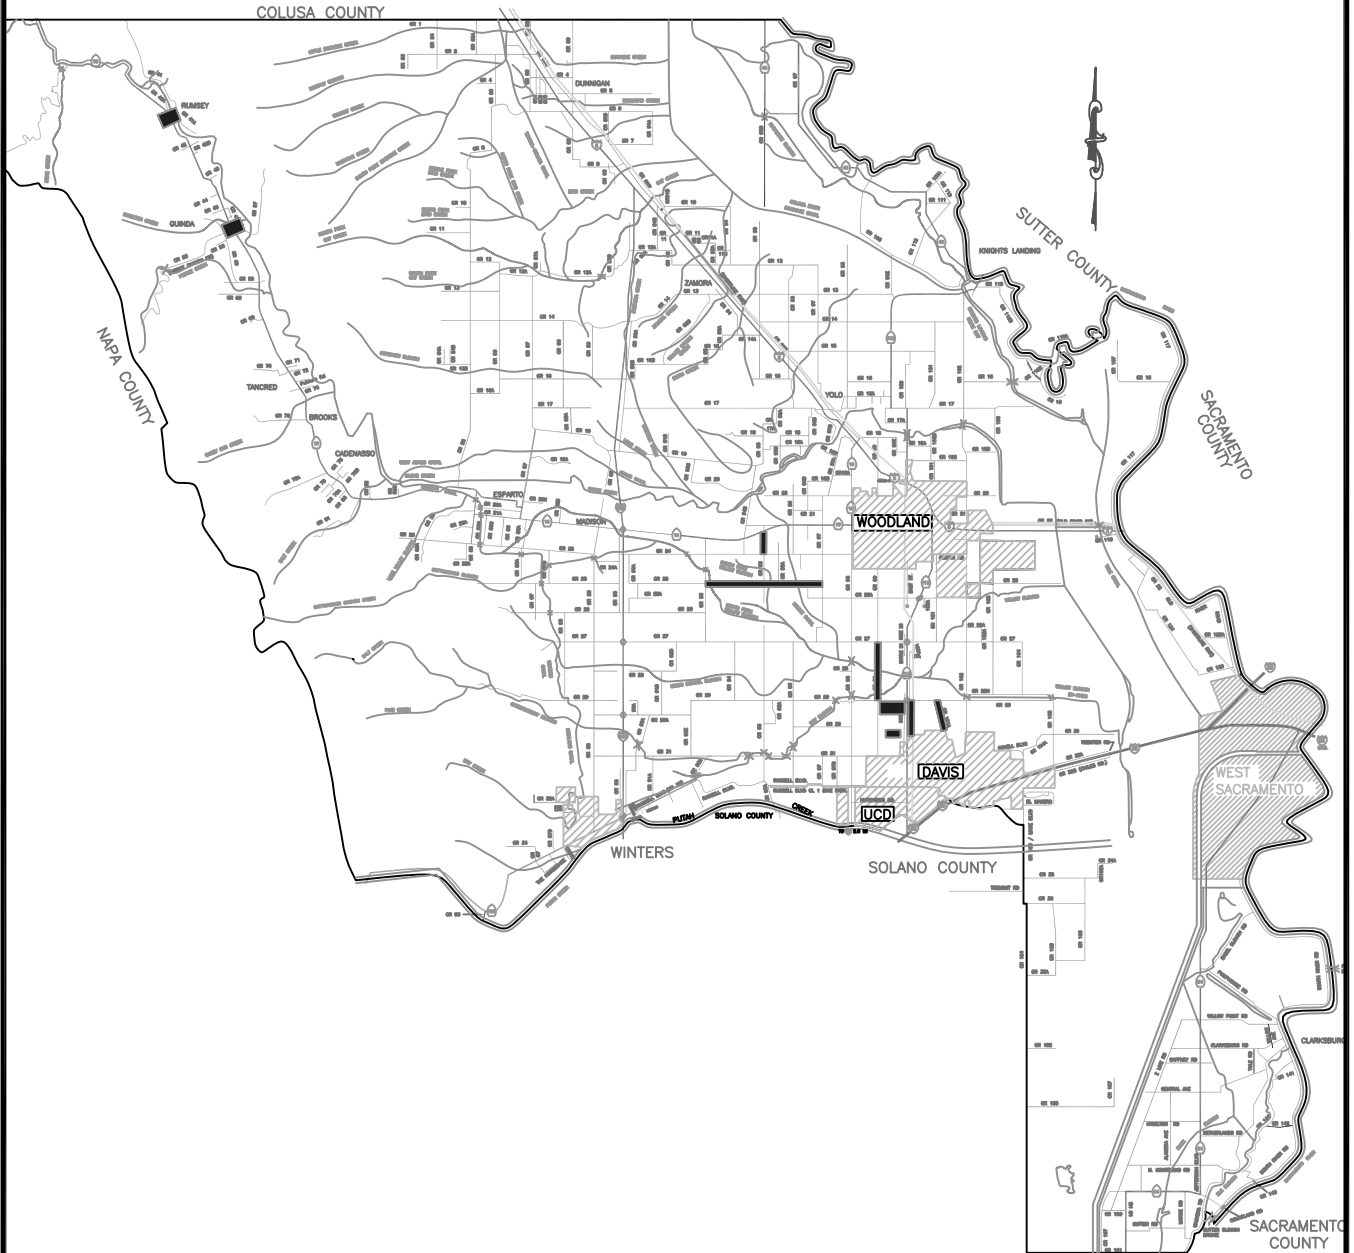


DESCRIPTION OF WORK: Pavement treatments on various County Roads; Preliminary Engineering, Environmental, and Construction Phases.

NOTES: SB1 Road Maintenance & Rehabilitation Account Funds.

# ROAD FUND PROJECT SITE MAPS

PROJECT: 2p

ROAD NO. OR NAME: Road Slope Stability Project

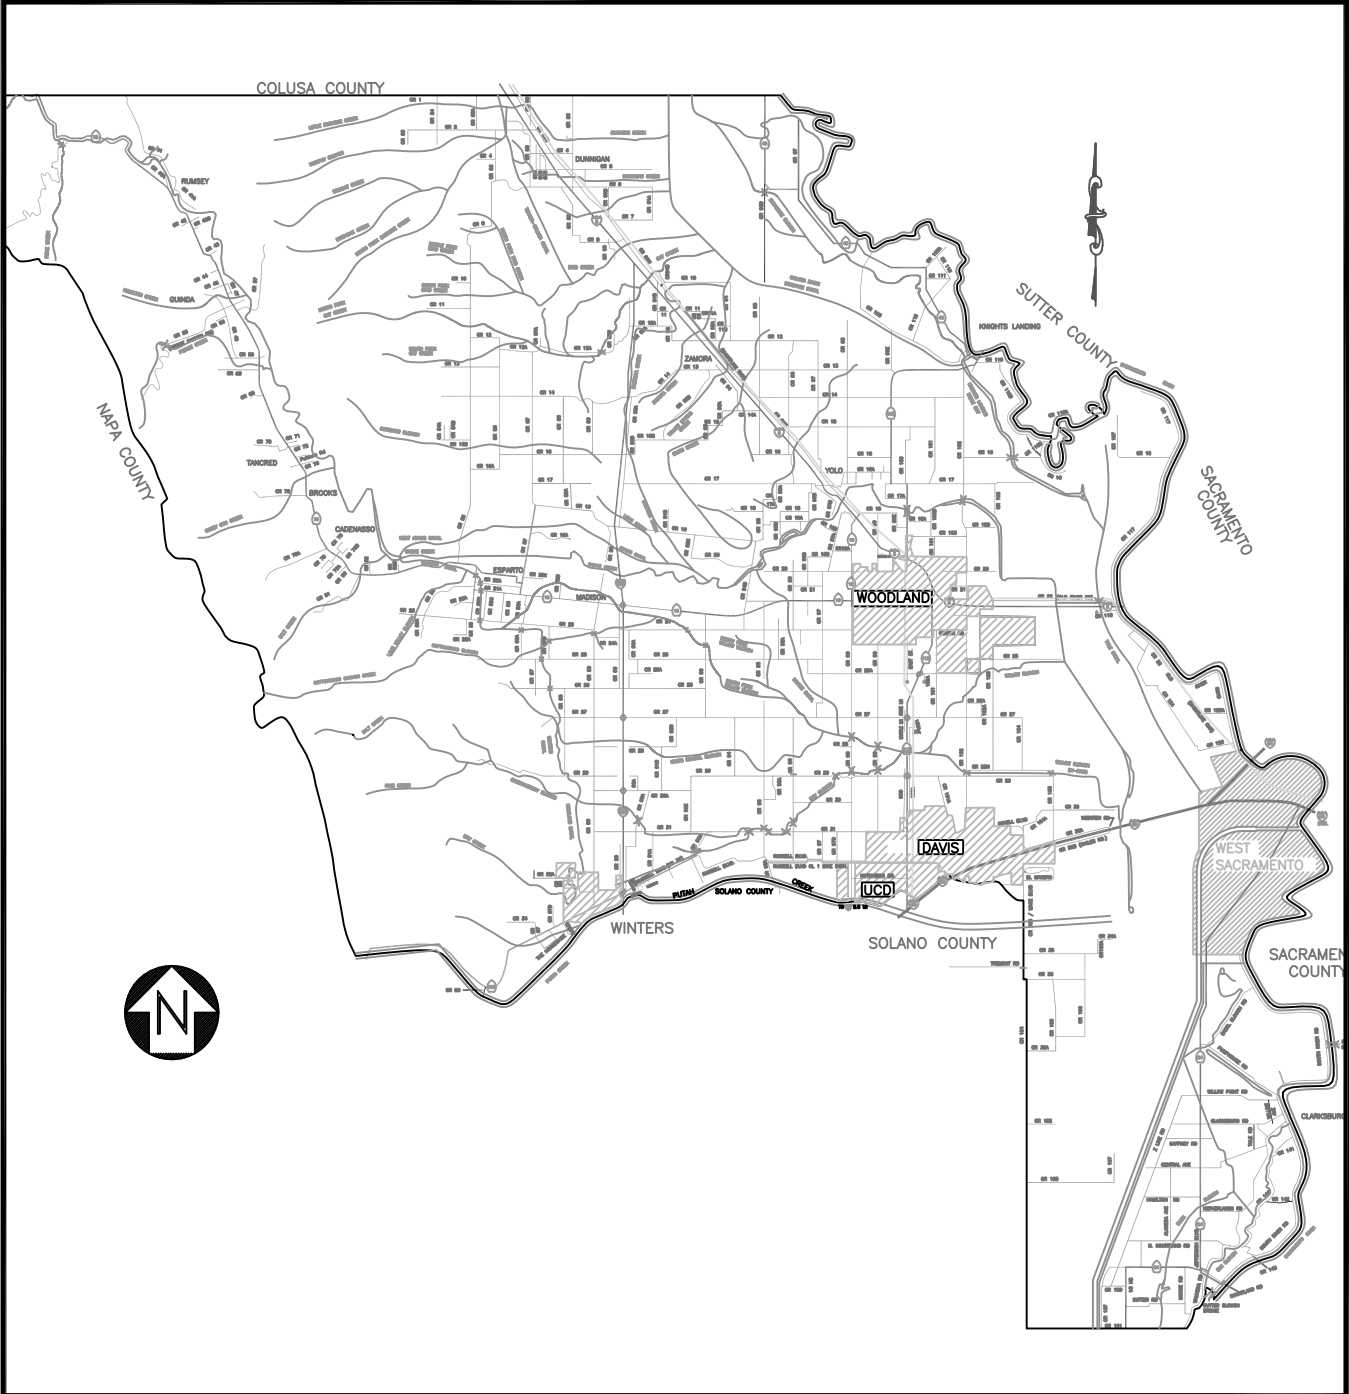


DESCRIPTION OF WORK: Road slope stability along various County Roads; Preliminary Engineering, Environmental, and Construction Phases.

NOTES: County Road Funds.

# ROAD FUND PROJECT SITE MAPS

PROJECT: 2q

ROAD NO. OR NAME: CUPCCAA Striping contract(s)

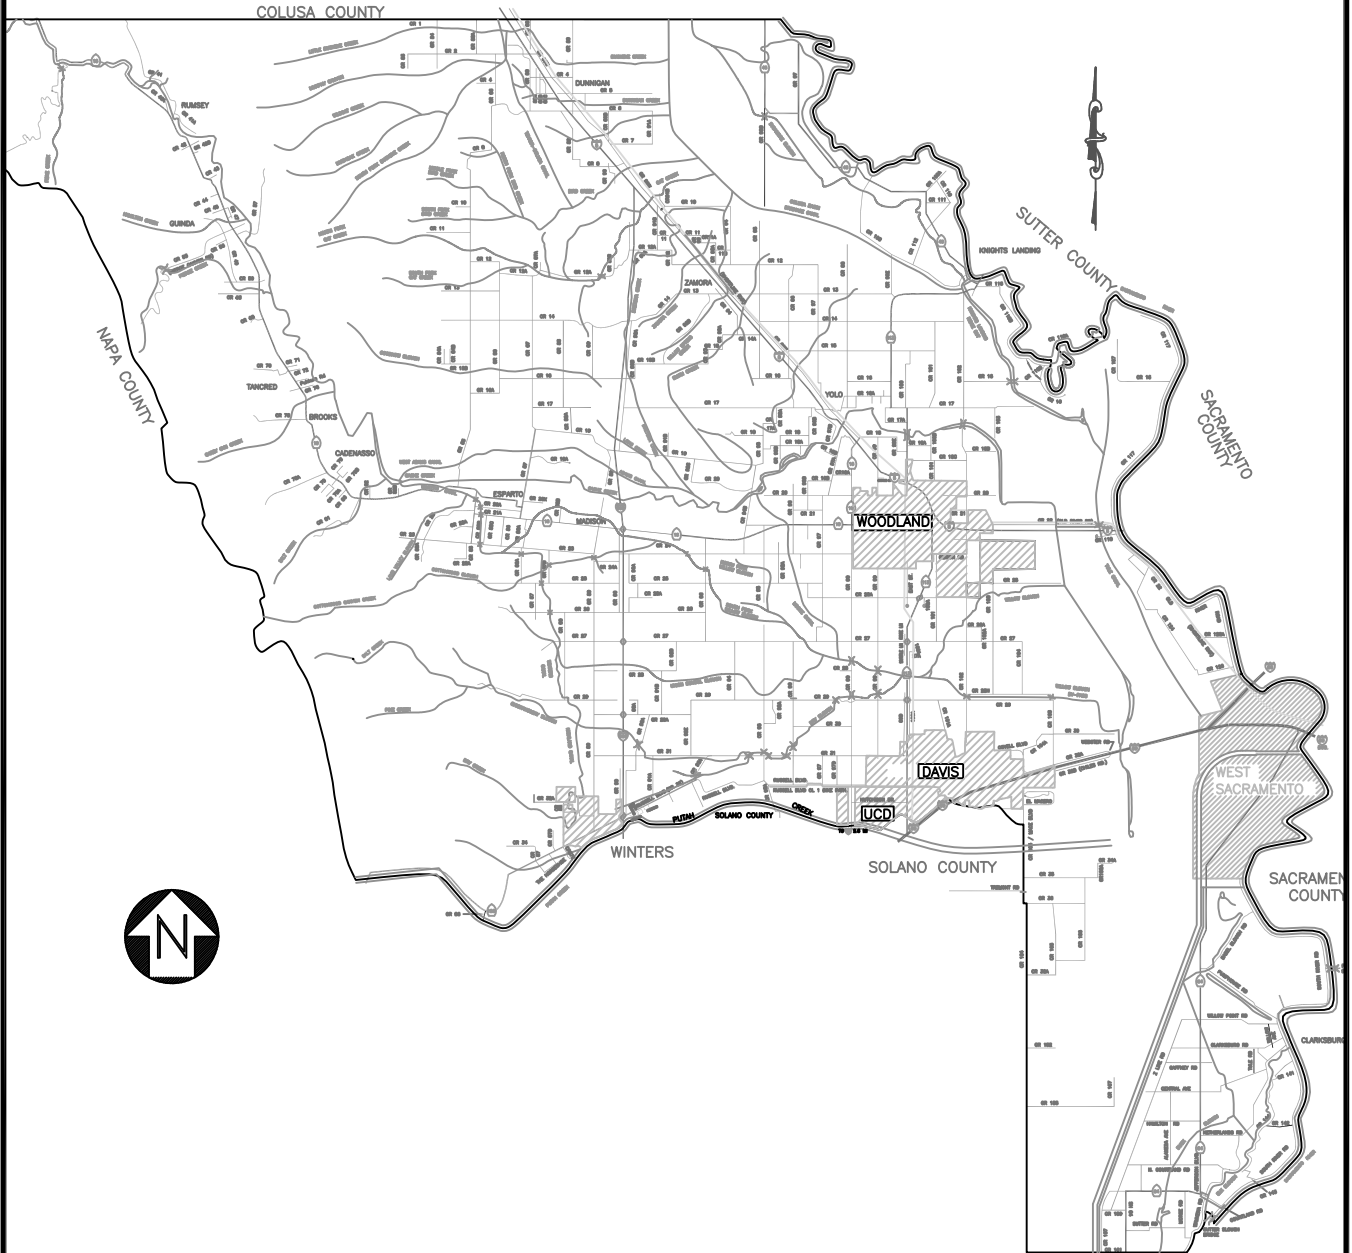


DESCRIPTION OF WORK: Road Striping various County Roads; Preliminary Engineering, Environmental, and Construction Phases.

NOTES: County Road Funds.

# ROAD FUND PROJECT SITE MAPS

PROJECT: 2r

ROAD NO. OR NAME: CUPCCAA Chip Seal Contract(s)

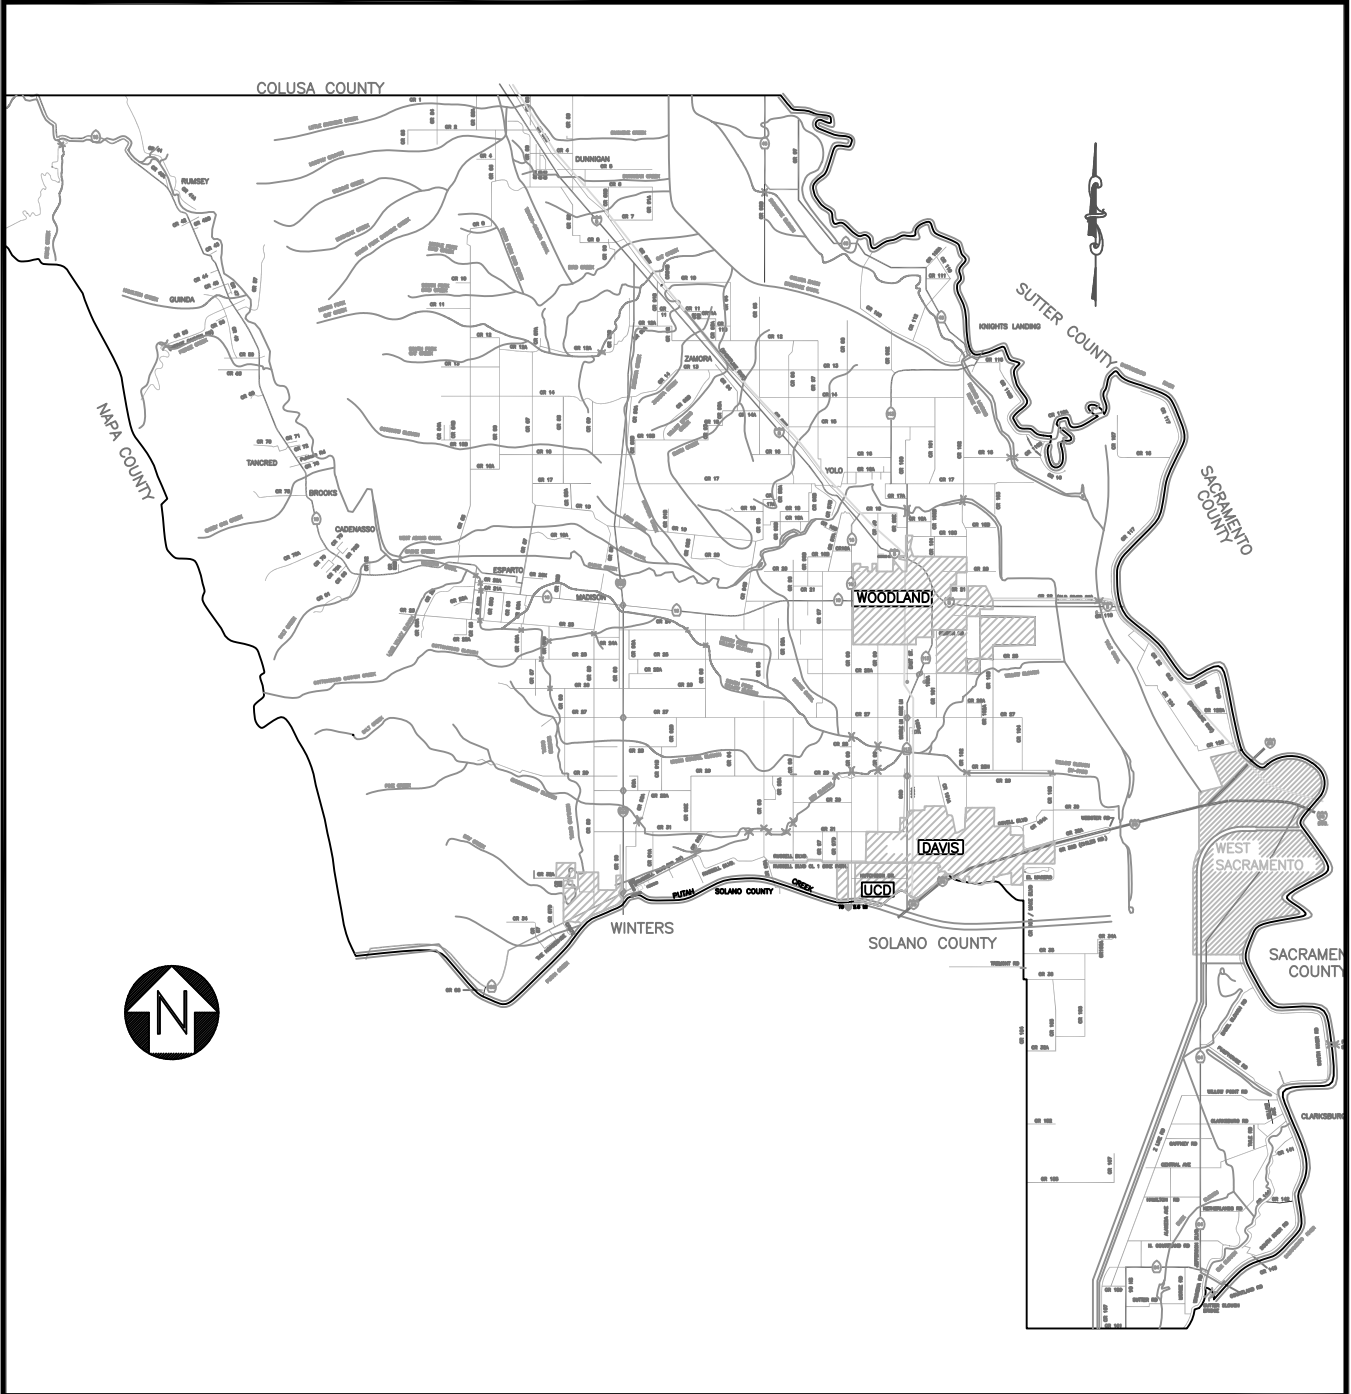

DESCRIPTION OF WORK: Chip sealing various County Roads; Preliminary Engineering, Environmental, and Construction Phases.

NOTES: County Road Funds.
