

Fourth St. / I-40 Bridge Replacement Update

June 4, 2019





Current Status

3 Possible Construction Scenarios





1. Two Construction Seasons
2. 2-4 Month Closure
3. Bridge Slide: 2-3 week closure



Fourth St. / I-40 Bridge Replacement



Bridge Slide Phasing

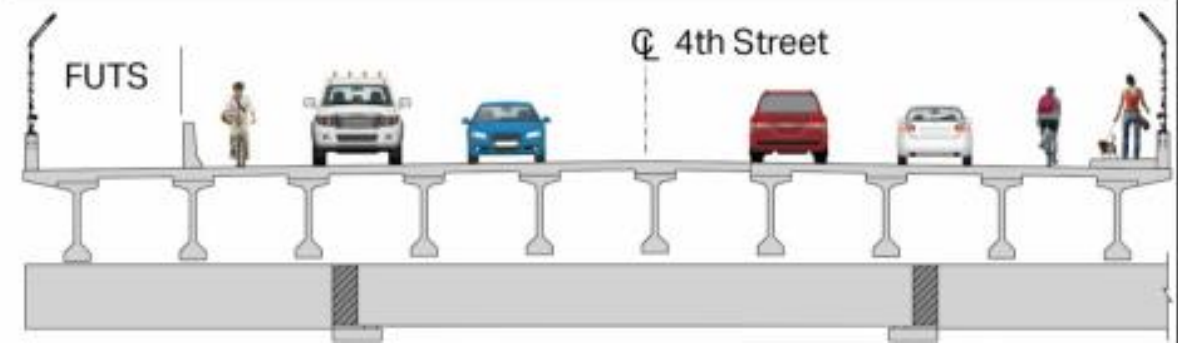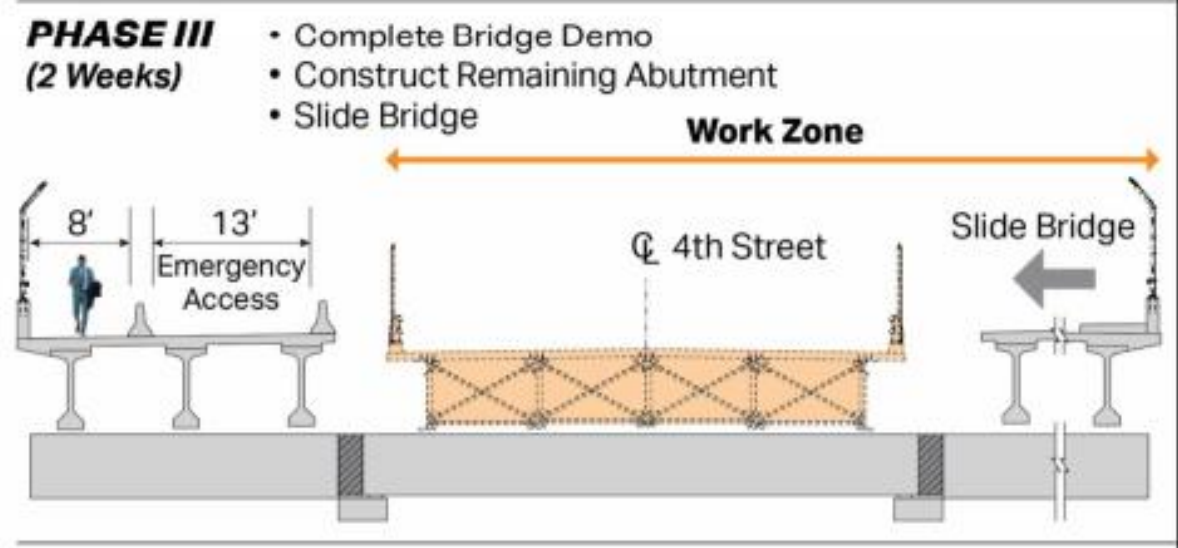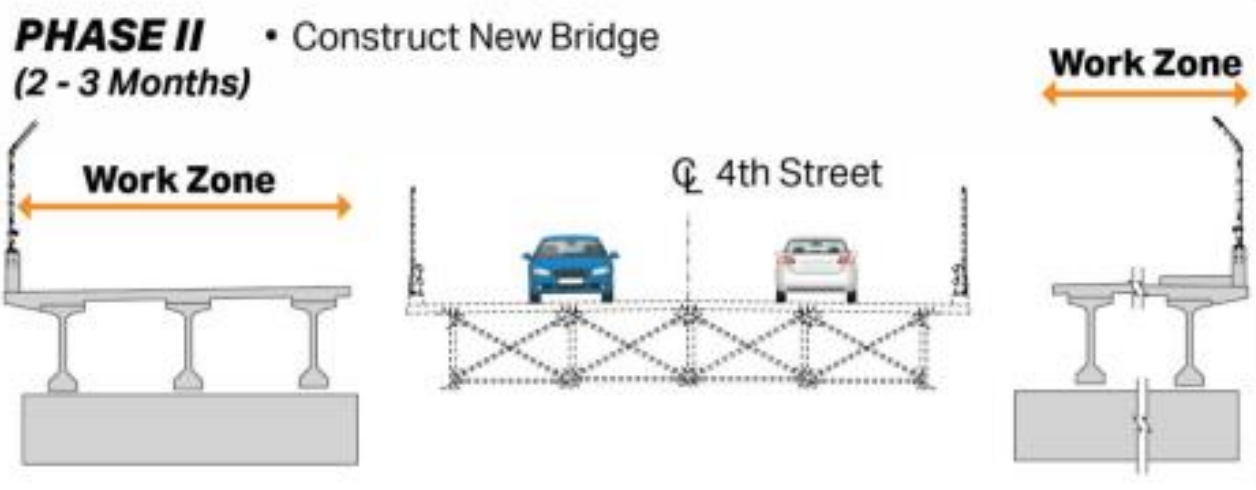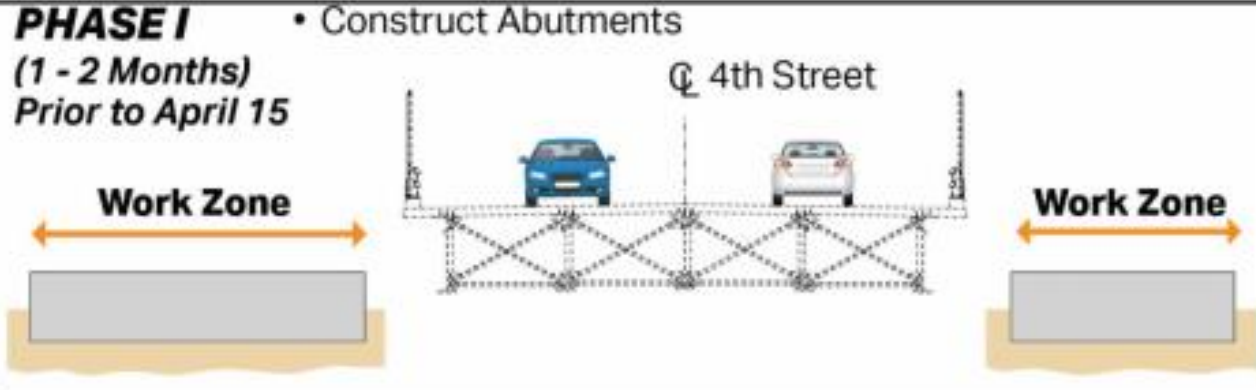



Fourth St. / I-40 Bridge Replacement

Budget Update

- Initial budget estimate:
 - \$10.2 million & 50/50 cost share with ADOT
 - Current budget estimate: \$12.0 million for Bridge Slide & 50/50 cost share with ADOT
 - Other options are in \$11.6-\$11.7 million range
- IGA to be updated this Fall to reflect new budget estimate and items for which the City will bear the entire cost
 - *i.e.* Additional Aesthetics, Retaining Walls and City IT Conduit



Fourth St. / I-40 Bridge Replacement

Public Information Meeting

- Public information meeting anticipated in mid-July
 - Specific date and details pending
 - Meeting to be conducted by ADOT and AECOM (Consultant)
 - City Staff will be available



Questions?
