

# *FDOT Project Update*

*441714-1: Drainage Improvements for US-1*


*441715-1: Outfall for Virginia Avenue*

*March 28, 2023*

# Project Overview

- FPID 441714-1-52-01 : Drainage Improvements for US-1
  - Improve chronic flooding issues along US-1 (SR 5) between Edwards Road and Tennessee Avenue.
    - Replace and supplement existing drainage system along US-1.
    - Dredge and replace side drains along the Savannah Road outfall ditch.
  - Project includes Resurfacing, Restoration and Rehabilitation (RRR) upgrades.
- FPID 441715-1-52-01 : Outfall for Virginia Avenue
  - Improve chronic flooding issues along Virginia Avenue (SR 70) from Oleander Blvd to US-1, caused by high peak water stages in the Mayflower Canal.
    - Fix adverse grading of the Mayflower Canal.
    - Interconnect the Mayflower and Virginia Ave Outfall canals with a proposed pipe along Gardenia Avenue.
    - Construct an outfall to Sand Mine Lake, along Indian Hills Drive.

# Project Layout

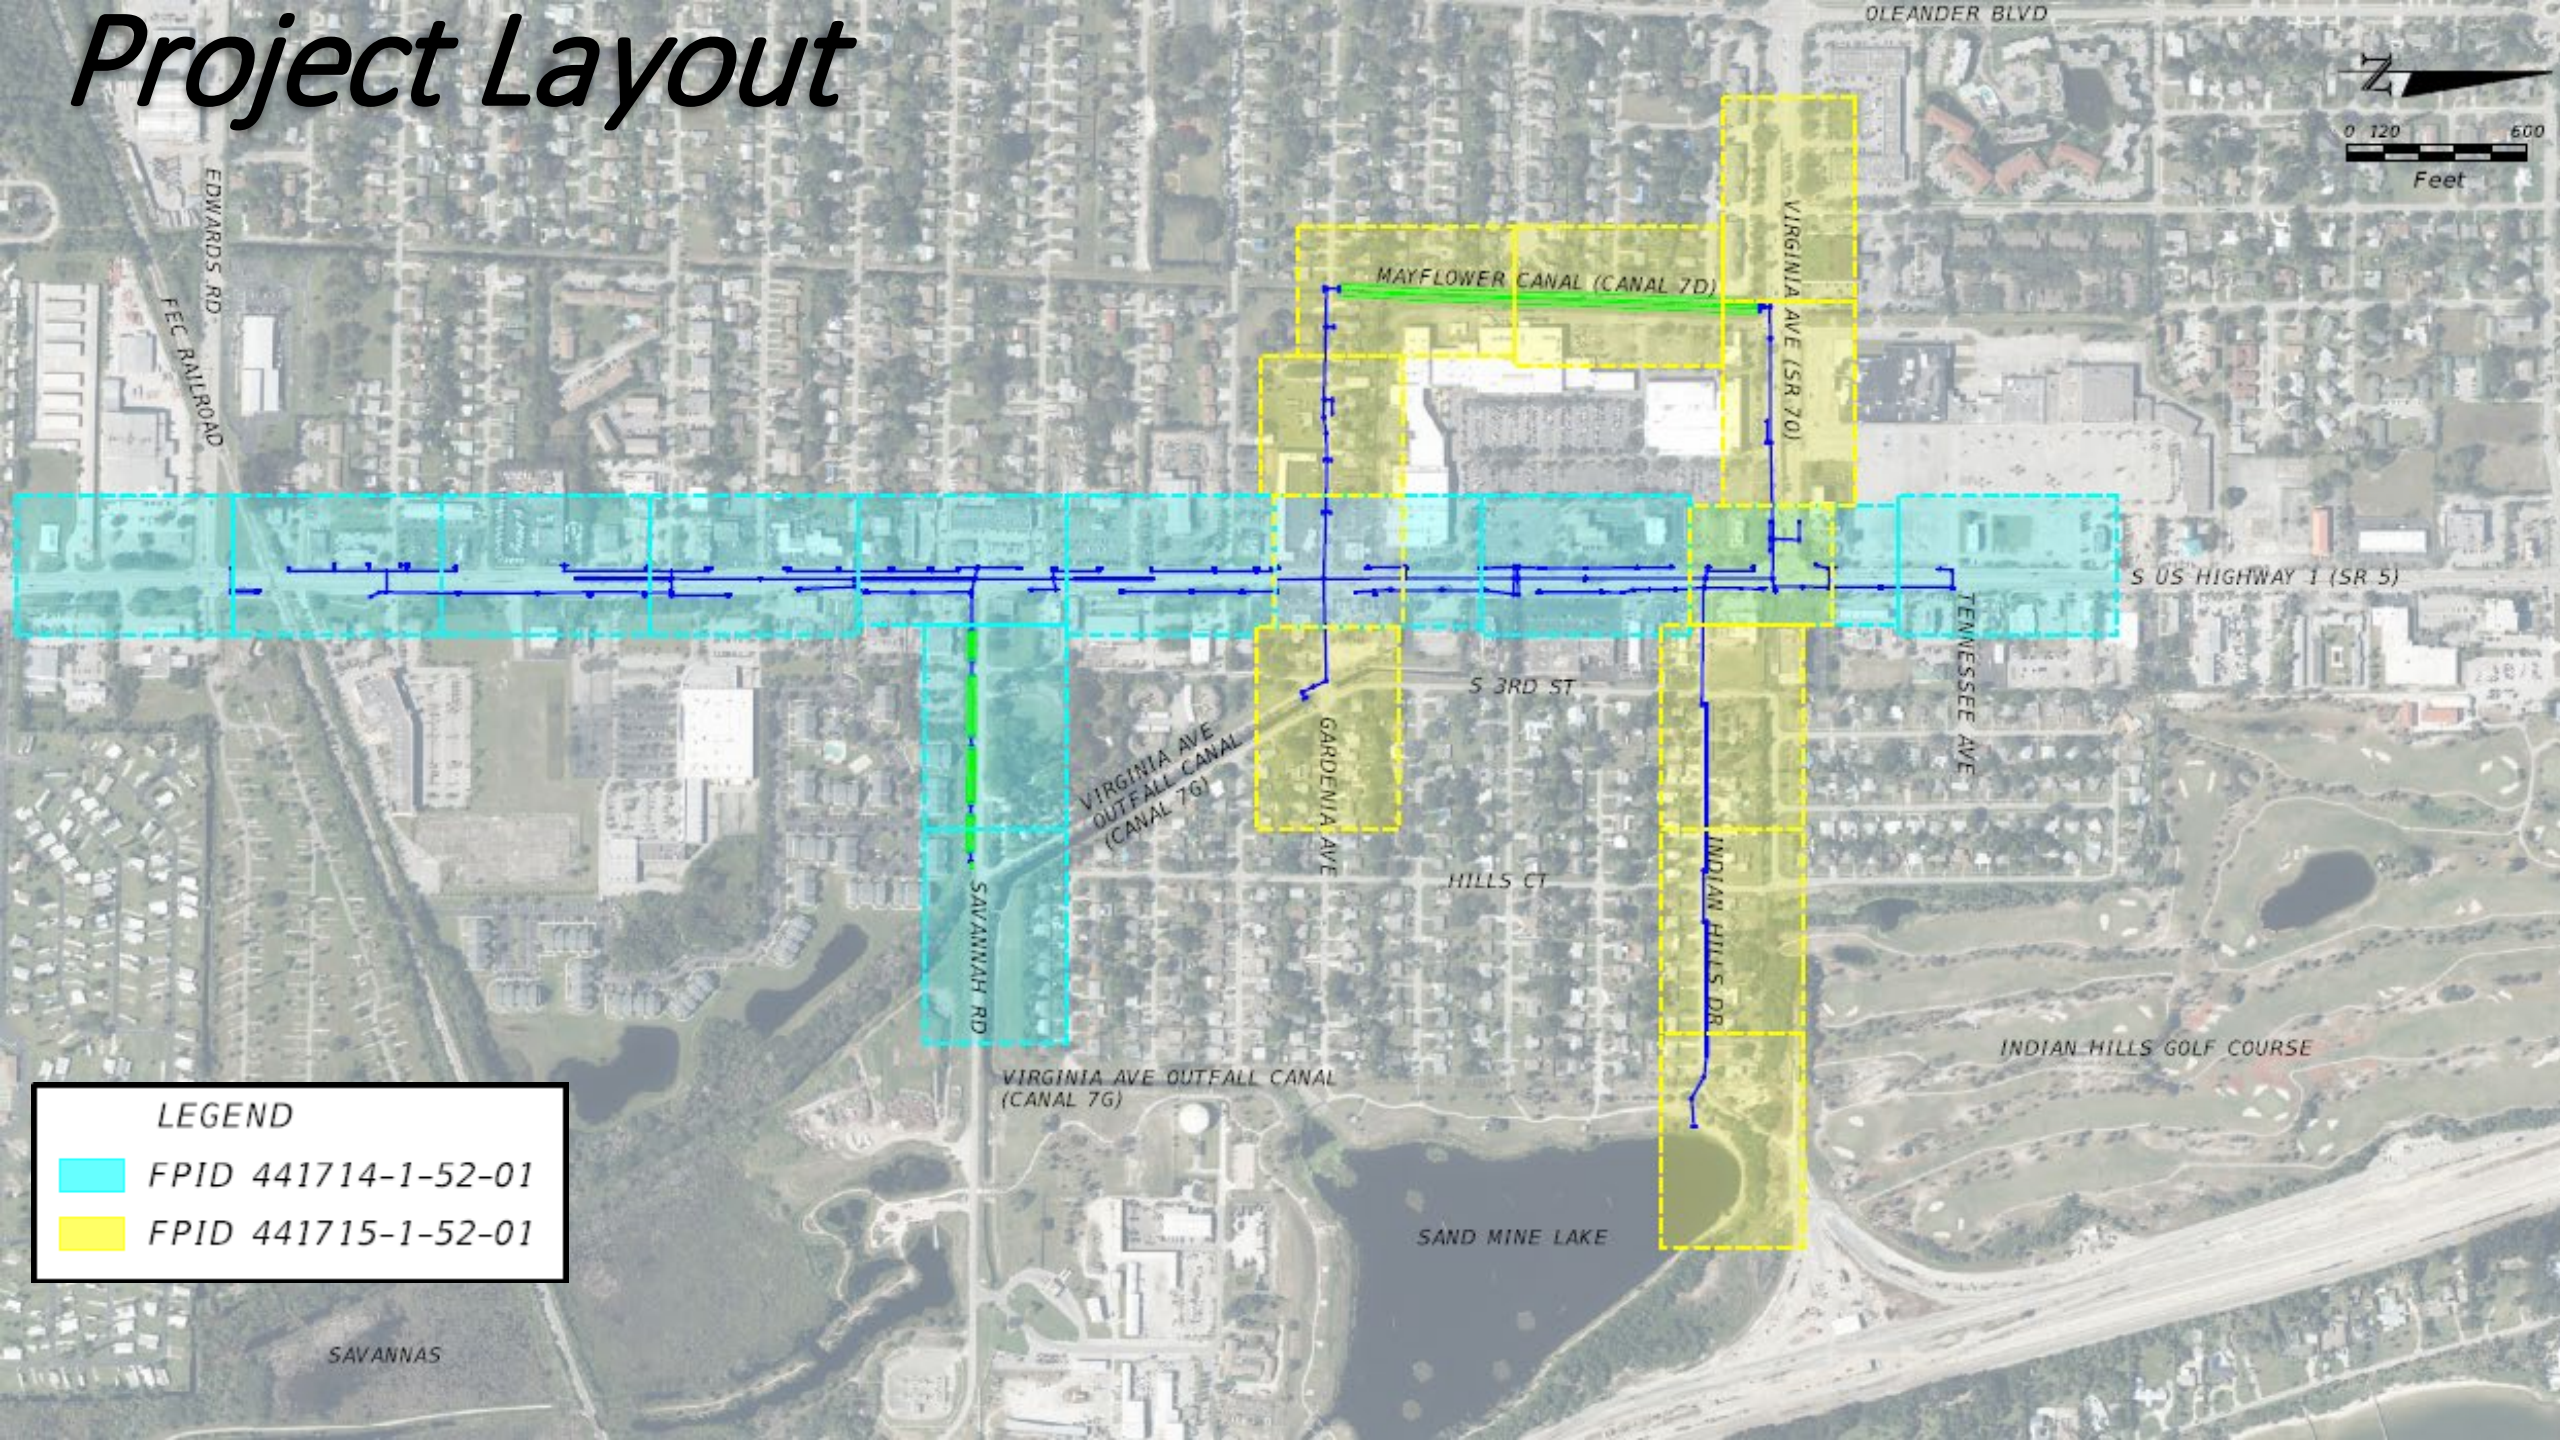

**LEGEND**

- FPID 441714-1-52-01
- FPID 441715-1-52-01

SAVANNAS

# Design Schedule

- 60% Plans – COMPLETE (*May 2022*)
- 90% Plans – August 2024 (*may be submitted early*)
- 100% Plans – December 2024
- Let for Construction – July 2026
- Construction NTP – November 2026
