



Project Update

February 1, 2016



Dakota Meadows Middle School





Bridges Community School

Contractor - 98% Complete

District - 40% Complete

On target to open in the Fall of 2016





Bridges Community School





Bridges Community School





Prairie Winds Middle School

- Project on Schedule
- Furniture order
- Equipment needs


Insert clear exterior picture

Exterior Finishes



Prairie Winds Middle School

Interior work

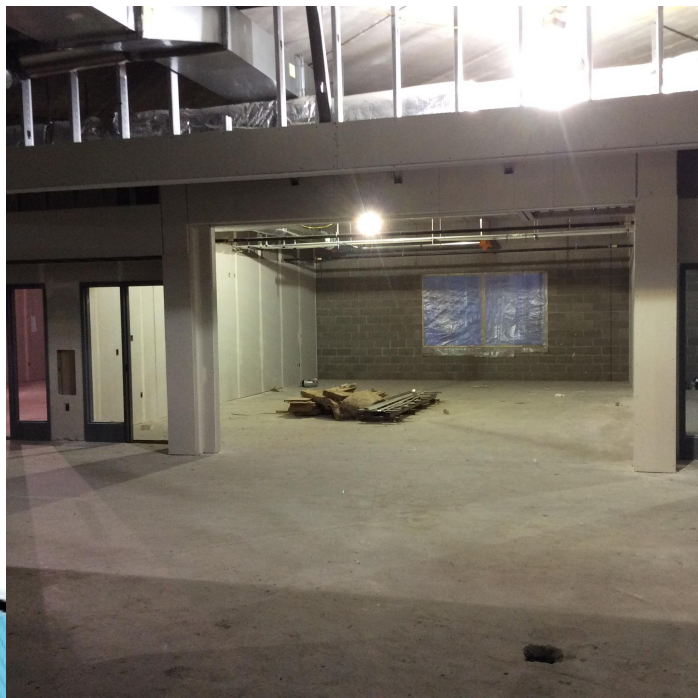



East High School

- Design Phase - Renovation to Academic Area
- Developing Construction Phase Schedule
- Bids in late February/ early March
 - Potential Alternates to project
 - Addition to Planetarium
 - Addition of Community/Team Locker rooms and spectator seating
 - Office Renovations
- Project to begin June of 2016
- Completion August 2017
