COST ITEMIZATION

000	NO
PCO	NU.

32

PROJECT:

Williamson County Sheriff's Office Training Center



CONSTR. MGR.:

American Constructors, Inc.

DOCUMENT NAME:

RFI 052

DATE:

09/08/17

\$2,825.00

SUBJECT:

RFI 052 Duct in Room 141

Funding Source CM Contingency Extended Calendar Days Requested: 3 Rain Days

ITEMIZED COST BREAKDOWN DESCRIPTION--Use Separate line for each item Sub Name Work Description FIRM ESTIMATED TOTAL AirCraft RFI 052 Duct in Room 141 \$2,825.00 \$2,825.00 ** Quote backup for sub pricing is attached***

Note:

The cost proposal as shown above is only inclusive of the cost of the work for this change proposal. If unforeseen conditions are encountered these costs may be revised and re-submitted. The Construction Manager's cost of bonds, insurance, and fee will be included at the rate stipulated in the contract in the final reconciliation and/or owner change order.

This Cost Proposal has no impact on the GMP of \$7,994,640.00.

David A. Achterberg CN

Brinkley Sargent Wiginton Architects

Date

Total



RFI

WCSOTC

8160 Chandler Road Hutto, Texas 78634 ACI Job #: 899

To:

David Achterberg

Brinkley Sargent Wiginton Architects

RFI #: 052

cc: HCE

Cedar Park, TX 78613

Date Submitted: 08/28/17

Response Requested By: 09/04/17

Subject: Duct in Room 141

Drawing: M211

Spec Section:

Schedule Impact: TBD

Request:

The ductwork over room 141 is shown to be 28"x18" Square wrapped with blanket insulation. Room 141 is a cage with the top of the cage at 10'0" above finished floor. This leaves this duct visible.

Please confirm this duct should be changed to spiral duct to starting in room 140 to match the duct in 143.

Dustin Wiegers

American Constructors

Response:

If the Owner and the Architect want this duct to be double walled spiral in this location, 24" round duct is equivalent to 28"x18" duct.

Refer to comments from HCE. Provide an estimate for the work for Owner review. DAA/BSWA 2017-08-30


Answered by

RCD (HCE)

8/30/17

Company

Date

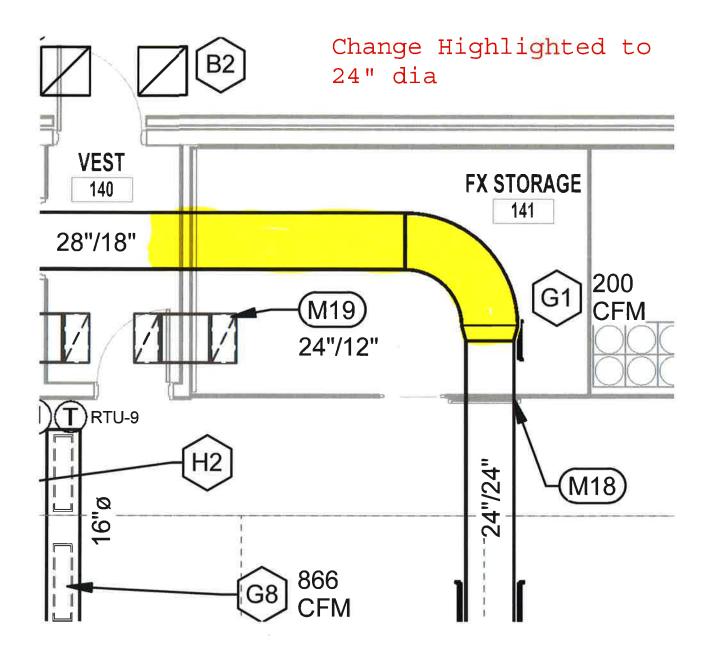

AIR CRAFT, INC.

Air Conditioning, Refrigeration, Heating 1916 Picadilly Drive, Round Rock, Texas 78664 (512) 836-1690 (phone) (512) 836-4988 (fax) TACLA020519C

DATE: 9/7/20 TO: AMERICAN CONSTRUCT ATTENTION: DUSTIN WIECE PHONE: 512-743-7107 FAX: LOCATION: WCSOTC	CTORS		
We propose to furnish and insta LABOR, MATERIALS, A WORK PER RFI 052 IN R	ND SUPERVISION TO	D DEMO AND REINSTALL I 0-2017.	DUCT
Quote Includes: MATERIALS 47% - \$1,35 LABOR 42% - \$1,186.50 P&O 10% - \$282.50 TOTAL - \$2,825.00	56.00 BID AMOUNT:	\$ 2,825.00	
EXCLUSIONS:			
"Regulated by the Texas Depart 78711, (800) 803-9202 or (512) Terms: C.O.D.	-	! Regulation, P.O. Box 12157	, Austin, Texas
APPROVAL:			

DATE:
