

March 12, 2024

Hon. Everardo Villarreal
 Commissioner, Hidalgo County Precinct #3
 724 Breyfogle Rd
 Mission, TX 78574

RE: El Paraiso Project (C-22-0213-09-06)
Work Authorization No. 2 ~ El Paraiso Health Clinic
B2Z Job # 3101B
B2Z Invoice # 30044

Dear Mr. Villarreal,

Attached for your review and approval is our invoice for services under Work Authorization #2 for the month of February 2024 on the subject referenced project.

The following is attached:

- Invoice No. 30044

The following is a narrative of the progress of this period.

| TASK | | |
|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--|--|
| Construction Material Testing | | |
| B2Z secured a sample of Flexbase material for testing on the following item: <ul style="list-style-type: none"> • Moisture/Density Standard Proctor • Atterberg Limits of Soil • Sieve Analysis Reports: EPHC-1S & EPHC-2S | | |
| B2Z prepares test reports in the field and in our office daily/weekly. The test reports are emailed to clients from our in-house laboratory located in Mission, Texas | | |

Should you have any questions regarding this submittal please do not hesitate to call me at (956) 585-3773.

Sincerely,

Oliver F. Salgado, P.E.
 Project Manager

Approved
David Chacon, PE
 03/13/2024



P.O. Box 2724
 McAllen, Tx. 78502
 (956) 585-3773

Invoice

| Date | Invoice # |
|-----------|-----------|
| 3/12/2024 | 30044 |

Please send remittance with copy of invoice to:

Attn: Mrs. Aisha Gonzalez
 P.O. Box 2724
 McAllen, Tx. 78502

Bill To:

Hidalgo County Precinct #3
 724 Breyfogle Rd.
 Mission, TX 78574

Project Info:

El Paraiso Project (C-22-0213-09-06)
 WA#2 - El Paraiso Health Clinic

B2Z JOB: # 3101B


Billing Period

February 2024

| Description | Contract | Previous Applications | Current Completed | Total Completed | % Complete |
|----------------------------------------------|--------------|-----------------------|-------------------|-----------------|-------------------|
| Construction Material Testing Services (CMT) | \$ 47,615.80 | \$ - | \$ 1,355.82 | \$ 1,355.82 | 3% |
| Total For This Billing Period | | | | | \$1,355.82 |

Work Authorization ~ Summary

| <u>WA No.</u> | <u>WA Amount</u> | <u>Previously Inv.</u> | <u>Percent Complete</u> | <u>Remaining Balance</u> |
|---------------|------------------|------------------------|-------------------------|--------------------------|
| 2 | \$47,615.80 | \$0.00 | 3% | \$46,259.98 |



Aisha Gonzalez - President


Client:
Hidalgo County
100 North Closner
Edinburg, TX 78539

Project:
3101B
El Paraiso- Health Clinic
1901 N. Los Ebanos Rd.
Alton, TX 78573

General Information

| | | | |
|---------------------|----------------|------------------------------|----------------------------|
| Sample Date: | 02/05/2024 | MF Sample Number: | 5262 |
| Sample From: | Stockpile | Material Description: | Flexbase |
| Sampled By: | Hector Vazquez | Location Details: | Martin Marietta Listos pit |

Test Results

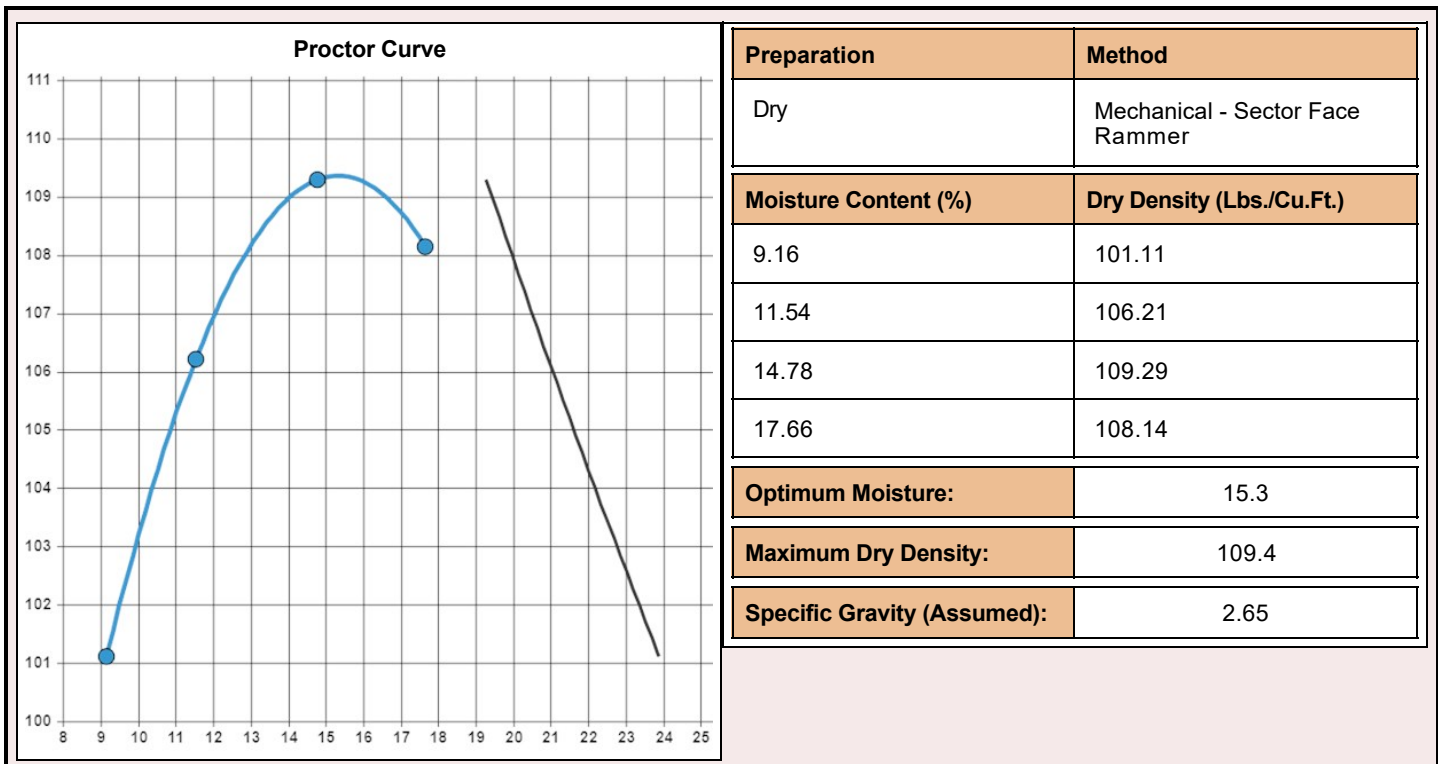

| | | | |
|-----------------------------|------------|---------------------------|-------------|
| Test Completed Date: | 02/08/2024 | Test Completed By: | Jorge Solis |
|-----------------------------|------------|---------------------------|-------------|

Test Results: The test is for informational purposes.

Test Method (As Applicable): Tex 114-E / ASTM D-698 Method-A, Method-B or Method-C ;
Tex 104-E, Tex 105-E, Tex 106-E / ASTM D4318 ;
Tex 110-E / ASTM C-136

Respectfully Submitted by B2Z Engineering

Jorge Solis

Jorge Solis, Laboratory Manager

Client:
 Hidalgo County
 100 North Closner
 Edinburg, TX 78539

Project:
 3101B
 El Paraiso- Health Clinic
 1901 N. Los Ebanos Rd.
 Alton, TX 78573

General Information

| | | | |
|---------------------|----------------|------------------------------|----------------------------|
| Sample Date: | 02/05/2024 | Sample Number: | 5262 |
| Sample From: | Stockpile | Material Description: | Flexbase |
| Sampled By: | Hector Vazquez | Location Details: | Martin Marietta Listos pit |

Sieve Analysis Results - Cumulative % Retained

| Sieve Size | Cumulative % Retained | Spec. Requirements | Pass/Fail |
|------------|-----------------------|--------------------|-----------|
| 2-1/2" | 0.0 | 0 | Pass |
| 1-3/4" | 3.5 | 0-10.0 | Pass |
| No. 4 | 50.7 | 45.0-75.0 | Pass |
| No. 40 | 81.3 | 60.0-85.0 | Pass |

Test Results: The above test result meets the technical specifications.

Atterberg Limits

| | |
|-------------------------------|------|
| LL (%) | 29 |
| PL (%) | 17 |
| Plastic Index: | 12 |
| Spec. Requirement Max: | ≤ 12 |
| Pass/Fail: | Pass |

Test Completed Date: 02/05/2024

Test Completed By: Jorge Solis

Test Method (As Applicable):
 Tex 110-E / ASTM C136; ASTM D6913;
 Tex 104-E, Tex 105-E, Tex 106-E / ASTM D4318 ;
 Tex 116-E; Tex 103-E / ASTM D2216; Tex 200-F; Tex 217-F

Respectfully Submitted by B2Z Engineering


 Jorge Solis, Laboratory Manager
