

CHANGE ORDER

No. 1


PROJECT <u>CR 210, 219, & 266 Project</u>	
DATE OF ISSUANCE <u>October 2, 2019</u>	EFFECTIVE DATE <u>When Signed by All Parties</u>
OWNER <u>Burnet County, Texas</u>	
OWNER's Contract No. _____	
CONTRACTOR <u>Pro Dirt Services, LLC</u>	ENGINEER <u>Greg Haley, P.E.</u>

You are directed to make the following changes in the Contract Documents (See Attachments):

Description: Delete the Pay Item "As-Built Drawings"
 Add Ty D Hot Mix at the Intersection of CR 266 and SH 29
 Revise the Quantity for the Pay Item "Remove Structures (Pipe) from 1 to 2
 Add the Provision to Use High Early Strength Cement to the CR 219 Location
 Reason for Change Order: 1) Requested by Burnet County

CHANGE IN CONTRACT PRICE:	CHANGE IN CONTRACT TIMES:
Original Contract Price	Original Contract Times
\$ <u>1,034,930.60</u>	Substantial Completion: <u>75</u> Ready for final payment: <u>90</u> days or dates
Net changes from previous Change Orders No. <u>0</u> to No. <u>1</u>	Net change from previous Change Orders No. <u>0</u> to No. <u>1</u>
\$ <u>0.00</u>	<u>0</u> days
Contract Price prior to this Change Order	Contract Times prior to this Change Order
\$ <u>1,034,930.60</u>	Substantial Completion: <u>75</u> Ready for final payment: <u>90</u> days
Net Increase (decrease) of this Change Order	Net Increase (decrease) of this Change Order
\$ <u>12,040.02</u>	<u>3</u> days
Contract Price with all approved Change Orders	Contract Times with all approved Change Orders
\$ <u>1,046,970.62</u>	Substantial Completion: <u>78</u> Ready for final payment: <u>93</u> days

RECOMMENDED:

By: Greg Haley, P.E.  By: [Signature]
 Engineer (Authorized Signature) Owner (Authorized Signature)
 Date: October 2, 2019 Date: 10-22-19
 APPROVED: ACCEPTED: 10/17/19

ATTACHMENT "A"
CHANGE ORDER NO. 1
COUNTY ROAD 210, 219, 266 PROJECT
BURNET COUNTY, TEXAS

LINE ITEM	PAY ITEM	DESCRIPTION	ORIGINAL CONTRACT				QUANTITY
			QUANTITY	UNIT	UNIT PRICE	AMOUNT	
1	010.16.1	SEQUENCE OF CONSTRUCTION	1	LS	\$ 35,000.00	\$ 35,000.00	1
2	010.16.2	FIELD ENGINEERING	1	LS	\$ 25,000.00	\$ 25,000.00	1
3	010.16.3	MOBILIZATION	1	LS	\$ 40,000.00	\$ 40,000.00	1
4	10.16.4	AS-BUILT DRAWINGS	1	LS	\$ 5,000.00	\$ 5,000.00	0
5	GEN. COND. ART. 5	BONDS AND INSURANCE	1	LS	\$ 25,000.00	\$ 25,000.00	1
6	102.4.5	SELECTIVE CLEARING AND GRUBBING	3	STA	\$ 2,500.00	\$ 6,750.00	3
7	104.4.1	REMOVE EXISTING ROADWAY	620	SY	\$ 8.00	\$ 4,960.00	620
8	106.4.1	SUBGRADE PREPARATION (6")	1,071	SY	\$ 7.00	\$ 7,497.00	1,071
9	200.5.1	EXCAVATION	60	CY	\$ 15.00	\$ 900.00	60
10	220.4.1	EMBANKMENT	92	CY	\$ 15.00	\$ 1,380.00	92
11	240.6.1	FLEXIBLE BASE, 6" DEPTH, DENSITY CONTROLLED	7,835	CY	\$ 32.00	\$ 250,720.00	7,835
12	TxDOT 251.1	REWORK BASE COURSES (TY C) (3") (ORD COMP)	49,749	SY	\$ 3.00	\$ 149,247.00	49,749
13	TxDOT 316	CHIP SEAL	43,124	SY	\$ 6.65	\$ 286,774.60	43,124
14	430.5.1	DRIVEWAY REMOVAL AND RECONSTRUCTION	8	SY	\$ 150.00	\$ 1,200.00	8
15	TxDOT 530	INTERSECTIONS, DRIVEWAYS, AND TURNOUTS	37	EA	\$ 500.00	\$ 18,500.00	37
16	310.4.1	REMOVING CONCRETE	106	SY	\$ 580.00	\$ 61,480.00	106
17	TxDOT 420	CONCRETE - CURB (EDGE BLOCKS)	22	EA	\$ 200.00	\$ 4,400.00	22
18	TxDOT 432	CONCRETE - CLASS "A"	57	CY	\$ 450.00	\$ 25,650.00	57
19	TxDOT 432	CONCRETE - CLASS "A" - TOEWALL	212	LF	\$ 50.00	\$ 10,600.00	212
20	TxDOT 467	SAFETY END TREATMENT TY II (SET) - DES 3 CMP	4	EA	\$ 1,500.00	\$ 6,000.00	4
21	TxDOT 469	REMOVING STRUCTURES (PIPE)	1	EA	\$ 2,500.00	\$ 2,500.00	2
22	600.5.1	30" CORRUGATED METAL PIPE (CMP)	230	LF	\$ 30.00	\$ 6,900.00	230
23	600.5.1	DES 3 CORRUGATED METAL PIPE (CMP)	166	LF	\$ 30.00	\$ 4,980.00	166
24	1100.9.1	TRENCH SAFETY, ALL DEPTHS	46	LF	\$ 2.00	\$ 92.00	46
25	TxDOT 503.1	BARRICADES, SIGNS, AND TRAFFIC HANDLING	1	LS	\$ 2,500.00	\$ 2,500.00	1

ATTACHMENT "A"
CHANGE ORDER NO. 1
COUNTY ROAD 210, 219, 266 PROJECT
BURNET COUNTY, TEXAS

LINE ITEM	PAY ITEM	DESCRIPTION	ORIGINAL CONTRACT				QUANTITY
			QUANTITY	UNIT	UNIT PRICE	AMOUNT	
31	TxDOT 666.1	REFL PAV MRK TY I (W) 8" (SLD) (100 MIL)	40	LF	\$ 40.00	\$ 1,600.00	40
32	TxDOT 666.1	REFL PAV MRK TY I (W) 12" (SLD) (100 MIL)	30	LF	\$ 30.00	\$ 900.00	30
33	TxDOT 666.1	REFL PAV MRK TY I (W) TURN ARROW	2	EA	\$ 500.00	\$ 1,000.00	2
34	SP 1000.1	PORTABLE CHANGEABLE MESSAGE SIGNS	4	EA	\$ 1,000.00	\$ 4,000.00	4
35	905.5.1	CONCRETE WASHOUTS	1	LS	\$ 500.00	\$ 500.00	1
36	750.10.1	LOCATING EXISTING UNDERGROUND FACILITIES	1	LS	\$ 1,000.00	\$ 1,000.00	1
36	300.16.1	HIGH EARLY STRENGTH CONCRETE					57
36	410.13	HOT MIX ASPHALT (1.5") - (TY D - TxDOT ITEM 340)					70
TOTAL AMOUNTS						\$ 1,034,930.60	

Change Order

PRO DIRT
SERVICES, LLC



Date: 9/26/2019
Owner: Burnet County
Project: CR 210, 219 & 266 Rehab
Change Order #:001

ProDirt Services, LLC
P.O. Box 1508
Pflugerville, Tx 78691

	Equipment/Material	Qty	Unit	Unit Cost	Total
1	Remove Structure(pipe)	1	LS	\$2,500.00	\$2,500.00
2	High Early Concrete ADD	57	CY	\$43.86	\$2,500.02
3					\$0.00
4					\$0.00
5					\$0.00
6					\$0.00
7					\$0.00
8					\$0.00
9					\$0.00
10					\$0.00
Description of work:				Sub-Total	\$5,000.02
Remove culvert at CR 266, replace Class A concrete W H/E on 219.				O&P	\$0.00
				Grand Total	\$5,000.02

Submitted By: Zachary Cason

Approved by: _____ Date: _____

Change Order

PRO DIRT
SERVICES, LLC



Date: 9/30/2019

Owner: Burnet County

Project: CR 210, 219 & 266 Rehab

Change Order #:002

ProDirt Services, LLC

P.O. Box 1508

Pflugerville, Tx 78691

	Equipment/Material	Qty	Unit	Unit Cost	Total
1	Option 1-Full overlay on CR 266(HMAC 1.5")	2100	TNS	\$47.00	\$98,700.00
2	Option 2-Overlay CR 266/SH29(HMAC 1.5")	70	TNS	\$172.00	\$12,040.00
3	Option 3-Overlay CR264/CR266(HMAC 1.5")	140	TNS	\$125.00	\$17,500.00
4					\$0.00
5					\$0.00
6					\$0.00
7					\$0.00
8					\$0.00
9					\$0.00
10					\$0.00
Description of work:				Sub-Total	\$128,240.00
Overlay options per Burnet County's request.				O&P	\$0.00
				Grand Total	\$128,240.00

Submitted By: Zachary Cason

Approved by: _____

Date: _____

BURNET CO. ROAD PROJECT PRECINCT 2


COUNTY ROADS 210, 219

BURNET COUNTY, TEXAS


PAVEMENT RECONSTRUCTION, FLEXIBLE BASE CHIP SEAL, AND STRUCTURE

INDEX OF SHEETS

SHEET NO.	DESCRIPTION
1.0	TITLE SHEET
2.0 - 2.12	GENERAL NOTES
3.0 - 3.2	PROJECT LAYOUT
4.0 - 4.2	EXISTING CONDITIONS AND DEMO PLAN
5.0 - 5.2	TYPICAL SECTIONS
6.0 - 6.6	PLAN LAYOUT COUNTY ROAD 210
7.0	PLAN AND PROFILE COUNTY ROAD 219
8.0 - 8.1	PLAN LAYOUT COUNTY ROAD 266
9.0	PLAN AND PROFILE COUNTY ROAD 266
10.0	OVERFLOW SECTION LAYOUT COUNTY ROAD 219
11.0 - 11.2	X-SECTS - ROADWAY COUNTY ROAD 219
12.0 - 12.2	X-SECTS - CULVERT COUNTY ROAD 219
13.0 - 13.1	X-SECTS-ROADWAY CR 266
14.0 - 14.6	EROSION CONTROL LAYOUT - CR 210
14.7	EROSION CONTROL LAYOUT - CR 219
14.8 - 14.9	EROSION CONTROL LAYOUT - CR 266
15.0	TRAFFIC CONTROL PLAN AND SEQUENCE OF CONSTRUCTION
16.0 - 16.1	TRAFFIC CONTROL PLAN COUNTY ROAD 219
17.0	PAVEMENT MARKING & SIGN LAYOUT
18.0 - 18.2	SWP3
19.0 - 19.3	DETAILS - EROSION CONTROL
20.0 - 20.3	DETAILS - SITE
21.0 - 21.2	*WZ(TD)-17; *WZ(UL)-13; *WZ(RCD)-13
22.0 - 22.2	*TCP(2-2)-18; *TCP(2-4)-18; *TCP(7-1)-13
23.0 - 23.2	*SMD (GEN)-08; *SMD-(SLIP-1)-08; *SMD-(SLIP-2)-08
24.0	*SMD-FRP
25.0	*FGA-15
26.0 - 26.1	*PM(1)-12 - *PM(2)-12
27.0 - 27.2	*D & OM(1)-15; *D & OM(2)-15; *D & OM(3)-15B
28.0 - 28.1	*SET P-PD-A
29.0 - 29.11	*BC(1)-14 - *BC(12)-14

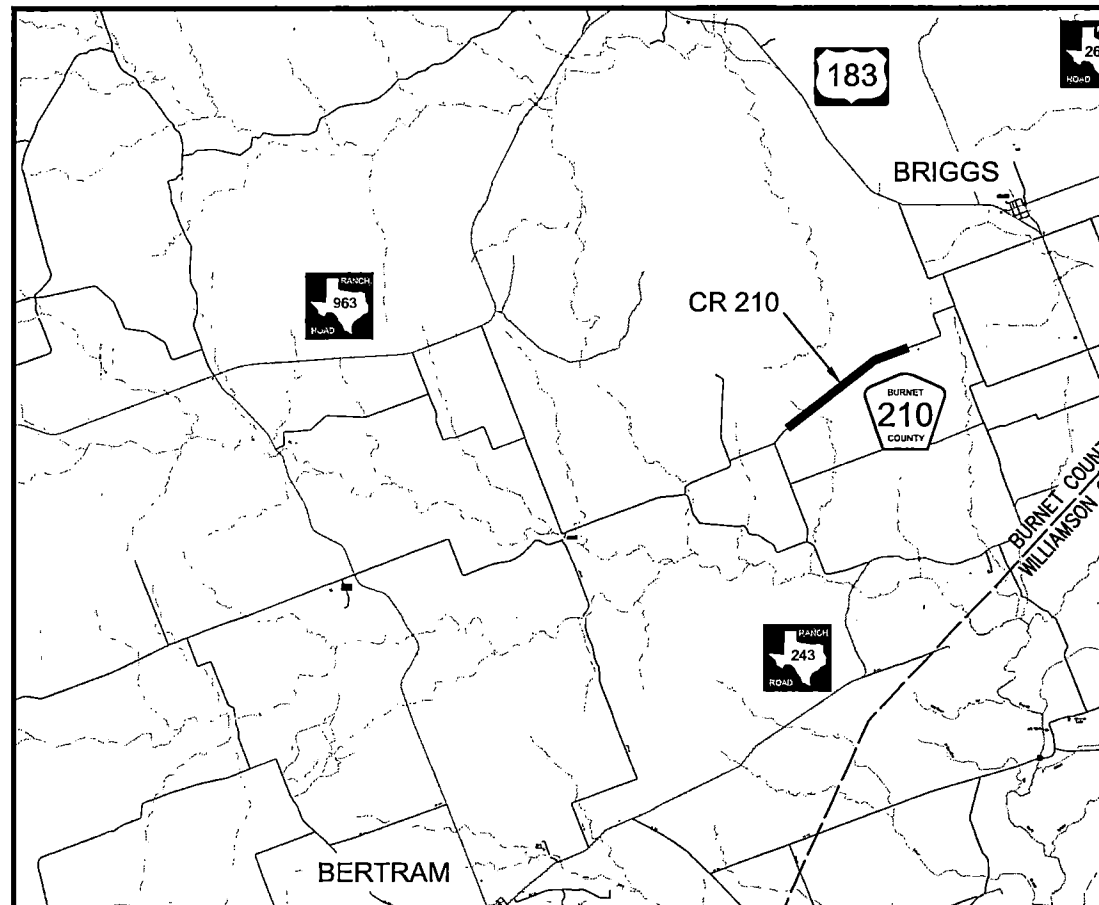

*THE STANDARD SHEETS SPECIFICALLY IDENTIFIED ABOVE, PREPARED AND PUBLISHED BY THE TEXAS DEPARTMENT OF TRANSPORTATION, HAVE BEEN SELECTED BY ME OR UNDER MY DIRECT SUPERVISION AND ARE APPLICABLE TO THIS PROJECT.



EDWARD F. CLARK &
NELLIE A. BURNS

HOWARD A. &
CARLA COURSEY

TOTAL ITEMS AND QUANTITIES - COUNTY ROAD 266		
ITEM	UNIT	QUANTITY
REWORK BASE COURSES	SY	11,467
SUBGRADE PREPARATION	SY	1,071
FLEX BASE	CY	1,871
CHIP SEAL (TWO COURSE SURFACE TREATMENT)	SY	9,835
DRIVEWAY REMOVAL AND RECONSTRUCTION	EA	3
INTERSECTIONS, DRIVEWAYS, AND TURNOUTS	EA	16

5:1 B/
3:1
2:1
*SEE
2.5' B/

MATCHLINE STA 34+00



INSTALL 1 EA
INTERSECTIONS,
DRIVEWAYS, &
TURNOUTS

INSTALL 1 EA
INTERSECTIONS,
DRIVEWAYS, &
TURNOUTS

INSTALL 1 EA
INTERSECTIONS,
DRIVEWAYS, &
TURNOUTS

35+00

L12

L13

40+00

L14

INSTALL 1 EA
INTERSECTIONS,
DRIVEWAYS, &
TURNOUTS

INSTALL 1 EA
INTERSECTIONS,
DRIVEWAYS, &
TURNOUTS

INSTALL 1 EA
INTERSECTIONS,
DRIVEWAYS, &
TURNOUTS



CW21-2

RECOMMEND PLACING ON
EACH END OF THE LAYING
OPERATION. RELOCATE AS
THE PAVING OPERATION
PROGRESSES. REMOVE AT
THE END OF THE DAY.



CWB-11



TO BE USED IF A
DIFFERENCE IN ELEVATION
GREATER THAN 1" EXISTS
BETWEEN ADJACENT LANES

THE HEADRICK
COLLECTIVE, LLC

CHERYL PEARSON

ZACHERY &
DAWN HAMILTON

JAMES ENGINEERING
& TECHNOLOGY, LLC

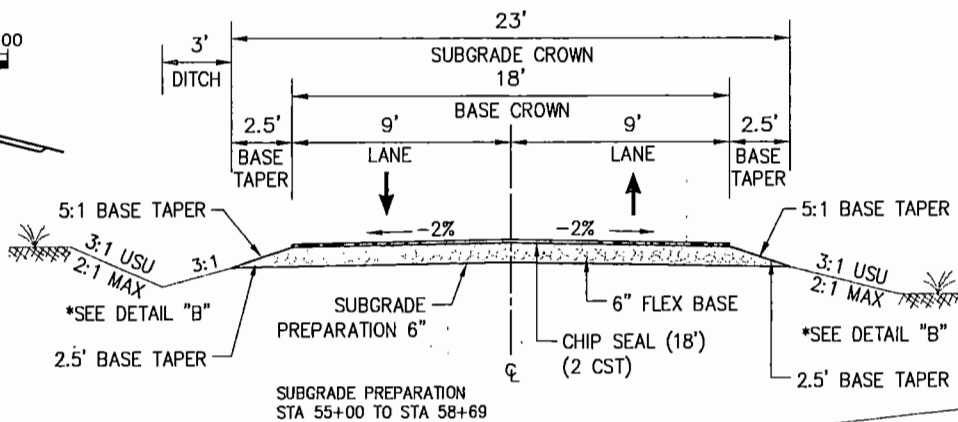

PAYMENT FOR TEMPORARY RAMP
INSTALLATION AND REMOVAL AND
INCIDENTAL DITCH GRADING IS
SUBSIDIARY TO THE CONTRACT

INSTALL 1 EA
INTERSECTIONS,
DRIVEWAYS, &
TURNOUTS

STA ±55+00
END REWORK BASE COURSES
BEGIN SUBGRADE PREPARATION
BEGIN TRANSITION
TO FULL DEPTH

55+00

STA ±57+00
END TRANSITION
TO FULL DEPTH

CARLA L. COSTON

50+00

L17

TA 48+00



Helen Cummins <hcummins@burnetcountytexas.org>

Change Order No. 1

1 message

Greg Haley <greg@kcengineering.com>

Mon, Oct 7, 2019 at 6:18 PM

To: "Damon Beierle (dbeierle@burnetcountytexas.org)" <dbeierle@burnetcountytexas.org>

Cc: "Burnet County Auditor (acctpay@burnetcountytexas.org)" <acctpay@burnetcountytexas.org>

Damon,

Attached is Change Order No. 1 for your CR 210, 219, & 266 Project. If you concur, please have it signed and dated in the spaces provided by someone authorized to execute change orders. After execution by the County, please return a scan to us to send to the contractor for his records.

If you need anything, please let us know. Thanks!

By:

Greg Haley, P.E.

K.C. Engineering, Inc.

705 N. Hwy 281

Suite 103

Marble Falls, TX 78654

Firm Reg. No. F-977

830-693-5635

www.kcengineering.com



The information contained in this E-mail message is confidential information intended only for use of the individual or entity named above. If the reader of this message is not the intended recipient, or the employee or agent responsible to deliver it to the intended recipient, you are hereby notified that any dissemination, distribution or copying of this communication is strictly prohibited.

This communication does not constitute an intention by the sender to conduct a transaction or make any agreement or contract by electronic means. Nothing contained herein or in any attached electronic file shall satisfy the requirements for a writing, nor constitute a contract or electronic signature, as those terms are defined in or contemplated by the Electronic Signatures In Global And National Commerce, 15 U. S. C. Section 7000 et seq. or any version of the Uniform Electronic Transaction Act adopted by any state or any other statute governing electronic transactions.

 **Change Order No. 1-Contractor Signed.pdf**

3778K
