

Received

MAR 14 2012 MAR 6 2012

HNTB Corporation
Round Rock

WILLIAMSON COUNTY, TEXAS

CHANGE ORDER NUMBER: 27

RECEIVED
MAR 09 2012
BY: PSD

- CONTRACTOR: J. C. Evans Construction
2. Change Order Work Limits: Sta. 622+00 to Sta. 624+00
3. Type of Change(on federal-aid non-exempt projects): Minor (Major/Minor)
4. Reasons: 1A, 4B (3 Max. - In order of importance - Primary first)

Project: 09 WC 706
Roadway: Williams Drive
Purchase Order Number: 2011-01-016

5. Describe the work being revised:

1A: Design Error or Omission. Incorrect PS&E. This Change Order provides compensation to the Contractor to modify the cross slope of the pedestrian crosswalk at the intersection of Wildwood and Williams Drive to meet ADA requirements. This work includes removing and replacing the asphalt surface to change the cross slope of the cross walk and removing and replacing the pedestrian ramps to match the new pavement slopes. 4B: Third Party Accommodation. Third party requested work. TXDOT requested additional signs on FM 3405.

6. Work to be performed in accordance with Items: See Attached
7. New or revised plan sheet(s) are attached and numbered: 113A
8. New Special Provisions to the contract are attached: ☐ Yes ☒ No
9. New Special Provisions to Item N/A No. N/A, Special Specification Item N/A are attached.

Each signatory hereby warrants that each has the authority to execute this Change Order (CO).

<p>The contractor must sign the Change Order and, by doing so, agrees to waive any and all claims for additional compensation due to any and all other expenses; additional changes for time, overhead and profit; or loss of compensation as a result of this change.</p>		<p>The following information must be provided</p>	
<p>THE CONTRACTOR Date 3/6/2012</p>		<p>Time Ext. #: N/A Days added on this CO: 0</p>	
<p>By Steve Owen</p>		<p>Amount added by this change order: \$25,870.26</p>	
<p>Typed/Printed Name Steve Owen</p>			
<p>Typed/Printed Title PROJ MANAGER</p>			

RECOMMENDED FOR EXECUTION:

Project Manager Date 3/6/12
Construction Observer

N/A
Design Engineer Date

Program Manager Date 3/9/2012

Design Engineer's Seal:

See Revised Plan Sheet

County Commissioner Precinct 1 Date
☐ APPROVED ☐ REQUEST APPROVAL

County Commissioner Precinct 2 Date
☐ APPROVED ☐ REQUEST APPROVAL

County Commissioner Precinct 3 Date
☐ APPROVED ☐ REQUEST APPROVAL

County Commissioner Precinct 4 Date
☐ APPROVED ☐ REQUEST APPROVAL

County Judge Date
APPROVED

WILLIAMSON COUNTY, TEXAS

CHANGE ORDER NUMBER: 27

Project # 09 WC 706

TABLE A: Force Account Work and Materials Placed into Stock[illegible]**TABLE B: Contract Items**

				ORIGINAL + PREVIOUSLY REVISED		ADD or (DEDUCT)	NEW		
ITEM	DESCRIPTION	UNIT	UNIT PRICE	QUANTITY	ITEM COST	QUANTITY	QUANTITY	ITEM COST	OVERRUN/ UNDERRUN
644-2001R	INS SM RD SN SUP & AM TY 10BWG (1) SA (P)	EA	\$450.00	0.00	\$0.00	3.00	3.00	\$1,350.00	\$1,350.00
644-2056	RELOCATE SM RD SUP & AM TY 10BWG	EA	\$305.00	0.00	\$0.00	1.00	1.00	\$305.00	\$305.00
644-WC01	REMOVE CHEVERON SIGN ASSEMBLIES	EA	\$250.00	0.00	\$0.00	3.00	3.00	\$750.00	\$750.00
9022-000	SUPPLY & INS CROSS TRF DOES NOT STOP ON EXT SIGN	EA	\$125.00	0.00	\$0.00	1.00	1.00	\$125.00	\$125.00
9023-000	MODIFY CROSS SLOPE OF WILDWOOD CROSS WALK	LS	\$23,340.26	0.00	\$0.00	1.00	1.00	\$23,340.26	\$23,340.26
TOTALS					\$0.00			\$25,870.26	\$25,870.26

CHANGE ORDER REASON(S) CODE CHART

1. Design Error or Omission	1A. Incorrect PS&E 1B. Other
2. Differing Site Conditions (unforeseeable)	2A. Dispute resolution (expense caused by conditions and/or resulting delay) 2B. Unavailable material 2C. New development (conditions changing after PS&E completed) 2D. Environmental remediation 2E. Miscellaneous difference in site conditions (unforeseeable)(Item 9) 2F. Site conditions altered by an act of nature 2G. Unadjusted utility (unforeseeable) 2H. Unacquired Right-of-Way (unforeseeable) 2I. Additional safety needs (unforeseeable) 2J. Other
3. County Convenience	3A. Dispute resolution (not resulting from error in plans or differing site conditions) 3B. Public relations improvement 3C. Implementation of a Value Engineering finding 3D. Achievement of an early project completion 3E. Reduction of future maintenance 3F. Additional work desired by the County 3G. Compliance requirements of new laws and/or policies 3H. Cost savings opportunity discovered during construction 3I. Implementation of improved technology or better process 3J. Price adjustment on finished work (price reduced in exchange for acceptance) 3K. Addition of stock account or material supplied by state provision 3L. Revising safety work/measures desired by the County 3M. Other
4. Third Party Accommodation	4A. Failure of a third party to meet commitment 4B. Third party requested work 4C. Compliance requirements of new laws and/or policies (impacting third party) 4D. Other
5. Contractor Convenience	5A. Contractor exercises option to change the traffic control plan 5B. Contractor requested change in the sequence and/or method of work 5C. Payment for Partnering workshop 5D. Additional safety work/measures desired by the contractor 5E. Other
6. Untimely ROW/Utilities	6A. Right-of-Way not clear (third party responsibility for ROW) 6B. Right-of-Way not clear (County responsibility for ROW) 6C. Utilities not clear 6D. Other

Williamson County Road Bond Program

**Williams Drive (RM 2338) from FM 3405 to DBWood
Williamson County Project No. 09WC706**

Change Order No. 27

Reason for Change

This Change Order provides compensation to the Contractor to modify the cross slope of the pedestrian crosswalk at the intersection of Wildwood and Williams Drive to meet ADA requirements. This work includes removing and replacing the asphalt surface to change the cross slope of the cross walk and removing & replacing the pedestrian ramps to match the new pavement slopes. In addition, this Change Order adds new Contract items for TxDOT requested modifications to the small signs on FM 3405.

Following is a summary of new item required for this Change Order:

Item	Description	Unit	Qty
644-2001	INS SM RD SN SUP & AM TY 10BWG (1)SA (P)	EA	3.00
644-2056	RELOCATE SM RD SUP & AM TY 10BWG	EA	1.00
644-WC01	REMOVE CHEVERON SIGN ASSEMBLIES	EA	3.00
9022-0000	SUPPLY & INS CROSS TRF DOES NOT STOP ON EXIST SIGN	EA	1.00
9023-0000	MODIFY CROSS SLOPE OF WILDWOOD CROSS WALK	LS	1.00

This Change Order results in a net increase of \$25,870.26 to the Contract amount, for an adjusted Contract amount of \$13,634,718.96. The original Contract amount was \$11,464,068.41. As a result of this and all Change Orders to date, \$2,170,650.55 has been added to the Contract resulting in an 18.9% net increase in the Contract Cost. No additional days will be added to or deducted from the Contract as a result of this Change Order.

HNTB Corporation

James Klotz, P.E.



Received

FEB 8 2012

HNTB Corporation
Round Rock

16409 Bratton lane
Austin, TX 78728
Office (512) 251-3713
Fax (512) 251-3709
jim@rammingpaving.com

BID PROPOSAL

SUBMITTED TO:

JC Evans
Ph: 512-848-2420

STEVE.OWEN@JCEVANS.COM

ATTENTION:

JOB NAME:

LOCATION:

Steve Owens
Asphalt HC Repair
Wildwood Dr
Georgetown, Tx

DATE: 4-Jan-12

We hereby submit specifications and estimates for the following asphalt paving listed above.
All scope of work includes labor, equipment and materials

DESCRIPTION OF Scope or Work	Units	Quantities	Thickness	Unit Price	Cost
Tack and Pave Type D HMA	SY	266	3"	\$58.61	\$15,590.26
Restripe W/Termal Paint	LS				\$2,250.00
R & R Wheel Chair Ramps	QTY	2		\$2,750.00	\$5,500.00
<u>We are Removing and Replacing Existing Asphalt)</u> <u>Pricing Includes Detouring Traffic / Milling of Existing Asphalt and Re-Stripe</u> <u>and New Concrete Wheel Chair Ramps</u> <u>(There is No Tax Included in this Pricing)</u>					\$23,340.26

(Pricing Only Includes what's Listed on this Proposal)

All material is guaranteed to be as specified. Any alteration or deviation from the above
specifications involving extra cost will be executed only upon written orders.
J.D. Ramming Paving Co. L.T.D carries General Liability and Workers Compensation Insurance

All material is guaranteed to be as specified. Any alteration or deviation from the above
specifications involving extra cost will be executed only upon written orders.
J.D. Ramming Paving Co. will carry general liability and workers compensation insurance.

When Accepting this Proposal please sign the bottom and email to jim@rammingpaving.com
or Fax within 15 Days from Bid Date for Quote to be Valid.

JAMES D RAMMING
Acceptance of Proposal


The above prices, specifications, and conditions are satisfactory and are hereby accepted.
Payment will be made as outlined above.

Accepted by:

Title

Company Name

Date

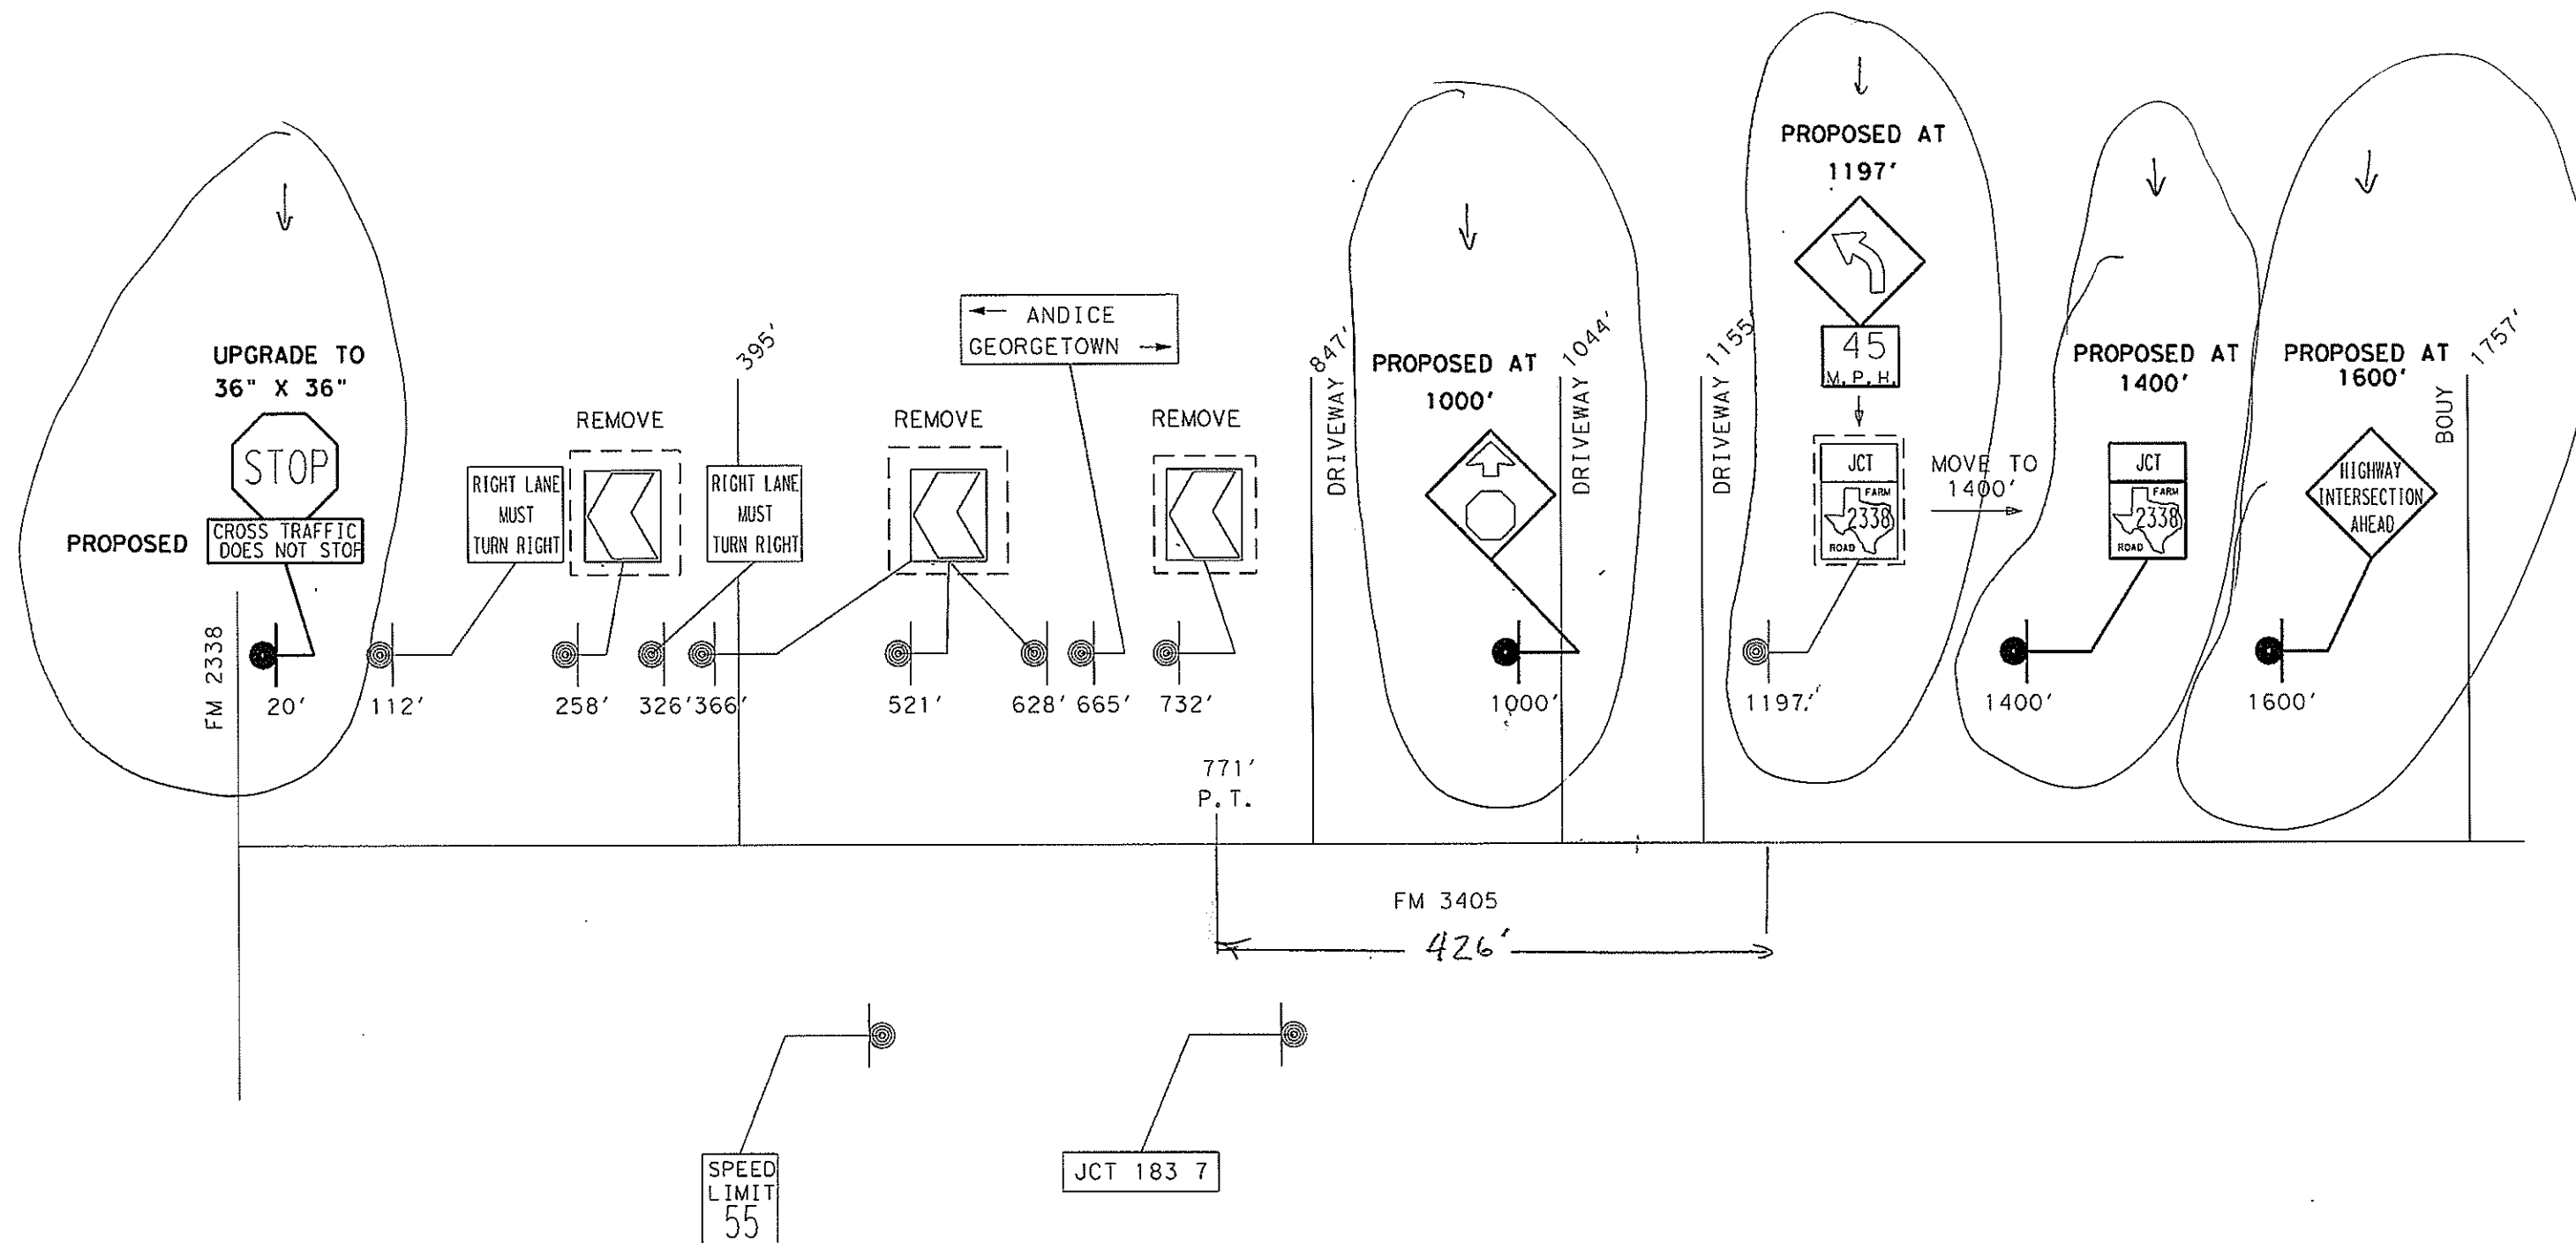



12909 Dessau Road
Austin, Texas 78754

(512) 990-9525
(512) 990-0336 Fax

PROJECT: WILLIAMS DRIVE
DATE: JULY 15, 2011
TERMS: PREPAY ONLY

QUOTE # 7M11-09

REVISED 2/9/12

SIGNAGE

ITEM	Description	Unit	Qty.	Price	Amount
1	INS SM RD SN SUP & AM TY 10BWG (1) SA (P)	EA	3	\$450.00	\$1,350.00
2	RELOCATE SM RD SN SUP & AM TY 10BWG	EA	1	\$305.00	\$305.00
3	REMOVE CHEVRON SING ASSEMBLIES	EA	3	\$250.00	\$750.00
4	SUPPLY AND INSTALL CROSS TRAFFIC DOES NOT STOP ON EXISTING SING POST	EA	1	\$125.00	\$125.00
TOTAL					\$2,530.00

NOTES AND EXCLUSIONS

SIGNAGE ITEMS

*NOTES AND EXCLUSIONS FROM ORIGINAL CONTRACT WILL APPLY.

GENERAL

* HT WARRANTS WORKMANSHIP AND MATERIALS ONLY. REPAIRS DUE TO NORMAL WEAR, VANDALISM, OR NEGLIGENCE WILL BE PERFORMED ON AN EXTRA WORK BASIS.

* ITEMS NOT SPECIFICALLY NOTED WILL BE ADDITIONAL.

* PRICES QUOTED ARE GOOD FOR 30 DAYS.

* **Any subcontracts entered into as a result of this quotation will be bound by the following indemnity clause:**

"Subcontractor shall indemnify and save harmless the contractor and its officers, agents, and employees from all suits, actions, losses, damages, claims, or liability of any character, type or description, including without limiting the generality of the foregoing all expenses of litigation, court costs, and attorney's fees provided such claims, damages and reasonable expenses are attributable to injury or death to any person, or injury to any property, received or sustained by any person or persons or property, arising out of, or occasioned by the negligent acts of subcontractor or its agents or employees, in the execution or performance of this contract. Subcontractors obligation to indemnify contractor shall extend only to the percentage of negligence of subcontractor in contributing to such claims, demands, liabilities or reasonable expenses."

SUBMITTED _____
MATT LANGENFELD / ESTIMATOR

ACCEPTED: _____
Name

Title

Date

Job/PO#
