

Received

JUL 12 2011

HNTB Corporation  
Round Rock

**WILLIAMSON COUNTY, TEXAS**

CHANGE ORDER NUMBER: 7

1. CONTRACTOR: Joe Bland Construction, L.P.
2. Change Order Work Limits: Sta. 272+01 to Sta. 457+12
3. Type of Change (on federal-aid non-exempt projects): Minor (Major/Minor)
4. Reasons: 2E, 4B (3 Max. - In order of importance - Primary first)

Project: 09WC722A  
Roadway: RM 2338 Phase 2  
CSJ: 0211-01-023

5. Describe the work being revised:

**2E: Differing Site Conditions (Unforeseeable). Miscellaneous Difference in Site Conditions. 4B: Third Party Accommodation. Third Party Requested Work.** Revises contract quantities and documents revisions to the installation of the Chisholm Trail Special Utility District (CTSUD) waterlines, to accommodate actual location of existing waterlines and water meters, as well as future realignment of CR 245.

6. Work to be performed in accordance with Items: See Attached
7. New or revised plan sheet(s) are attached and numbered: CTSUD Sheets 5,13 and 14
8. New Special Provisions to the contract are attached: ☐ Yes ☒ No

9. New Special Provisions to Item N/A No. N/A, Special Specification Item N/A are attached.

Each signatory hereby warrants that each has the authority to execute this Change Order (CO).

<p><small>The contractor must sign the Change Order and, by doing so, agrees to waive any and all claims for additional compensation due to any and all other expenses; additional changes for time, overhead and profit; or loss of compensation as a result of this change.</small></p> <p>THE CONTRACTOR Date <u>7-12-2011</u></p> <p>By <u>[Signature]</u></p> <p>Typed/Printed Name <u>DAVID R. BURROUGHS</u></p> <p>Typed/Printed Title <u>P.M.</u></p>	<p><b>The following information must be provided</b></p> <p>Time Ext. #: <u>N/A</u> Days added on this CO: <u>0</u></p> <p>Amount added by this change order: <u>\$31,951.08</u></p>
---	--

RECOMMENDED FOR EXECUTION:

[Signature] P.E. 7/13/11  
Project Manager  
Construction Observer

County Commissioner Precinct 1 Date  
☐ APPROVED ☐ REQUEST APPROVAL

County Commissioner Precinct 2 Date  
☐ APPROVED ☐ REQUEST APPROVAL

County Commissioner Precinct 3 Date  
☐ APPROVED ☐ REQUEST APPROVAL

County Commissioner Precinct 4 Date  
☐ APPROVED ☐ REQUEST APPROVAL

Design Engineer Date

Program Manager Date

Design Engineer's Seal:

See Revised Plans

[Signature] 07-21-11  
☒ APPROVED County Judge Date

## WILLIAMSON COUNTY, TEXAS

CHANGE ORDER NUMBER: 7

Project # 09WC722A

**TABLE A: Force Account Work and Materials Placed into Stock**[illegible]**TABLE B: Contract Items**[illegible]

## WILLIAMSON COUNTY, TEXAS

CHANGE ORDER NUMBER: 7

Project # 09WC722A

TABLE B: Contract Items (Continued)

[illegible]

## CHANGE ORDER REASON(S) CODE CHART

1. Design Error or Omission	1A. Incorrect PS&E 1B. Other
2. Differing Site Conditions (unforeseeable)	2A. Dispute resolution (expense caused by conditions and/or resulting delay) 2B. Unavailable material 2C. New development (conditions changing after PS&E completed) 2D. Environmental remediation 2E. Miscellaneous difference in site conditions (unforeseeable)(Item 9) 2F. Site conditions altered by an act of nature 2G. Unadjusted utility (unforeseeable) 2H. Unacquired Right-of-Way (unforeseeable) 2I. Additional safety needs (unforeseeable) 2J. Other
3. County Convenience	3A. Dispute resolution (not resulting from error in plans or differing site conditions) 3B. Public relations improvement 3C. Implementation of a Value Engineering finding 3D. Achievement of an early project completion 3E. Reduction of future maintenance 3F. Additional work desired by the County 3G. Compliance requirements of new laws and/or policies 3H. Cost savings opportunity discovered during construction 3I. Implementation of improved technology or better process 3J. Price adjustment on finished work (price reduced in exchange for acceptance) 3K. Addition of stock account or material supplied by state provision 3L. Revising safety work/measures desired by the County 3M. Other
4. Third Party Accommodation	4A. Failure of a third party to meet commitment 4B. Third party requested work 4C. Compliance requirements of new laws and/or policies (Impacting third party) 4D. Other
5. Contractor Convenience	5A. Contractor exercises option to change the traffic control plan 5B. Contractor requested change in the sequence and/or method of work 5C. Payment for Partnering workshop 5D. Additional safety work/measures desired by the contractor 5E. Other
6. Untimely ROW/Utilities	6A. Right-of-Way not clear (third party responsibility for ROW) 6B. Right-of-Way not clear (County responsibility for ROW) 6C. Utilities not clear 6D. Other





## CHANGE ORDER MEMORANDUM

TO: James D. Klotz, P. E. HNTB Corp.	Date: June 22, 2011
	Project: 09WC722A
	Control: 2211-01-023
From: Darren Muenster, Construction Project Manager, Atkins	Highway: RM 2338
	County: Williamson

Re: Change Order No. 07, CTSUD Water Line revisions

---

Enclosed find Change Order No. 07 for the above referenced project. This change order documents revisions to the installation of the Chisholm Trail Special Utility District (CTSUD) waterlines to adjust for actual site conditions.


All changes to the waterlines were reviewed and approved by CTSUD. Refer to the attached Plan Sheets for details. Plan revisions for the CTSUD waterline were necessary at the following locations:

- The actual locations of existing waterlines in the vicinity of Ronald Reagan Blvd and CR 248 differed from the locations shown on the plans. Plan revisions (by CTSUD/Halff Associates) and quantity revisions were required to connect proposed waterline "A" to the existing waterlines on each side of the roadway.
- The layout of waterline "D" was revised to accommodate the future realignment of CR 245 at the intersection with RM 2338. These changes included additional encasement pipe and fittings.

This Change Order is considered minor with reasons 2E, Miscellaneous Difference in Site Conditions, and 4B, Third Party Requested work. No new bid items were added as a result of these changes.

This Change Order results in a net increase of \$31,951.08 to the Contract amount, for an adjusted total Contract amount of \$8,824,125.88. The original contract amount was \$8,700,198.56. As a result of this and all Change Orders to date, \$123,927.32 has been added to the Contract, resulting in a 1.4% net increase in the Contract Cost. No additional days will be added to the Contract as a result of this Change Order.



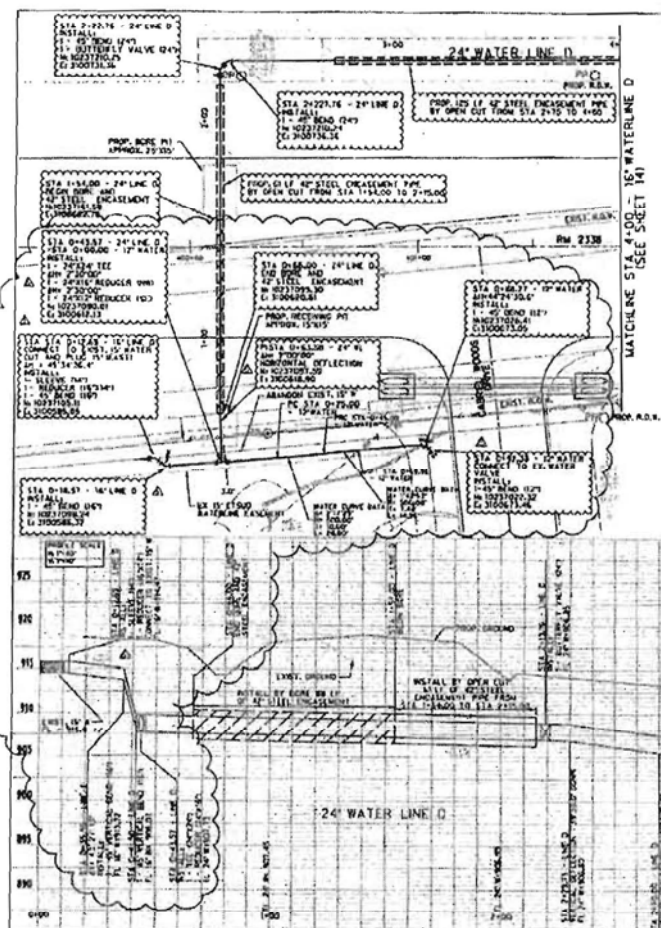


MATCHLINE STA 4+00 - 16\"/>

PROJ. A.D.



- NOTES:
1. THE LOCATION AND DEPTH OF ALL EXISTING WATER LINES SHOWN ON THE PLANS ARE APPROXIMATE AND FIELD SURVEY IS REQUIRED TO LOCATE EXISTING LINES. EXISTING LINES NOT SHOWN ON THE PLANS ARE LOCATED BY FIELD SURVEY AND INDICATED BY THE LOCATION PREPARED TO THE SURVEY OF CONSTRUCTION.
  2. THE WATER SERVICE LOCATIONS SHOWN ARE APPROXIMATE OR UNKNOWN. CONSTRUCTION IS REQUIRED TO LOCATE ALL EXISTING SERVICES AND RECORDS.
  3. PIPES IN CURVES OR SLOPED AT ANGLES SHALL BE LINED STRAIGHT AND SHALL BE LINED BY THE METHOD OF BENTONITE. THE PIPES AT THE CURVE SHALL BE LINED TO THE CURVE AND SHALL NOT BE LINED AT AN ANGLE TO THE CURVE.

- LEGEND:
- EXISTING 24\"/>

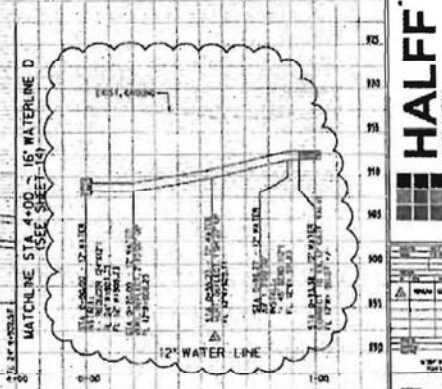

**HALFF**  
 ENGINEERS, INC.  
 10000 WEST 10TH AVENUE  
 SUITE 100  
 DENVER, CO 80231  
 (303) 751-1000



