

RECEIVED
NOV 28 2011
BY: PST

WILLIAMSON COUNTY, TEXAS

CHANGE ORDER NUMBER: 13

1. CONTRACTOR: JC Evans Construction
2. Change Order Work Limits: Sta. 23+08 to Sta. 132+22.19
3. Type of Change (on federal-aid non-exempt projects): Minor (Major/Minor)
4. Reasons: 2E, 1A (3 Max. - In order of importance - Primary first)

Project: 08WC608

Roadway: Westinghouse Rd

Purchase Order Number: _____

5. Describe the work being revised:

2E: Differing Site Conditions. Miscellaneous difference in site conditions (unforeseeable). Adjustment of quantities to meet field conditions. **1A: Design Error or Omission.** Incorrect PS&E. Addition of contract item to compensate the Contractor for additional work related to revisions to the outfall of the detention pond, including mobilization, drilling, dowels, grout, rebar, forms, concrete, and backfill behind the pond curb.

6. Work to be performed in accordance with Items: See Attached
7. New or revised plan sheet(s) are attached and numbered: 158
8. New Special Provisions to the contract are attached: ☐ Yes ☒ No

9. New Special Provisions to Item N/A No. N/A Special Specification Item N/A are attached.

Each signatory hereby warrants that each has the authority to execute this Change Order (CO).

The contractor must sign the Change Order and, by doing so, agrees to waive any and all claims for additional compensation due to any and all other expenses, additional changes for time, overhead and profit; or loss of compensation as a result of this change.

The following information must be provided

Time Ext. #: N/A Days added on this CO: 0

Amount added by this change order: (\$157,582.36)

THE CONTRACTOR Date 11/21/11

By Steve Owen

Typed/Printed Name Steve Owen

Typed/Printed Title P.M.

RECOMMENDED FOR EXECUTION:

[Signature] C.E. 11/23/11
Project Manager Date

N/A
Design Engineer Date

[Signature] 11/29/2011
Program Manager Date

Design Engineer's Seal:

See Revised Plan Sheet

County Commissioner Precinct 1 Date
☐ APPROVED ☐ REQUEST APPROVAL

County Commissioner Precinct 2 Date
☐ APPROVED ☐ REQUEST APPROVAL

County Commissioner Precinct 3 Date
☐ APPROVED ☐ REQUEST APPROVAL

County Commissioner Precinct 4 Date
☐ APPROVED ☐ REQUEST APPROVAL

[Signature] 12-12-2012
☒ APPROVED County Judge Date

WILLIAMSON COUNTY, TEXAS

CHANGE ORDER NUMBER: 13

Project #

08WC608

TABLE A: Force Account Work and Materials Placed into Stock

[illegible]

TABLE 8: Contract Items

TABLE 01. CONTRIBUTIONS									
ITEM	DESCRIPTION	UNIT	UNIT PRICE	ORIGINAL + PREVIOUSLY REVISED		ADD or (DEDUCT)		NEW	
				QUANTITY	ITEM COST	QUANTITY	ITEM COST	QUANTITY	ITEM COST
150-2002	BLADING	HR	\$50.00	200.00	\$10,000.00	(200.00)	\$0.00	0.00	\$0.00
164-2029	CELL FBR MLCH SEED(TEMP)(WARM)	SY	\$0.20	28,606.00	\$5,721.20	(28,606.00)	\$0.00	0.00	\$0.00
164-2031	CELL FBR MLCH SEED(TEMP)(COOL)	SY	\$0.20	28,606.00	\$5,721.20	(28,606.00)	\$0.00	0.00	\$0.00
310-2005	PRIME COAT (MC-30 OR AE-P)	GAL	\$1.90	16,275.00	\$30,922.50	(489.00)	\$29,993.40	15,786.00	\$29,993.40
402-2002	TRENCH EXCAVATION PROTECTION	LF	\$1.00	5,405.00	\$5,405.00	667.00	\$6,072.00	6,072.00	\$6,072.00
430-2012	CL C CONC FOR EXT STRUC (CULV) (3'X2')	LF	\$390.00	24.00	\$9,360.00	3.00	\$1,170.00	27.00	\$10,530.00
432-2002	RIPRAP (CONC)(5 IN)	CY	\$118.31	414.00	\$131,780.34	73.50	\$8,685.79	487.50	\$155,176.13
464-2003	RC PIPE (CL III)(18 IN)	LF	\$40.44	9,759.00	\$394,653.96	(20.00)	\$393,845.16	9,739.00	\$393,845.16
464-2005	RC PIPE (CL III)(24 IN)	LF	\$52.00	1,172.00	\$60,944.00	2.00	\$104.00	1,174.00	\$104.00
506-2002	ROCK FILTER DAMS (INSTALL) (TY 2)	LF	\$20.00	236.00	\$4,720.00	(72.00)	\$3,280.00	164.00	\$3,280.00
506-2009	ROCK FILTER DAMS (REMOVE)	LF	\$1.00	236.00	\$236.00	(72.00)	\$0.00	164.00	\$164.00
506-2016	CONSTRUCTION EXITS (INSTALL) (TY 1)	SY	\$150.00	100.00	\$15,000.00	(100.00)	\$0.00	0.00	\$0.00
506-2019	CONSTRUCTION EXITS (REMOVE)	SY	\$2.00	100.00	\$200.00	(100.00)	\$0.00	0.00	\$0.00
506-2034	TEMPORARY SEDIMENT CONTROL FENCE	LF	\$2.25	13,582.00	\$30,559.50	1,554.00	\$34,056.00	15,136.00	\$34,056.00
506-2040	TEMP SEDIMENT CONTROL FENCE (REMOVE)	LF	\$0.10	13,582.00	\$1,358.20	1,554.00	\$153.60	15,136.00	\$153.60
508-2001	CONSTRUCTING DETOURS	STA	\$2,521.00	44.00	\$110,924.00	(15.00)	\$73,109.00	29.00	\$73,109.00
512-2008	PORT CTB (FUR & INST)(LOW PROF)TY 1)	LF	\$30.00	2,800.00	\$84,000.00	(2,722.00)	\$2,340.00	78.00	\$2,340.00
512-2009	PORT CTB (FUR & INST)(LOW PROF)TY 2)	LF	\$30.00	280.00	\$8,400.00	(280.00)	\$0.00	0.00	\$0.00
512-2044	PORT CTB (REMOVE)(LOW PROF)TY 1)	LF	\$3.00	2,800.00	\$8,400.00	(2,722.00)	\$234.00	78.00	\$234.00
512-2045	PORT CTB (REMOVE)(LOW PROF)TY 2)	LF	\$3.00	280.00	\$840.00	(280.00)	\$0.00	0.00	\$0.00
TOTALS					\$905,645.90		\$771,361.29		\$134,284.62

TABLE B: Contract Items (Continued)

[illegible]

CHANGE ORDER REASON(S) CODE CHART

1. Design Error or Omission	1A. Incorrect PS&E 1B. Other
2. Differing Site Conditions (unforeseeable)	2A. Dispute resolution (expense caused by conditions and/or resulting delay) 2B. Unavailable material 2C. New development (conditions changing after PS&E completed) 2D. Environmental remediation 2E. Miscellaneous difference in site conditions (unforeseeable)(Item 9) 2F. Site conditions altered by an act of nature 2G. Unadjusted utility (unforeseeable) 2H. Unacquired Right-of-Way (unforeseeable) 2I. Additional safety needs (unforeseeable) 2J. Other
3. County Convenience	3A. Dispute resolution (not resulting from error in plans or differing site conditions) 3B. Public relations improvement 3C. Implementation of a Value Engineering finding 3D. Achievement of an early project completion 3E. Reduction of future maintenance 3F. Additional work desired by the County 3G. Compliance requirements of new laws and/or policies 3H. Cost savings opportunity discovered during construction 3I. Implementation of improved technology or better process 3J. Price adjustment on finished work (price reduced in exchange for acceptance) 3K. Addition of stock account or material supplied by state provision 3L. Revising safety work/measures desired by the County 3M. Other
4. Third Party Accommodation	4A. Failure of a third party to meet commitment 4B. Third party requested work 4C. Compliance requirements of new laws and/or policies (impacting third party) 4D. Other
5. Contractor Convenience	5A. Contractor exercises option to change the traffic control plan 5B. Contractor requested change in the sequence and/or method of work 5C. Payment for Partnering workshop 5D. Additional safety work/measures desired by the contractor 5E. Other
6. Untimely ROW/Utilities	6A. Right-of-Way not clear (third party responsibility for ROW) 6B. Right-of-Way not clear (County responsibility for ROW) 6C. Utilities not clear 6D. Other

Williamson County Road Bond Program

**Westinghouse Rd
Williamson County Project No. 08WC608**

Change Order No. 13

Reason for Change

This Change Order provides for balancing the overrun / underrun Contract quantities for the project as a result of addressing field conditions not accounted for in the original plan quantities.

This Change Order compensates the Contractor for additional work related to revisions to the outfall of the detention pond, including mobilization, drilling, dowels, grout, rebar, forms, concrete, and backfill behind the pond curb.


Following is a summary of the new item required for this change order.

ITEM	DESCRIPTION	QTY	UNIT
9999-113	DETENTION POND MODIFICATIONS	1	LS

The change results in a net decrease of \$157,582.36 to the Contract amount, for an adjusted Contract total of \$6,485,463.20. The original Contract amount was \$5,864,053.94. As a result of this and all Change Orders to date, \$621,409.26 has been added to the Contract, resulting in a 10.6% net increase in the Contract cost. No additional days will be added to or deducted from the Contract as a result of this Change Order.


HNTB Corporation

James Klotz, P.E.

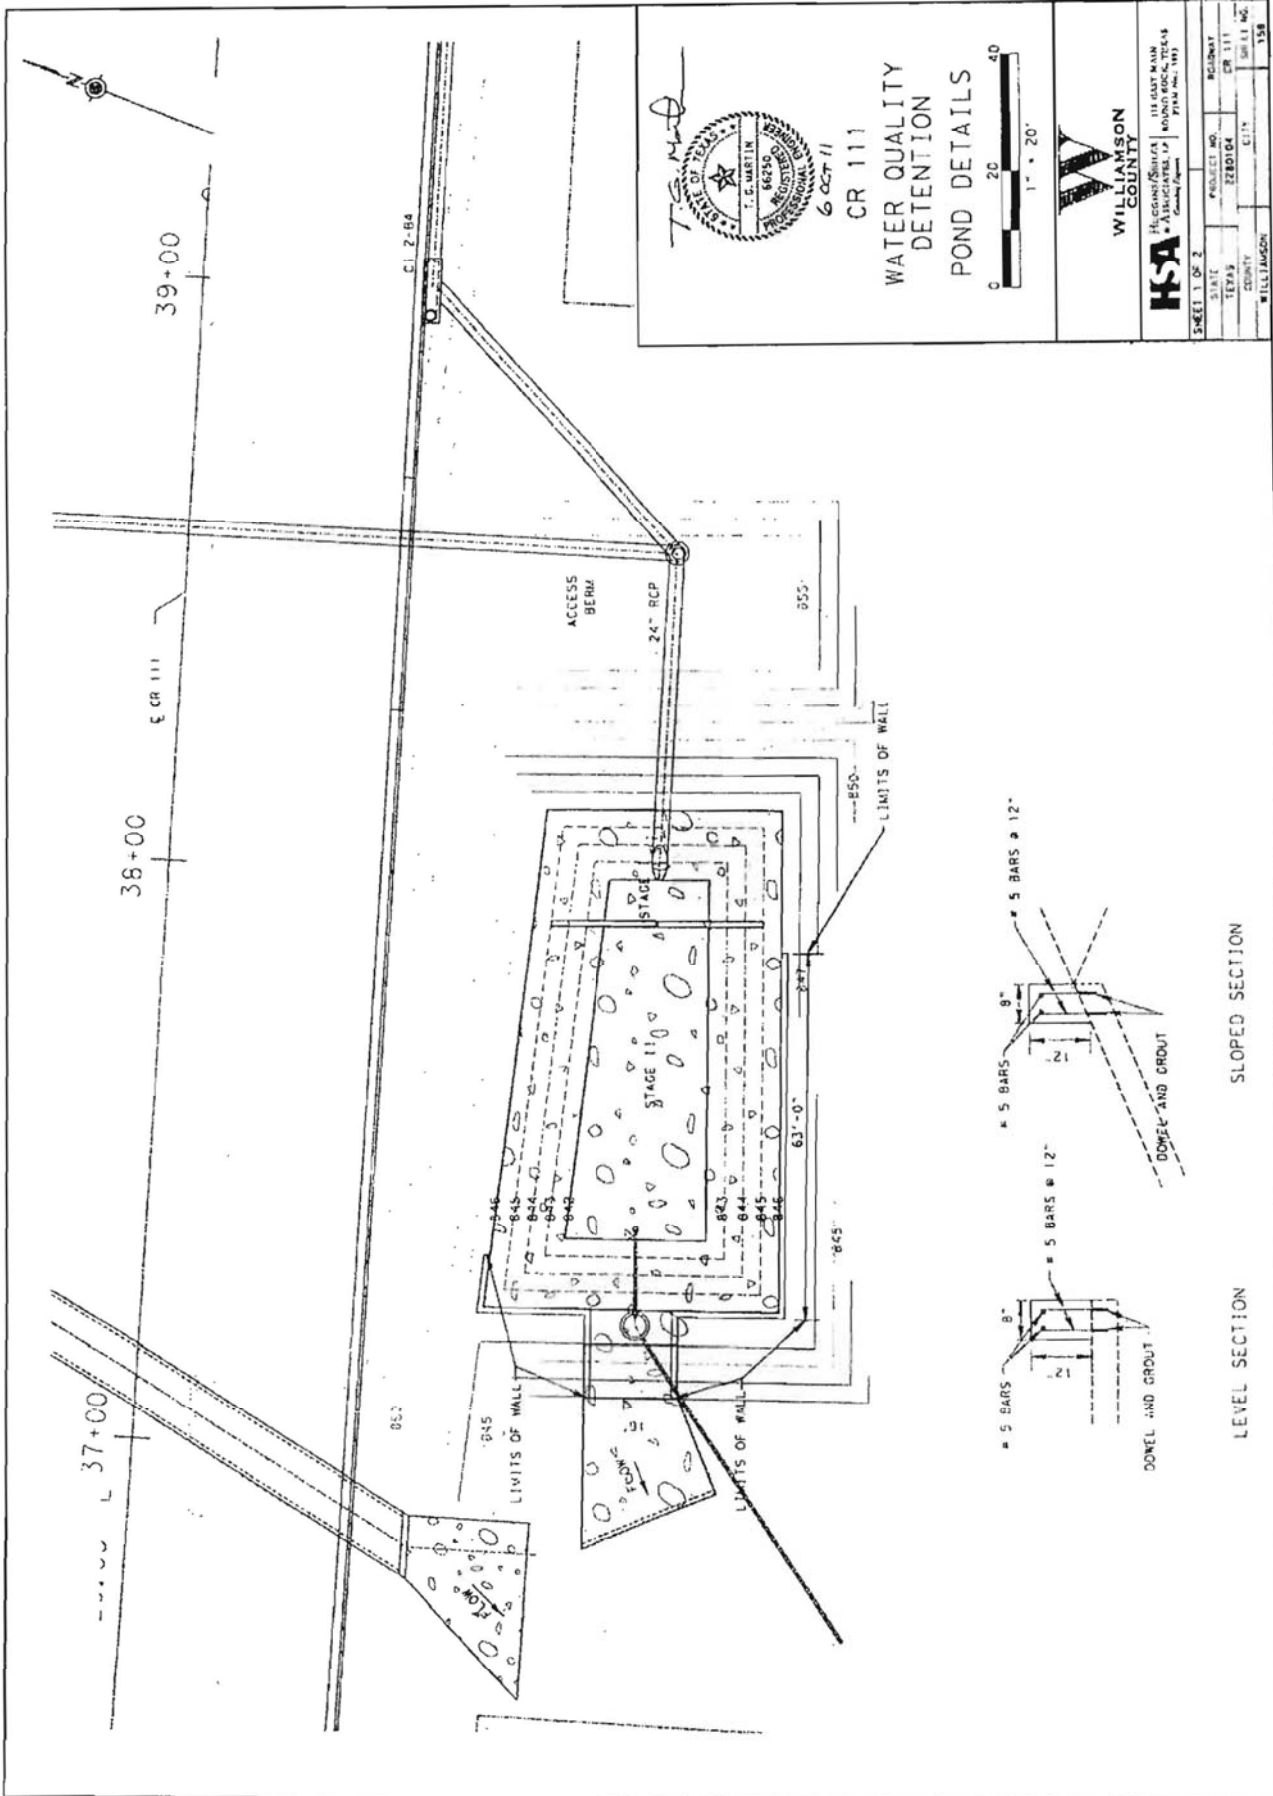

SLOPED SECTION

LEVEL SECTION



FILE, NOTES
DATE, NUMBER

TIME, NUMBER
